Hanover Community School Corporation
Construction Projects

Board Report
August 23, 2022



Hanover Community School Corporation
Construction Projects

Board Report
August 23, 2022

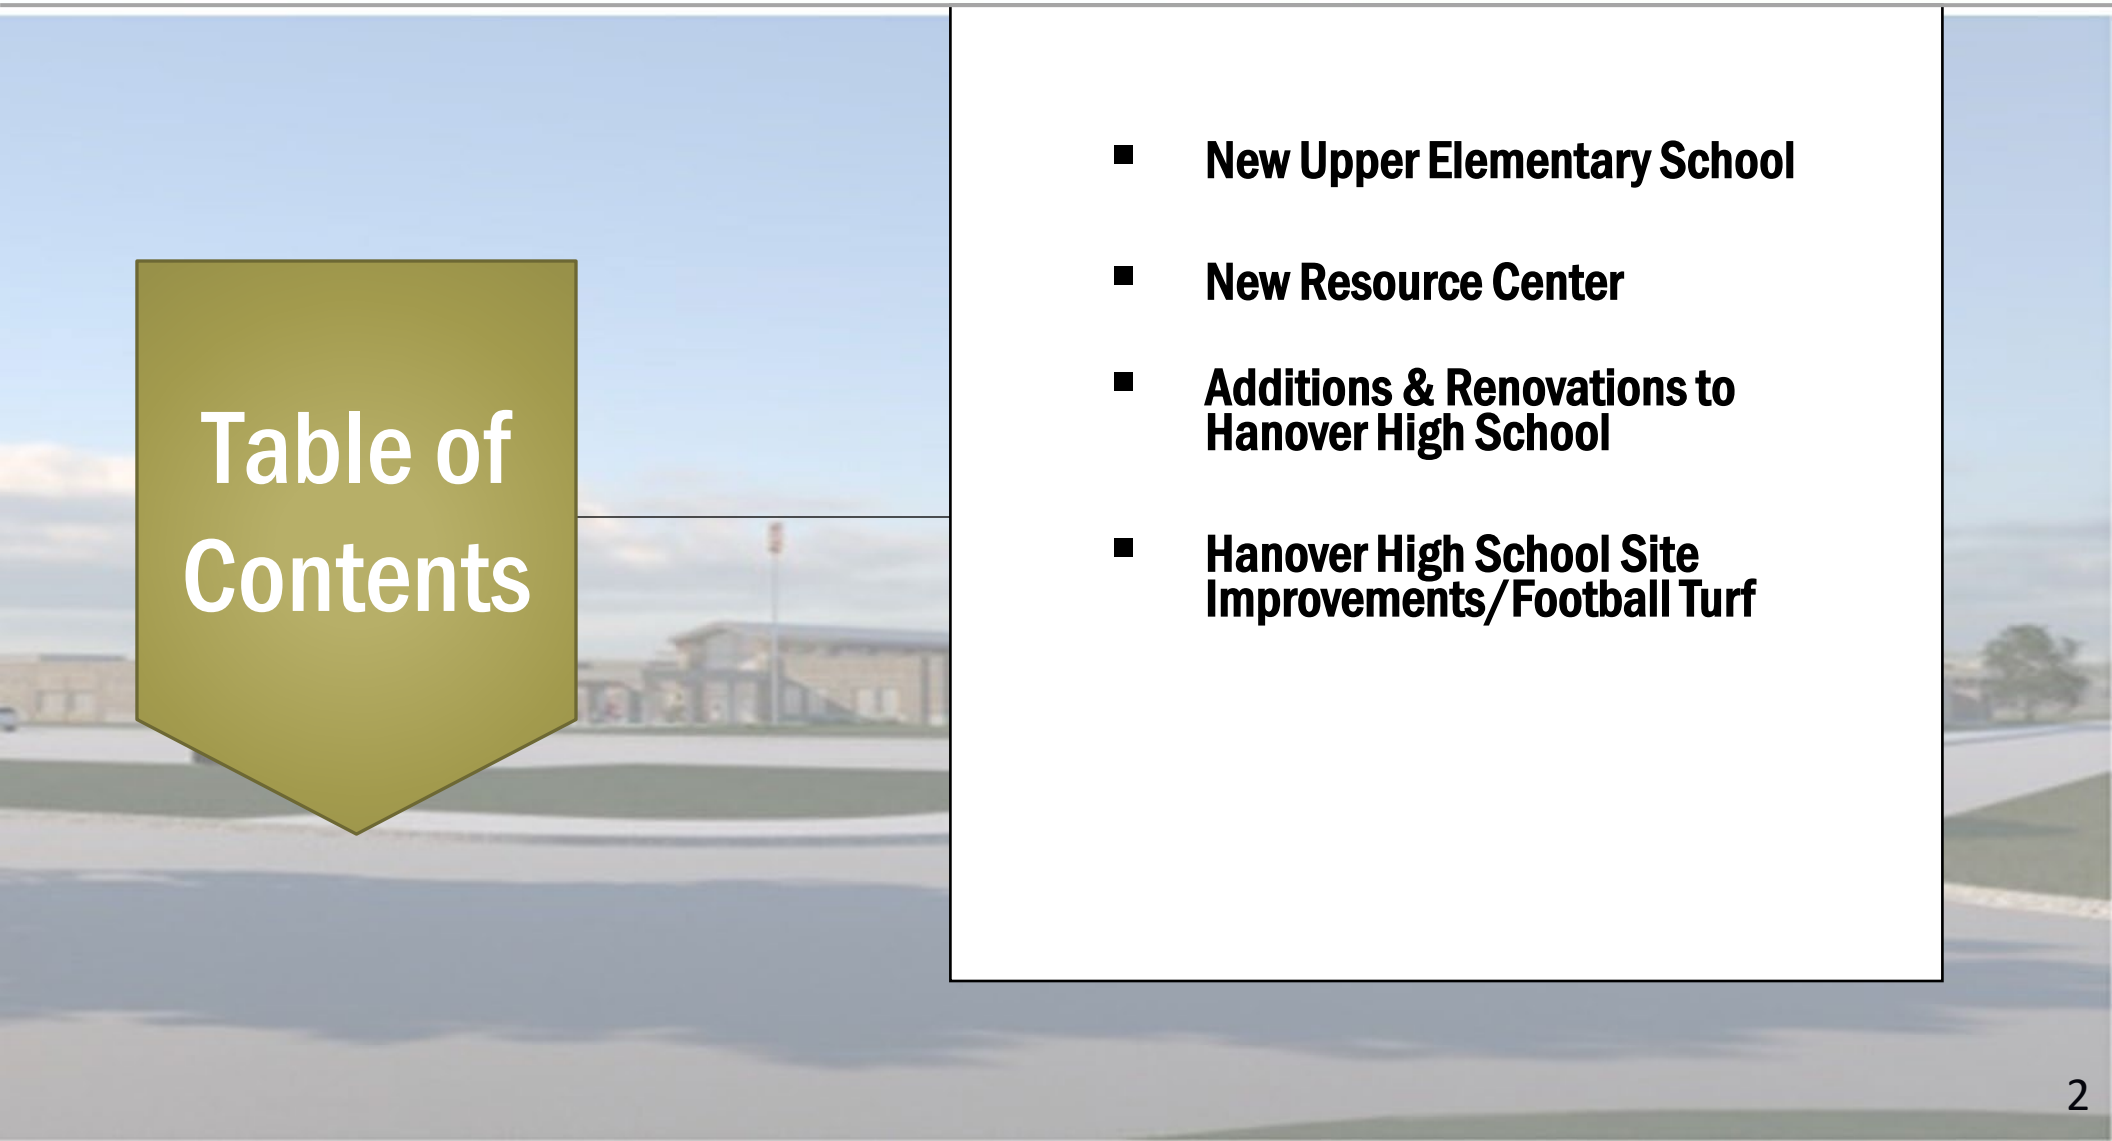


Table of Contents

- New Upper Elementary School
- New Resource Center
- Additions & Renovations to Hanover High School
- Hanover High School Site Improvements/Football Turf

Progress Photographs



Front Entry of Red Cedars

New Upper Elementary:

- Turned over school for start of the school year
- Completed finishes in corridors
- Completed remaining doors and hardware
- Installed temporary key cores for teacher use

Progress Photographs



Cafeteria

New Upper Elementary:

Next Four Weeks

- Complete punch list items
- Install permanent key cores upon delivery
- Begin Gymnasium floor
- Complete remaining exterior grading and seeding

Progress Photographs



Resource Center Aerial

New Resource Center:

- Continued wall finishes within the New Admin building
- Completed concrete floors in Bus Garage
- Continued roofing on Bus Garage
- Began underground utilities for fuel distribution equipment

Progress Photographs



Resource Center Fuel Island

New Resource Center:

Next Four Weeks

- Complete ceilings and finishes within New Admin Building
- Complete underground utilities for fuel distribution equipment
- Pave concrete and asphalt lots/drives
- Install overhead doors for Bus Garage
- Paint office areas for Bus Garage, Mechanics and Maintenance Buildings

Progress Photographs



High School Main Entry

High School Additions & Renovations:

- Turned over new CTE classrooms and Art rooms for use
- Completed re-install of VCT floor in remaining science classrooms
- Completed VCT corridor install in majority of academic areas
- Installed temporary partitions to separate remaining construction areas from staff and students
- Continued renovations in Music/Choir areas, Building Trades and CTE Lab areas

Progress Photographs



High School English Corridor

High School Additions & Renovations:

Next Four Weeks

- Continue VCT install in corridors
- Continue remaining demolition and modifications to utilities for Music/Choir areas
- Continue wall finishes in Building Trades and CTE Lab
- Begin wall construction for restrooms near Cafeteria

Progress Photographs



New Turf Field

High School Site Improvements and Turf Project:

- Completed turf installation

Next Four Weeks

- Complete remaining punch list items
- Monitor turf field for touch up areas
