Hanover Community School Corporation
Construction Projects

Board Report
September 27, 2022



Hanover Community School Corporation
Construction Projects

Board Report
September 27, 2022

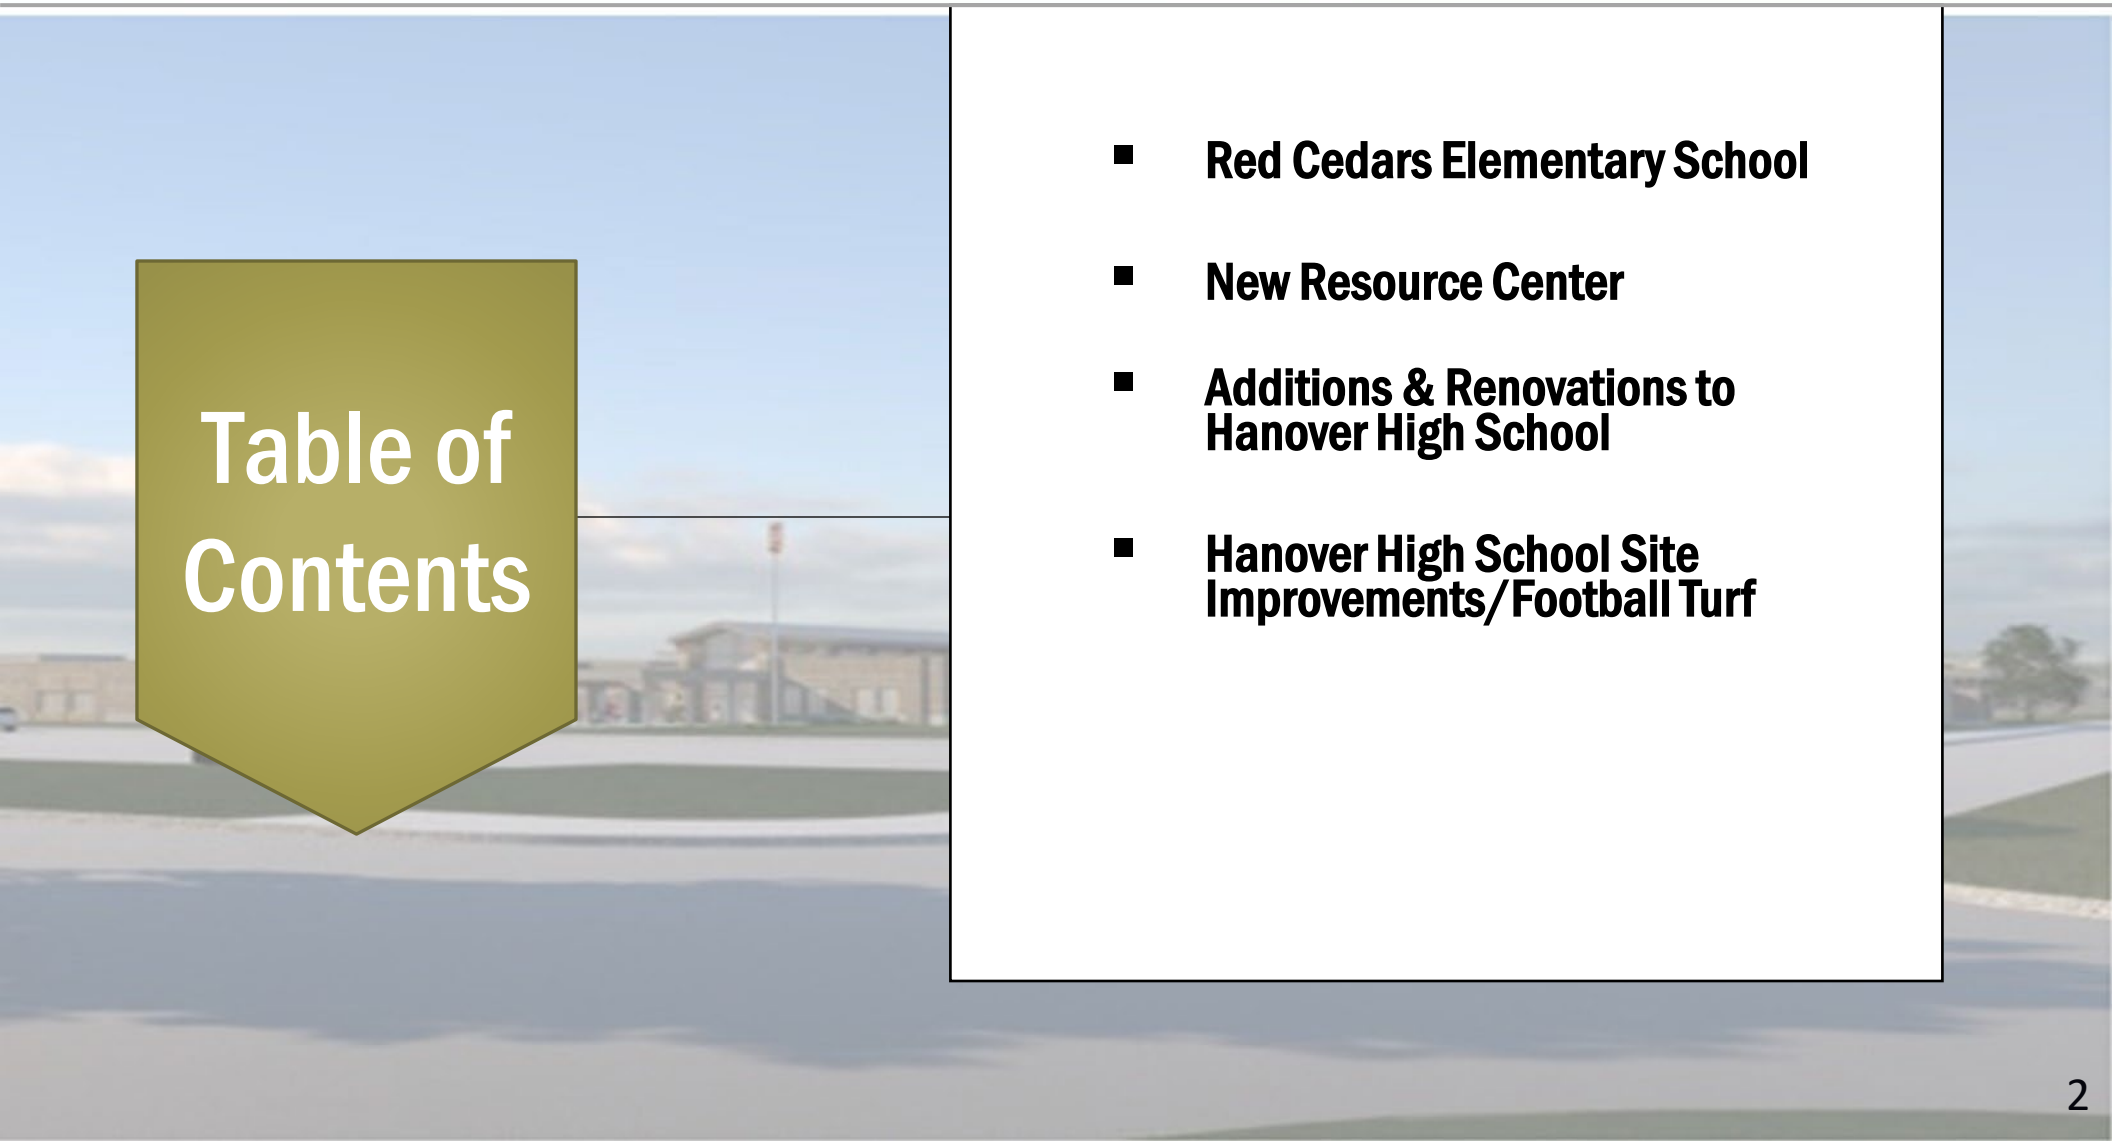


Table of Contents

- Red Cedars Elementary School
- New Resource Center
- Additions & Renovations to Hanover High School
- Hanover High School Site Improvements/Football Turf

Progress Photographs



Red Cedars Elementary

Red Cedars Elementary:

Remaining Items:

- Complete punch list items
- Install permanent key cores upon delivery
- Begin Gymnasium floor
- Touch up site grading and overseed

Progress Photographs



Resource Center Fuel Island

New Resource Center:

- Began ceilings and equipment at Admin
- Began painting and final utilities in Bus Garage
- Completed roofing on Bus Garage
- Completed rough-ins for fuel dispensing equipment
- Poured concrete paving at fuel island
- Began final stone grading for asphalt roads and parking lots

Progress Photographs



Resource Center Admin

New Resource Center:

Next Four Weeks (Admin)

- Complete ceilings in remaining areas
- Install final wall finishes in board room
- Install remaining casework items
- Install flooring in all areas
- Move in furniture
- Turn over building for staff
- Begin final punch list

Progress Photographs



Mechanics Bus Lift

New Resource Center:

Next Four Weeks

(Bus Garage, Mech., Maint. Buildings)

- Complete remaining overhead utilities in Bus Garage
- Install ceilings, final paint, and temporary doors in maintenance building
- Complete concrete slabs in mechanics building, final paint and ceilings, begin equipment installation
- Complete asphalt paving around all buildings
- Begin fencing install
- Begin fuel distribution equipment installation
- Begin bus wash equipment installation

Progress Photographs



High School Corridor Intersection

High School Additions & Renovations:

- Completed and turned over latest classrooms for use
- Began renovations of last six classrooms in the lower east end of the building
- Continued remodeling masonry walls in music rooms and building trades
- Continued VCT installation in corridors
- Continued punch list items in previous areas

Progress Photographs



Building Trades Shop

High School Additions & Renovations:

Next Four Weeks

- Complete VCT install in academic corridors
- Begin VCT install in athletic corridors
- Continue utility relocations in music and building trade areas
- Begin painting in CTE lab areas
- Begin demolition on last set of classrooms

Progress Photographs



Band Room

High School Additions & Renovations:

Next Four Weeks

- Continue installation of metal framing and drywall for bulkheads in music area
- Begin cafeteria restroom ceramic tile
- Complete casework in athletic rooms
- Complete plumbing fixtures in athletic rooms
- Complete flooring in athletic rooms
- Complete remaining metal roof panels and detailing work

Progress Photographs



Athletic Building and New Turf Field

High School Site Improvements and Turf Project:

Next Four Weeks

- Complete remaining punch list items
- Monitor turf field for touch up areas
- Install new fencing at athletic building
