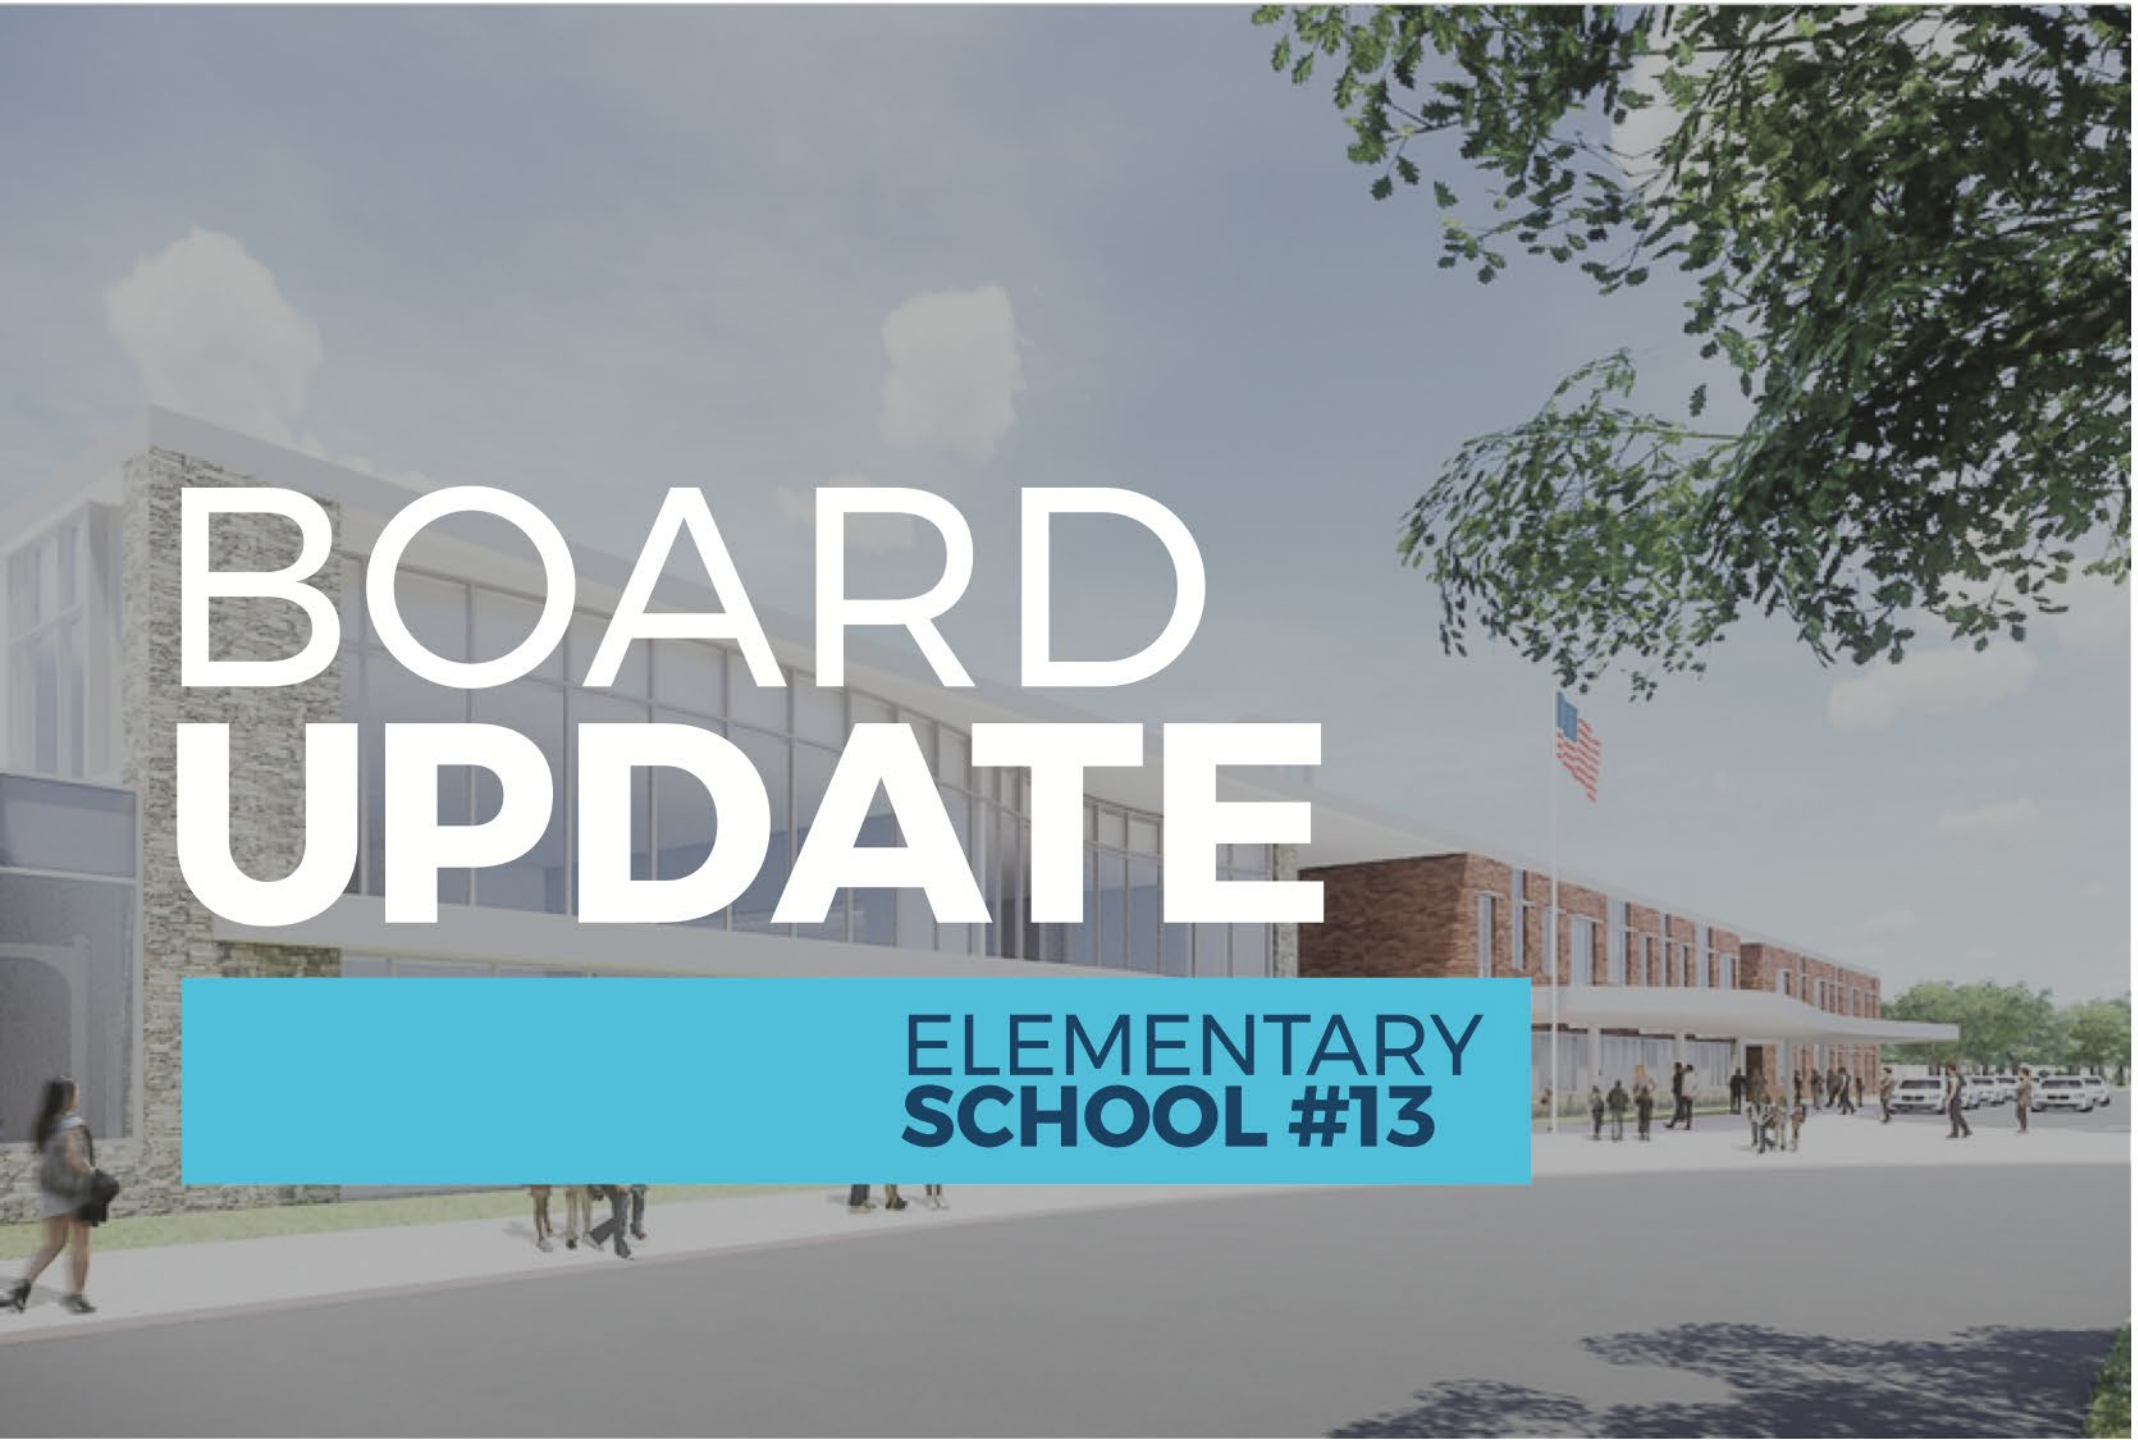


# BOARD UPDATE

## ELEMENTARY SCHOOL #13

CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH ARCHITECTS + PLANNERS

# RAINFALL

| MONTH | AVERAGE RAINFALL | ACTUAL RAINFALL |
|---|---|---|
| Dec-19 | 3.44 | 9.31 |
| Jan-20 | 3.95 | 5.84 |
| Feb-20 | 3.79 | 6.14 |
| Mar-20 | 4.03 | 6.00 |
| Apr-20 | 2.96 | 3.10 |
| May-20 | 2.91 | 7.10 |
| TOTAL | **21.08** | **37.49** |

# PROGRESS UPDATE

CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH ARCHITECTS + PLANNERS

- Second floor steel and deck completion is exactly on the original schedule.
- Starting second floor masonry 2.5 weeks ahead of schedule. *(had we not done the early site package first floor masonry would have just started)*
- All roof steel and deck is to be complete by 9/3. On schedule.
- Roofing starts 6/8, which is one month ahead of schedule.
- Brick is starting 3-4 weeks ahead of schedule.
- Windows are starting mid-July. One month ahead of schedule.
- Painting will start one month ahead of schedule.
- ***ALL OF THIS IS SETTING US UP FOR A SUCCESSFUL MAY 2021 COMPLETION!***

# OCTOBER **2019**

CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH ARCHITECTS + PLANNERS



# NOVEMBER **2019**

CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH ARCHITECTS + PLANNERS



# DECEMBER **2019**

CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH ARCHITECTS + PLANNERS



# JANUARY **2020**

CONTRACT CONSTRUCTION

District Five of Lexington & Richland Counties

QUACKENBUSH
ARCHITECTS + PLANNERS



# FEBRUARY **2020**

CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH
ARCHITECTS + PLANNERS



# MARCH **2020**

CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH
ARCHITECTS + PLANNERS



# APRIL **2020**

CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH
ARCHITECTS + PLANNERS



# MAY **2020**

CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH
ARCHITECTS + PLANNERS



# JUNE **2020**

CONTRACT CONSTRUCTION

District Five of Lexington & Richland Counties

QUACKENBUSH
ARCHITECTS + PLANNERS



# SOUTH **RENDERING**



QUESTIONS & **ANSWER**

# BOARD UPDATE

## ELEMENTARY SCHOOL #13



CONTRACT CONSTRUCTION

District Five OF LEXINGTON & RICHLAND COUNTIES

QUACKENBUSH ARCHITECTS + PLANNERS
