# Purchase Orders Processed

| | PO amount |
|---|---|
| **Addenbrooke Academy** | **$1,043,172.17** |
| **Jefferson Aca Building Addition** | **$6,154,299.36** |
| **Charter Admin** | **$750,000.00** |
| **Lincoln Aca** | **$302,633.00** |
| **Mountain Phoenix** | **$324,000.00** |
| **Rocky Mountain Deaf School** | **$391,430.00** |
| **Excel Academy** | **$262,900.75** |
| **Compass Montessori WR** | **$166,040.00** |
| **Collegiate Academy** | **$234,555.00** |
| | $9,629,030.28 |

# HIGH SCHOOLS
# Starting Construction
# Early 2020

Design Development Documents Estimate
$8,482,956
22,206SF
$382/SF

NOTE:
The footprint of the addition is influenced by the site constraints. There is a limited area at the east end of the building before the grade drops significantly. The remaining parking lot on the east side still needs access as well as the kitchen for deliveries and trash collection. All these parameters have been considered to shape the solution presented.




**Conifer HS** – Addition
Cannon – CMGC FCI



Construction Documents Estimate
$26,300,000
169,235SF
$155.4/SF



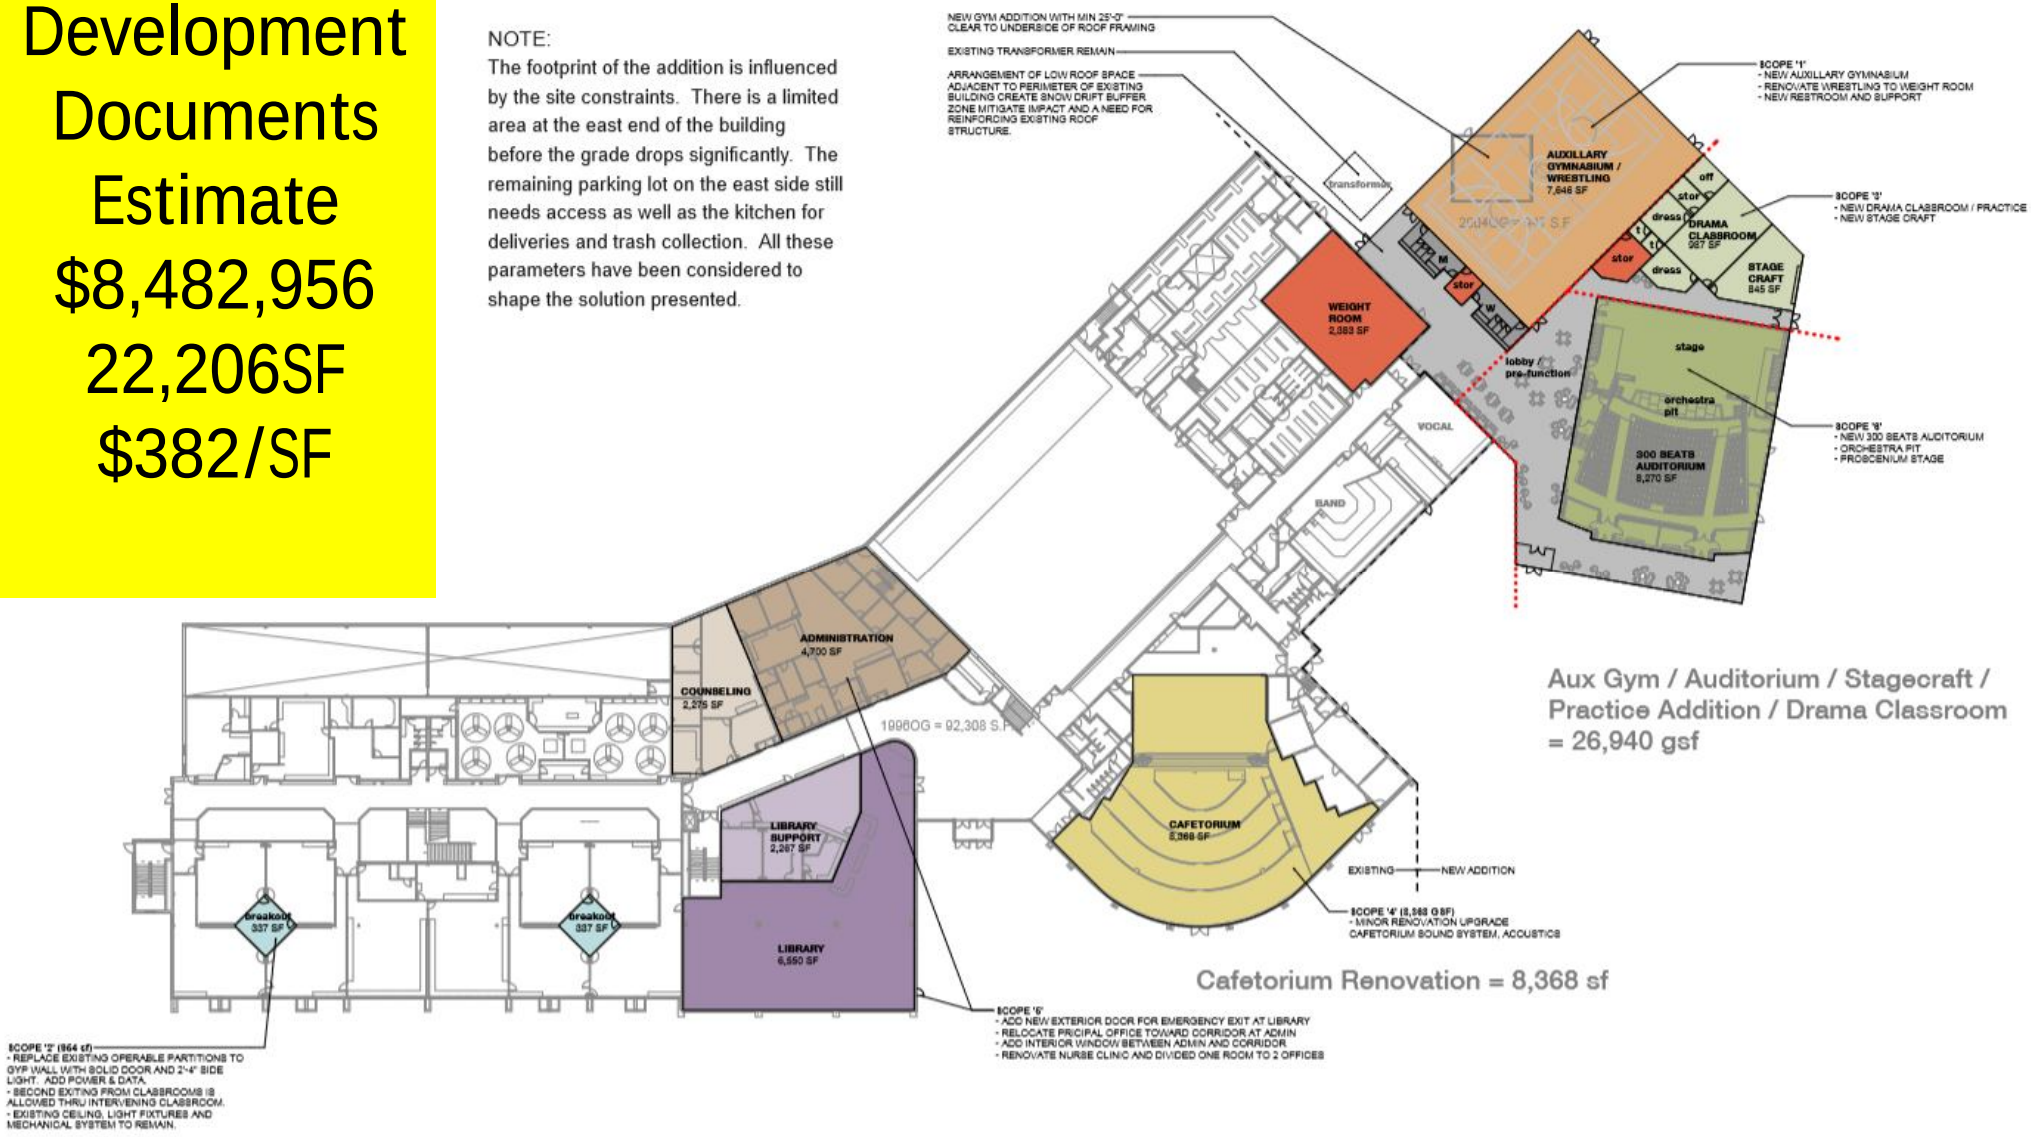



**Alameda HS** – Addition
Wold – CMGC Phipps

Construction Documents Estimate
$14,185,271
124,765SF
$114/SF




**Columbine HS** – Addition
Eidos – CMGC Swinerton




**Green Mountain HS** – Addition

MOA – CMGC GE Johnson

Construction
$12,971,690
49,194SF
$263.68/SF

Complete – Phase I

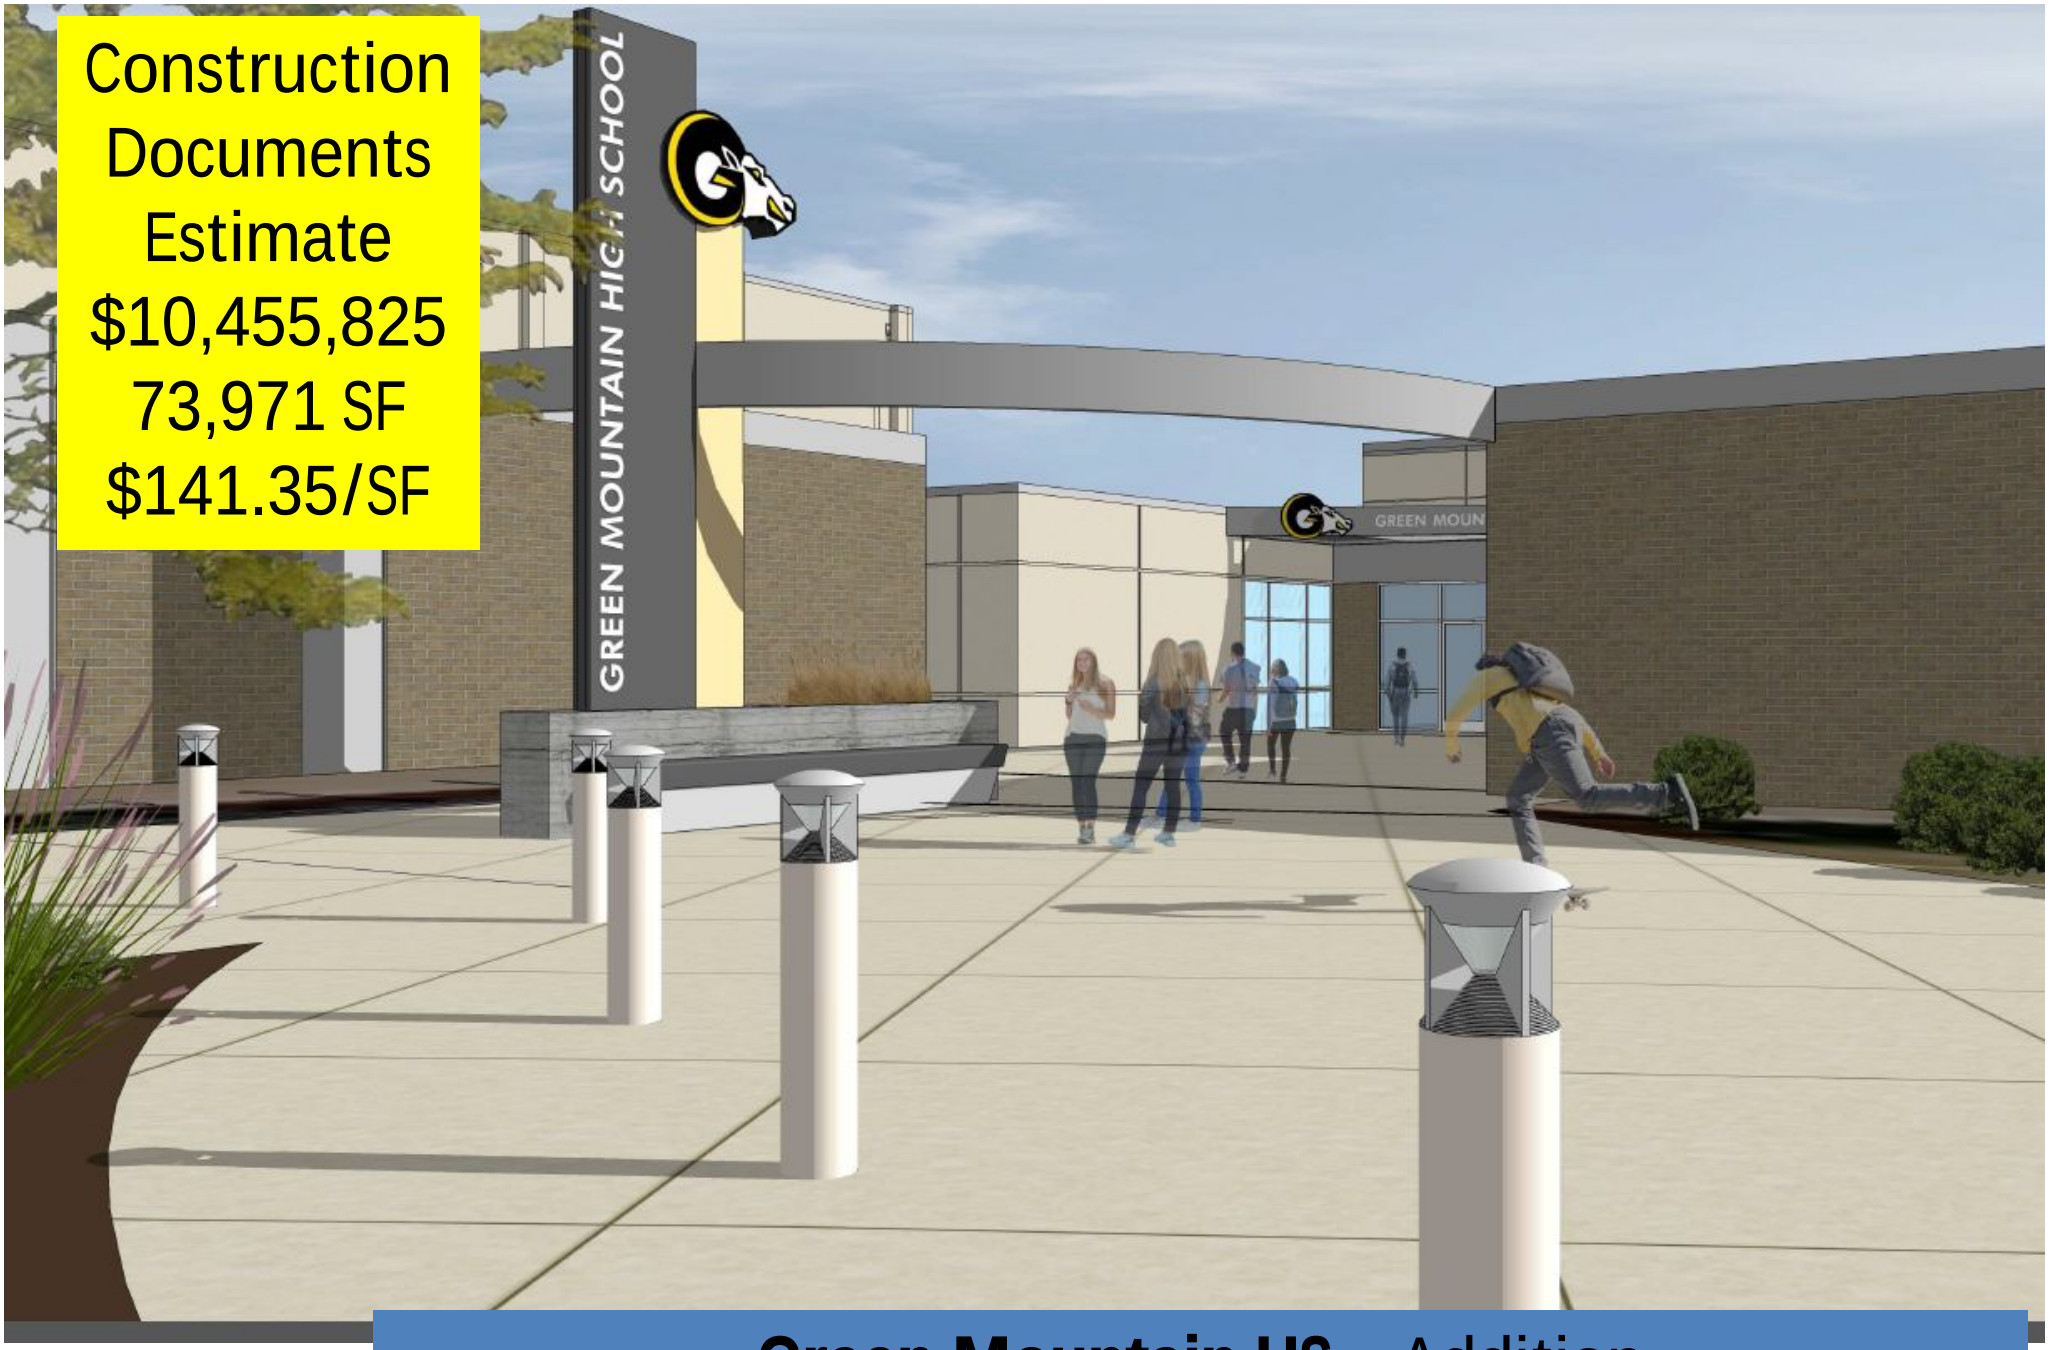



**Arvada HS** – Addition – (Phase II)
HCM – CMGC Saunders

# 2020 - PROJECTS

Complete

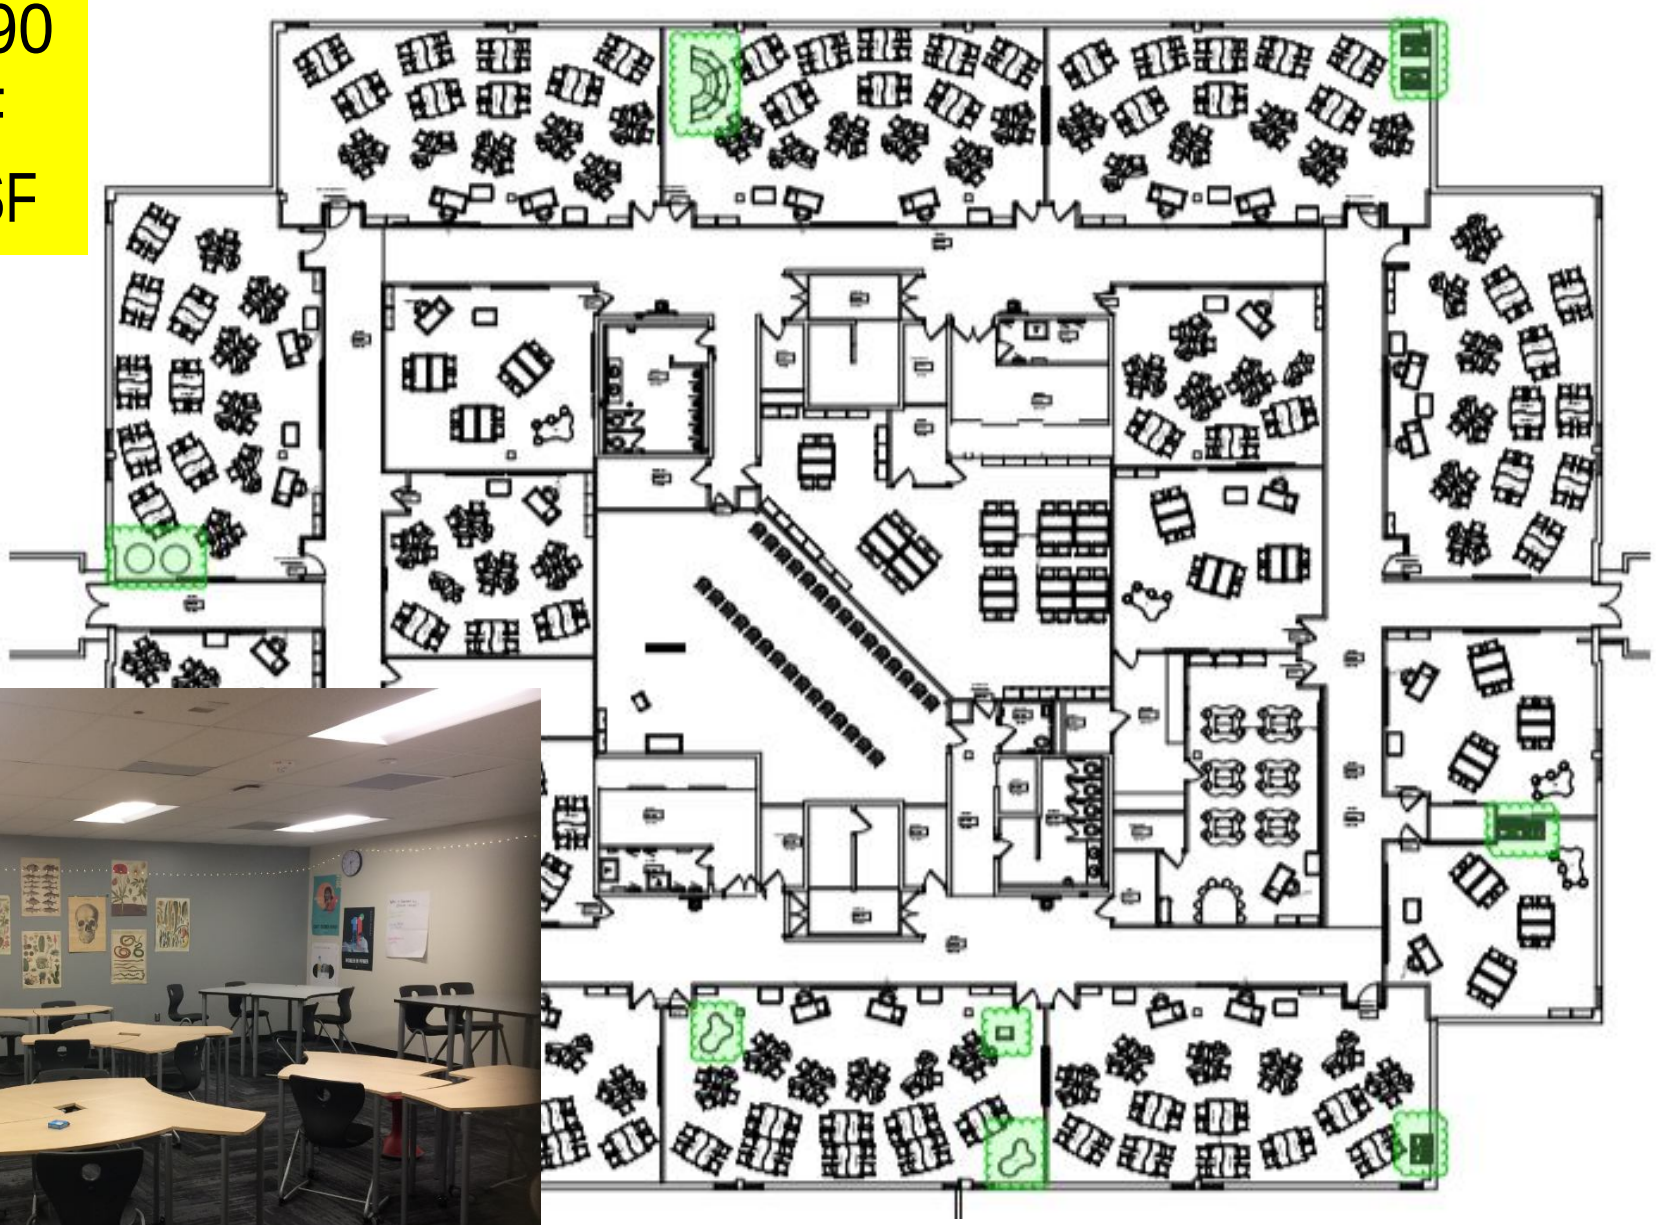


**Coronado ES** – Gym Floor
OZ – Colorado Floorworks

Kyffin ES
Complete

Stevens ES
90% Complete

Peck ES
90% Complete

Secrest ES
Glass ordered



# Security Glass Installation - Elementary School

4 Schools –

Construction
$4,589,755
15,137SF
$303.21/SF

May 2020
Completion






**Three Creeks K8** – Addition –
HCM – CMGC Phipps

Construction
$6,694,785.
16,890SF
$396.38/SF

August 2020
Completion



**Wilmot ES** – Addition
DLR – CMGC Himmelman

Construction
$16,736,000
58,537 SF
$286/SF

Dec. 2020
Completion



**Kendrick Lakes ES** – Replacement
Larson Incitti – Roche

# Summer 2020 Construction Documents



$2,443,643

ARVADA WEST HIGH SCHOOL
11595 ALLENDALE DRIVE, ARVADA, CO 80004



$2,985,029

COLUMBINE HIGH SCHOOL
6201 S PIERCE STREET, LITTLETON, CO 80123



$2,501,031

GOLDEN HIGH SCHOOL
701 24TH STREET, GOLDEN, CO 80401



$4,027,821

GREEN MOUNTAIN HIGH SCHOOL
13175 WEST GREEN MOUNTAIN DRIVE, LAKEWOOD, CO 80228



$2,971,103

POMONA HIGH SCHOOL
8101 WEST POMONA DRIVE, ARVADA, CO 80005



$3,014,278

STANDLEY LAKE HIGH SCHOOL
9300 WEST 104TH AVENUE, WESTMINSTER, CO 80021

**2020 Field Improvements**

Awest HS, Columbine HS, Golden HS

Green Mountain HS, Pomona HS, Standley Lake HS

HCM – CMGC ECI

Summer 2020
Design
Development
Documents

Estimate
$1,366,534
17,000 SF
$80/SF




1 Science Lab Casework - West Wall
1/4" = 1'-0" • Similar at four classrooms




2 Science Lab Casework - North Wall
1/4" = 1'-0" • Similar at four classrooms

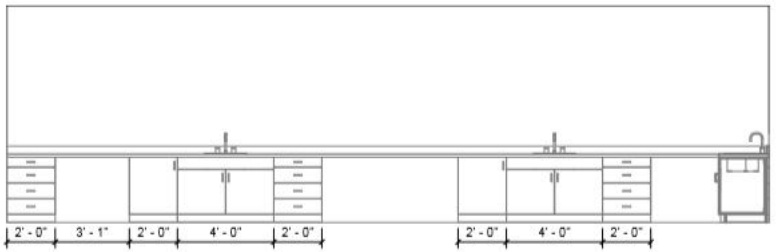


3 Classroom Casework - Typical
1/4" = 1'-0" • Similar at twelve classrooms

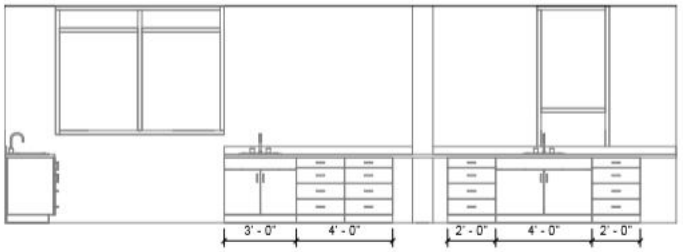


4 Level 01 Plan
1/16" = 1'-0"

**West Jefferson MS** – Upgrades
Cannon – CMGC FCI

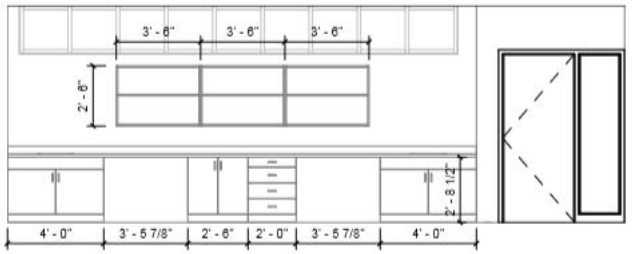Summer 2020

Green Mtn ES
$739,250

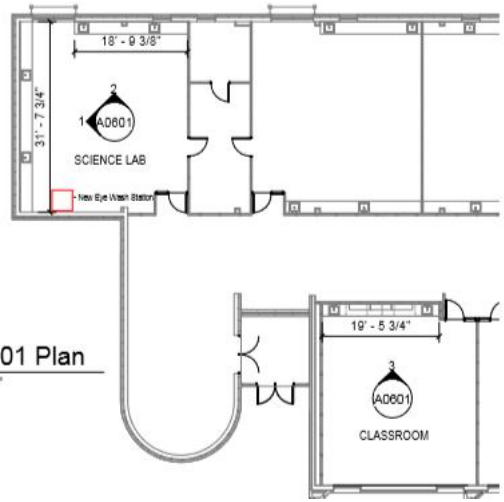Lasley ES
$255,700

Bid 12/10/19



**DW Roofing I –** Green Mtn ES, Lasley ES
WJE – CMC & United Materials

Summer 2020

Golden HS
$434,930

Bid 12/12/19



**Chiller Replacement –** Golden HS
Columbine – K&M

Summer 2020

Patterson ES
$467,489

Parr ES
$617,180

Bid 1/07/20



**DW Roofing I Part two –** Patterson ES, Par ES
WJE –United Materials, Flynn

Summer 2020

$1,636,479.00

Bid 1/13/20









**DW Mechanical –** Stott RTU , Ryan RTU ,
Patterson (AHU, Boilers)
Columbine - Braconier

Summer 2020

$193,082 KES
$220,960 CMS
EHS

Bid 2/5/20



**DW Roofing II** – Kullerstrand ES, Carmody MS, Evergreen HS
Rooftech – TBD

Summer 2020

$3,225,500

Bid 2/5/20




**Trailblazer –** Locker Room & Press Box

Mellin & Assoc. – TBD

# Summer 2020

| Location | Description | A/E | Contractor | H Budget | Variance | Bid |
|---|---|---|---|---|---|---|
| DW Mech | 3 ~ Schools - **Stott** ,**Ryan** Boiler ahu controls, **Patterson** AHU Boiler, | Columbine | Braconier | $1,588,162.00 | -$48,317.00 | $1,636,479.00 |
| Golden HS | Chiller Replacement | Columbine | K&M | $600,000.00 | $165,070.00 | $434,930.00 |
| Trailblazer Stadium | Trailblazer Stadium Efficiency & Future Ready | Mellin & Assoc | W E O'neal | $3,374,029.00 | $148,529.00 | $3,225,500.00 |
| DW Roofing II | Kullerstrand | Roof Tech | Graubau | $265,666.00 | $72,584.00 | $193,082.00 |
| DW Roofing II | Carmody | Roof Tech | B&M Roofing | $366,551.00 | $145,591.00 | $220,960.00 |
| DW Roofing I | Patterson ES, Parr ES | WJE | United Materials Flynn | $1,127,957.00 | $43,288.00 | $1,084,669.00 |
| DW Roofing I | Green Mountain ES | WJE | CMC | $739,250.00 | $0.00 | $739,250.00 |
| DW Roofing I | Lasley ES (Base Bid) A | WJE | United Materials | $343,200.00 | $87,500.00 | $255,700.00 |

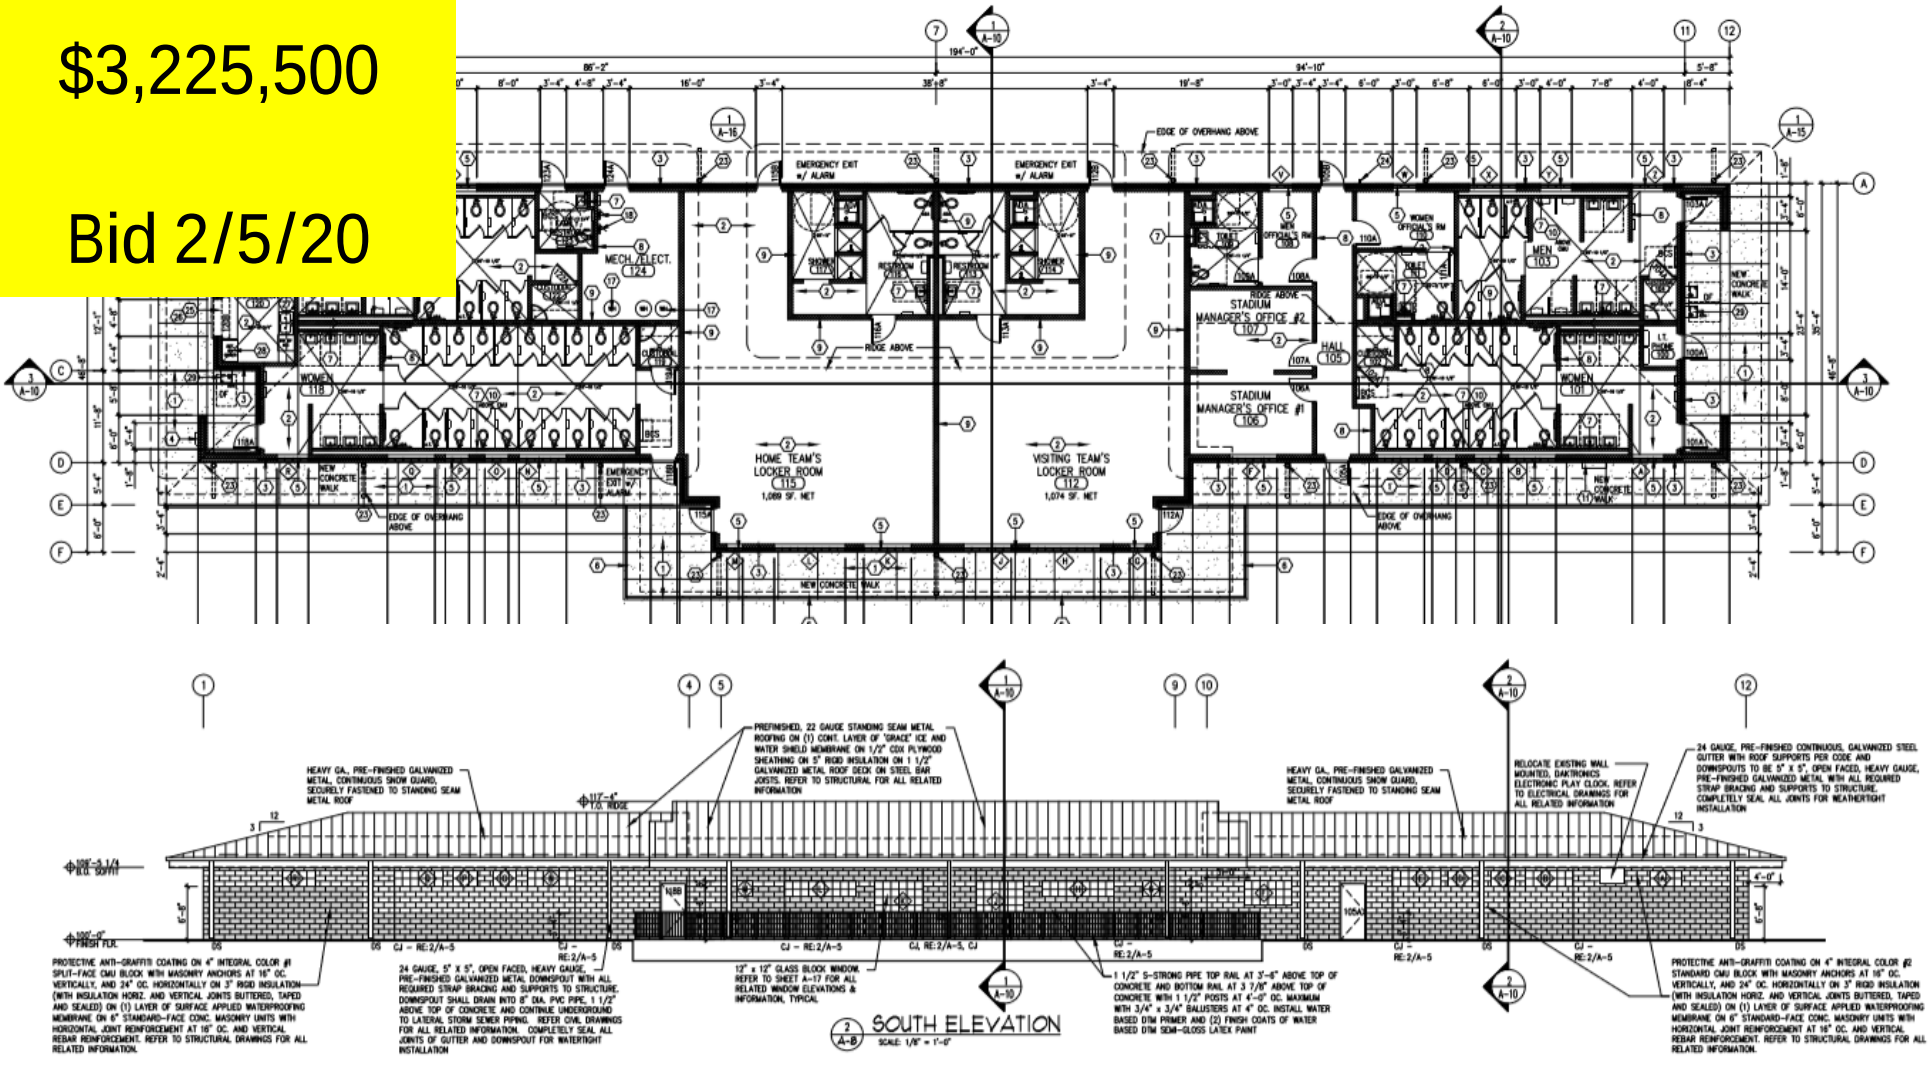**2020 Bids**

Summer 2020
Bids 2/13/20



**AHU Replacement -** Westridge ES
Branch Pattern - TBD

# Summer 2020 Bids 2/25/20



1 KENDALLVUE PLAY STRUCTURE
Scale: NTS



1 REVOLUTION SPINNER - LITTLE TIKES

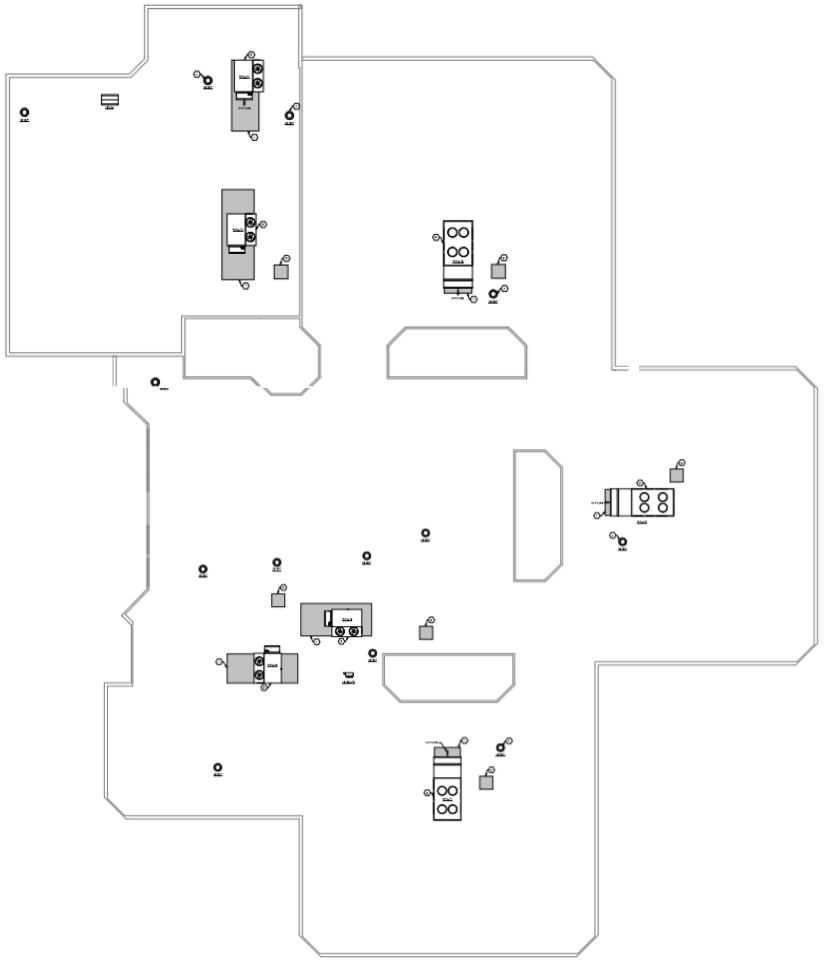

2 SPIRAL SLIDE - LITTLE TIKES

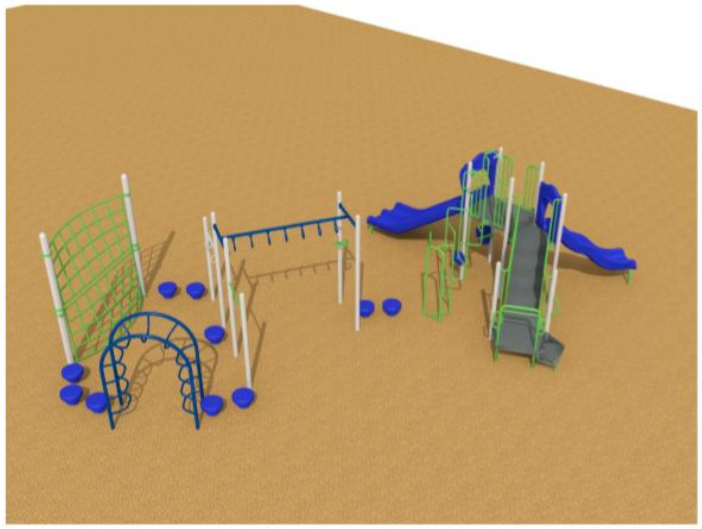

3 TEAM TOTTER - LITTLE TIKES




1 GAMETIME PLAY EQUIPMENT AT FLETCHER MILLER SCHOOL
Scale: Not To Scale



2 LITTLE TIKES PLAY EQUIPMENT AT SHERIDAN GREEN ELEMENTARY SCHOOL
Scale: Not To Scale

**DW Playgrounds (9)**– Allendale , Stott , Vanderhoof, Sheridan Green , Fletcher Miller, ,Westridge, Kendallvue, Dutch Creek, Stony Creek
Design Concepts – TBD

Summer 2020
Bids 2/28/20



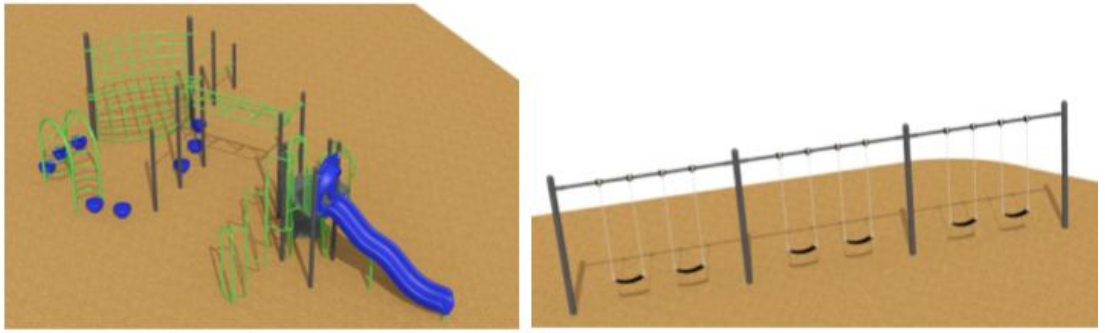


**Belmar ES, Eiber ES** – Upgrades
AMD – TBD

Summer 2020
Bids 3/4/20




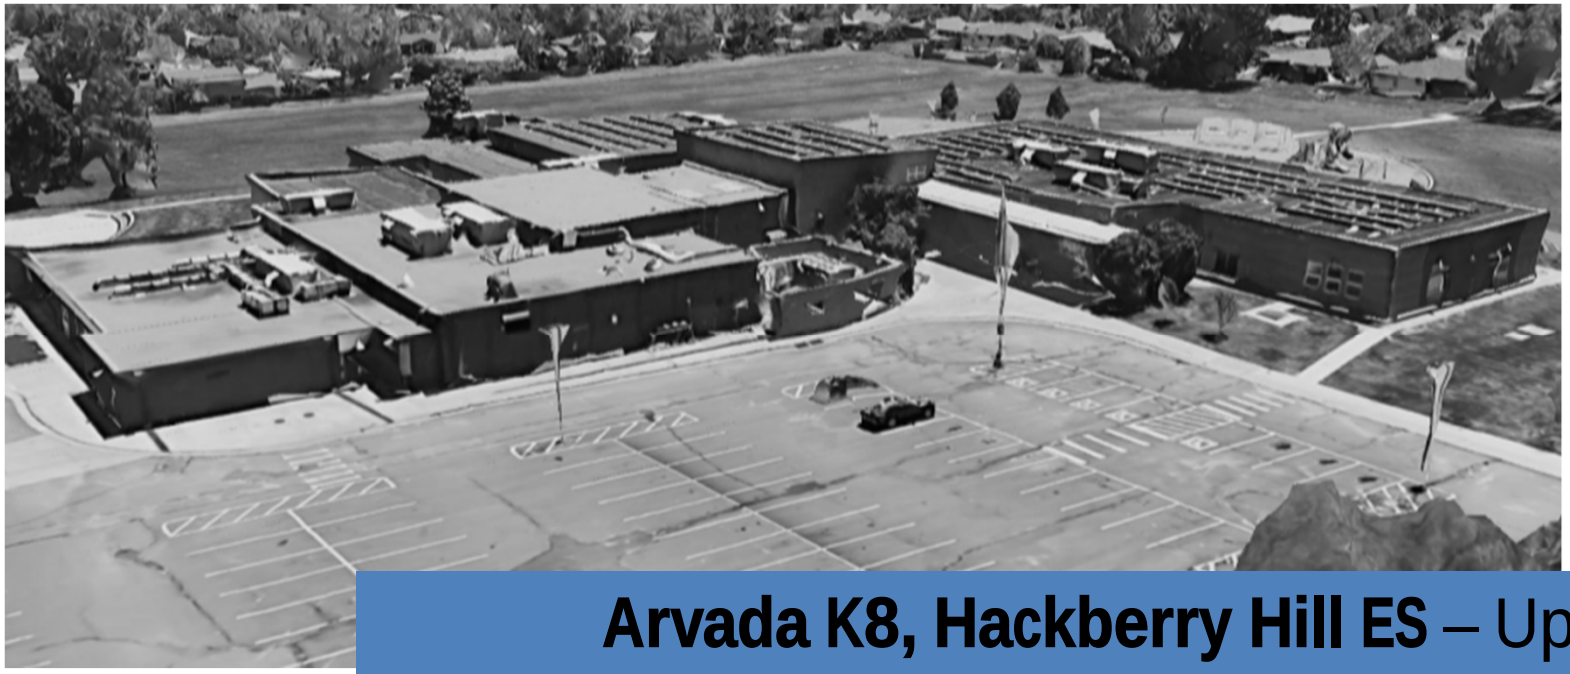

**Arvada K8, Hackberry Hill ES** – Upgrades
RTA – TBD

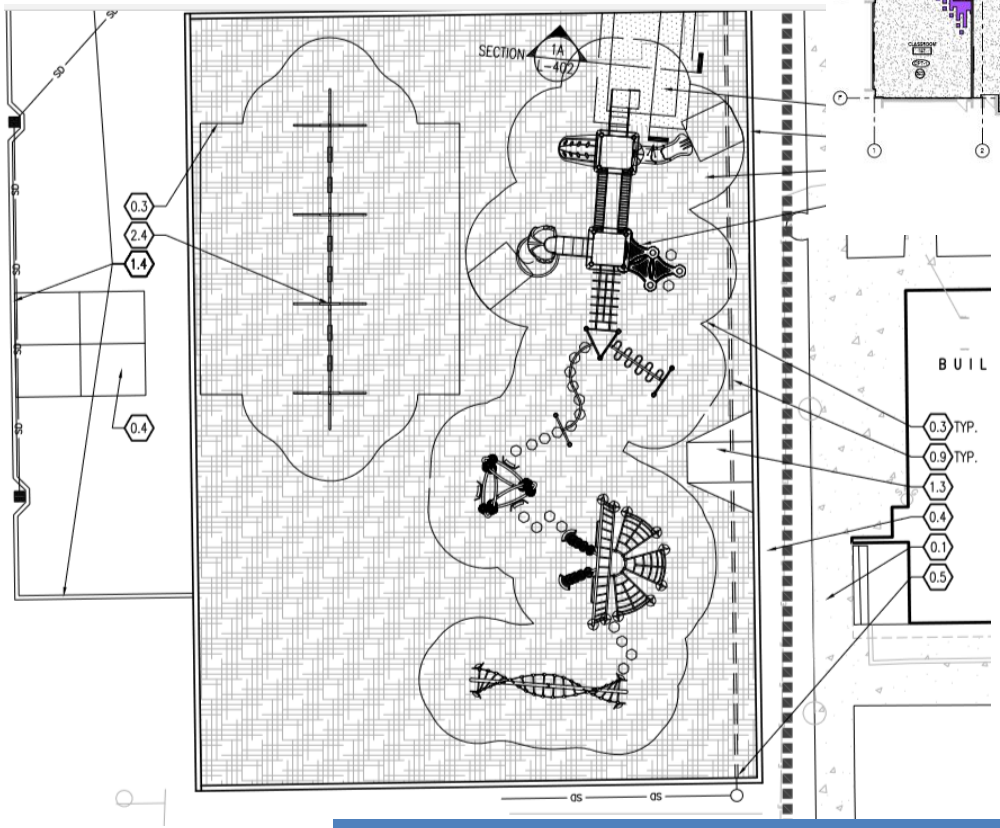Summer 2020
Bids 3/5/20







**Green Gables ES, Hutchinson ES** – Upgrades
Sybazz – TBD

Summer 2020
Bids 3/5/20

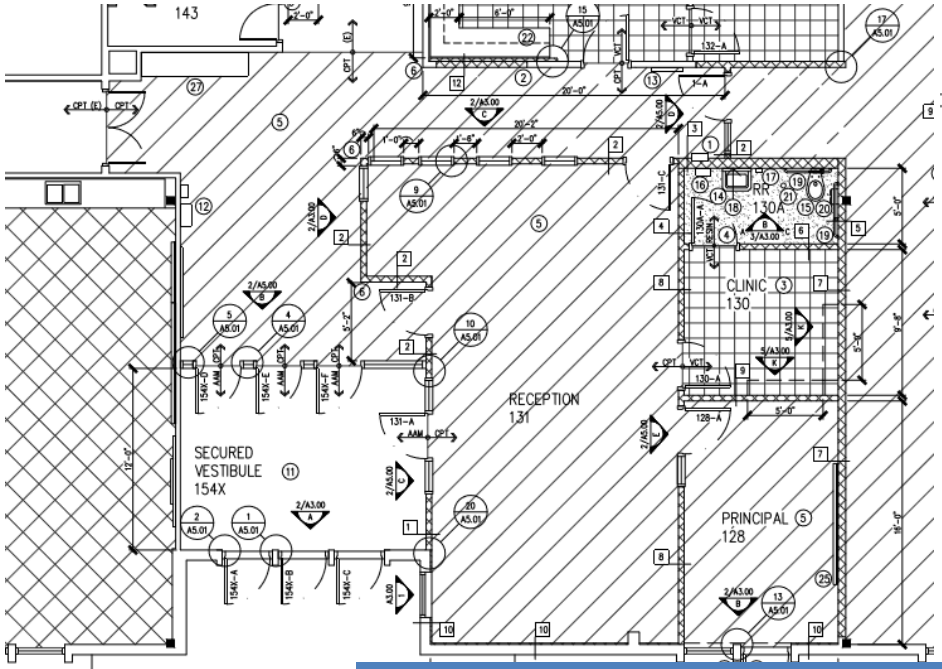

**DW Paving I** – Columbine Hills, Everitt MS, Lawrence Dadey – TBD

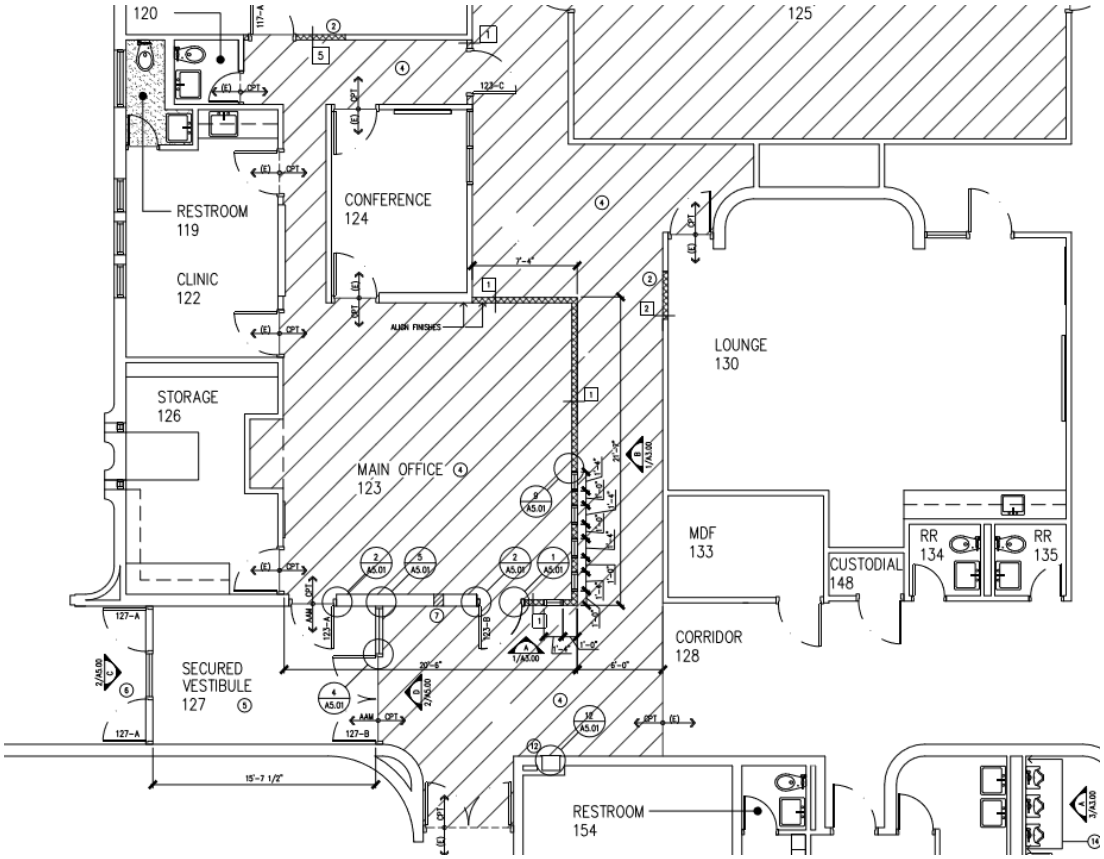Summer 2020
Bids 3/10/20




**Dutch Creek ES** – Upgrades
Cunningham Group – TBD

Summer 2020
Bids 3/10/20




**Ken Caryl** – Signage & FACS Room Upgrades
HCM – TBD

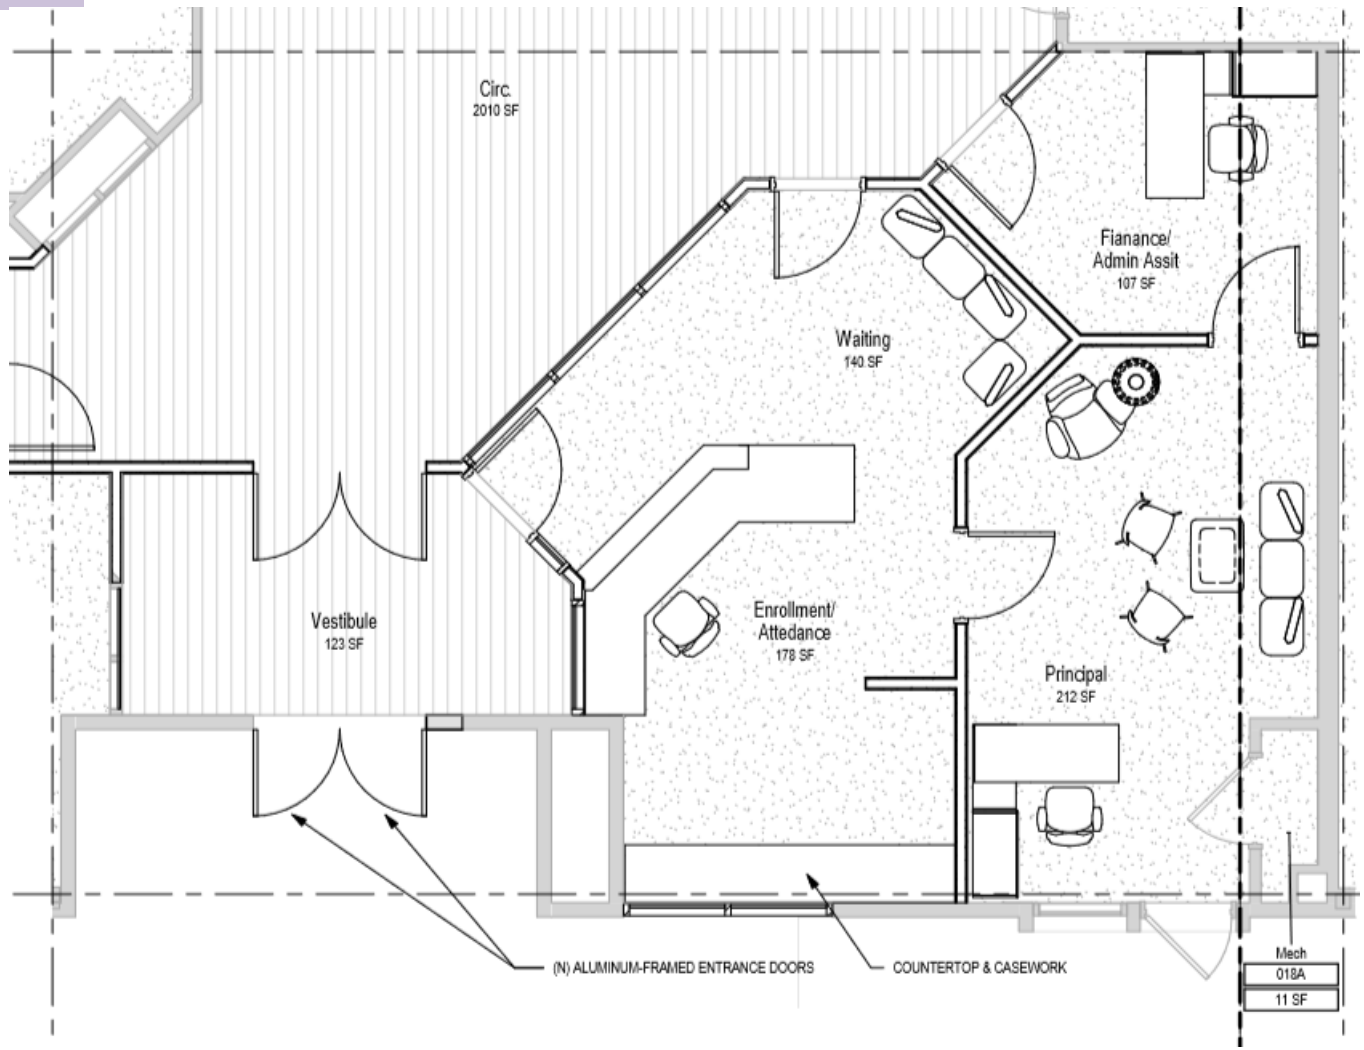Summer 2020
Bids 3/12/20







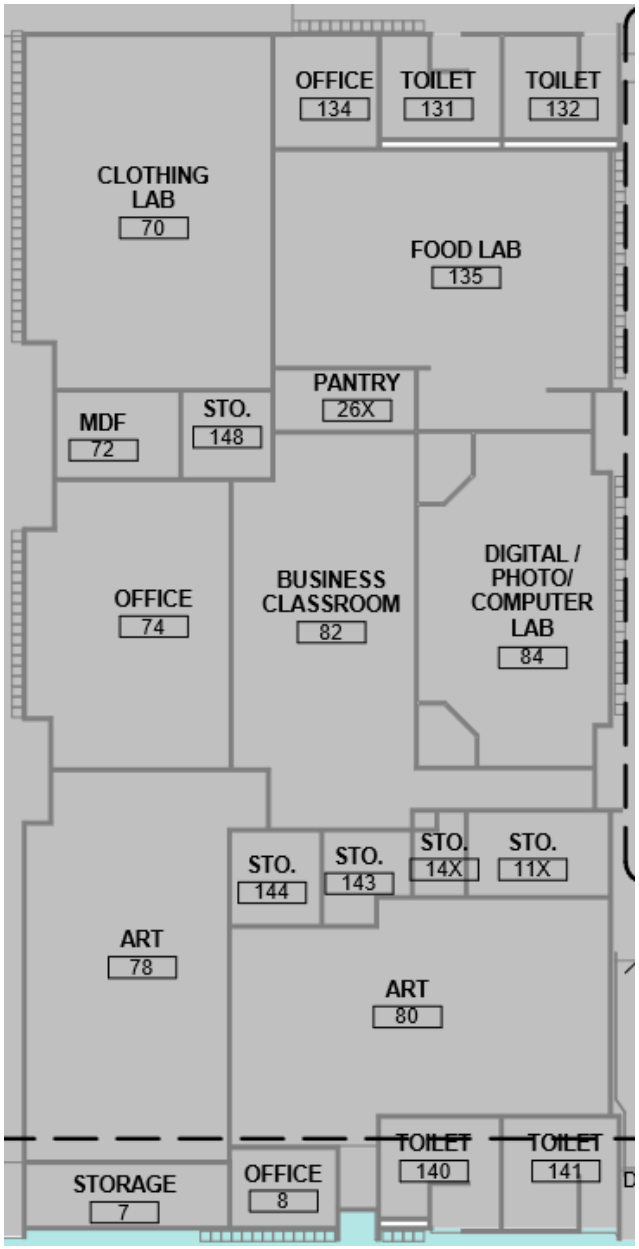




**Adams ES, Lukas ES, Semper ES, Witt** – Upgrades
RB+B – TBD

Summer 2020
Bids 3/17/20

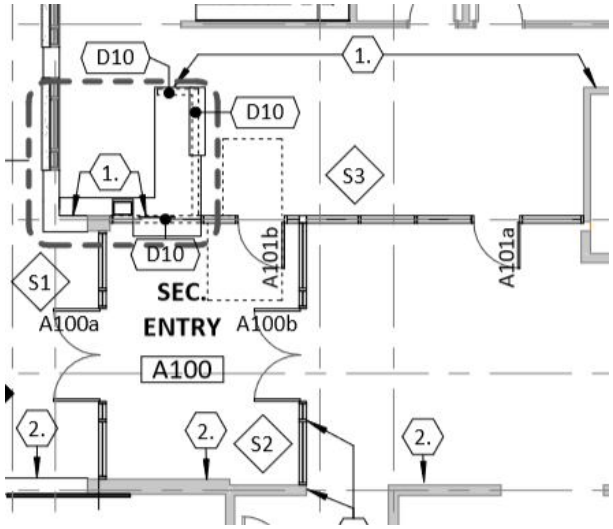


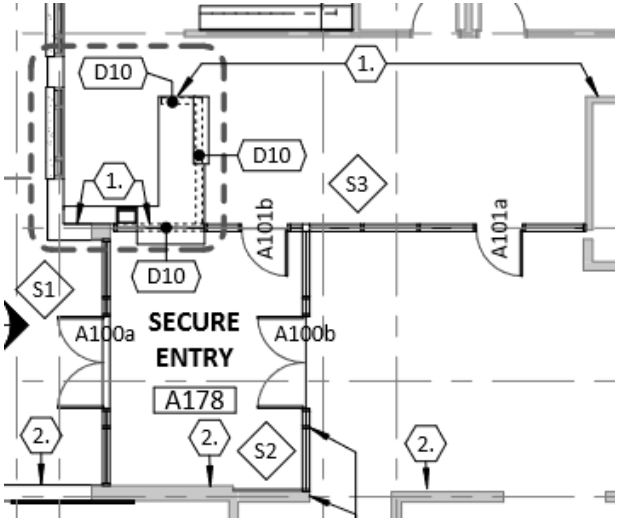**Fremont ES** – Upgrades
Jordin – TBD

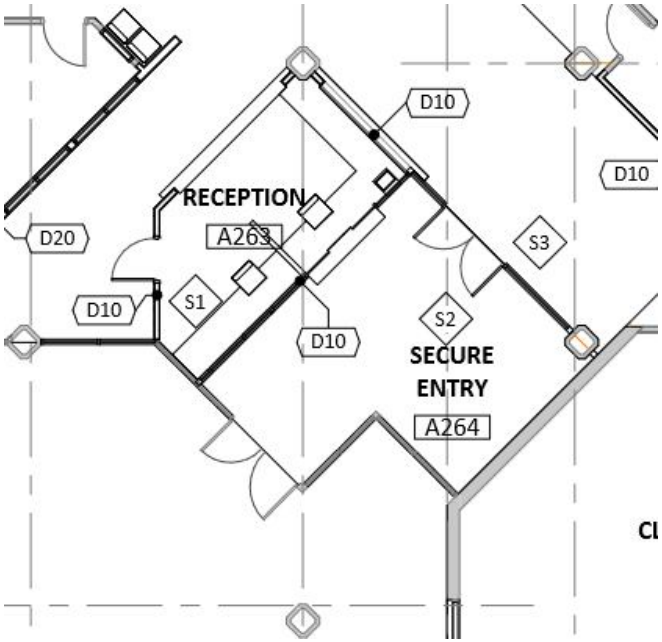Summer 2020
Bids 3/18/20

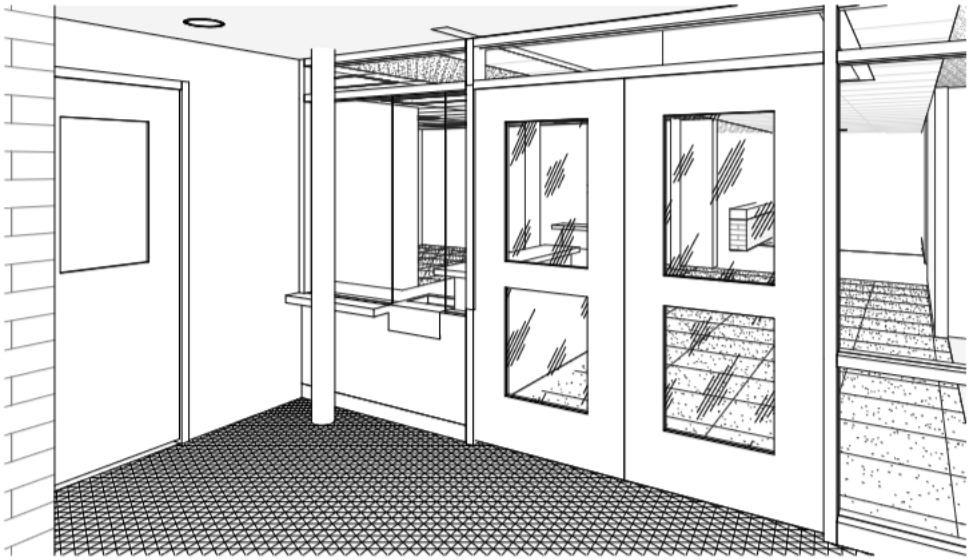

**DW Paving II –** Bradford Int, Ryan, Mitchell, Shelton
JVA – TBD

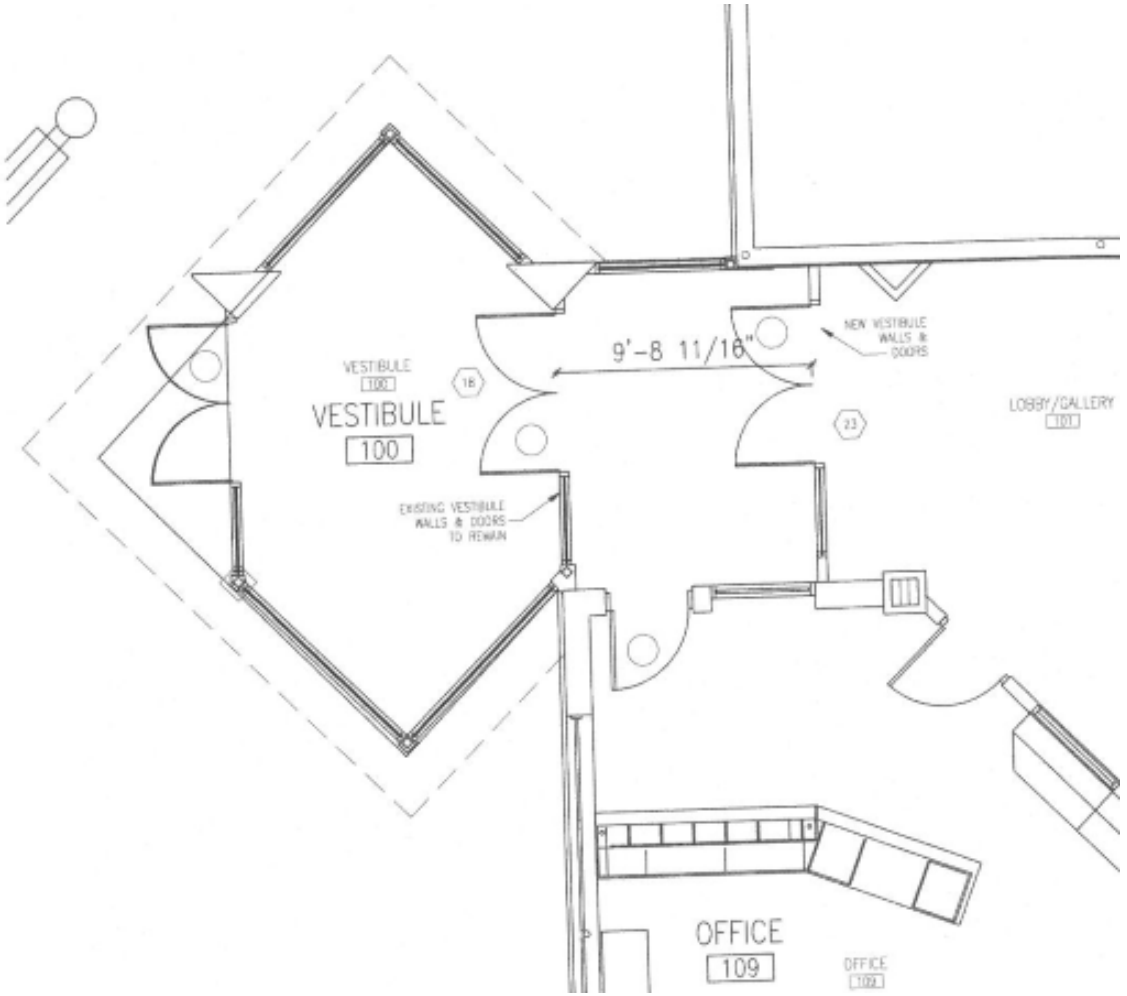Summer 2020
Bids 3/19/20



**DW Flooring -** Fletcher Miller, Lasley ES,
Free Horizon & Fitzmorris
Farnsworth Group – TBD

Summer 2020
Bids 3/19/20













# Foothills ES, Ralston ES, Vivian ES , Welchester ES

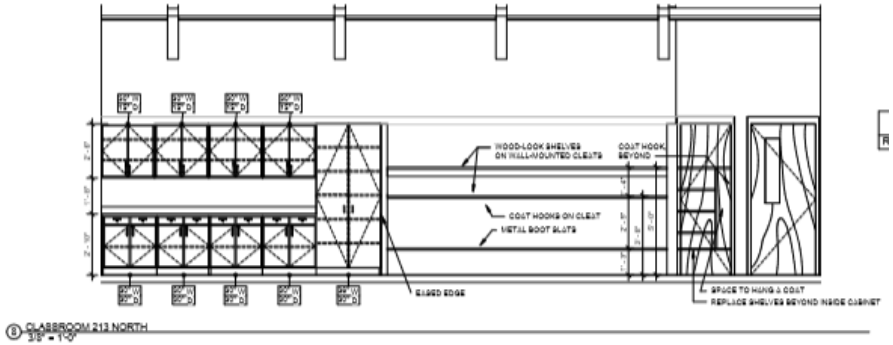Upgrades

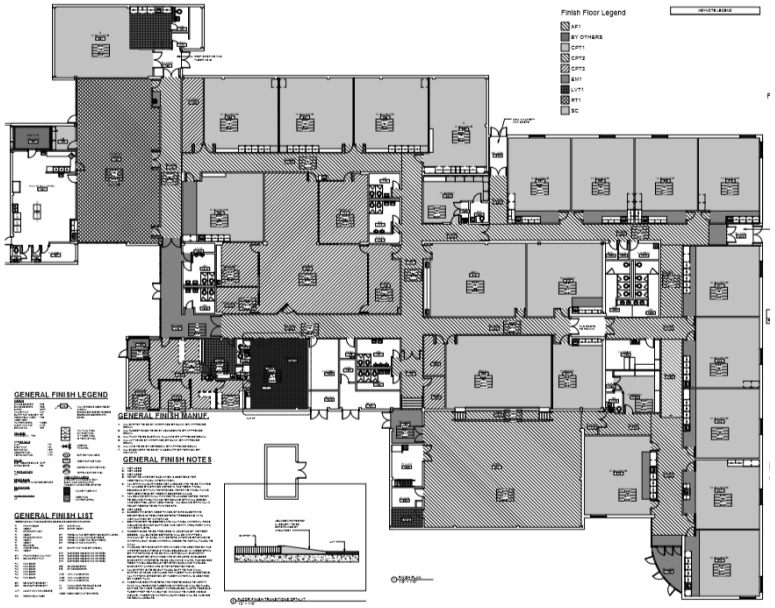CRP – TBD

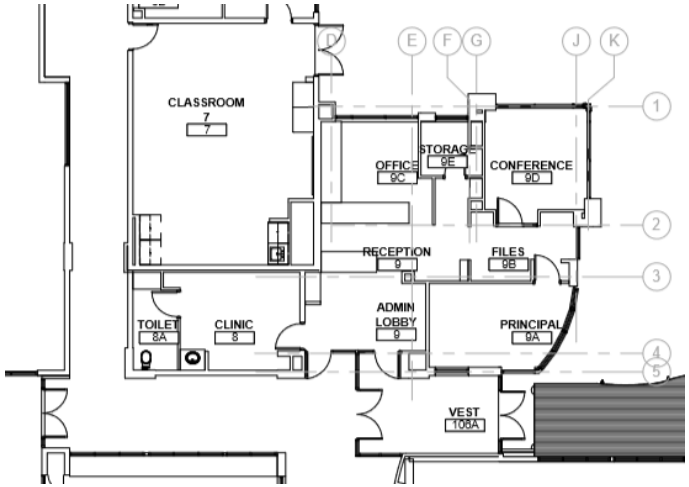Summer 2020
Bids 3/25/20

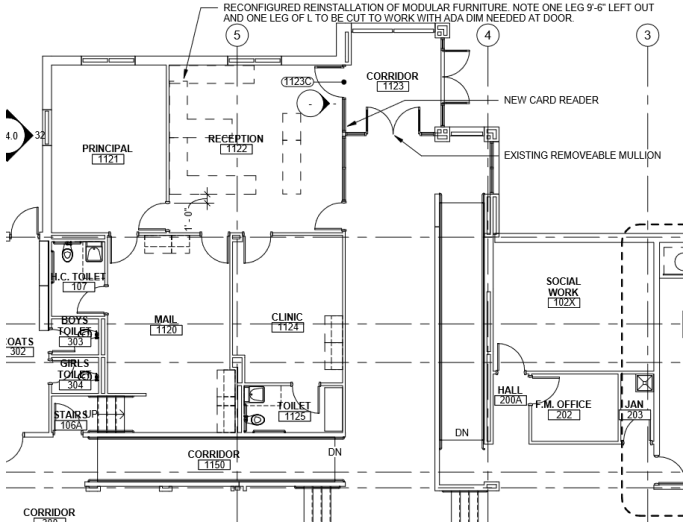


**Stober ES** Upgrades
LOA – TBD

Summer 2020
Bids 4/2/20






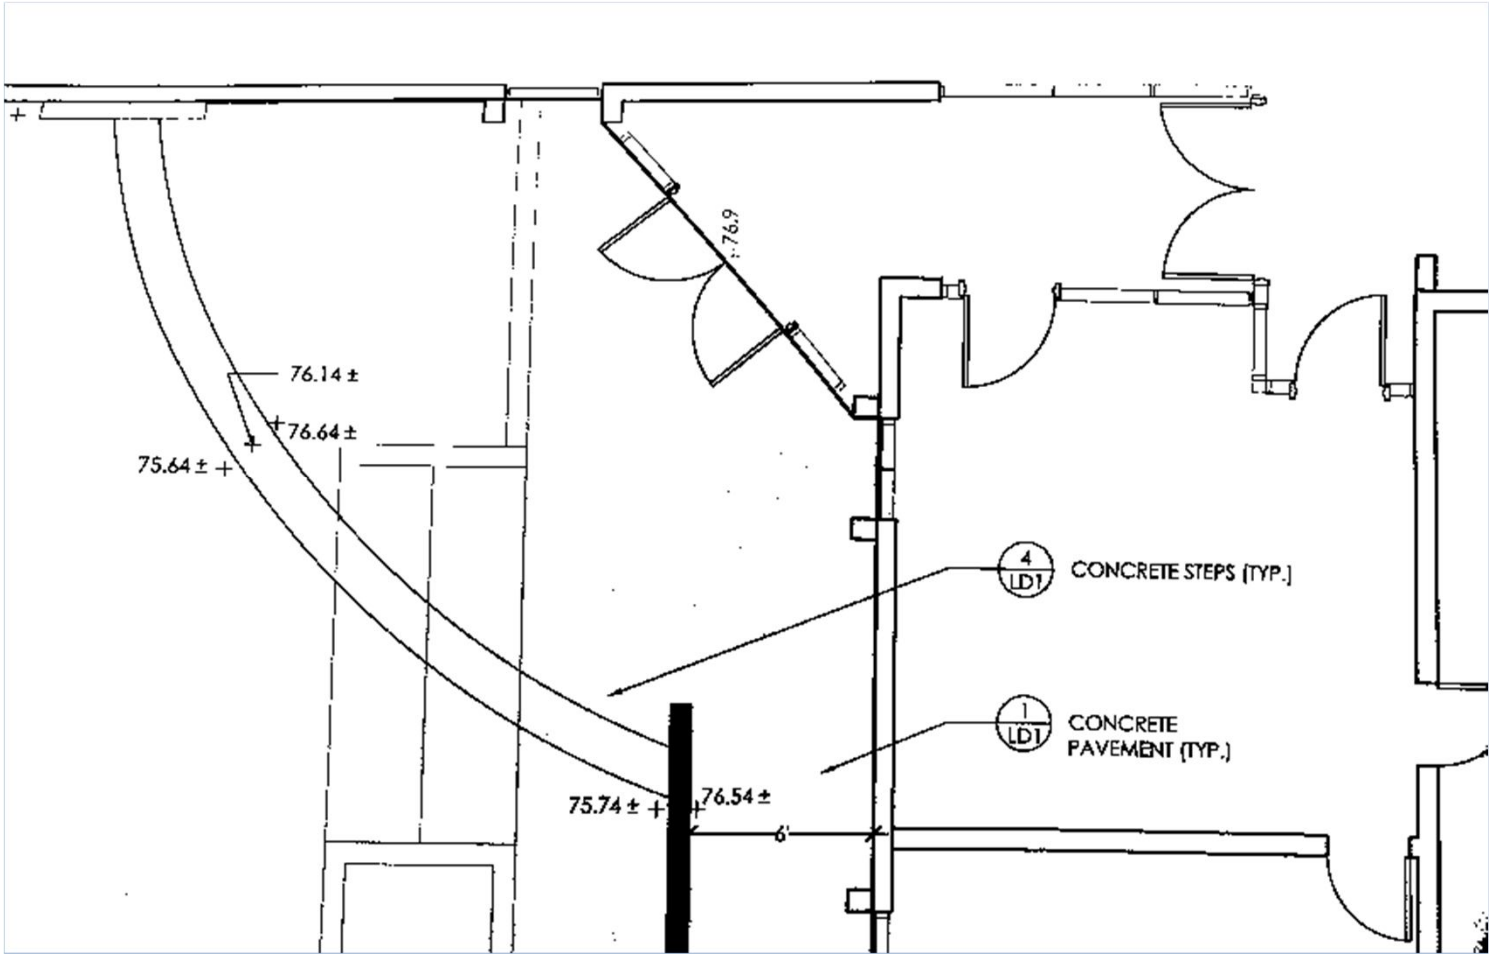



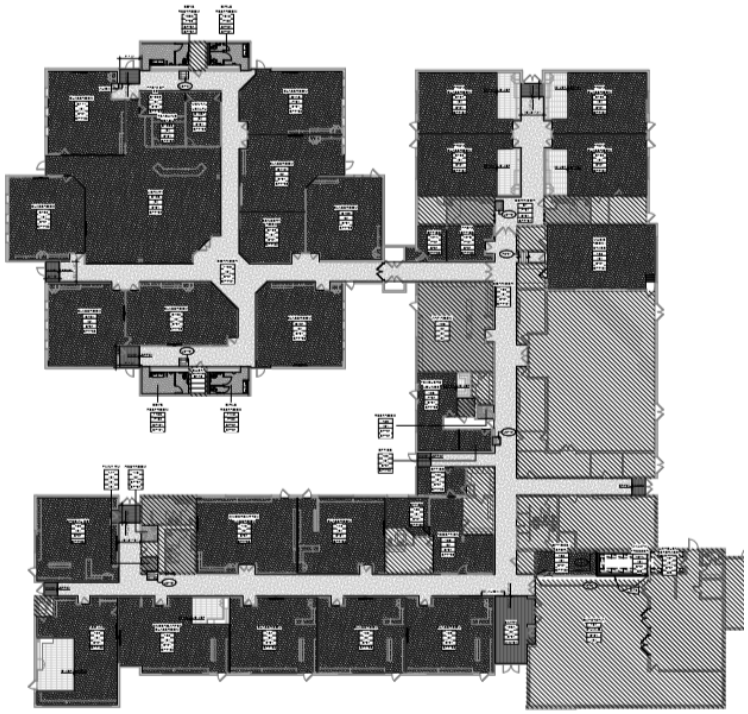


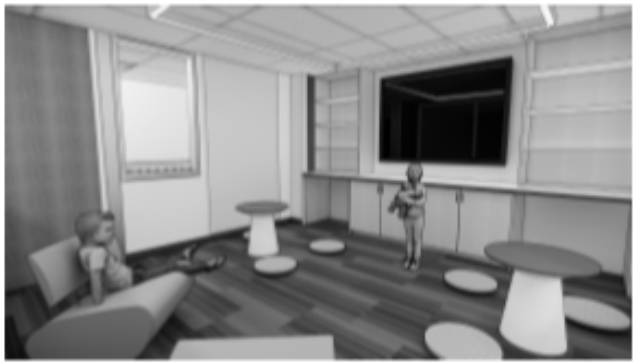

**Columbine Hills ES, Coronado ES** – Upgrades
OZ – TBD

Design Development Documents

Summer & School Year work



1. Columbine Hills ES
2. Deane ES
3. Devinny ES
4. Dennison ES
5. Fitzmorris ES
6. Kullerstrand ES
7. Lasley ES
8. Maple Grove ES
9. Patterson International
10. Peck ES
11. Powderhorn ES
12. Ryan ES
13. Secrest ES
14. Sheridan Green ES
15. Stott ES
16. Vanderhoof ES
17. Westgate ES
18. Westridge ES

**DW LED -** 18 Schools

Ackerman – CMGC Weifield

New Construction and ADDITIONS

Start

Summer / Fall

# Design Development






**Bell MS** – 1 Story - 4 Classroom Addition
Eidos – Contractor TBD

# Design Development



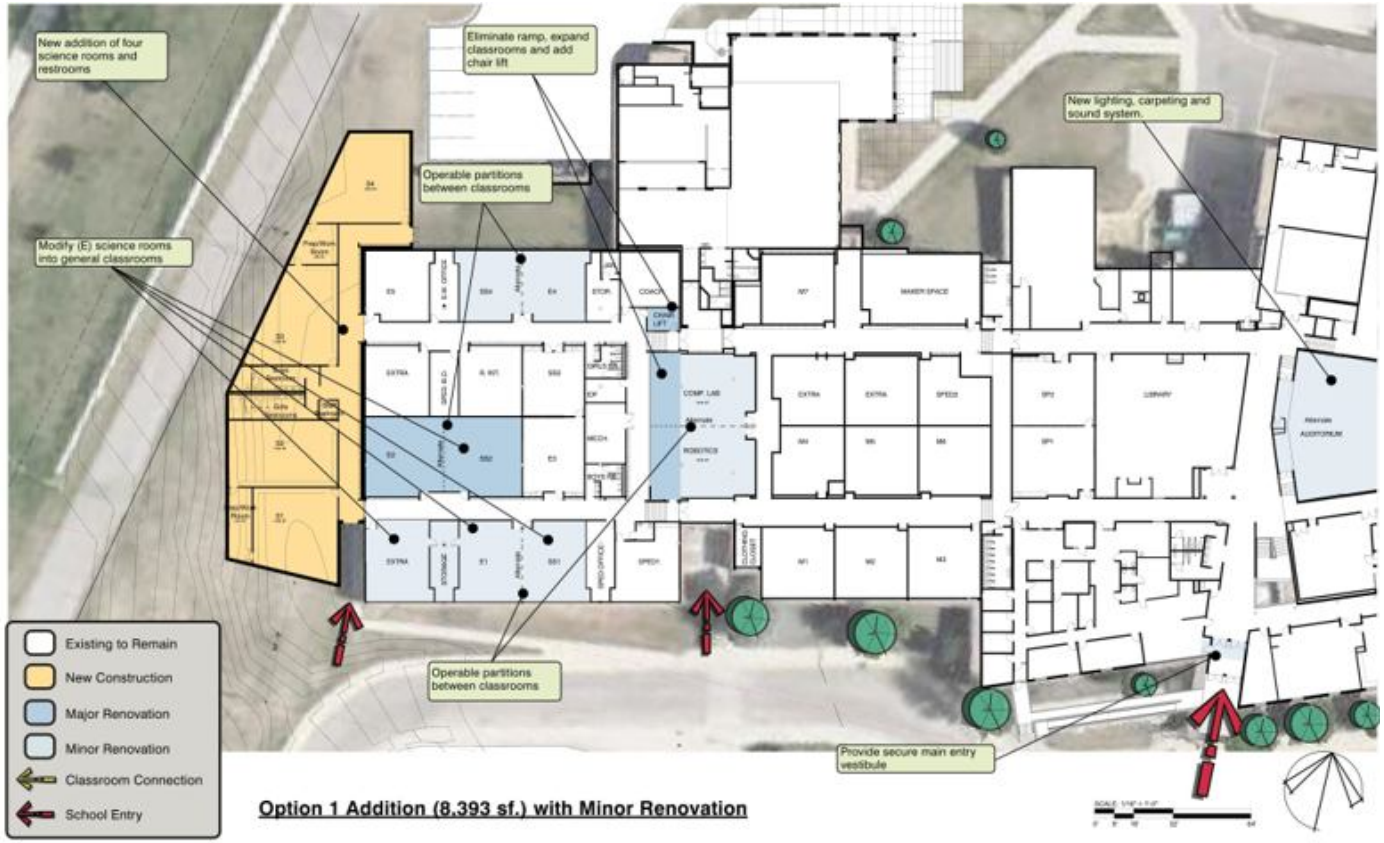

**CTE South** – New Building
HCM – Contractor TBD

# Design Development




**Jefferson HS** – Aux Gym Addition
MOA – Haselden

Design Development



**Lumberg ES** – 4 CR Addition
MOA – CMGC Haselden

# Design Development



**Manning Opt** – 1 Story - 7 Classroom Addition
AMD – Contractor TBD

Design Development

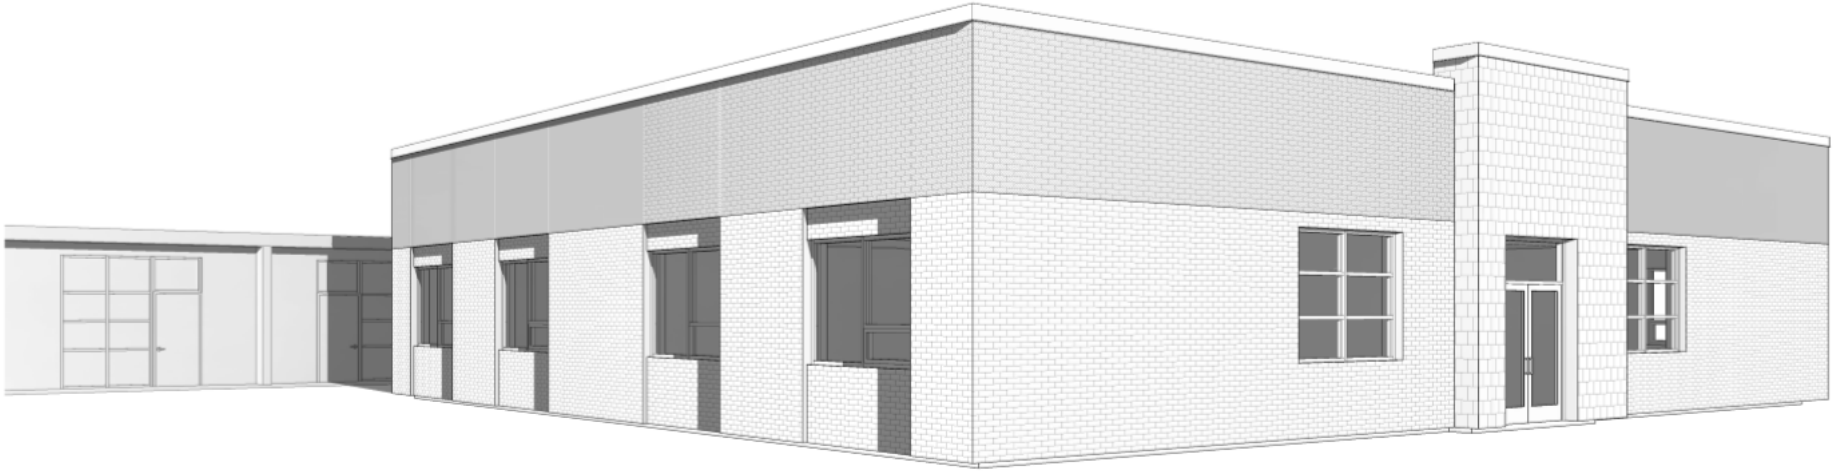


**Wayne Carle** – 2 Story – 8 Classroom Addition
AMD – Contractor TBD




**Parmalee ES** – 1 Story – 5/6 Classroom Addition
OZ – Contractor TBD



Construction Documents Estimate
$26,300,000
169,235SF
$155.4/SF



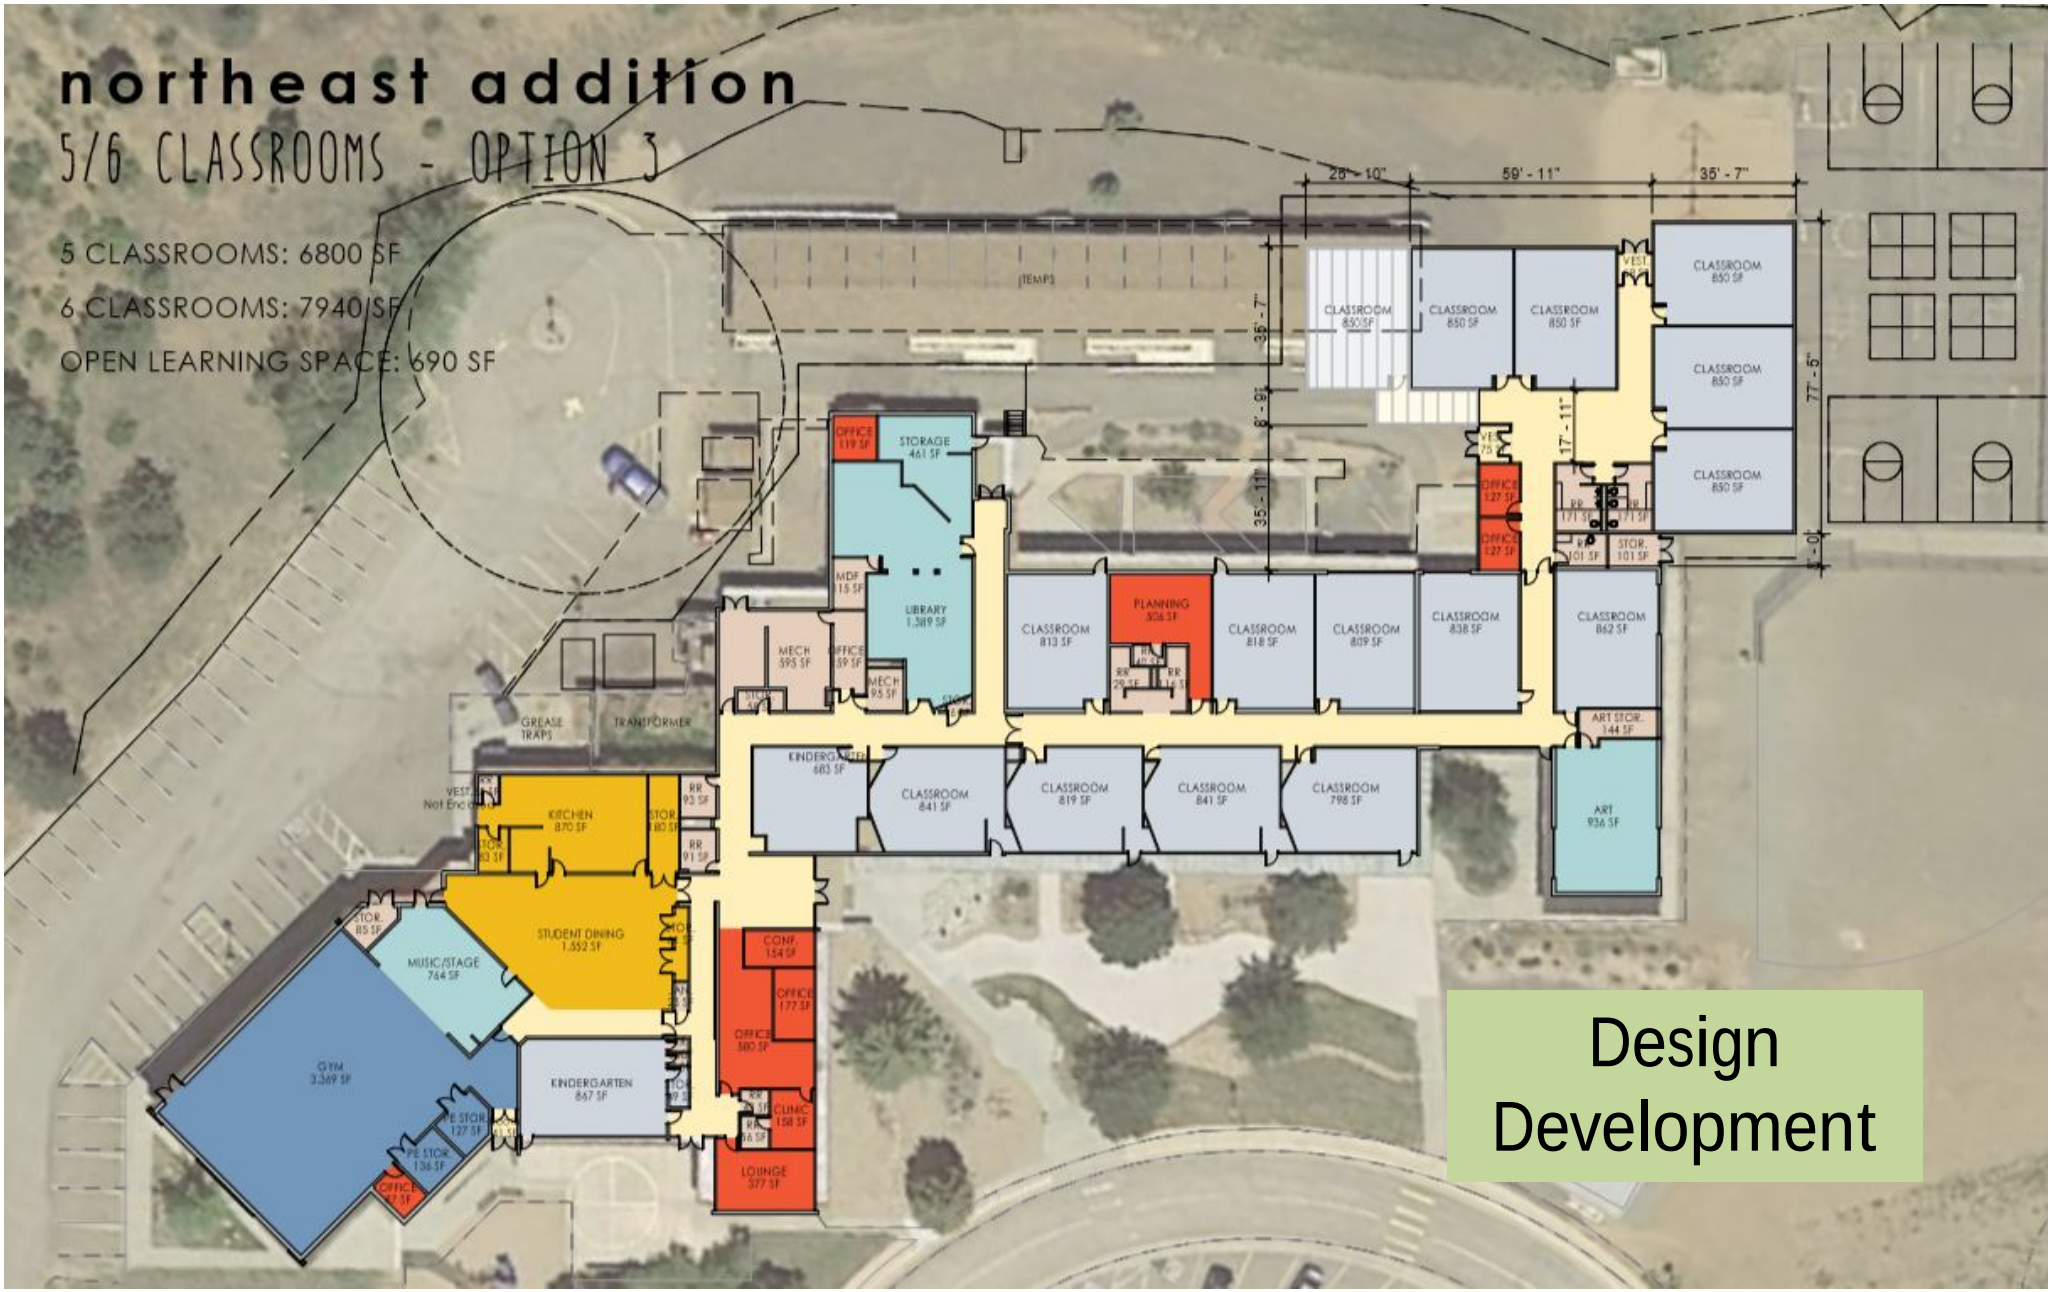



**Alameda HS** – Addition
Wold – CMGC Phipps

Construction Documents Estimate
$14,185,271
124,765SF
$114/SF




**Columbine HS** – Addition
Eidos – CMGC Swinerton

# Summer 2020 Construction Documents



$2,443,643

ARVADA WEST HIGH SCHOOL
11595 ALLENDALE DRIVE, ARVADA, CO 80004



$2,985,029

COLUMBINE HIGH SCHOOL
6201 S PIERCE STREET, LITTLETON, CO 80123



$2,501,031

GOLDEN HIGH SCHOOL
701 24TH STREET, GOLDEN, CO 80401



$4,027,821

GREEN MOUNTAIN HIGH SCHOOL
13175 WEST GREEN MOUNTAIN DRIVE, LAKEWOOD, CO 80228



$2,971,103

POMONA HIGH SCHOOL
8101 WEST POMONA DRIVE, ARVADA, CO 80005



$3,014,278

STANDLEY LAKE HIGH SCHOOL
9300 WEST 104TH AVENUE, WESTMINSTER, CO 80021

**2020 Field Improvements**

Awest HS, Columbine HS, Golden HS

Green Mountain HS, Pomona HS, Standley Lake HS

HCM – CMGC ECI

JEFFCO PUBLIC SCHOOLS

# 2018 Bond Program Communications Update
## Capital Asset Advisory Committee
### February 2020

## Completed Work:

- Wrote and published looking forward to 2020 construction:
  - Shared in Feb. Chalk talk and posted on Jeffcobuilds.org
- Held Arvada Groundbreaking event
  - The groundbreaking video was shared on Jeffco social and website

**Website analytics:**
Dates: Jan. 8 - Feb. 5
Jeffcobuilds.org and all pages with "jeffcobuilds" in the URL (ie sub-pages)
Pageviews: 2,198
Unique page views: 1,730

## Upcoming Work:

- Plan upcoming celebratory events for big construction projects
- Planning featured project stories and adding content for highlighted projects for articulation area pages
- Planning site tours for the board, media, and CAAC members



