

BOARD UPDATE

WILLIAM J. CLARK MIDDLE SCHOOL

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P

PROGRESS **UPDATE**

WILLIAM J. CLARK MIDDLE SCHOOL

IN THE LAST FEW WEEKS, WE HAVE:

- Finished footers on 10/11
- Began installing foundation block on 10/16
- Completed all underground electrical and plumbing
- We began to run our fire sprinkler main lines outside of the building
- Slab On Grade Prep began on 10/30

LOOK AHEAD:

- 10/30-11/7 – 1st Floor Slab on Grade Prep. Install sand, vapor barrier, expansion joint, floor drains, clean outs.
- 11/8 – Slab on Grade Poured
- 11/9 – Above Slab Masonry layout
- 11/10 – Above Slab Masonry Block will begin
- Mechanical, Electrical, and Plumbing rough-in will begin and keep up with the mason laying block
- 11/13 - Demolition Contractor will be on site to look at removing existing brick and window at back of school at tie-in
- Middle/End of next week steel will deliver
- Week of 11/20 steel will begin to be set
- Fire Mains are being run prior to exterior Sewer and Storm Drain continuation. Exterior sewer is complete other than the acid dilution tank tie in.

- NO SAFETY OR SECURITY ISSUES -

WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P





BOARD UPDATE

WILLIAM J. CLARK MIDDLE SCHOOL

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



BOARD UPDATE

LAKE MARION MIDDLE SCHOOL

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P

PROGRESS **UPDATE**

LAKE MARION MIDDLE SCHOOL

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P

IN THE LAST FEW WEEKS, WE HAVE:

- Finished pouring footers on 10/17
- Foundation block began on 10/23 and was completed by 10/30
- Completed all underground electrical and plumbing
- Completed installation of new exterior water mains
- Began running new exterior Sanitary Sewer Lines
- Slab On Grade Prep began on 10/30

LOOK AHEAD:

- 10/30-11/7 - Prepping to Pour Slab on Grade A. Installing sand, vapor barrier, expansion joint, floor drains, clean outs. Continuing to run exterior Sanitary Sewer
- 11/8 – Pour Slab on Grade A
- 11/9-11/14 – Prep Slab on Grade B. Install sand, vapor barrier, expansion joint, floor drains, clean outs, electrical floor boxes
- 11/15 – Pour Slab on Grade B. Door Frames and Steel will deliver this week
- 11/16 – Mason will begin above slab lay out, and will begin block work on 11/17
- Mechanical, Electrical, and Plumbing rough-in will begin as block is being laid.

- NO SAFETY OR SECURITY ISSUES -

LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG
COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG
COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG
COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG
COUNTY SCHOOL DISTRICT

LS3P





BOARD UPDATE

LAKE MARION MIDDLE SCHOOL

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P

OCSD – East Elementary

WEEK OF October 20th, 2023









SAFETY

Incidents to Date	0
First Aids to Date	0

SCHEDULE MILESTONES

- Completed building pad for areas B & C.

WEATHER

Working Days	5
Weather Days	0
Activities Delayed	0

MANPOWER

Number of Trades	3
Average Workers *(per day)*	15

TOP ACTIVITIES THIS WEEK

- Stake out building points on building pads B & C.
- Installed batter boards at areas B & C.
- Continued pond excavation.
- Start the development of building pad at area A.

UPCOMING ACTIVITIES


- Electrical subcontractor mobilization to begin underground roughs at area B kitchen.
- Continued development of building pad at area A.
- OAC Meeting #3 10/26 at 1PM

Thompson Turner Construction

CONSTRUCTION DYNAMICS, INC.
A General Contracting and Construction Management Firm

OCSD – East Elementary

WEEK OF October 27th, 2023

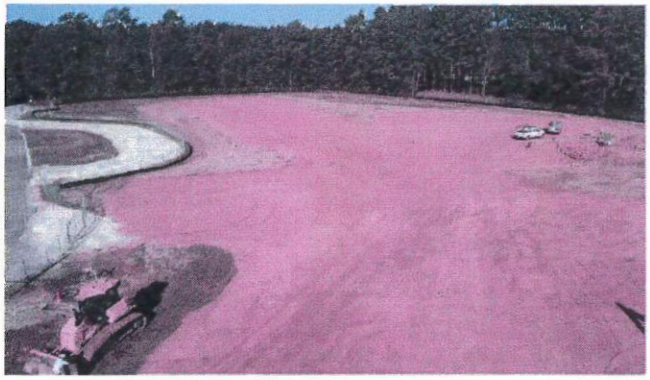







SAFETY

Incidents to Date	0
First Aids to Date	0

SCHEDULE MILESTONES

- Completed Area A Building Pad.

WEATHER

Working Days	5
Weather Days	0
Activities Delayed	0

MANPOWER

Number of Trades	3
Average Workers *(per day)*	18

TOP ACTIVITIES THIS WEEK

- Completed Area A Building Pad
- Began Underground Electrical Rough Ins
- Installed and Inspected Electrical Roughs at the Riser Room.
- OAC #3 Meeting

UPCOMING ACTIVITIES


- Foundations will begin on 10/31 at Area C & B.
- Underground Electrical and Plumbing Rough Ins at Area C & B.
- Install RCP at the Entrance off Way St
- Survey Building Points at Area A Building Pad.
- Install Batter Boards at Area A.

Thompson Turner Construction

CONSTRUCTION DYNAMICS, INC.
A General Contracting and Construction Management Firm


OCSD – East Elementary

WEEK OF November 3rd, 2023

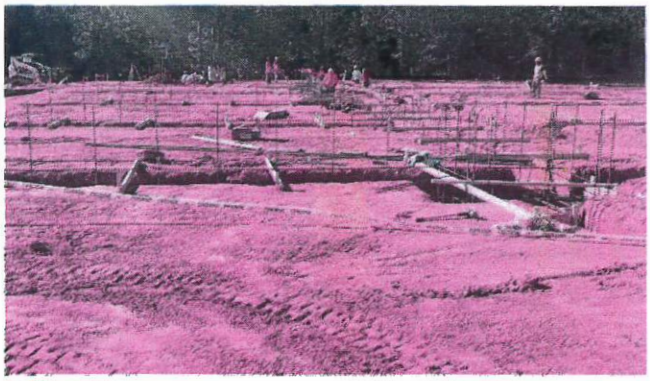





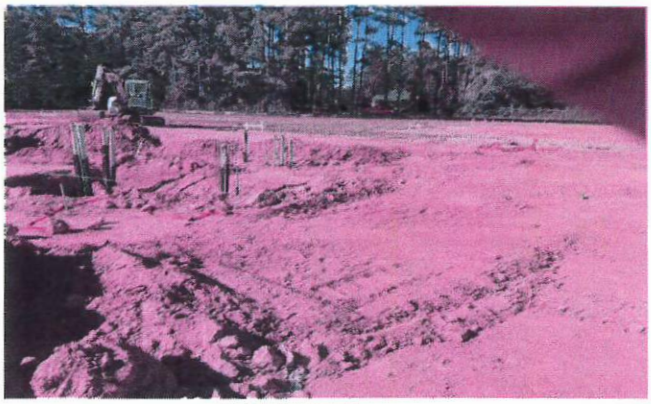

SAFETY

Incidents to Date	0
First Aids to Date	0

SCHEDULE MILESTONES

- Began Foundations at Area C & B

WEATHER

Working Days	5
Weather Days	0
Activities Delayed	0

MANPOWER

Number of Trades	4
Average Workers *(per day)*	30

TOP ACTIVITIES THIS WEEK

- Began foundations at Area C & B
- Continued underground electrical
- Stake building points at Area A
- Continued excavating at the pond

UPCOMING ACTIVITIES

- Pour footings at Area C & B
- Install batter boards at Area A
- CMU foundations
- Underground plumbing

Thompson Turner Construction

CONSTRUCTION DYNAMICS, INC.
A General Contracting and Construction Management Firm
