ORANGEBURG WILKINSON HIGH SCHOOL

SAFETY

Incidents to Date	#0
First Aids to Date	#0

WEATHER

Working Days	#2
Weather Days	#0
Activities Delayed	#0

MANPOWER

Number of Trades	#1
Average Workers *(per day)*	#10

SCHEDULE MILESTONES

- Groundbreaking Ceremony 4/18/24
- Land Disturbance Pre-Con 4/26/24
- Site Contractor Moblization 5/3/24

Top Activities This Week

- Layout and staking of the project property lines began on 5/6/24.
- The clearing subcontractor began clearing property lines on 5/6/24.
- Installation of silt fencing began on 5/7/24.
- Project submittals are in progress.

Upcoming Activities

- Clearing and grubbing of the site.
- Installation of all silt fencing and erosion control measures.
- Installation of Cook Road construction entrance.
- Mass grading of the site will begin.
- Construction of the building pad will begin.









Week of

May 6, 2024


OCSD – East Lake Elementary

WEEK OF April 12th, 2024







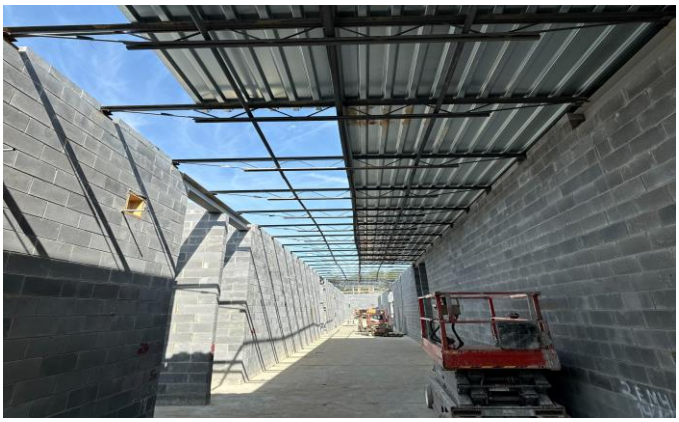

SAFETY

Incidents to Date	0
First Aids to Date	0

SCHEDULE MILESTONES

WEATHER

Working Days	5
Weather Days	1
Activities Delayed	3

MANPOWER

Number of Trades	8
Average Workers *(per day)*	100

TOP ACTIVITIES THIS WEEK

- Continued overhead rough ins at Areas B & C
- Started CMU at the Area C second floor
- Temporary roof dry in at the kitchen
- Install steel joist and decking at Area A
- Electrical in wall rough ins at the auditorium
- Continued CMU at Areas A and B
- Continued plumbing and electrical rough ins at Area B/C second floor

UPCOMING ACTIVITIES

- Continue MEP overhead at Areas B/C
- Continue CMU Installation at Area A, B, the rotunda, and at the second floor of Area C
- Continue steel joist and decking at Area A
- Continue in wall rough ins at the second floor of Area C

Thompson Turner Construction

CONSTRUCTION DYNAMICS, INC.
A General Contracting and Construction Management Firm

OCSD – East Lake Elementary

WEEK OF April 19th, 2024









SAFETY

Incidents to Date	0
First Aids to Date	0

SCHEDULE MILESTONES

WEATHER

Working Days	5
Weather Days	0
Activities Delayed	0

MANPOWER

Number of Trades	9
Average Workers *(per day)*	109

TOP ACTIVITIES THIS WEEK

- Continued overhead rough ins at Areas B & C
- Continued CMU at the Area C/B second floor
- Temporary roof dry in at the kitchen
- Continued steel joist and decking at Area A
- Electrical in wall rough ins at the auditorium
- Continued CMU at Areas A and B
- Continued plumbing and electrical rough ins at Area B/C second floor
- Poured concrete stair treads for Stair #2
- Wood blocking around the windows
- Parged walls in the kitchen

UPCOMING ACTIVITIES

- Continue MEP overhead at Areas B/C
- Continue CMU Installation at Area A, B, the rotunda, and at the second floor of Area C
- Continue steel joist and decking at Area A
- Continue in wall rough ins at the second floor of Area C/B

Thompson Turner Construction

CONSTRUCTION DYNAMICS, INC.
A General Contracting and Construction Management Firm

OCSD – East Lake Elementary

WEEK OF April 26th, 2024









SAFETY

Incidents to Date	0
First Aids to Date	0

SCHEDULE MILESTONES

WEATHER

Working Days	5
Weather Days	0
Activities Delayed	0

MANPOWER

Number of Trades	9
Average Workers *(per day)*	109

TOP ACTIVITIES THIS WEEK

- Began installing brick at the kitchen
- Started MEP overhead at Area A
- Began priming in the kitchen
- Continued overhead rough ins at Areas B & C
- Continued CMU at the Area C/B second floor
- Temporary roof dry in at the kitchen
- Continued steel joist and decking at Area A
- Electrical in wall rough ins at the auditorium
- Continued CMU at Areas A and B
- Continued plumbing and electrical rough ins at Area B/C second floor

UPCOMING ACTIVITIES

- Continue MEP overhead at Areas A,B,C
- Continue CMU Installation at Area A, B, the rotunda, and at the second floor of Area C/B
- Continue steel joist and decking at Area A
- Continue in wall rough ins at the second floor of Area C/B
- Continue brick at the kitchen

Thompson Turner Construction

CONSTRUCTION DYNAMICS, INC.
A General Contracting and Construction Management Firm

OCSD – East Lake Elementary

WEEK OF May 3rd, 2024









SAFETY

Incidents to Date	0
First Aids to Date	0

SCHEDULE MILESTONES

WEATHER

Working Days	5
Weather Days	1
Activities Delayed	4

MANPOWER

Number of Trades	9
Average Workers *(per day)*	111

TOP ACTIVITIES THIS WEEK

- Continue installing brick at the kitchen and Area A
- Applied spray foam insulation
- Continued MEP overhead at Area A
- Continued overhead rough ins at Areas B & C
- Continued CMU at the Area B second floor
- Continued roof installation at Area A
- Continued steel joist and decking at the auditorium
- Electrical in wall rough ins at the auditorium
- Continued CMU at the admin area
- Continued plumbing and electrical rough ins at Area B/C second floor
- Sewer tie in

UPCOMING ACTIVITIES

- Continue MEP overhead at Areas A
- Continue CMU Installation at the rotunda, and at the second floor of Area B
- Continue steel joist and decking at the auditorium
- Continue in wall rough ins at the second floor of Area C/B
- Continue brick at the kitchen and Area A

Thompson Turner Construction

CONSTRUCTION DYNAMICS, INC.
A General Contracting and Construction Management Firm



BOARD UPDATE

WILLIAM J. CLARK MIDDLE SCHOOL

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P

PROGRESS **UPDATE**

WILLIAM J. CLARK MIDDLE SCHOOL

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P

IN THE LAST FEW WEEKS WE HAVE:

- Set our rooftop units and equipment
- Installed windows
- Finished all interior masonry
- Hung and finished all Sheetrock
- Continued to work towards completing overhead MEPs on both floors

IN THE NEXT FEW WEEKS WE WILL:

- Install all roof metal and downspouts
- Start and complete paint on May 8
- Start ceiling grid
- Wrap up all above ceiling MEP work

- NO SAFETY OR SECURITY ISSUES -

WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



WILLIAM J. CLARK **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P





BOARD UPDATE

LAKE MARION MIDDLE SCHOOL

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P

PROGRESS **UPDATE**

LAKE MARION MIDDLE SCHOOL

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P

IN THE LAST FEW WEEKS WE HAVE:

- Installed all canopy footings
- Begun installation of canopy
- Begun rough grading around the building
- Began installing all doors interior and exterior

IN THE NEXT FEW WEEKS WE WILL:

- Turn permanent power on the building
- Mechanical start up of the classroom bars units on 5/13
- 3rd party above ceiling inspection on 5/16 of remainder of building
- Epoxy flooring starting on 5/20
- Final paint will begin on 5/20

- NO SAFETY OR SECURITY ISSUES -

LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG
COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P



LAKE MARION **MIDDLE**

CONTRACT
CONSTRUCTION

ORANGEBURG COUNTY SCHOOL DISTRICT

LS3P

