ID	Task Name	Duration	Start	Finish	Predecessors
1	**Witter Field Completion Schedule**				
2	**Track and Field**	**50 days**	**Mon 6/3/24**	**Fri 8/9/24**	
3	Remobilize to Witter Field	1 day	Mon 6/3/24	Mon 6/3/24	
4	Demo Existing AC and Base Material	4 days	Tue 6/4/24	Fri 6/7/24	3
5	Lay Geogrid, Import and Compact Base Rock	5 days	Mon 6/10/24	Fri 6/14/24	4
6	Pave Track	1 day	Mon 6/17/24	Mon 6/17/24	5
7	AC Cure	28 edays	Mon 6/17/24	Mon 7/15/24	6
8	Base Mat Installation	5 days	Mon 7/15/24	Fri 7/19/24	7FS-1 day
9	Base Mat Seal Coat Installation	5 days	Mon 7/22/24	Fri 7/26/24	8
10	Top Coat Installation/Granule Broadcast	5 days	Mon 7/29/24	Fri 8/2/24	9
11	Striping	6 days	Fri 8/2/24	Fri 8/9/24	10FS-1 day

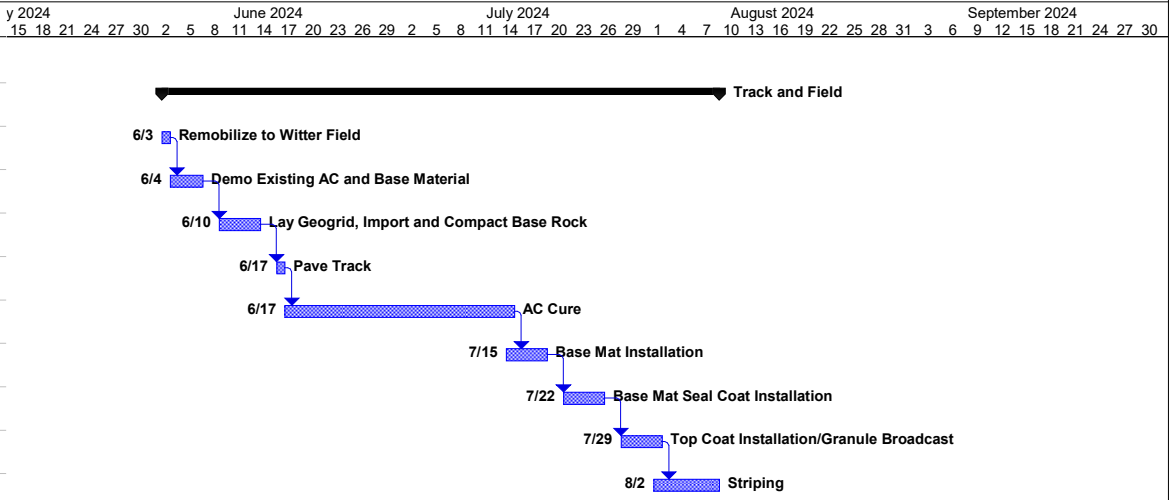

Robert A. Bothman, Inc.
2690 Scott Boulevard, Santa Clara, CA 95050
