JULY 2024

Saturdays - Hard ground conditions have slowed progress so there will be Saturday work for the entire month of July.

- Ground improvement work under the footprint of the building will continue throughout July into August.
- Rammed aggregate piers will be installed. Boreholes filled with compacted gravel will be installed in a pattern under the footprint of the building. This will increase the soil bearing capacity to support the load of the new building. This work is being done in preparation for the concrete footings and foundation that will follow.
- Water supply pipe, storm sewer pipe and manhole installation will start up in July. This work will take place in the same general areas as the sanitary sewer pipe installation.
- Soil will continue to be exported from the site. As excess material is removed, grading and compacting work will also continue.
- The concrete contractor will mobilize to the site.
- Concrete footing work will begin towards the end of July / beginning of August.

APRIL 2024

April 1 - A new traffic pattern will go into effect for student drop-off and pick-up. Norwalk Police and Norwalk Public Schools security officers will provide assistance to parents/guardians who are dropping off and picking up. NPD will also be on site to help direct traffic. Signage will also be posted in the area.

MARCH 2024

UPDATE (3/22)

Dear Norwalk Families,

We have several updates for the Norwalk High School/P-TECH Norwalk construction project that will be occurring over the next week and a half.

March 25 - Students can no longer park on the NHS/P-TECH campus. All students must park at Andrews Field. The Norwalk Police Department will be on site to help students cross the street.

Note: There will be no footpath access between the NHS/P-TECH campus and Naramake Elementary School.

For more information and all the updates on this project, please visit the Norwalk High School/P-TECH Norwalk project page on the NPS School Construction website.

Again, we thank you for your patience and support throughout this process. Please look for our April 2024 Update next week.

NPS Communications

TRAFFIC PATTERN

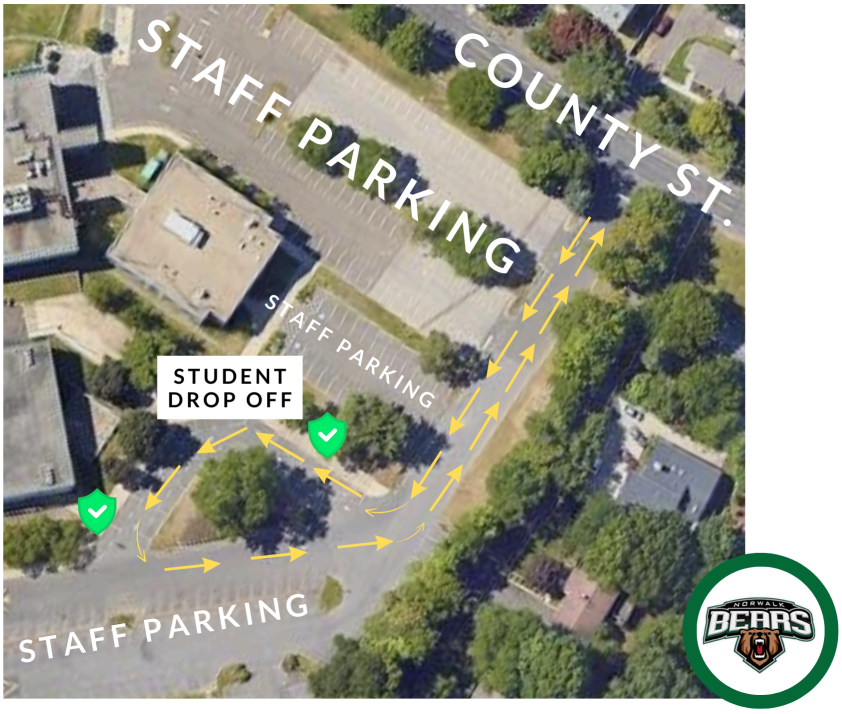

ORIGINAL (3/11)

Dear Norwalk Families,

We're excited to announce that construction is getting underway for the new Norwalk High School/P-TECH Norwalk building. While we look forward to sharing this new space with our students, staff, families and community, we fully understand that the construction process may cause some inconvenience for the community.

Throughout the next three to five years, we intend to keep you apprised of upcoming construction events so you can plan accordingly. Operations at the current Norwalk High/P-TECH school will continue throughout construction as well as operations at our neighborhood schools, and we want to make sure the construction activity on the fields doesn't interrupt the learning experience and environment of our students and staff.

If you have any questions regarding the Norwalk High/P-TECH campus, please contact NHS Asst. Principal Job Fernandez.

Updates will be posted on the NPS School Construction website. Please check here for more information throughout the project: Norwalk High School/P-TECH Norwalk

Thank you for your patience and support throughout this process. We look forward to opening the new school in 2027!

March 2024 Updates

Gilbane Building Company, the construction management company for the NHS/P-TECH project, is already on-site and mobilizing.

March 11 - Fencing will start to go up around the construction site. This will not have an immediate impact on campus traffic, but it will close the football field and track.

March 18 - Some student parking will be affected (reassignments will be done by the NHS/P-TECH staff).

March 29 - Student parking on campus will be closed and relocated to Andrew's Field. Drop off and pick up will be modified.

Click here for more information regarding NHS/P-TECH student parking.

Norwalk Public Schools
