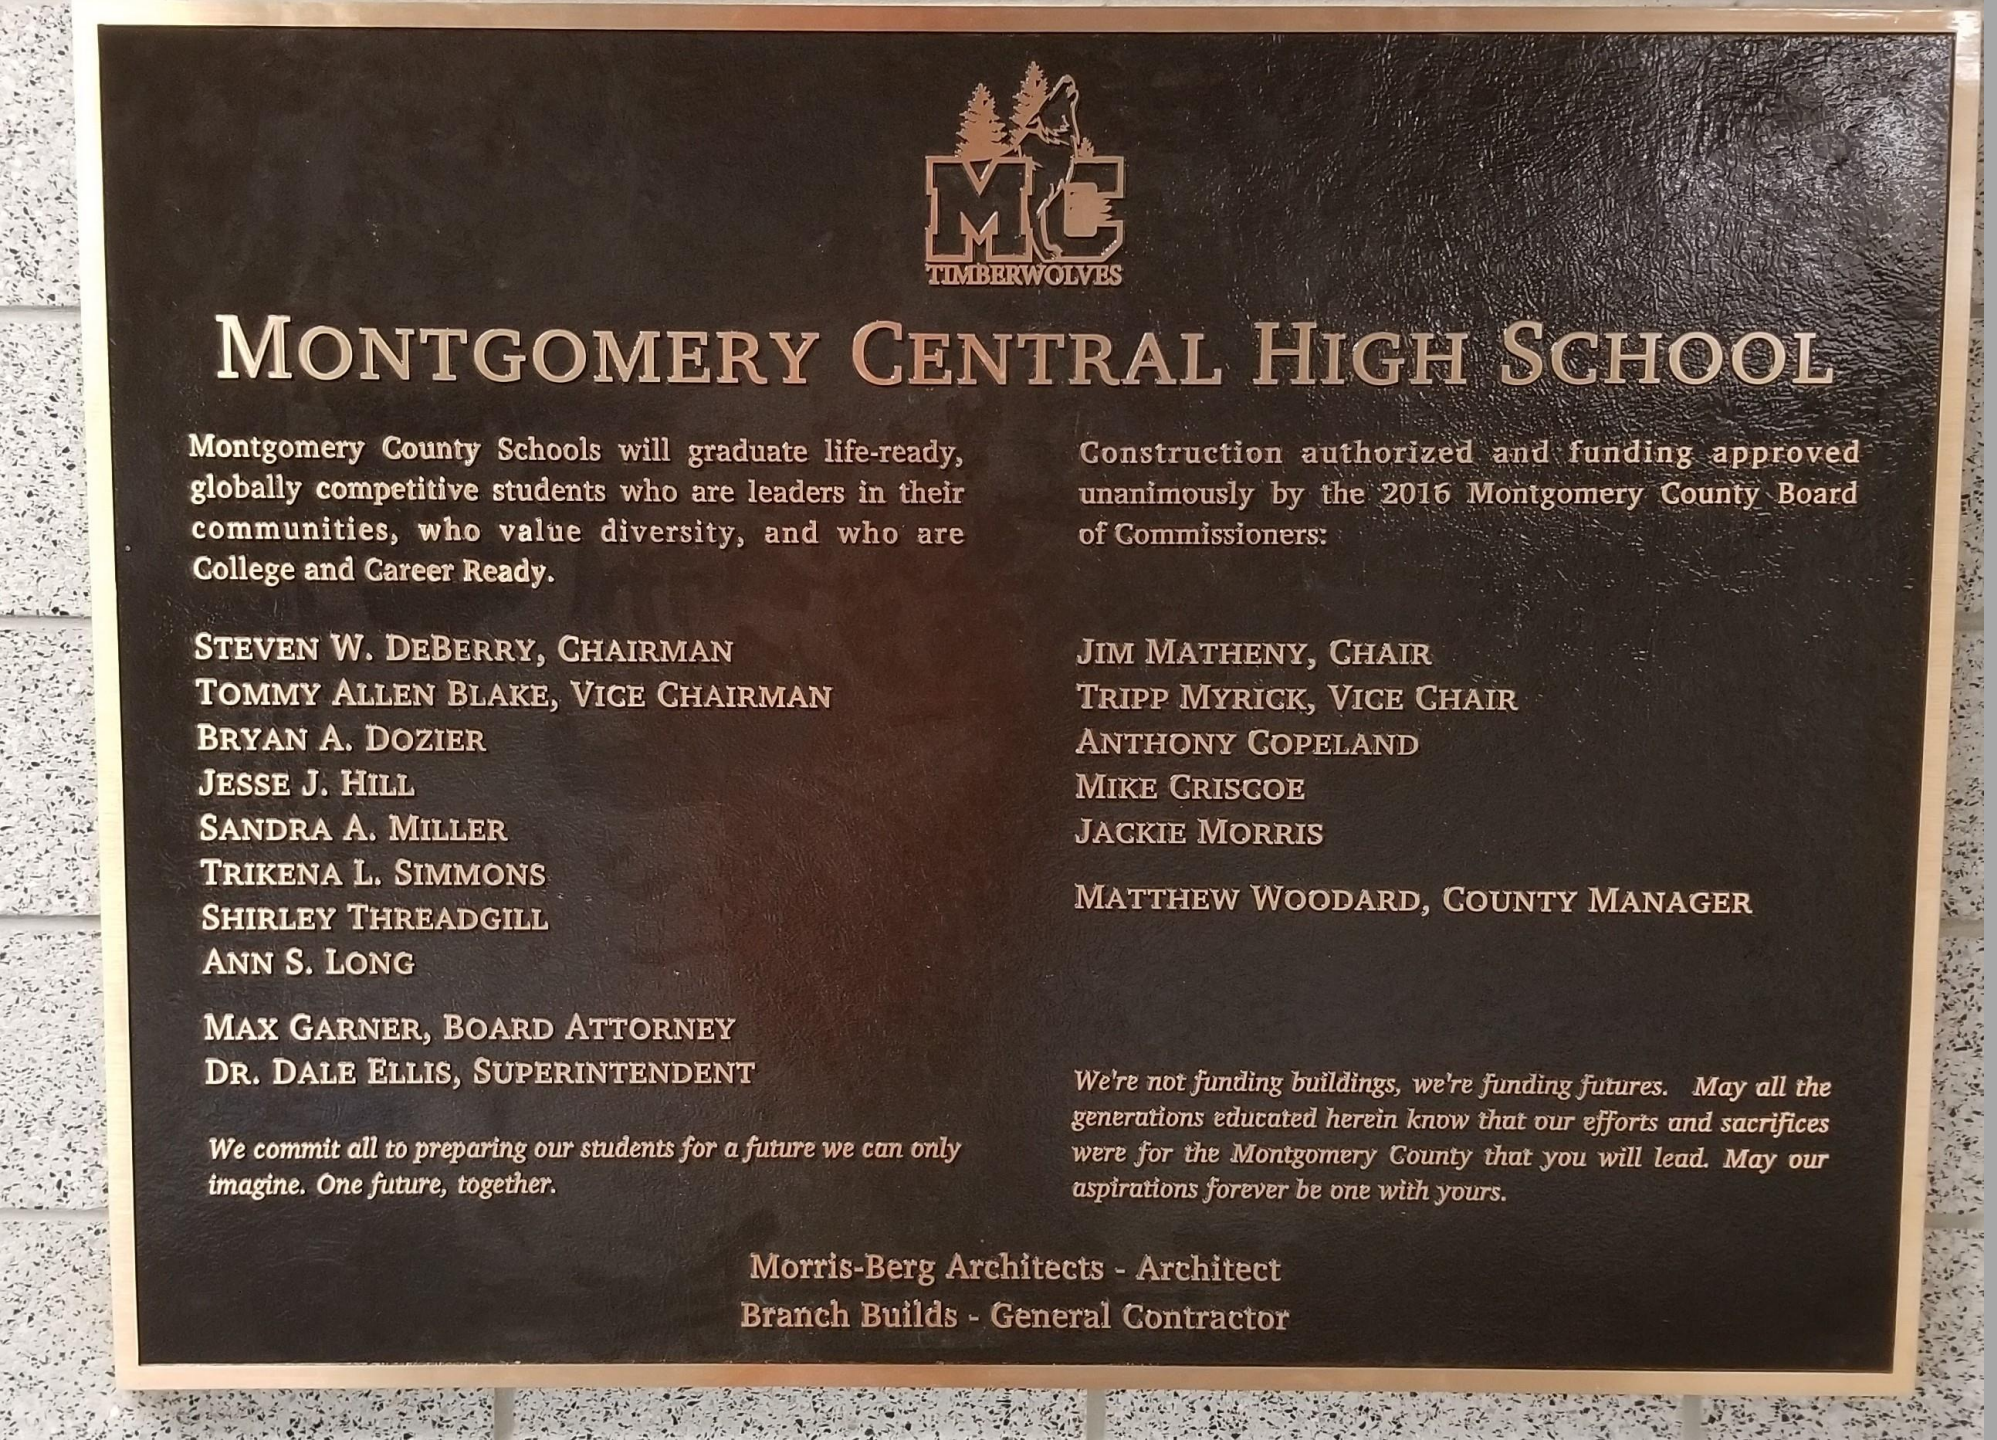



# PROJECT UPDATE

# JULY 6, 2020

# Owner/Architect Acceptance Dates:

May 27 Review – By Dates

**HIGHCAP's Last Review Conducted 6/30/2020 – Pending Data Not Available**

| | | Date | Met -7/1/2020 |
|---|---|---|---|
| Area E/F | Instructional Wing – Second Floor | June 30 | NO |
| Area A1 | Locker Rooms/athletic support | July 1 | NO |
| Area E/F | Instructional Wing – First Floor | July 1 | NO |
| Area B | Kitchen | July 13 | |
| Area C | Second Floor – Media | July 20 | |
| Area B | Dining | July 21 | |
| Site | Athletic Structures | July 24 | |
| Area A2 | Main/Auxiliary Gymnasiums | July 27 | |
| Area C | First Floor – Office Areas | July 28 | |
| Area D | Auditorium/Performing Arts/Band: | August 3 | |
| Site | Site work CTE & HS | August 7 | |
| Site | HS Landscaping | August 14 | |
| Exterior | HS Façade | September 14 | |

Project Substantial Completion - September 15

Project Final After Closeout Documents – October 15



## Furniture Fixtures and Equipment:

| | | Start Install* | Work Days* | Complete* |
|---|---|---|---|---|
| Area A1 | Locker Rooms/athletic support | July 2** - NO | 5 | July 8 |
| Area B | Kitchen | July 14 | 5 | July 27 |
| Area C | Second Floor – Media | July 21 | 5 | July 27 |
| Area B | Dining | July 22 | 5 | July 28 |
| Area E/F | Instructional Wing – Second Floor | July 1** - NO | 20 | July 28 |
| Area E/F | Instructional Wing – First Floor | July 2** - NO | 20 | July 29 |
| Area A2 | Main/Auxiliary Gymnasiums | July 28 | 5 | August 3 |
| Area C | First Floor – Office Areas | July 29 | 5 | August 4 |
| Area D | Auditorium/Performing Arts/Band: | August 4 | 5 | August 10 |


*Dates proposed by Branch Builds, not yet confirmed by Learning Environments – the furniture vendor.


**These dates fall within the typical July 4th Holiday period

NO Indicates Vendor not starting installation as proposed.




# Main Entrance – Montgomery Central High School

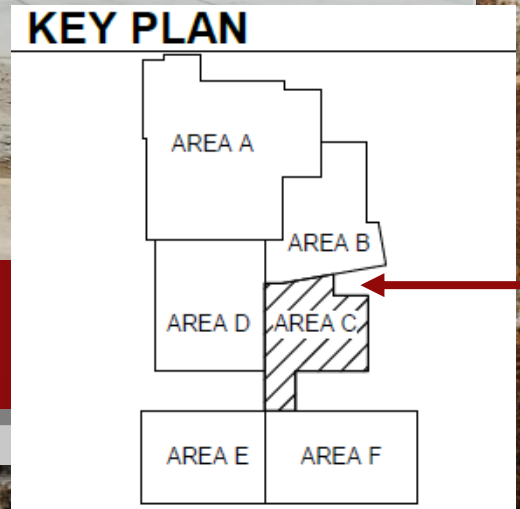

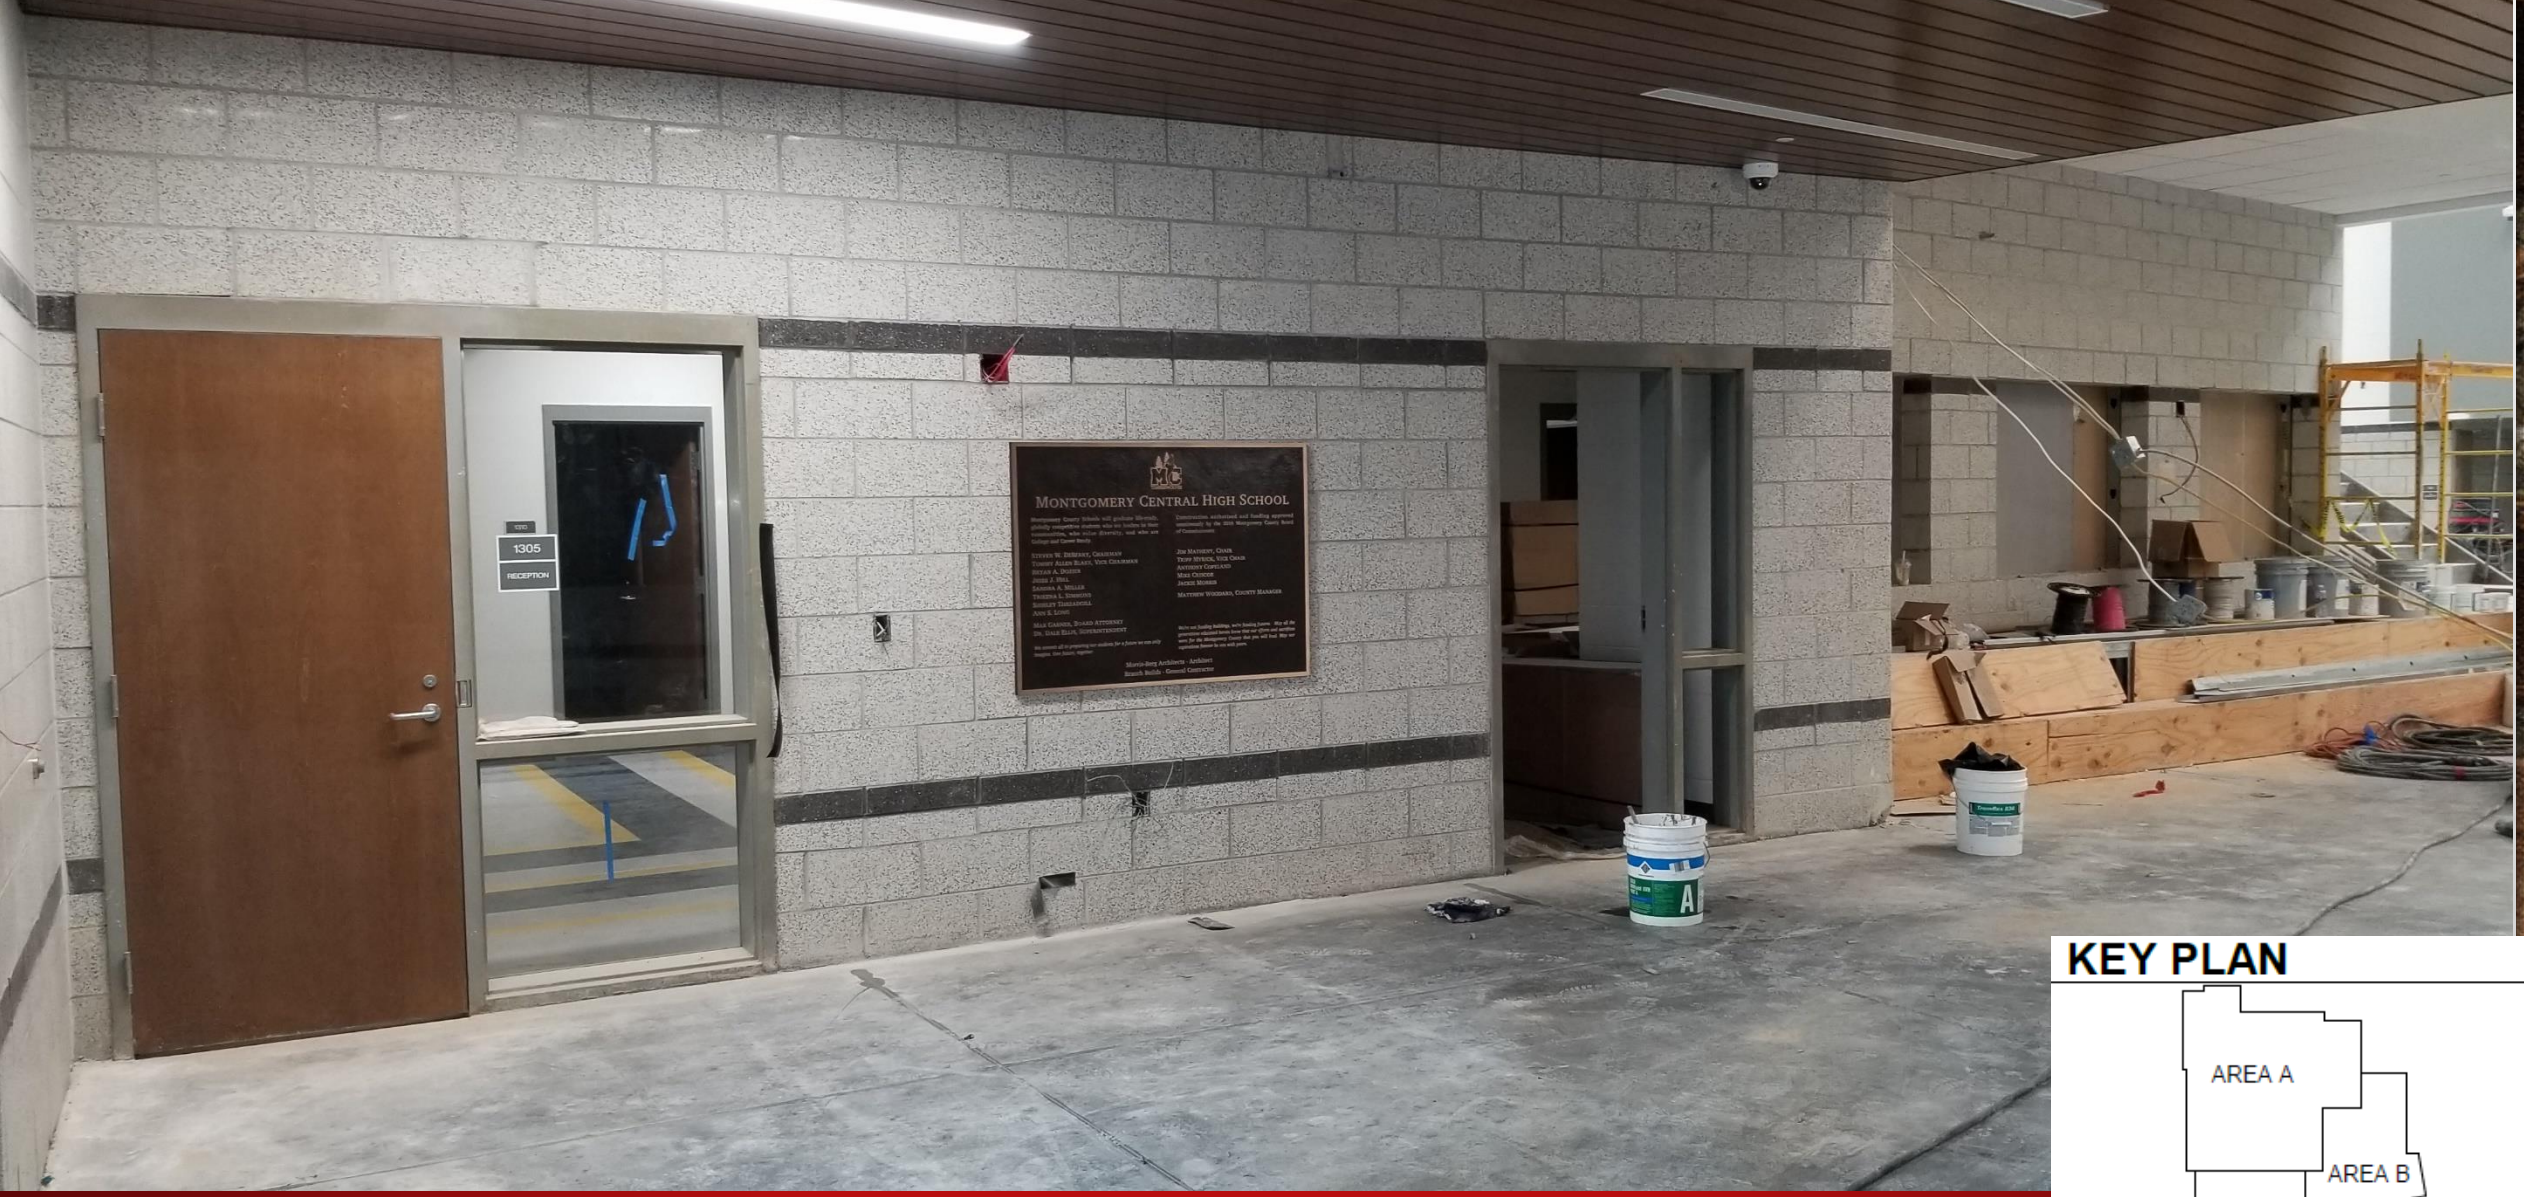



# Main Office Entrance

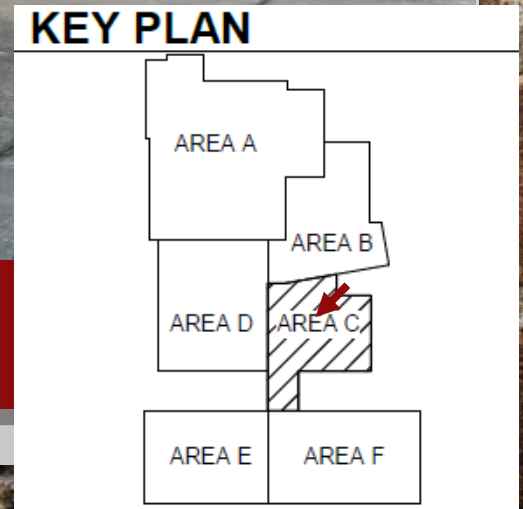




# Main Lobby Wall


## KEY PLAN

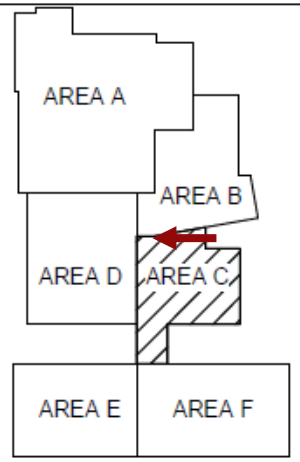




# Main Entrance Facing East



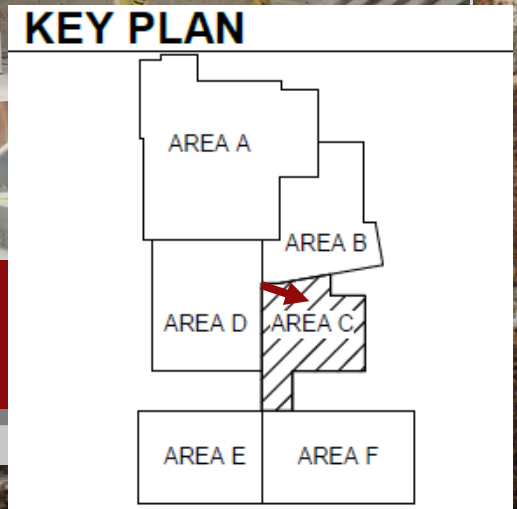




# Main Corridor – Concrete Polishing in Progress

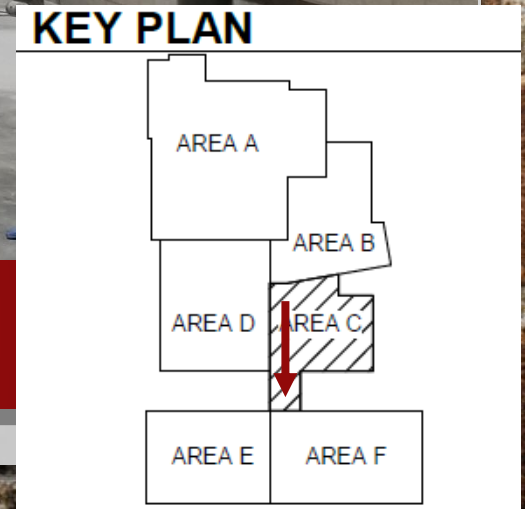


# Area B – Dining – Ceiling Clouds in Progress

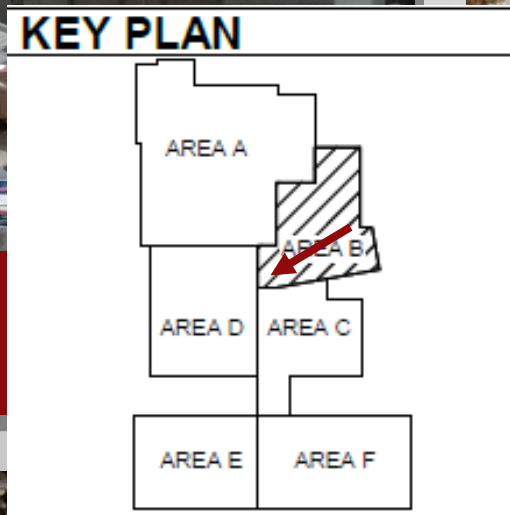


# Main Gymnasium – South Wall

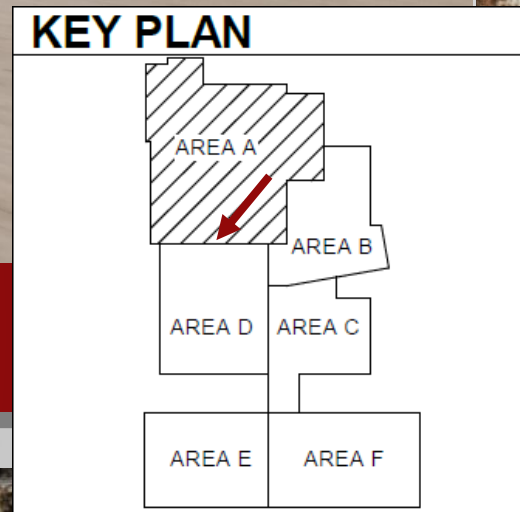

# Main Gymnasium – North Wall



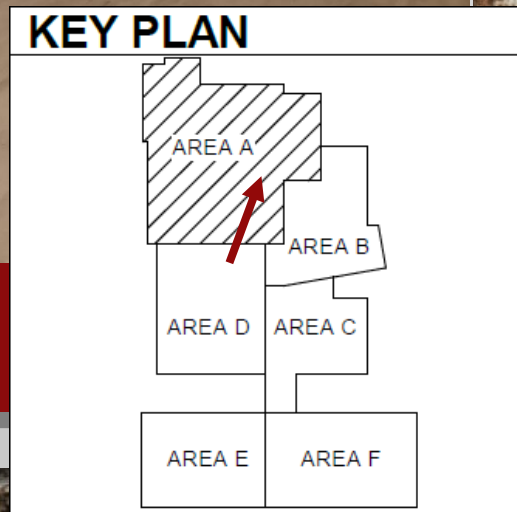

# Area D – Auditorium – Carpet Tile Installed




# Area D – Auditorium – Wood Stage Floor Installed





# Area D – Dance – Wood Floor Installed

**KEY PLAN**


# Area C 2nd Floor – Connector

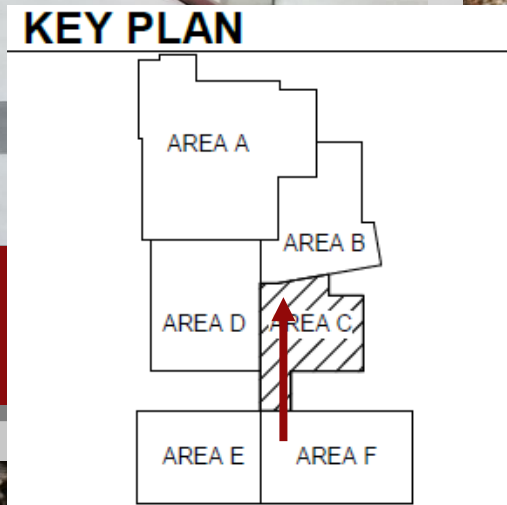


# Area C 2nd Floor – Art/Performing Arts Courtyard

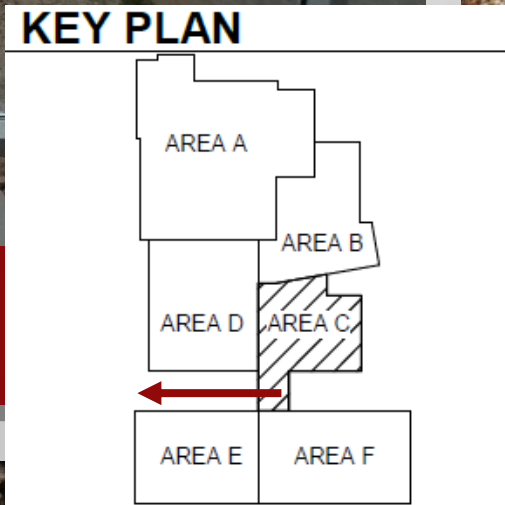


# Area C 2nd Floor – Area between C-F

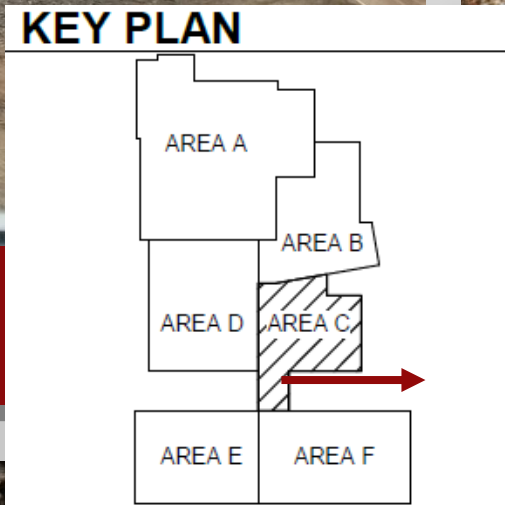

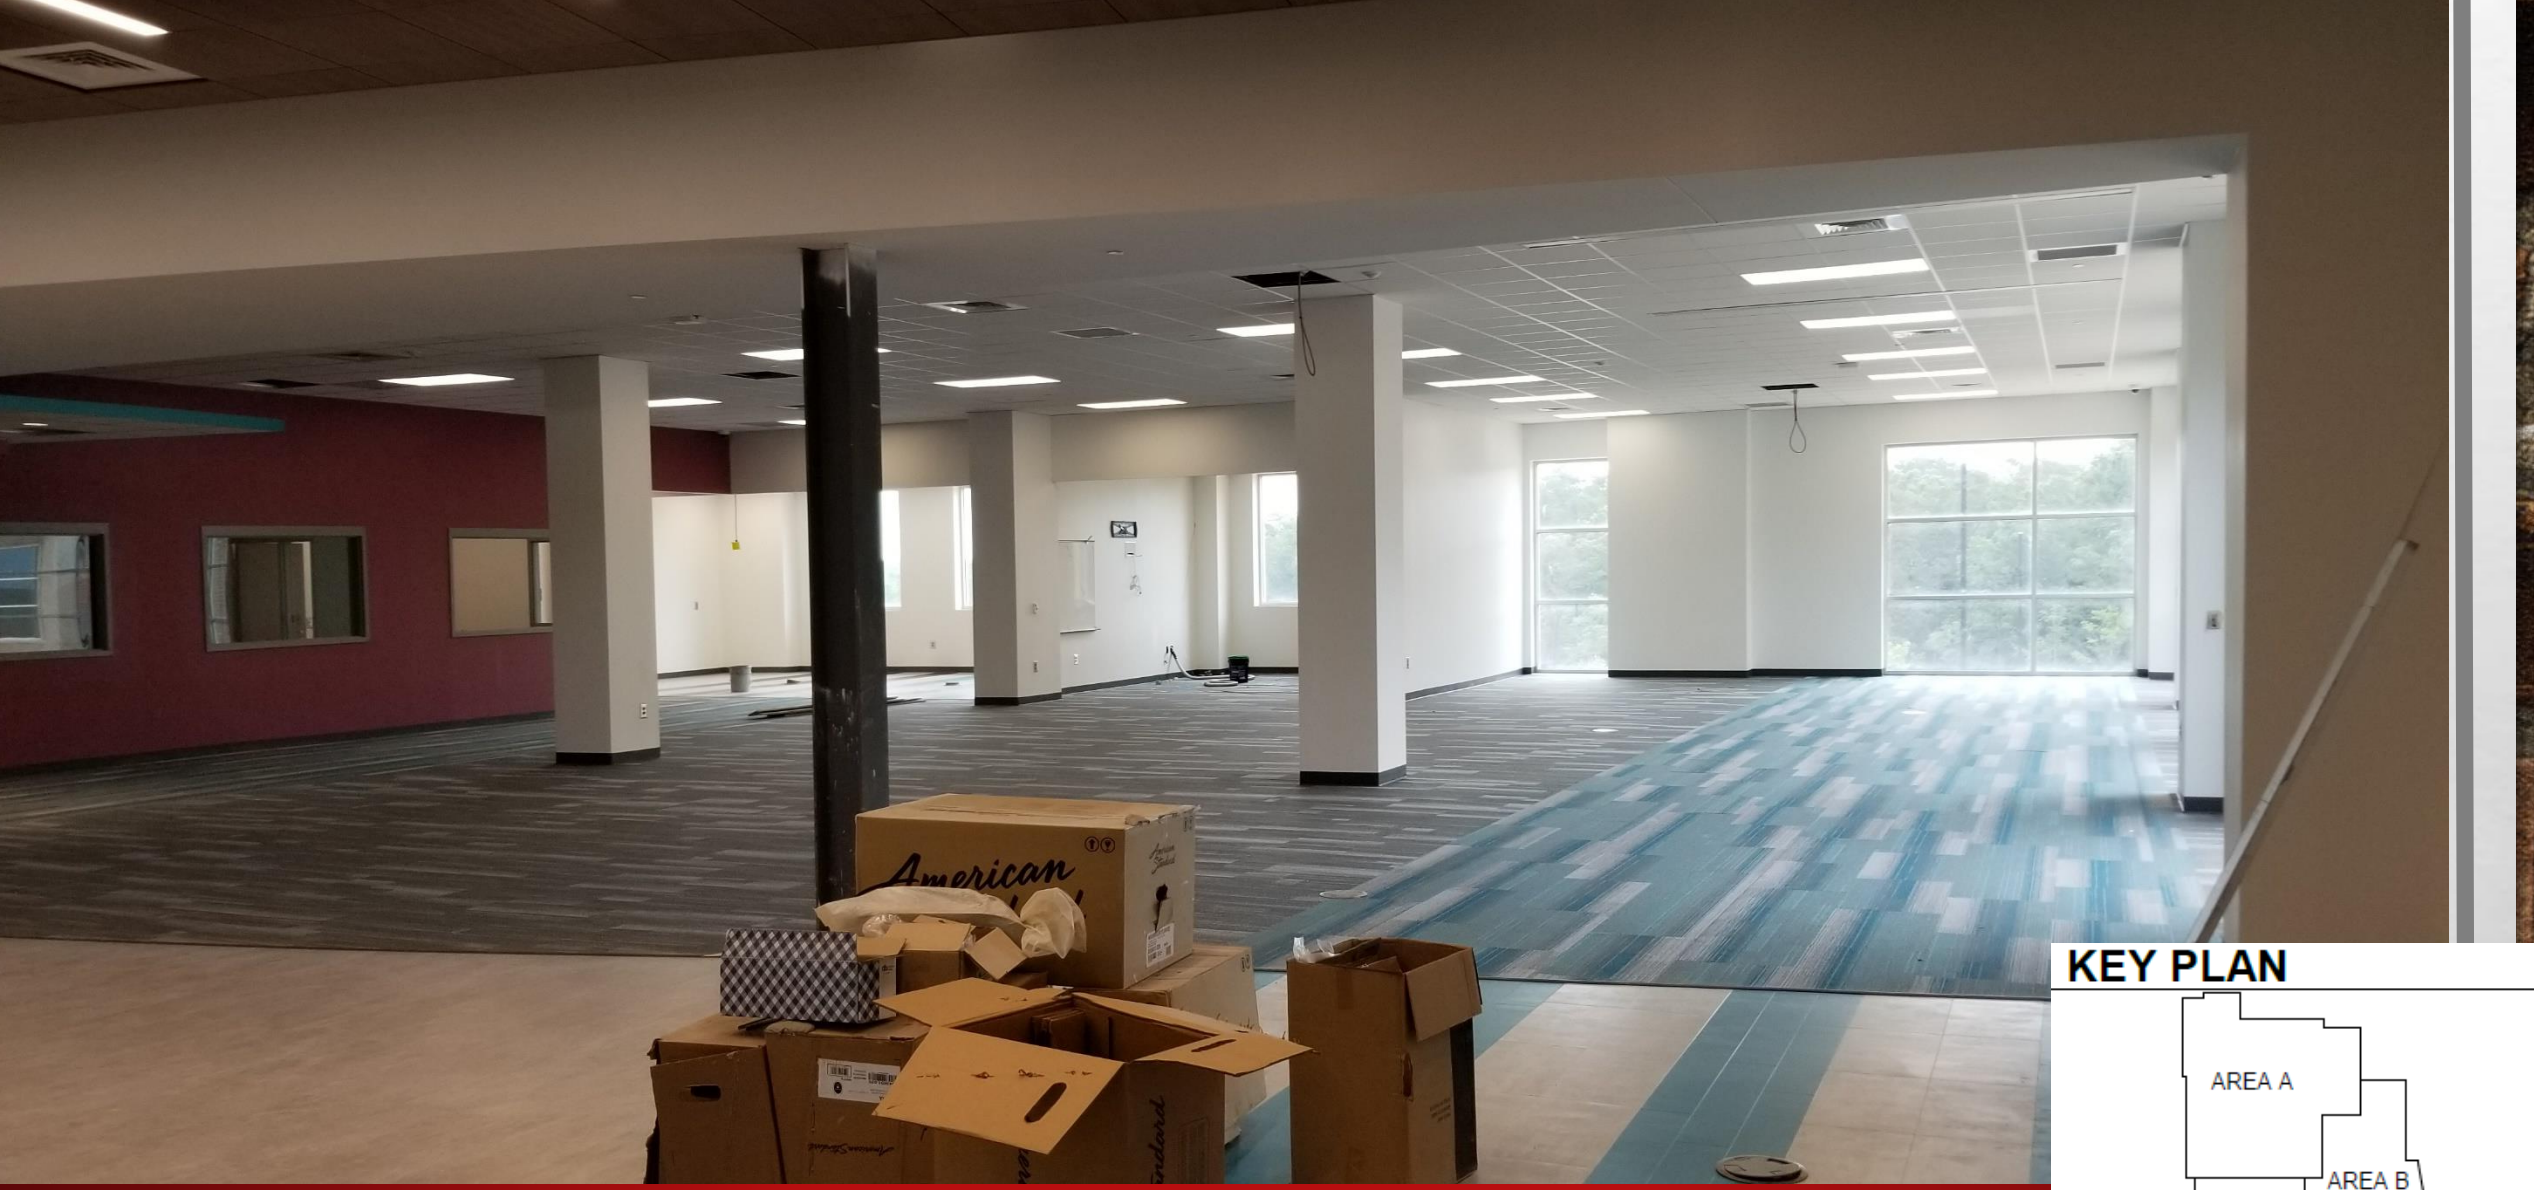



# Area C 2nd Floor – Media – Looking Through Sky Fold Door

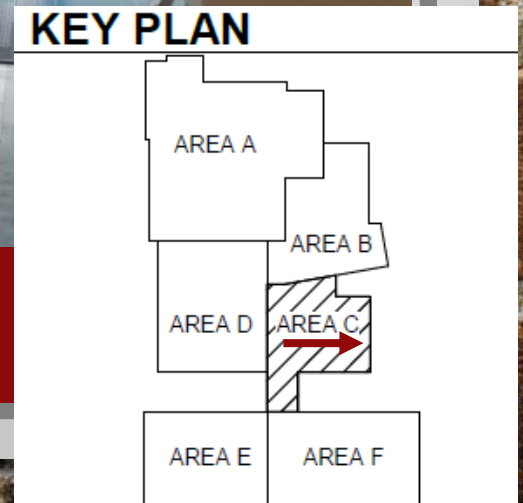





# Area C 2nd Floor – Media – Looking Through Sky Fold Door

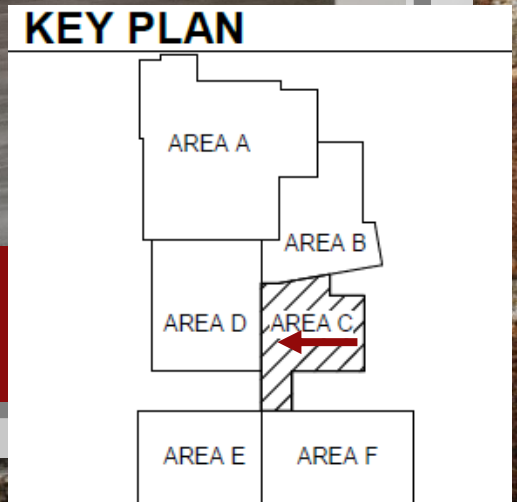


# Media – Looking At Workrooms/Cyber Café/Computer Lab

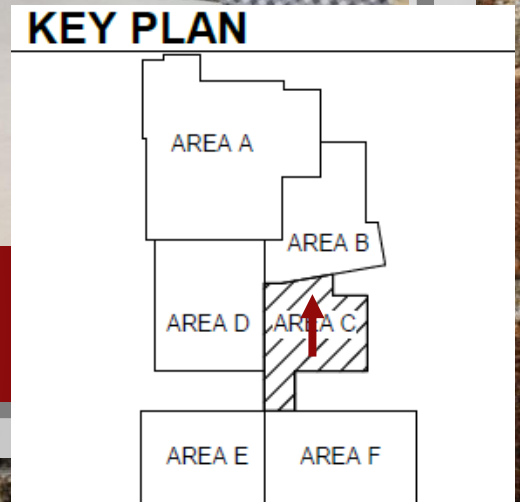




Cyber Café – View down to Main Lobby

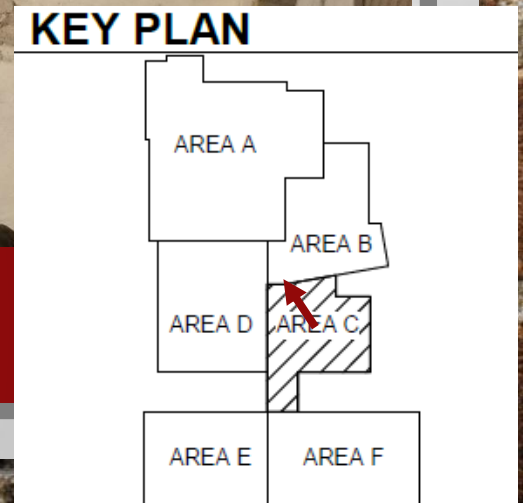


# Area F 2nd Floor - Chemistry Room

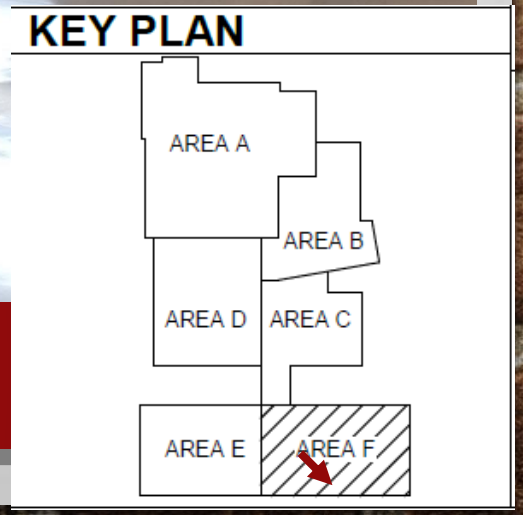



# Area F 2nd Floor - Gang Restrooms

# Area E 1st Floor – Common/Distance Learning Lab

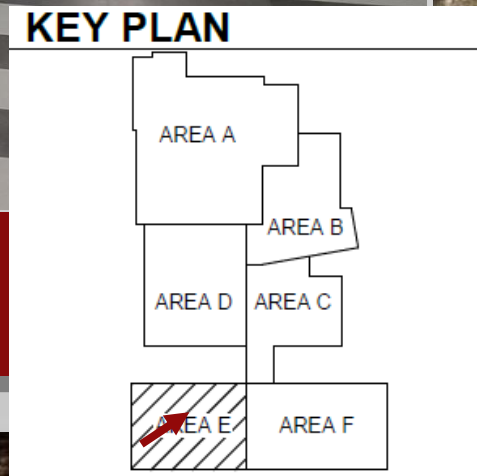

# ??QUESTIONS??

# Let's ask Kevin!




**Happy Retirement to my Boss and Friend!**





END SLIDE – QUESTIONS???


KEY PLAN

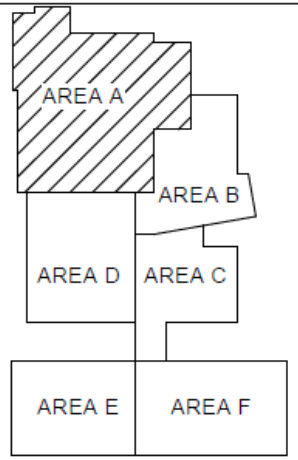



KEY PLAN

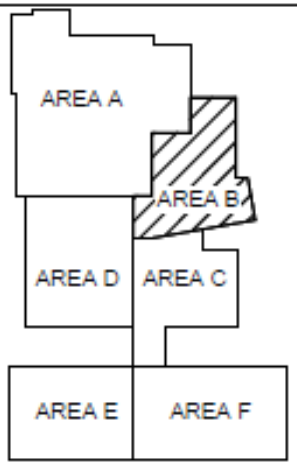



KEY PLAN

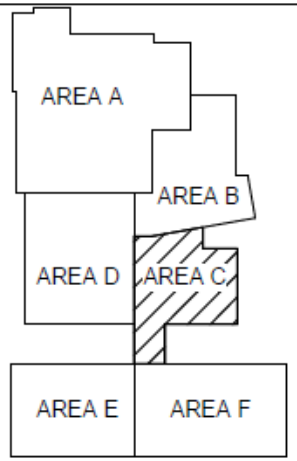



KEY PLAN

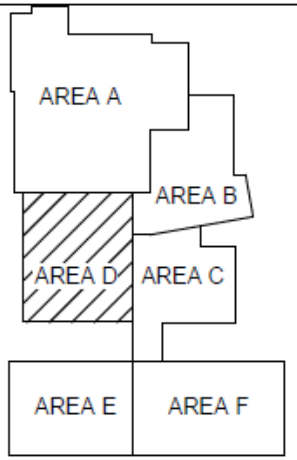


KEY PLAN

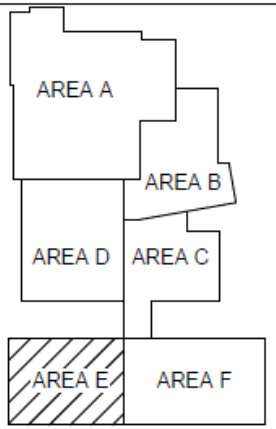



KEY PLAN

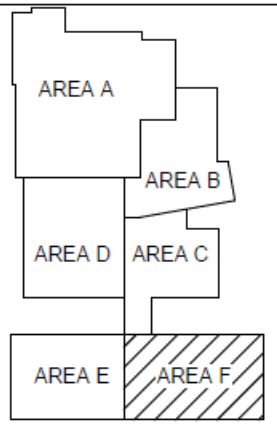



KEY PLAN




KEY PLAN




SITE KEY PLAN

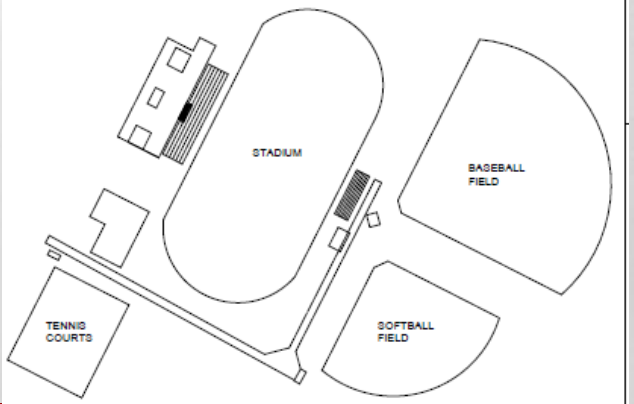


KEY BLOCK – DO NOT DELETE
