MCHS

CONSTRUCTION PROJECT UPDATE – DECEMBER 2, 2019

CONSTRUCTION PROJECT UPDATE

- **BUILDINGS – COMPLETED LAST 30 DAYS**
  - CTE…OUTSIDE FENCE HAS BEEN INSTALLED. HARD TILE IN CTE IS COMPLETE. PLUMBING FIXTURES IS COMPLETE. TOILET PARTITIONS ARE COMPLETE. LP TANKS INSTALLED. LOCK HARDWARE STARTED.
  - HS…TPO IS AREA B IS COMPLETE. REWORK OF PLUMBING IN AREA B IS COMPLETE. AUDITORIUM CEILING WORK IS 99%, SCAFFOLDING REMOVED. SHEET ROCK IN AREA C FIRST FLOOR IS COMPLETE. TRUSSES COMPLETED AT OUTBUILDINGS. POLE BASES AND LIGHTS ALONG ROADS AND PARKING LOT ARE COMPLETE. TOPSOIL AT SPORTS FIELDS IS COMPLETE. TRANSFORMER IS INSTALLED AND ENERGIZED.

CONSTRUCTION PROJECT UPDATE

- **NEXT 30 DAYS**
  - CTE – GOAL IS TO ACHIEVE CERTIFICATE OF OCCUPANCY, THEN THE MOVING BEGINS! CARRIED OVER FROM LAST MONTH.
  - HS –CONTINUE OVERHEAD ROUGH IN AREAS E AND F. BEGIN SHEETROCK WORK SECOND FLOOR OF AREA C. CONTINUE SHEETROCK WORK AREA E AND F SECOND FLOOR. DRY FALL CEILING PAINTING IN A2 WILL CONTINUE. AREA A1 CEILING GRID STARTED.
  - SITE –CONTINUE TO PAVE ROADWAYS AND PARKING LOTS.



CTE SUBSTANTIAL COMPLETION DATE – November 25, 2019

NOT MET – Project is currently overdue. HI-CAPS to meet on Tuesday, December 3 to review project schedule and update.

MCHS SUBSTANTIAL COMPLETION DATE – March 25, 2020

Second Semester Start Date for Students – January 23, 2020

Next Meeting Date 12/5/2019




The Following CTE Photographs were all taken on the morning of November 25, 2019.




11-25 Main Corridor

KEY PLAN



11-25 Culinary Arts


KEY PLAN

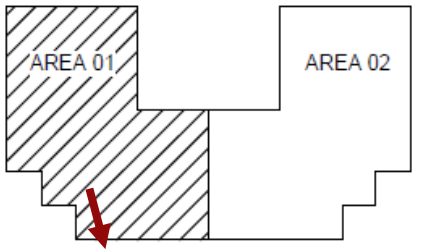




11-25 AG-Science



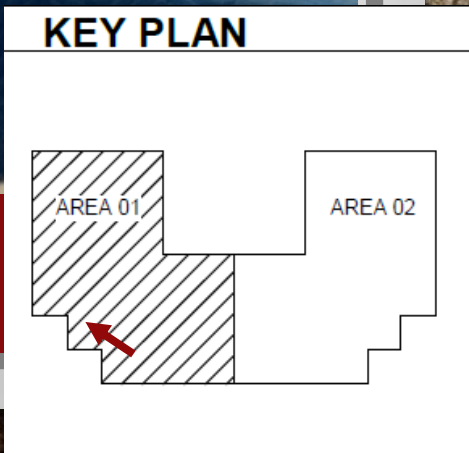




11-25 Construction Trades (this floor is to be polished)

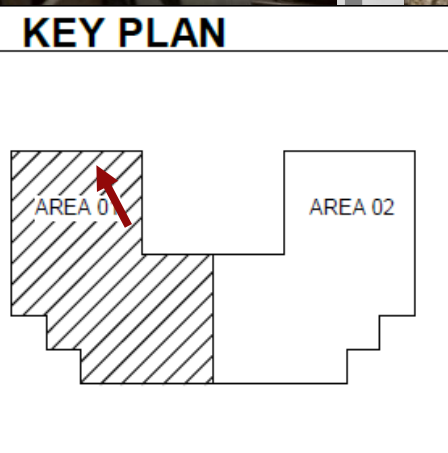



11-25 Construction Trades Classroom


KEY PLAN





11-25 HVAC


KEY PLAN







11-25 Main Entrance

KEY PLAN




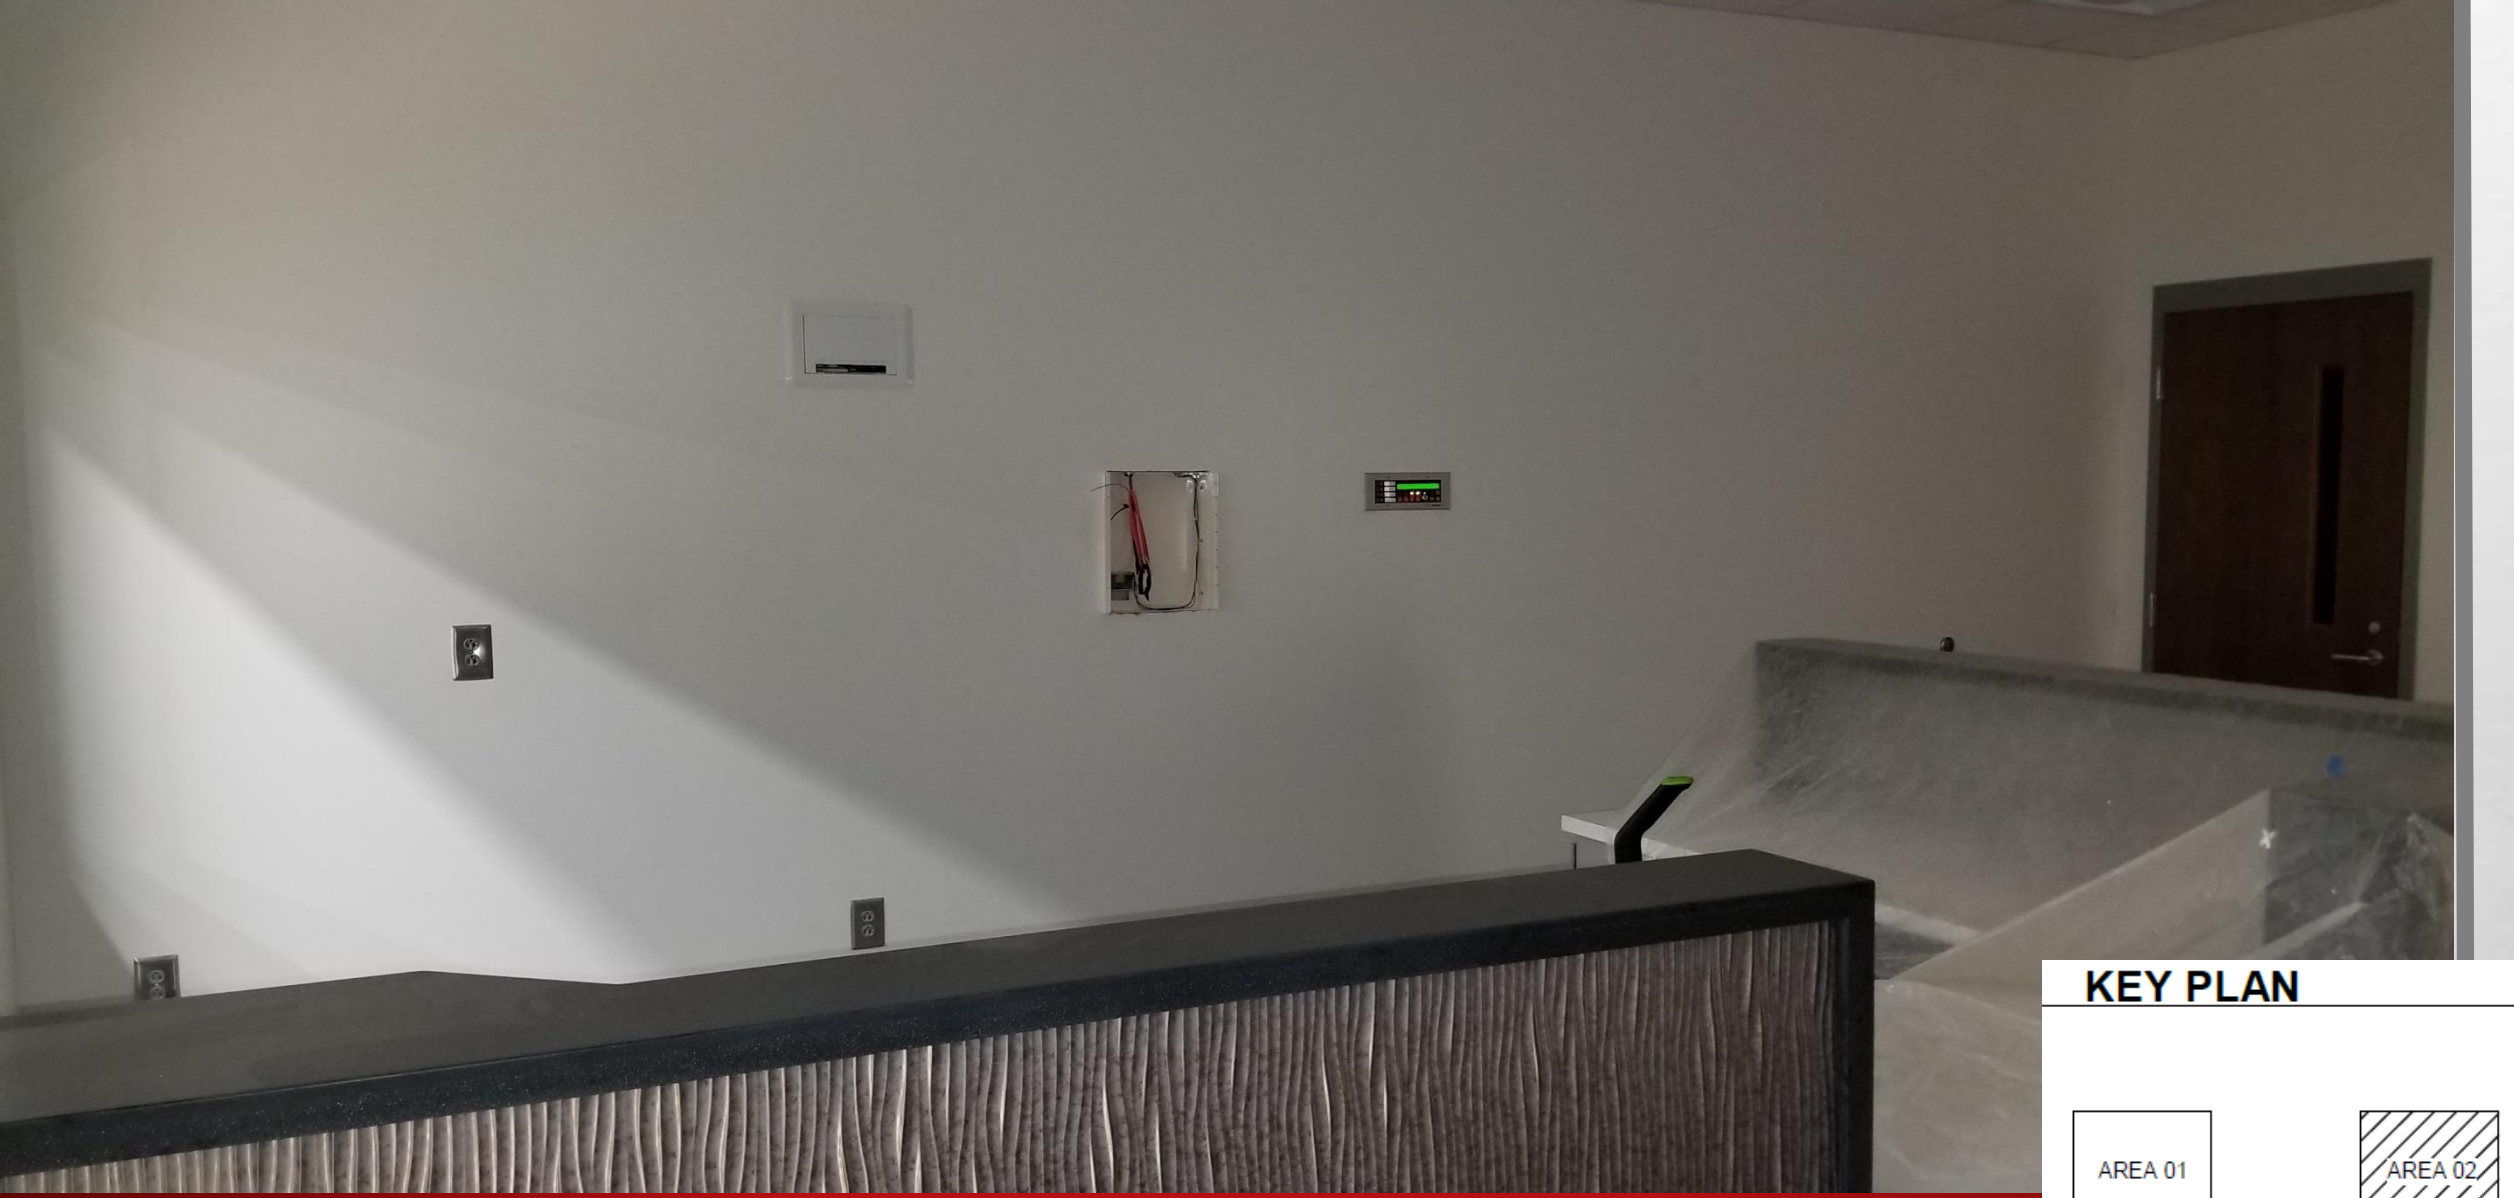

11-25 Front Reception

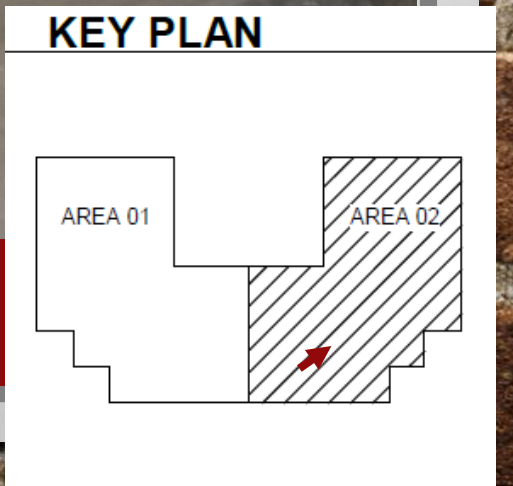


11-25 MCC Robotics

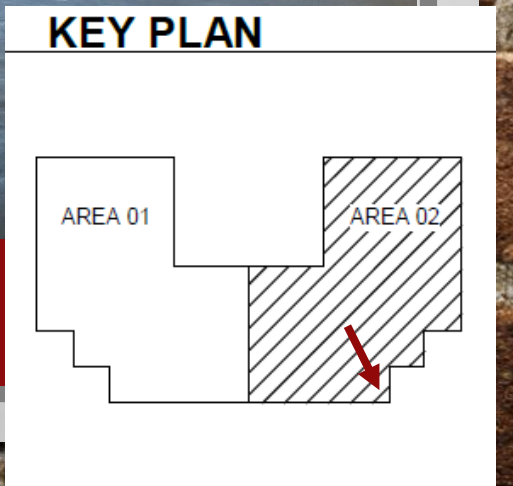



11-25 Second Floor Main Corridor


KEY PLAN

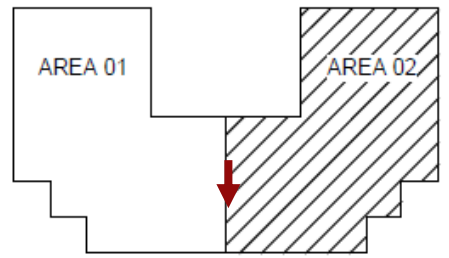

11-25 Health Classroom



KEY PLAN

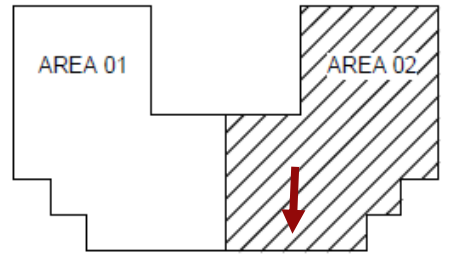



Sample Polishing of Main Floor




MC

TIMBERWOLVES




Area C Media/Office

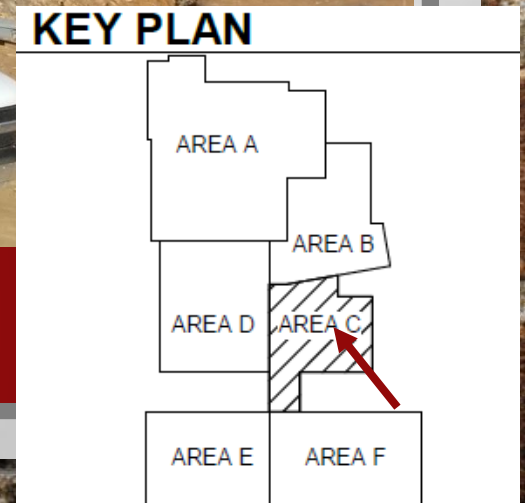




Main Driveway

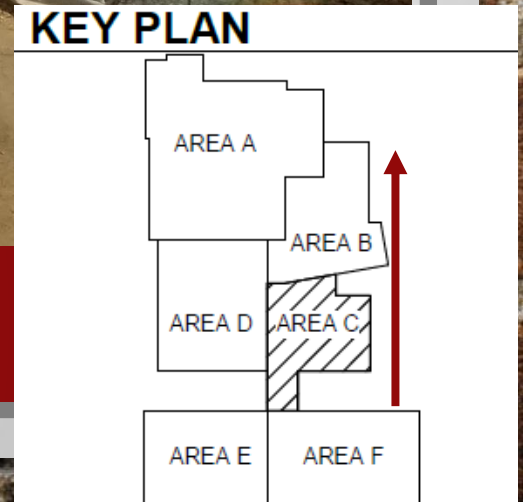


Visitor and Student Parking Lots

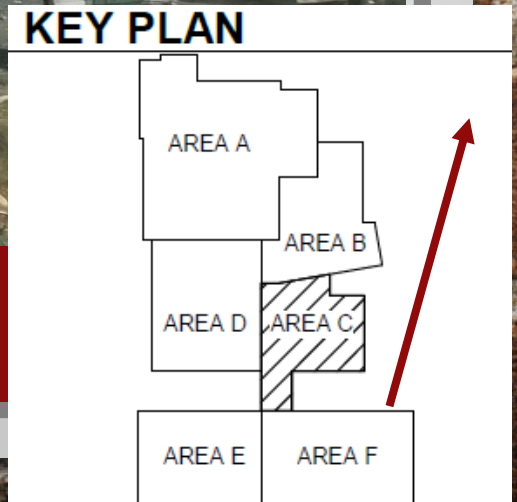




Dry Fall Paint in Main Gym

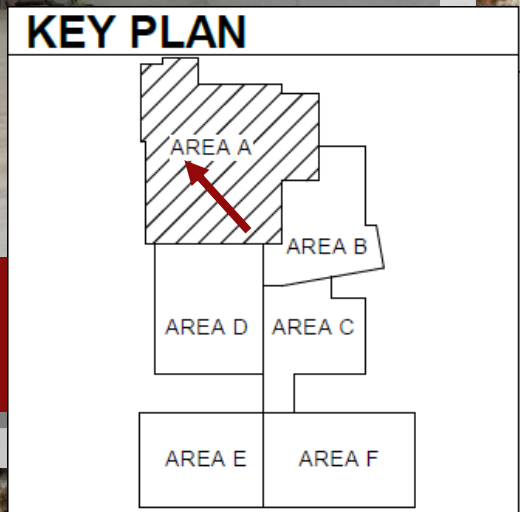




Mr. Brown Inspecting Team Lockers

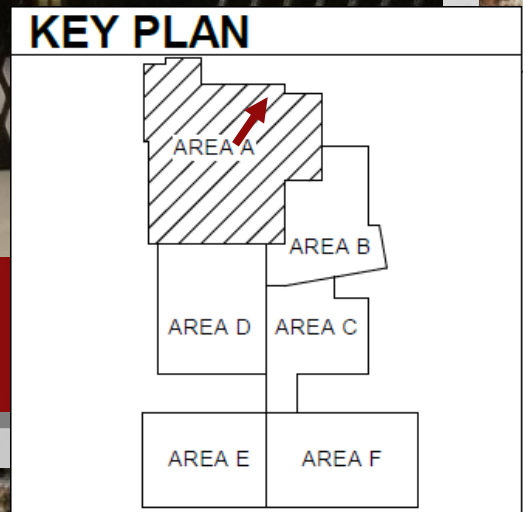


Locker Room Showers

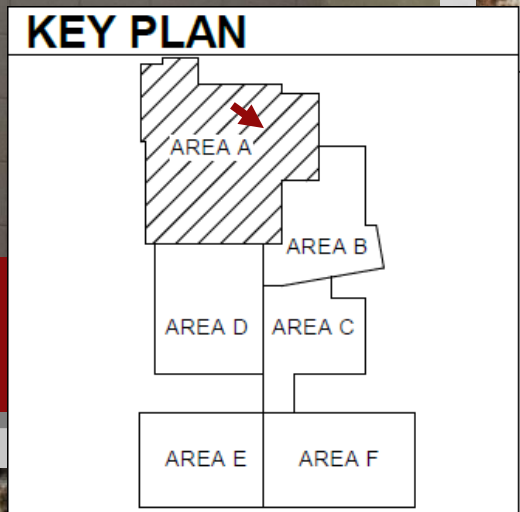





Ceiling Grid Work in Area A1

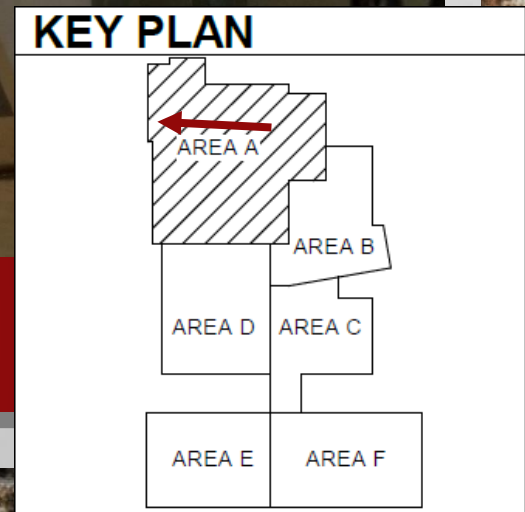

Area B Dining/Kitchen/Main Receiving

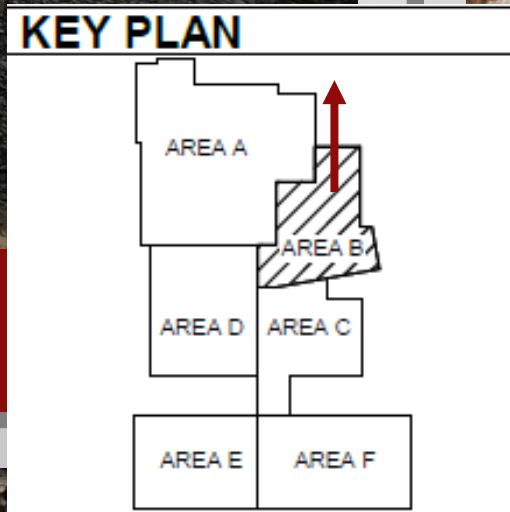


Area B Kitchen

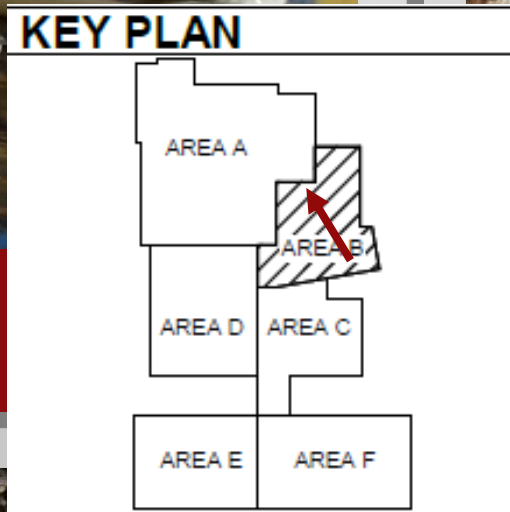




Area B Dining

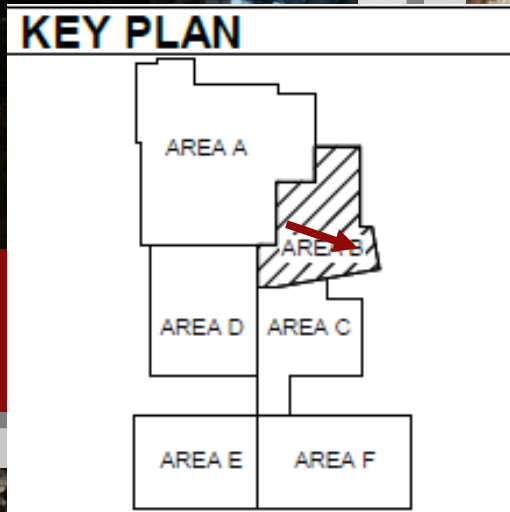





Main Entrance

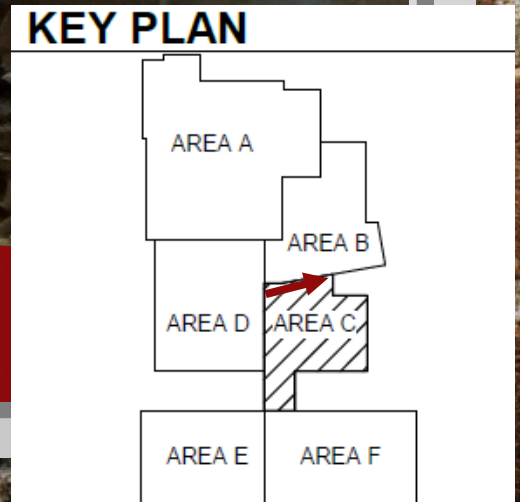


SRO Office Window – Display Case Location

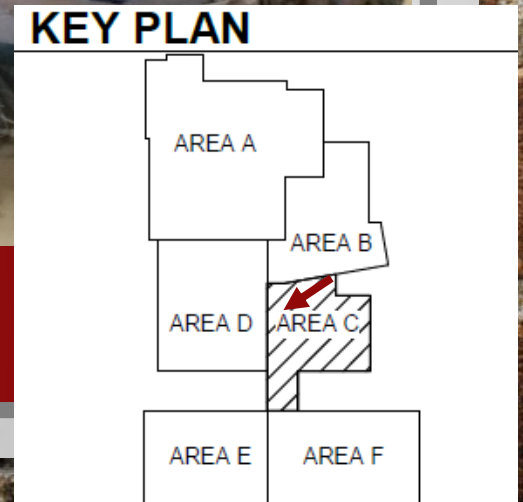


Main Corridor

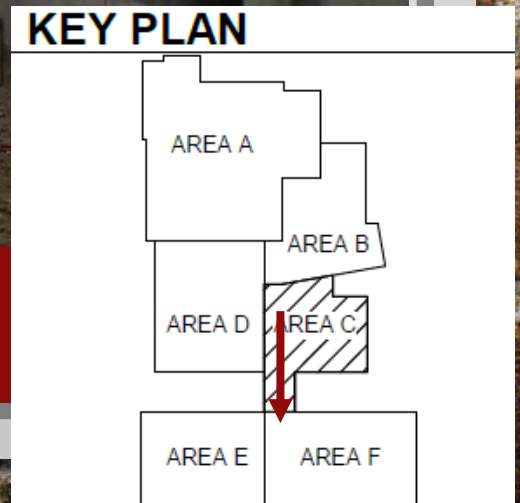


Area C Second Floor Framing

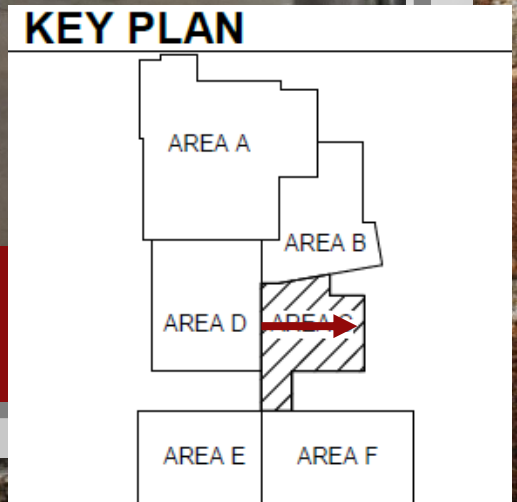

Removal of Auditorium Scaffold System

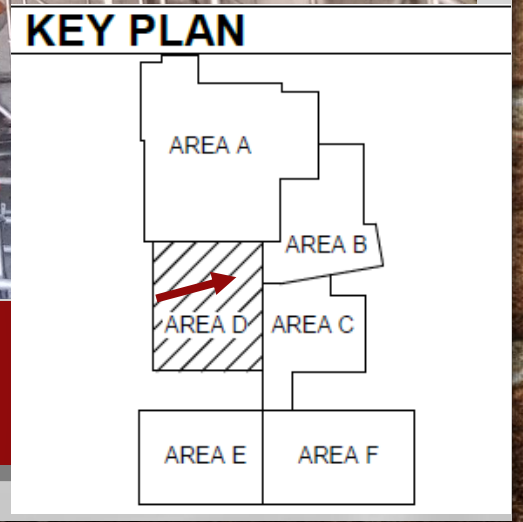

Auditorium Ceiling Clouds

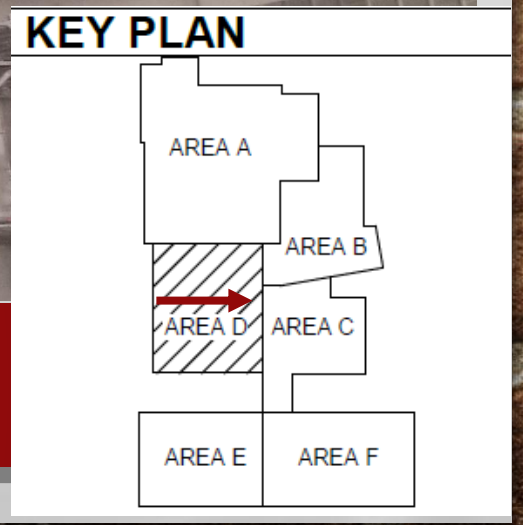





Auditorium Ceiling Clouds

KEY PLAN


Area E West Exterior Wall

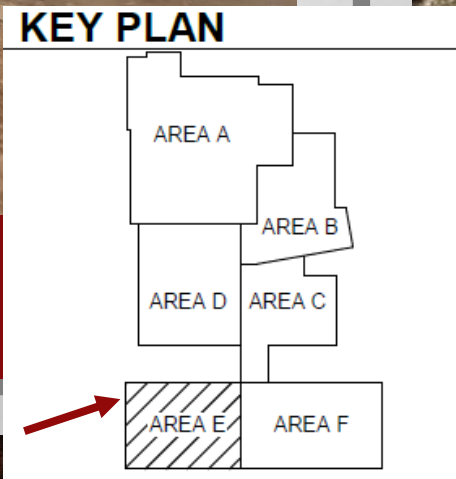


Area E First Floor

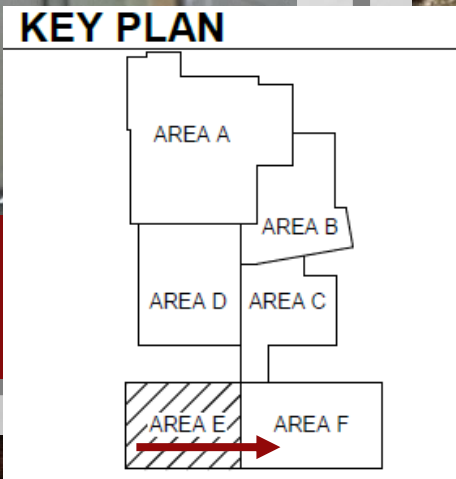


Area F Second Floor Shared Space

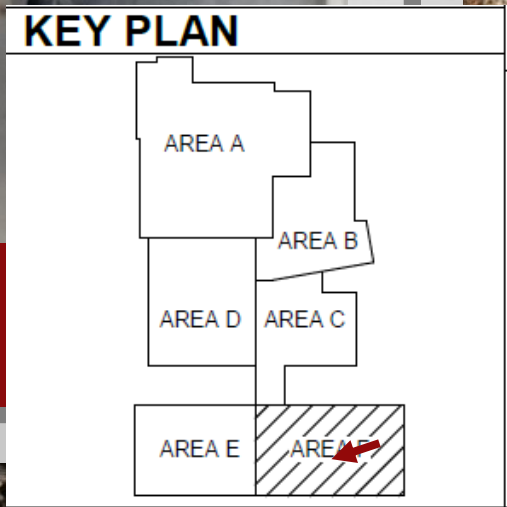


Area F Second Floor Classroom

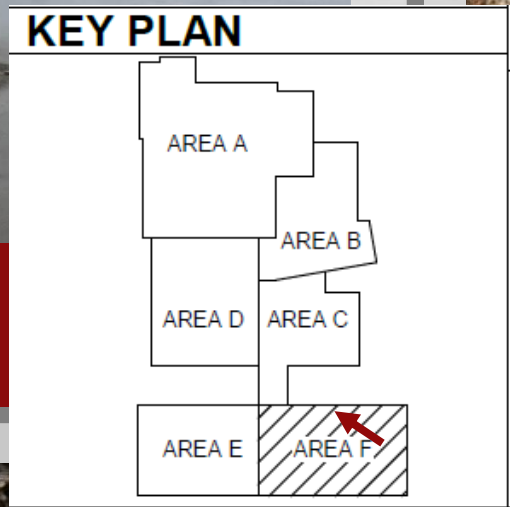


Home Side Athletic Facilities

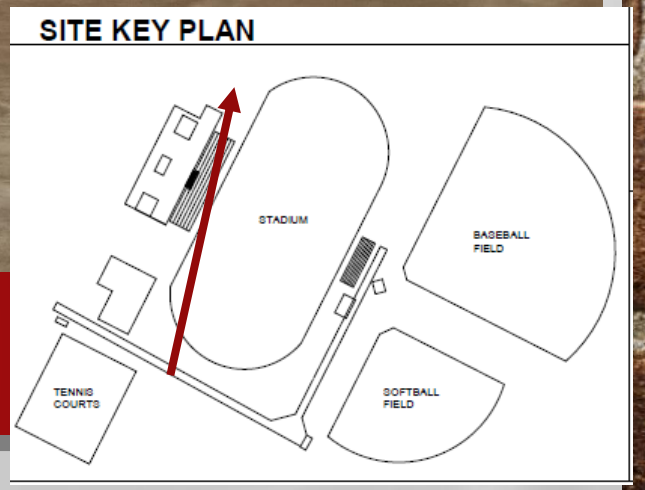

Visitors Side Athletic Facilities

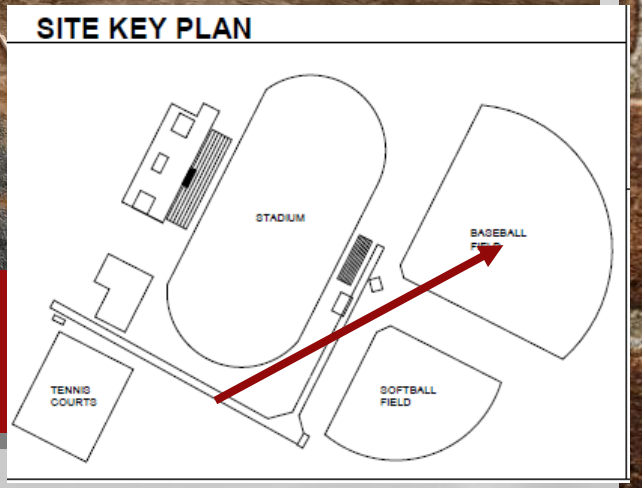


Tennis Courts – Area A1 of MCHS

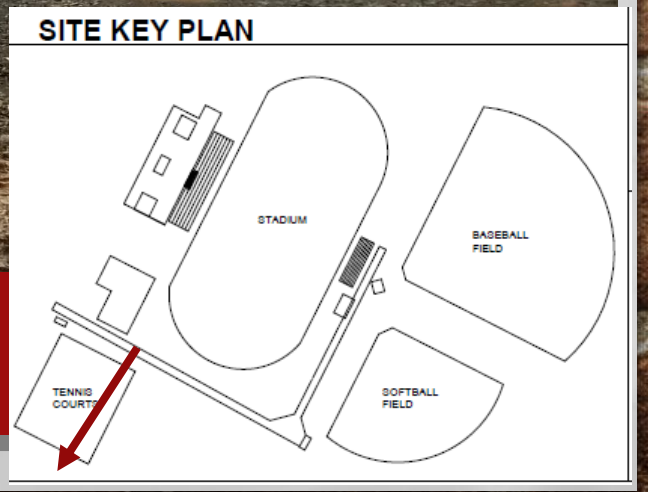




END SLIDE – QUESTIONS???


KEY PLAN

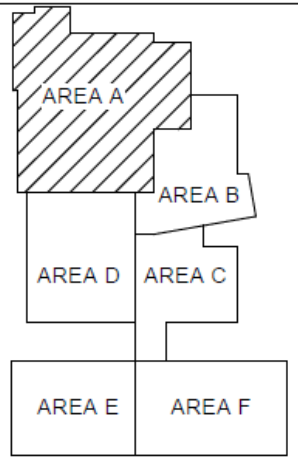


KEY PLAN

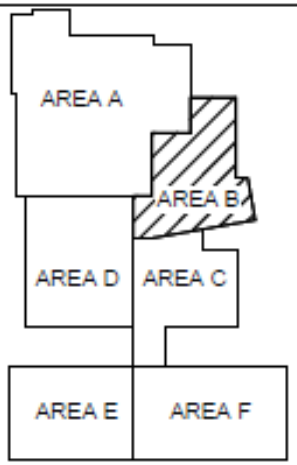


KEY PLAN

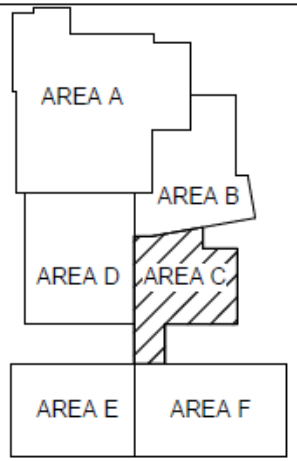


KEY PLAN

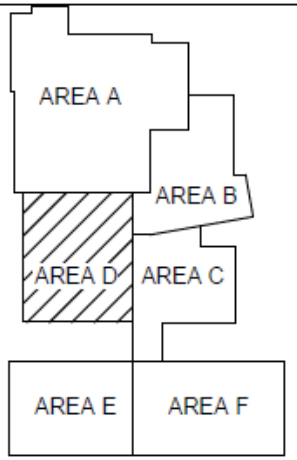

KEY PLAN

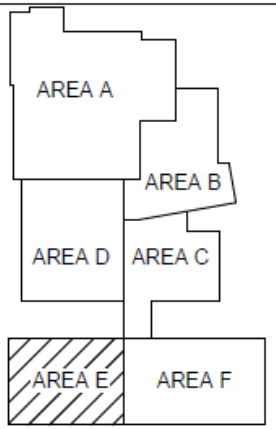


KEY PLAN

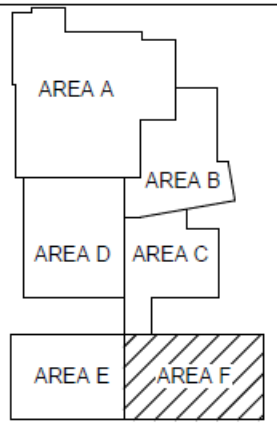


KEY PLAN



KEY PLAN



SITE KEY PLAN

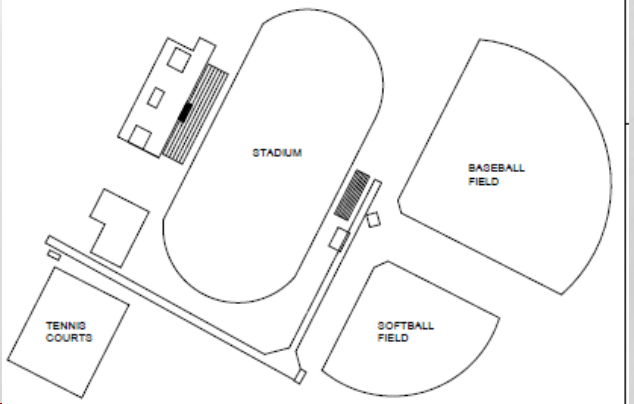

KEY BLOCK – DO NOT DELETE
