

Construction update – 10/5/2020

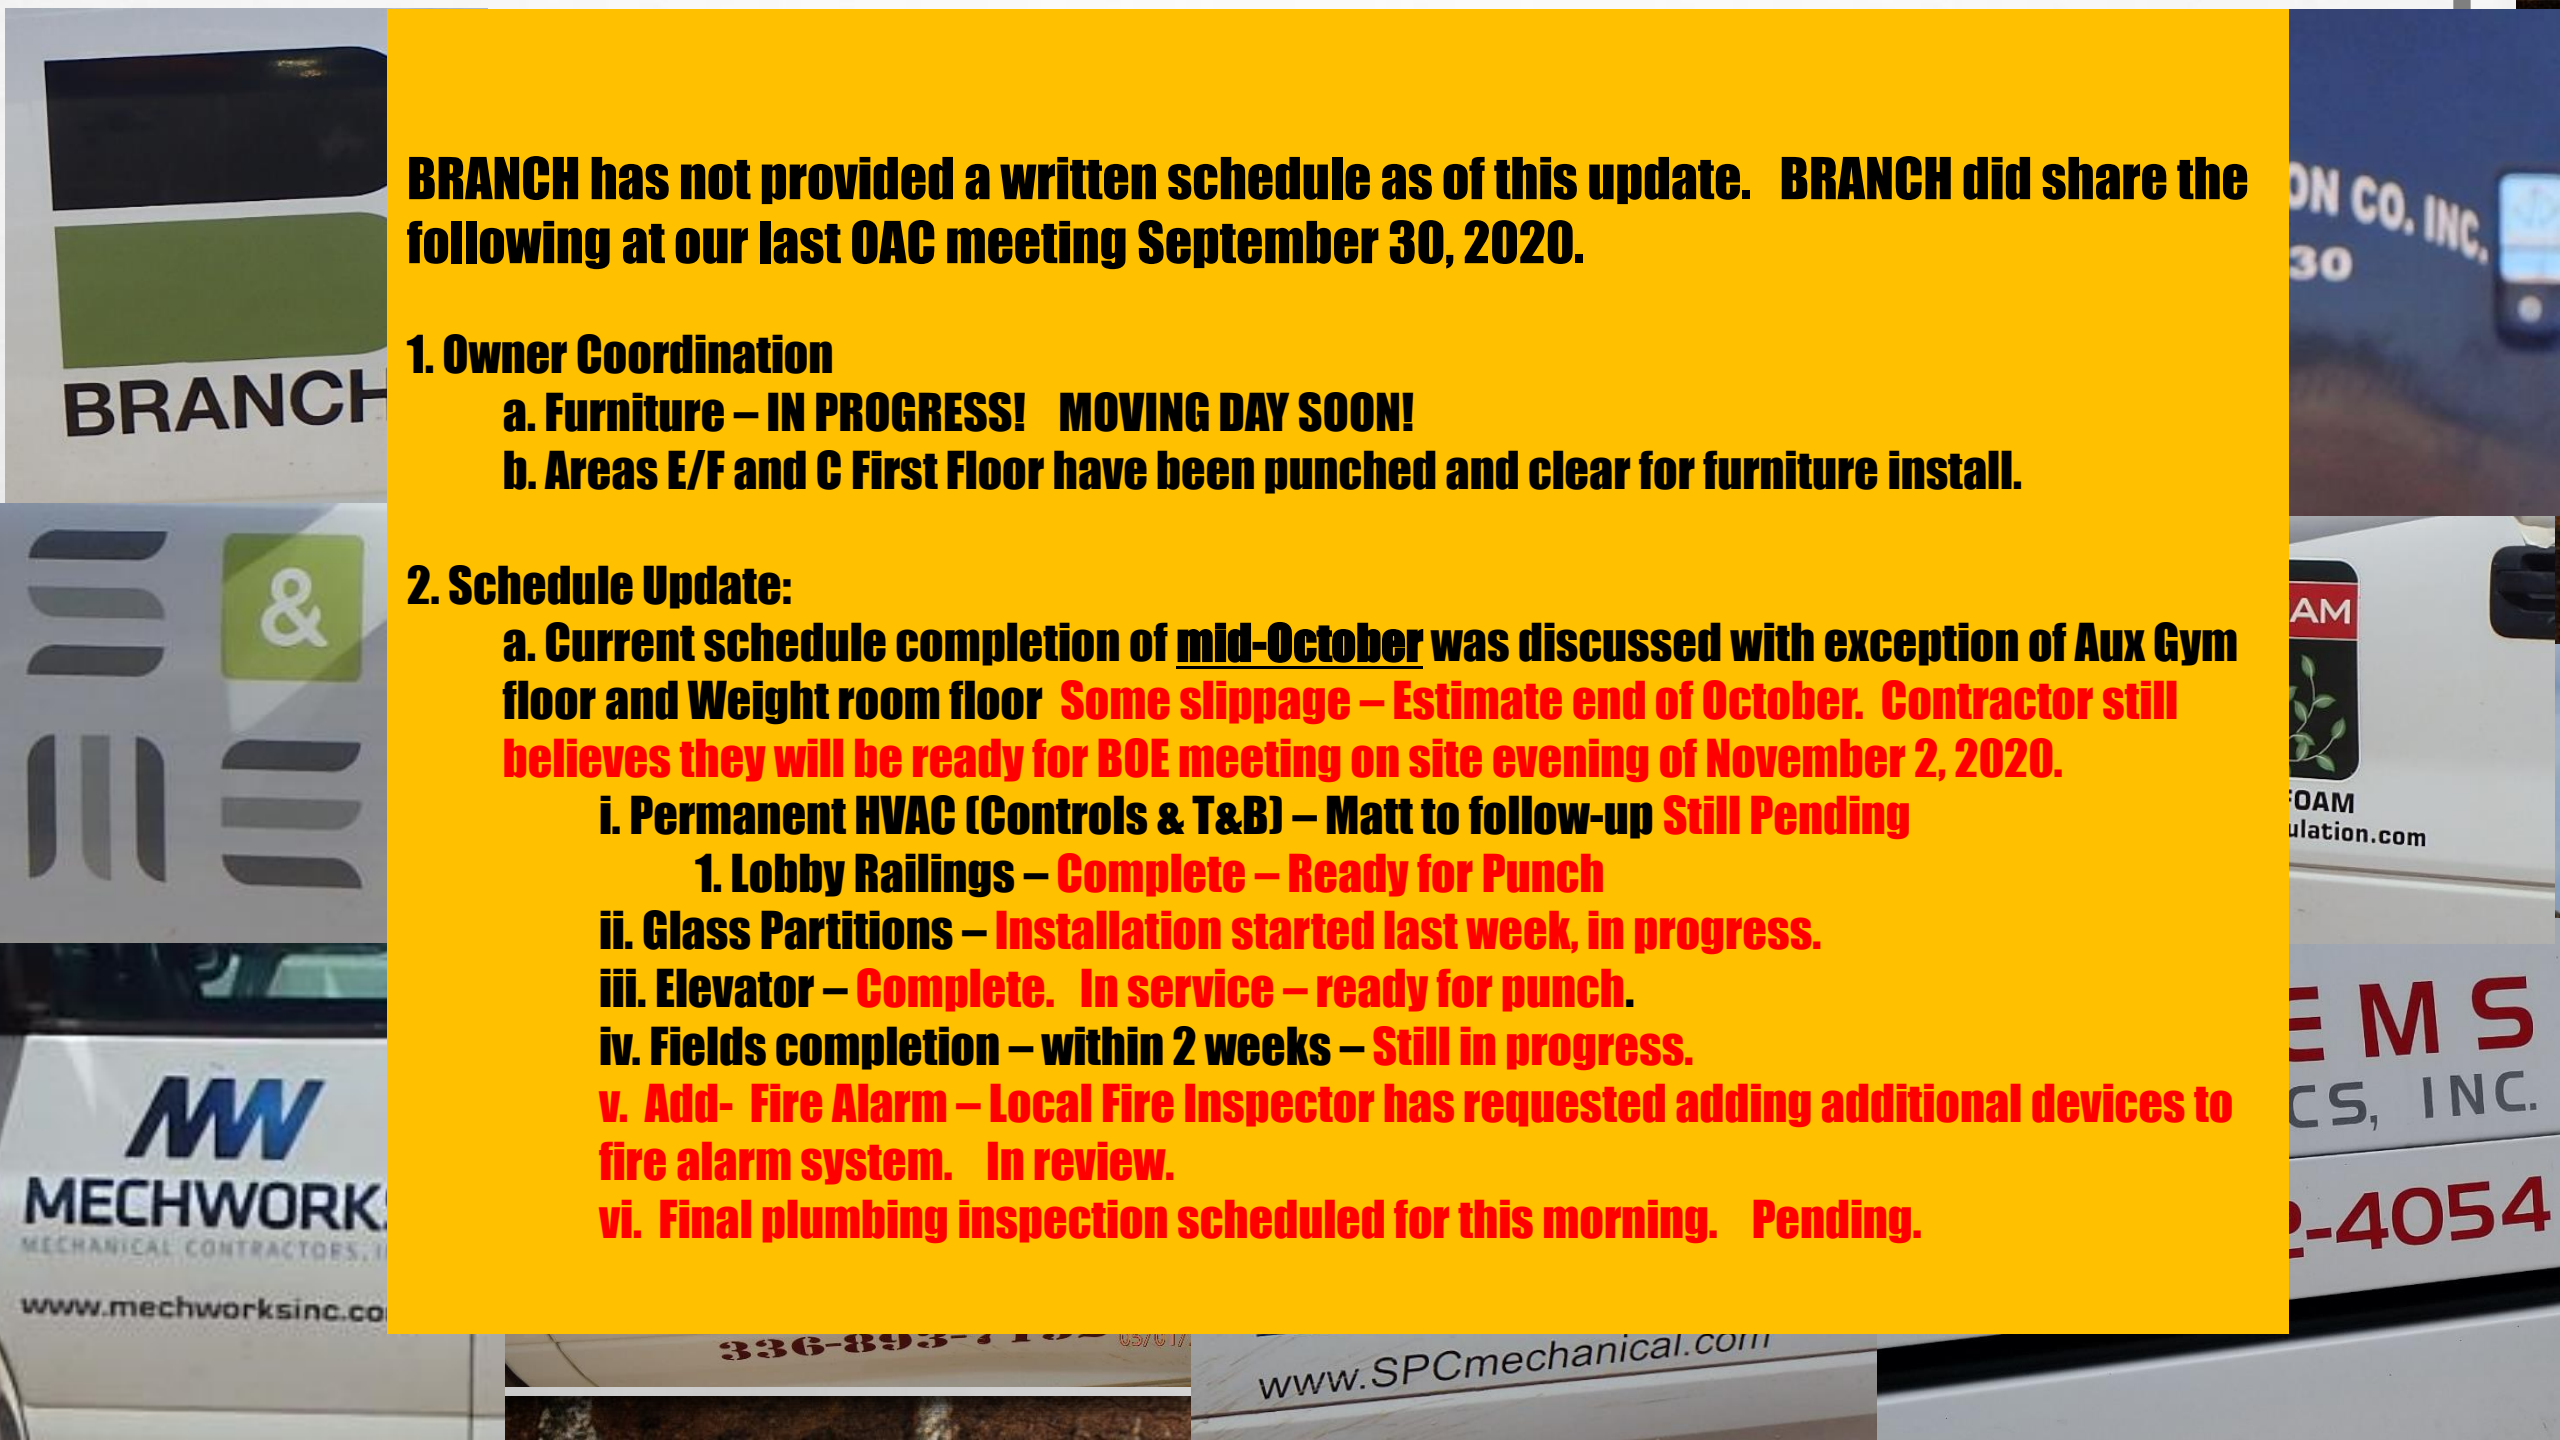

BRANCH has not provided a written schedule as of this update. BRANCH did share the following at our last OAC meeting September 30, 2020.

1. Owner Coordination

- **a. Furniture – IN PROGRESS! MOVING DAY SOON!**
- **b. Areas E/F and C First Floor have been punched and clear for furniture install.**

2. Schedule Update:

- **a. Current schedule completion of mid-October was discussed with exception of Aux Gym floor and Weight room floor Some slippage – Estimate end of October. Contractor still believes they will be ready for BOE meeting on site evening of November 2, 2020.**
  - **i. Permanent HVAC (Controls & T&B) – Matt to follow-up Still Pending**
    - **1. Lobby Railings – Complete – Ready for Punch**
  - **ii. Glass Partitions – Installation started last week, in progress.**
  - **iii. Elevator – Complete. In service – ready for punch.**
  - **iv. Fields completion – within 2 weeks – Still in progress.**
  - **v. Add- Fire Alarm – Local Fire Inspector has requested adding additional devices to fire alarm system. In review.**
  - **vi. Final plumbing inspection scheduled for this morning. Pending.**




Main Lobby – Glass wall bottom rail in progress




Main Lobby Stairs – Touchup paint in progress

Main Corridor – Handrail completed

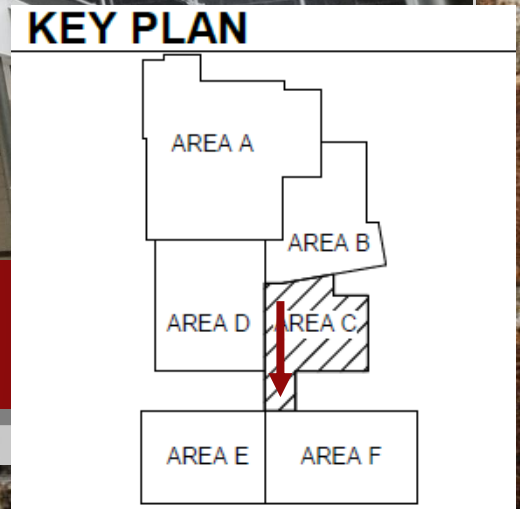



Area C 2nd Floor – Casework in progress

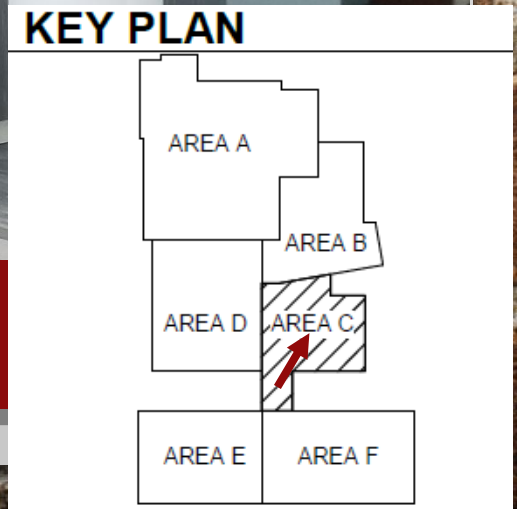




Area C 2nd Floor – bookcases in progress

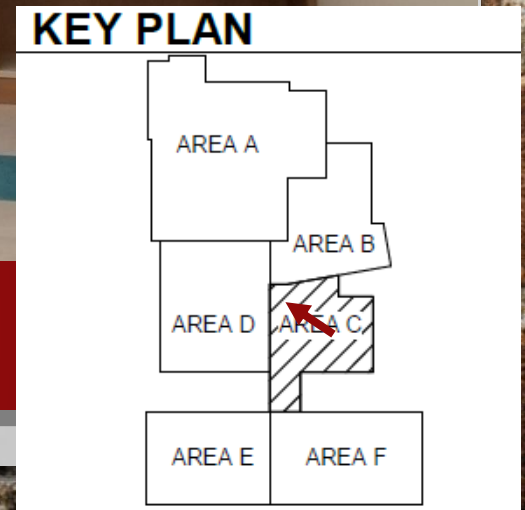

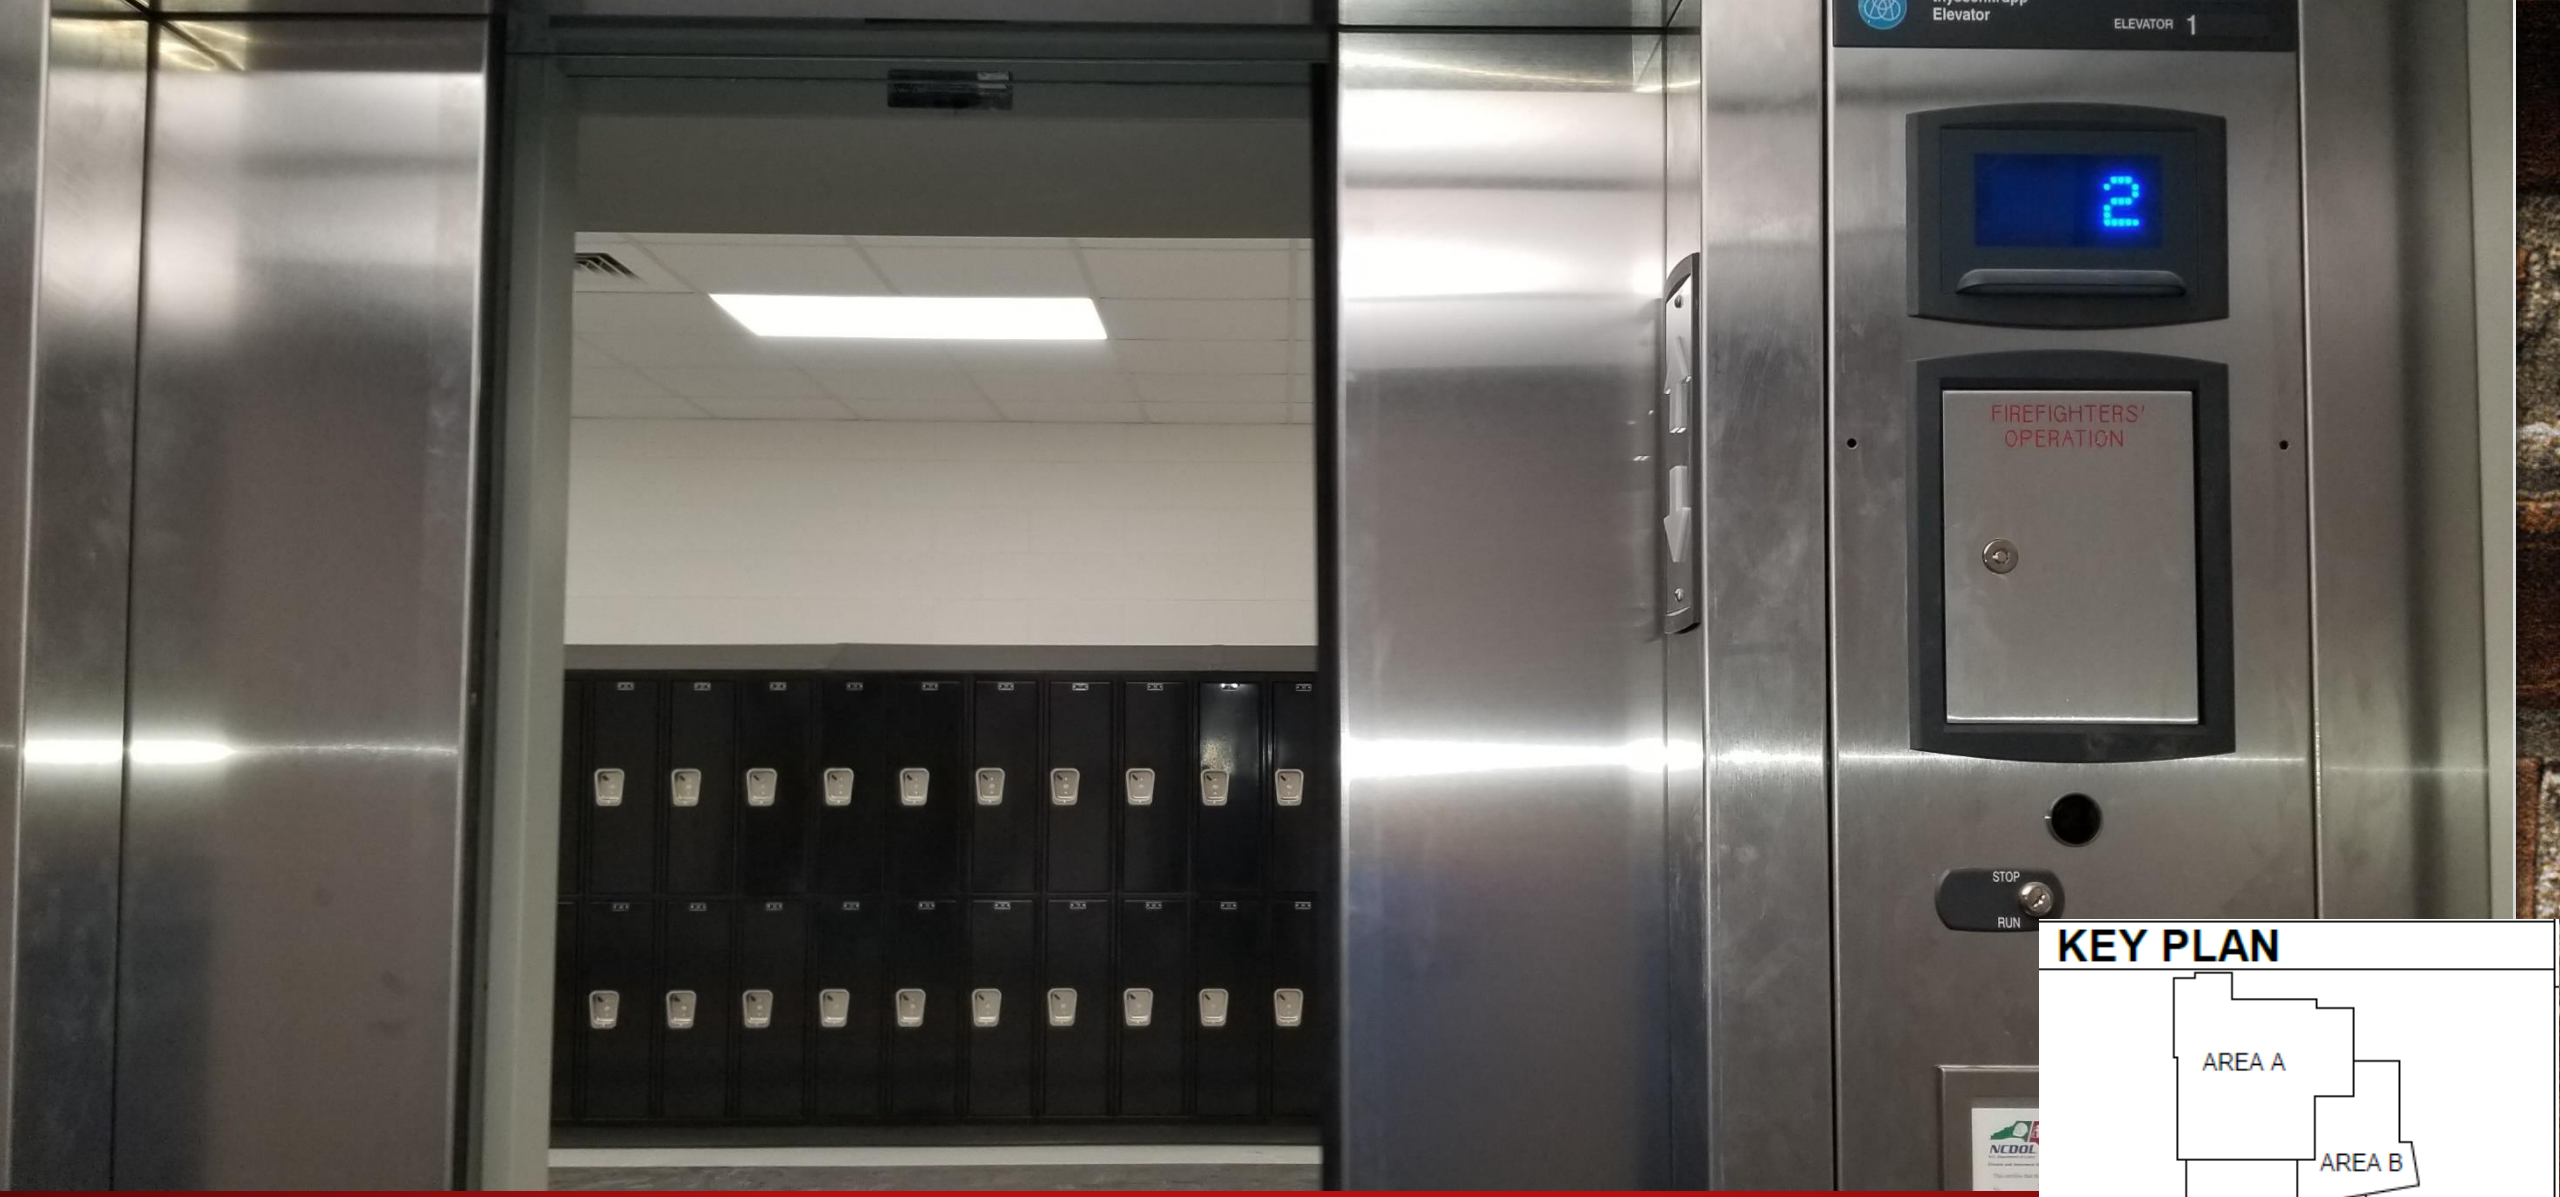


Area F 2nd Floor – Elevator Works! Going back downstairs.

Area B – Dining – Dish room window – serving line doors

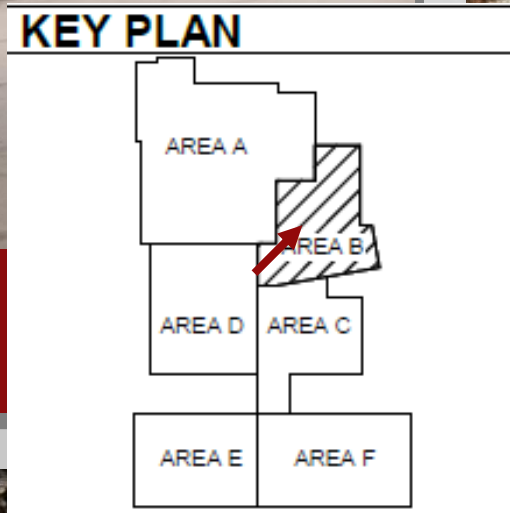





Area B – Serving – Not one, not two, but three serving lines!

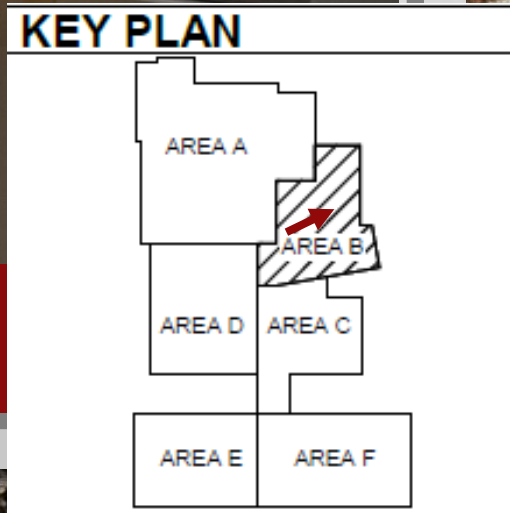

Area B – Dining – Auxiliary Gym Floor in staging.

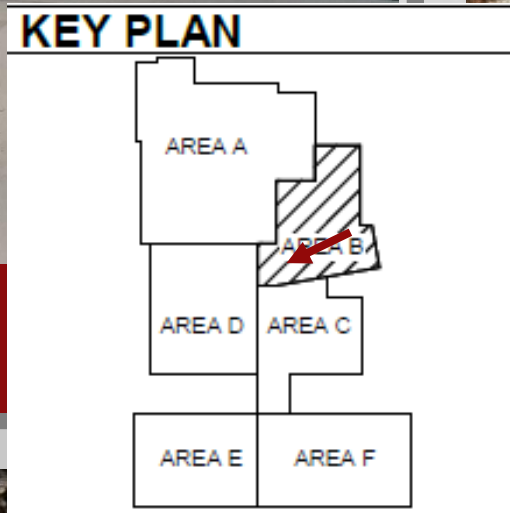

Main Gym – just punch list work in main gym this past month.

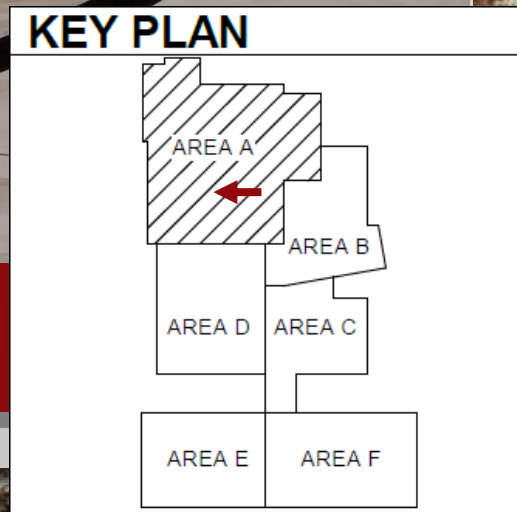



Weight Room – Rubber Floor is in progress






Area D – Auditorium- Stage and ramp trim has been stained.



Area D – Dance – Ballet bars mounted, awaiting glassless mirrors.


Learning Environments has begun installing classroom furniture as Architect develops punch list!



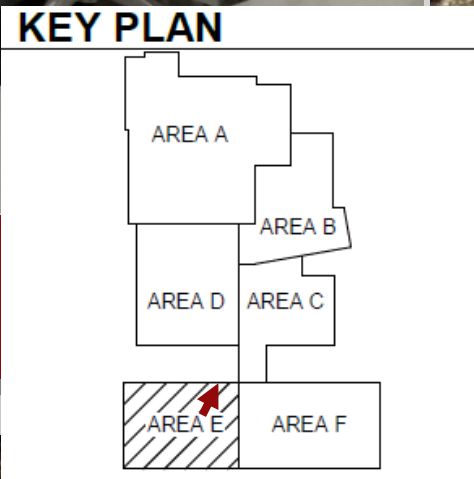




Art Room cabinet work in progress.

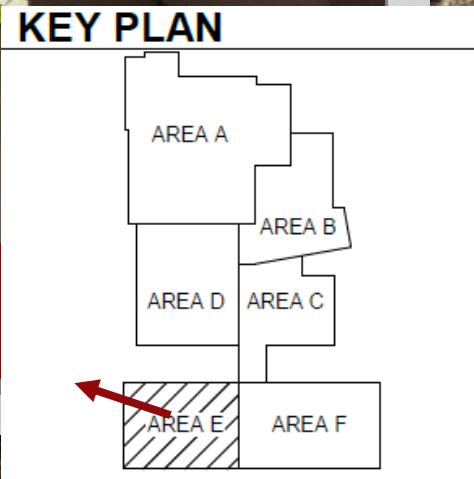



Area F 2nd Floor – State of the Art science prep rooms!!

Area F 2nd Floor – Future view for one of our math teachers.

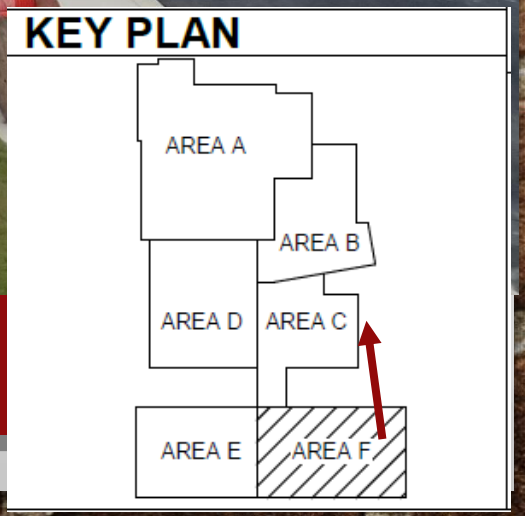



Area F 2nd Floor – Visitor and student parking.




Area F 2nd Floor – This room has two big windows! Main Drive Exit.




Page Street Entrance, Staff Parking, and Bus Lot


Visitor Ramp System is being re-poured to proper slope.

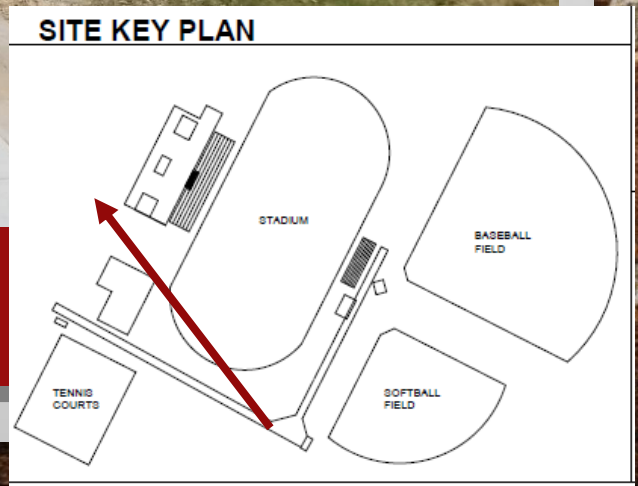


First coat of rubber has been applied to track. Note handrail on Home Ramp far side of Bleachers.

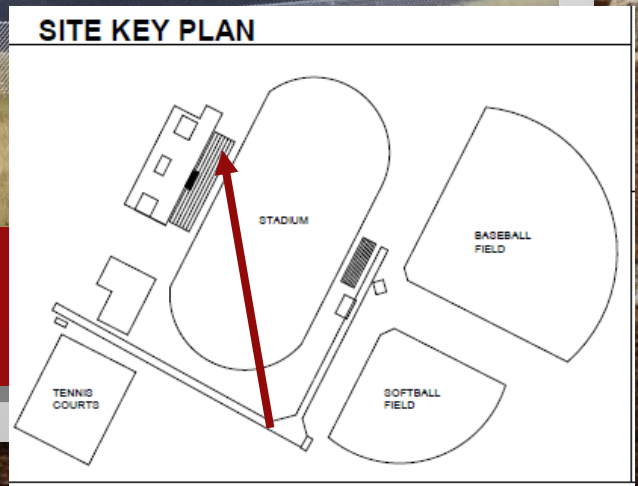


Visitor steps being formed, sidewalk repairs in progress.

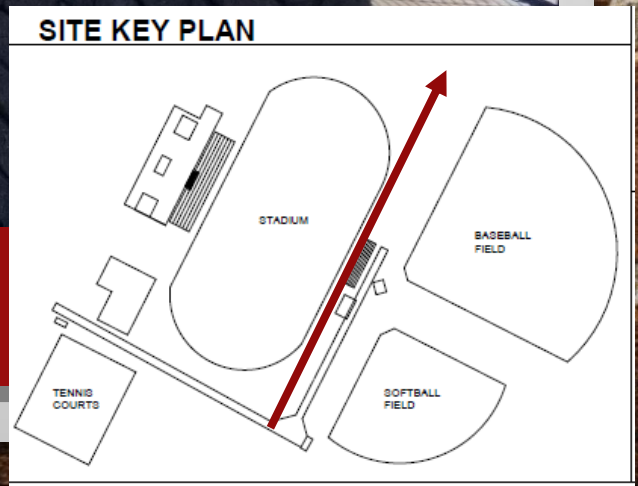

Boys Baseball and Girls Softball Fields.

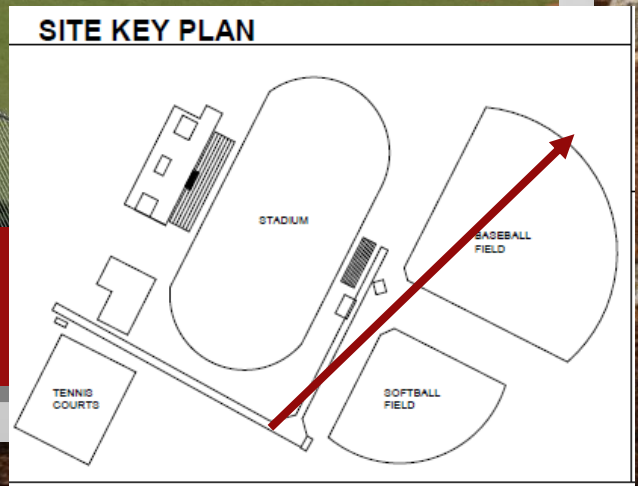


Girls Softball Outfield.

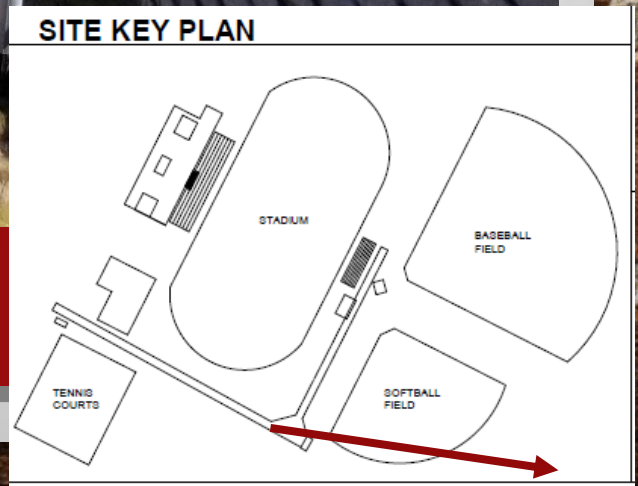


??QUESTIONS??


CRYSTAL WILL KNOW THE ANSWER!

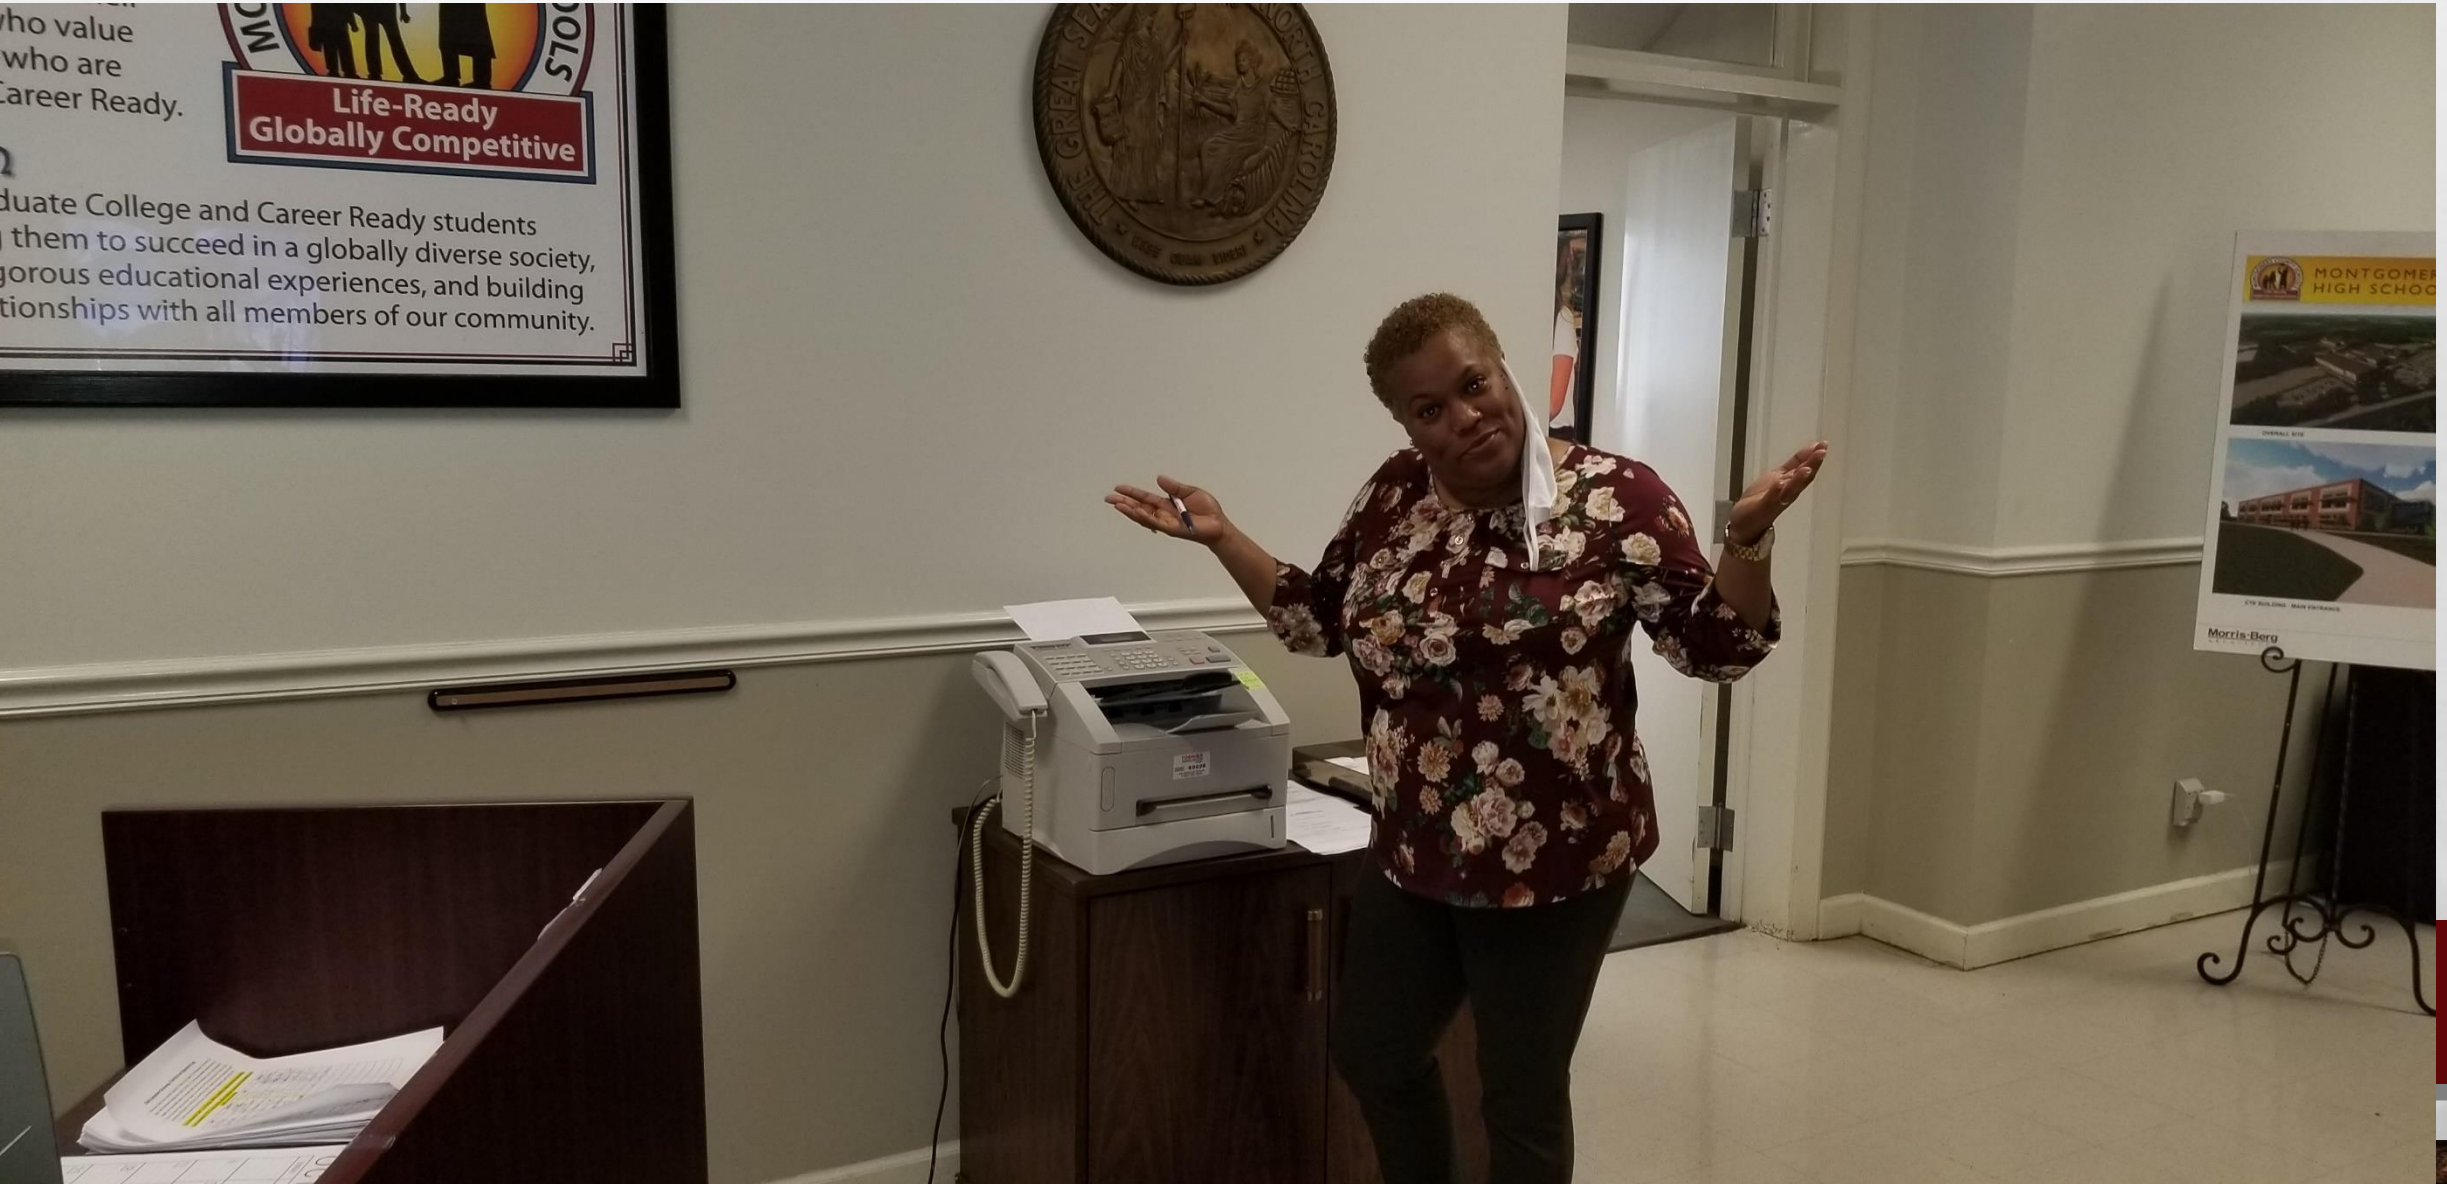


KEY PLAN

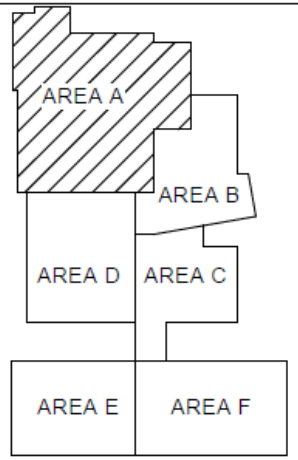


KEY PLAN

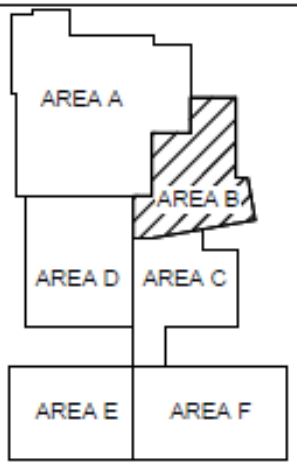


KEY PLAN

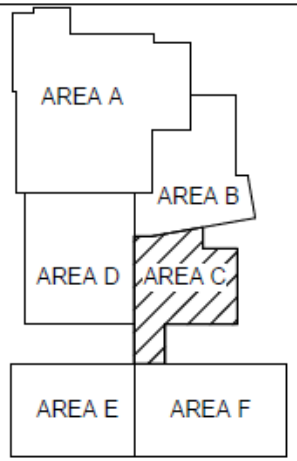


KEY PLAN

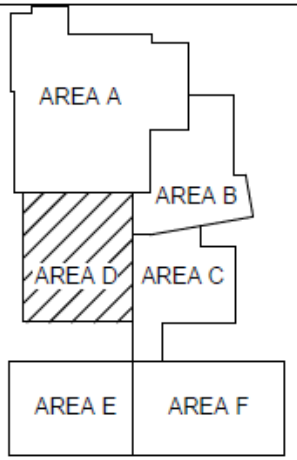

KEY PLAN

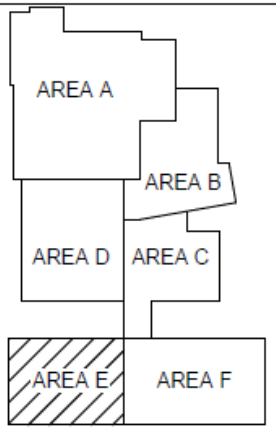


KEY PLAN

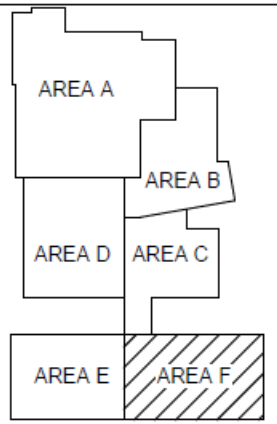


KEY PLAN



KEY PLAN



SITE KEY PLAN

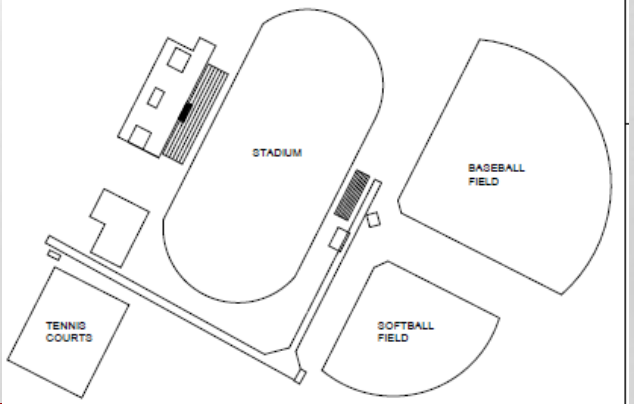

KEY BLOCK – DO NOT DELETE
