MCHS

CONSTRUCTION PROJECT UPDATE – MAY 4, 2020




CTE – Punch list items ongoing


MCHS SUBSTANTIAL COMPLETION DATES:	February 18	March 24 REVIEW		April 21 Review	
CTE/HS Site work	*	May 15		June 22	-38
Athletic Structures HS	*	May 11		June 9	-29
Landscape HS	*	June 10		July 7	-27
Area A1 – Locker Rooms/athletic support:	April, 20	May 18	-28	June 10	-23
Area A2 – Main/Auxiliary Gymnasiums:	June 16	June 16	-0	June 30	-14
Area B – Kitchen/Dining:	July 23	July 29	-6	July 28	+1
Area C – Office/Media:	July 2	June 25	+7	July 15	-20
Area D – Auditorium/Performing Arts/Band:	June 25	June 18	+7	July 20	-34
Area E/F – Instructional Wing:	July 13	June 25	+18	July 1	-5
PROJECT:	July 24	July 30	-6	August 6	-7

Dates last reviewed by HICAPS April 21, 2020


Next Meeting Date: May 7, 2020 @ via Conference Call

Area A1 – JROTC

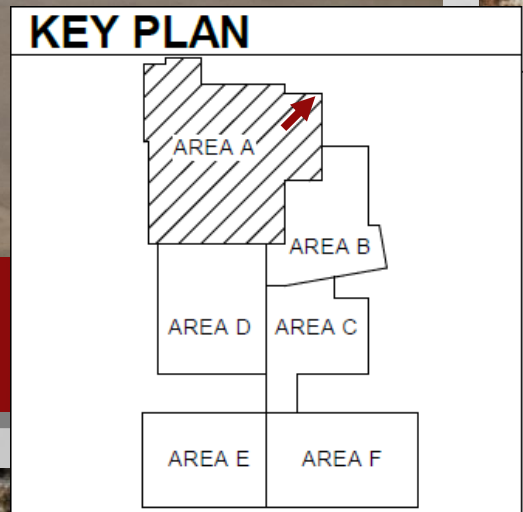

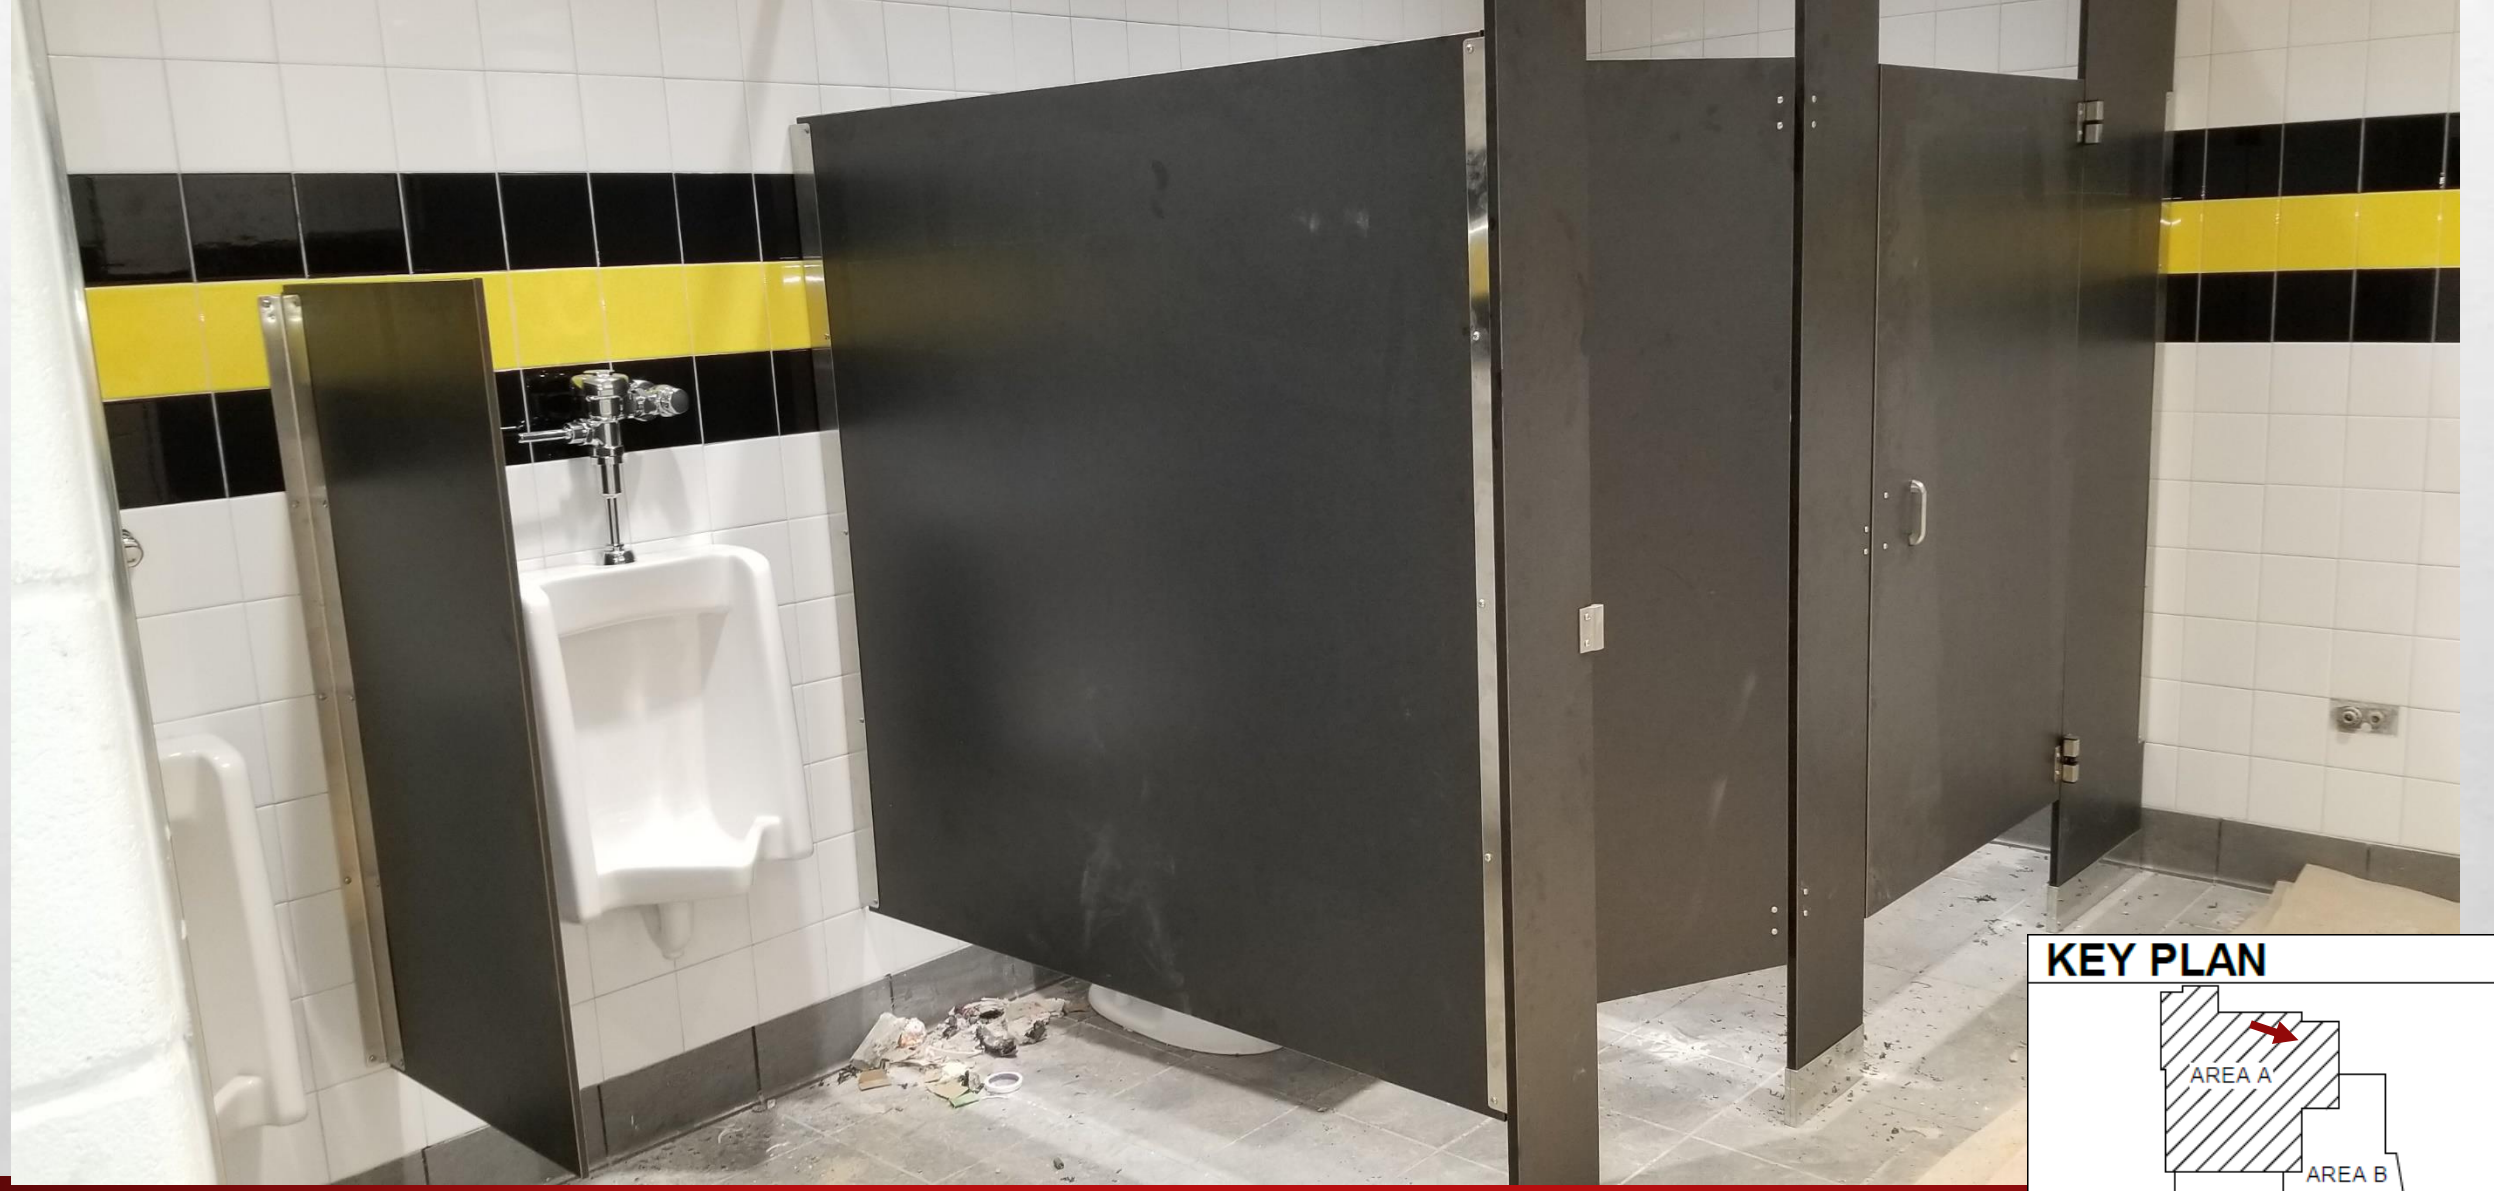


A1-Boys PE Locker Room – Restroom Fixtures Installed

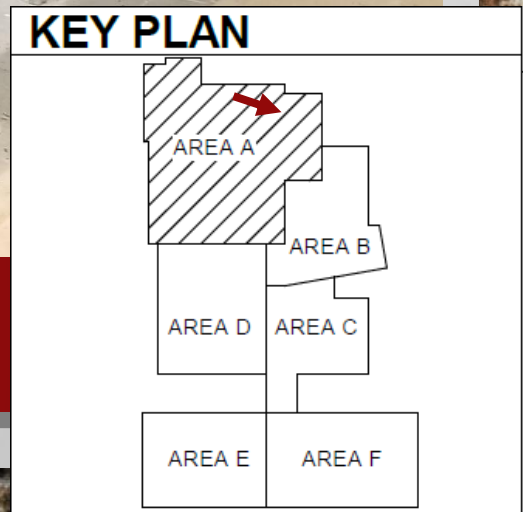




A2 - Main Gymnasium – Limited Progress due to High Moisture Readings in Slab

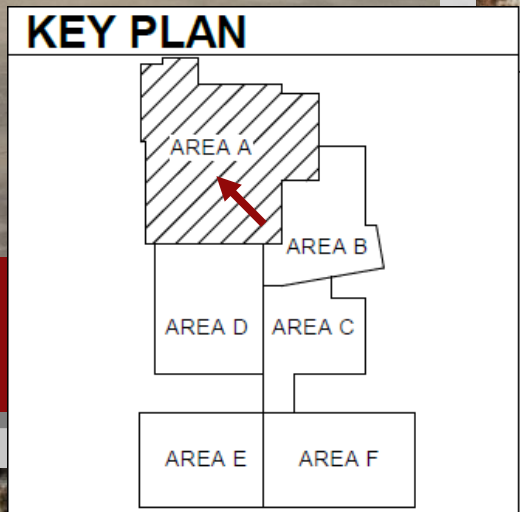


A2 – Auxiliary Gymnasium – Owner FFE in Storage

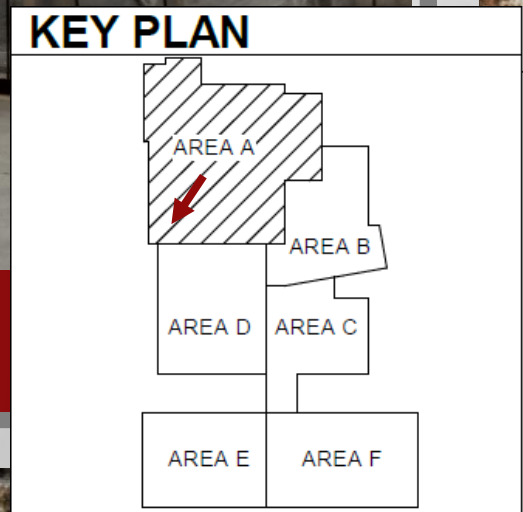




Area B – Dining Room – Slab Scheduled to Pour Today

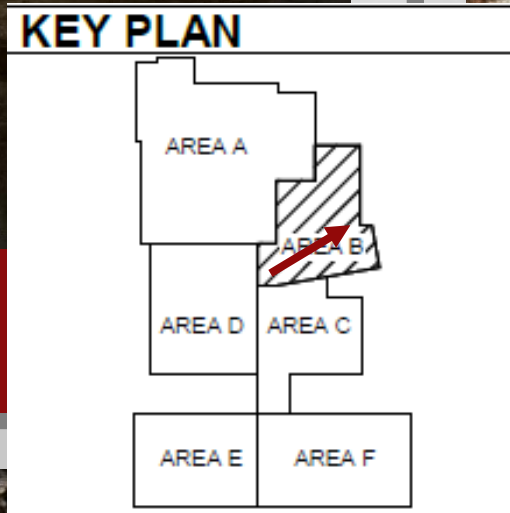




Area B – Kitchen Area – Cooler/Freezer in Background

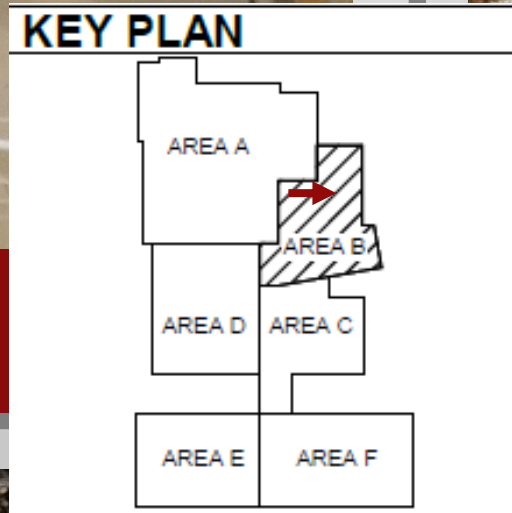





Area B – Serving Line

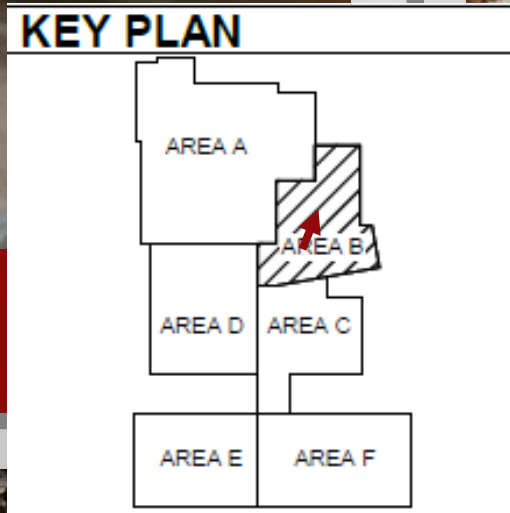





Area B – View down Main Corridor Last Month

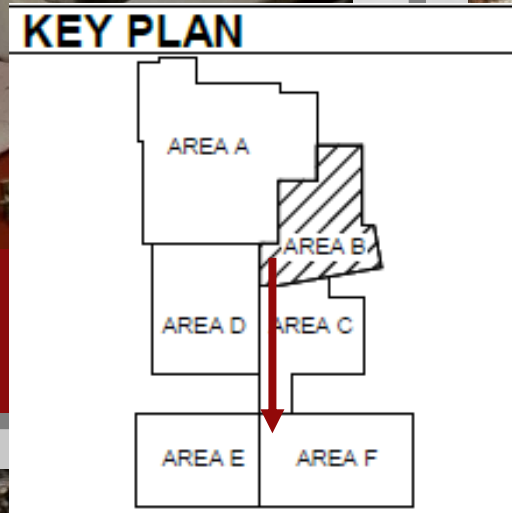

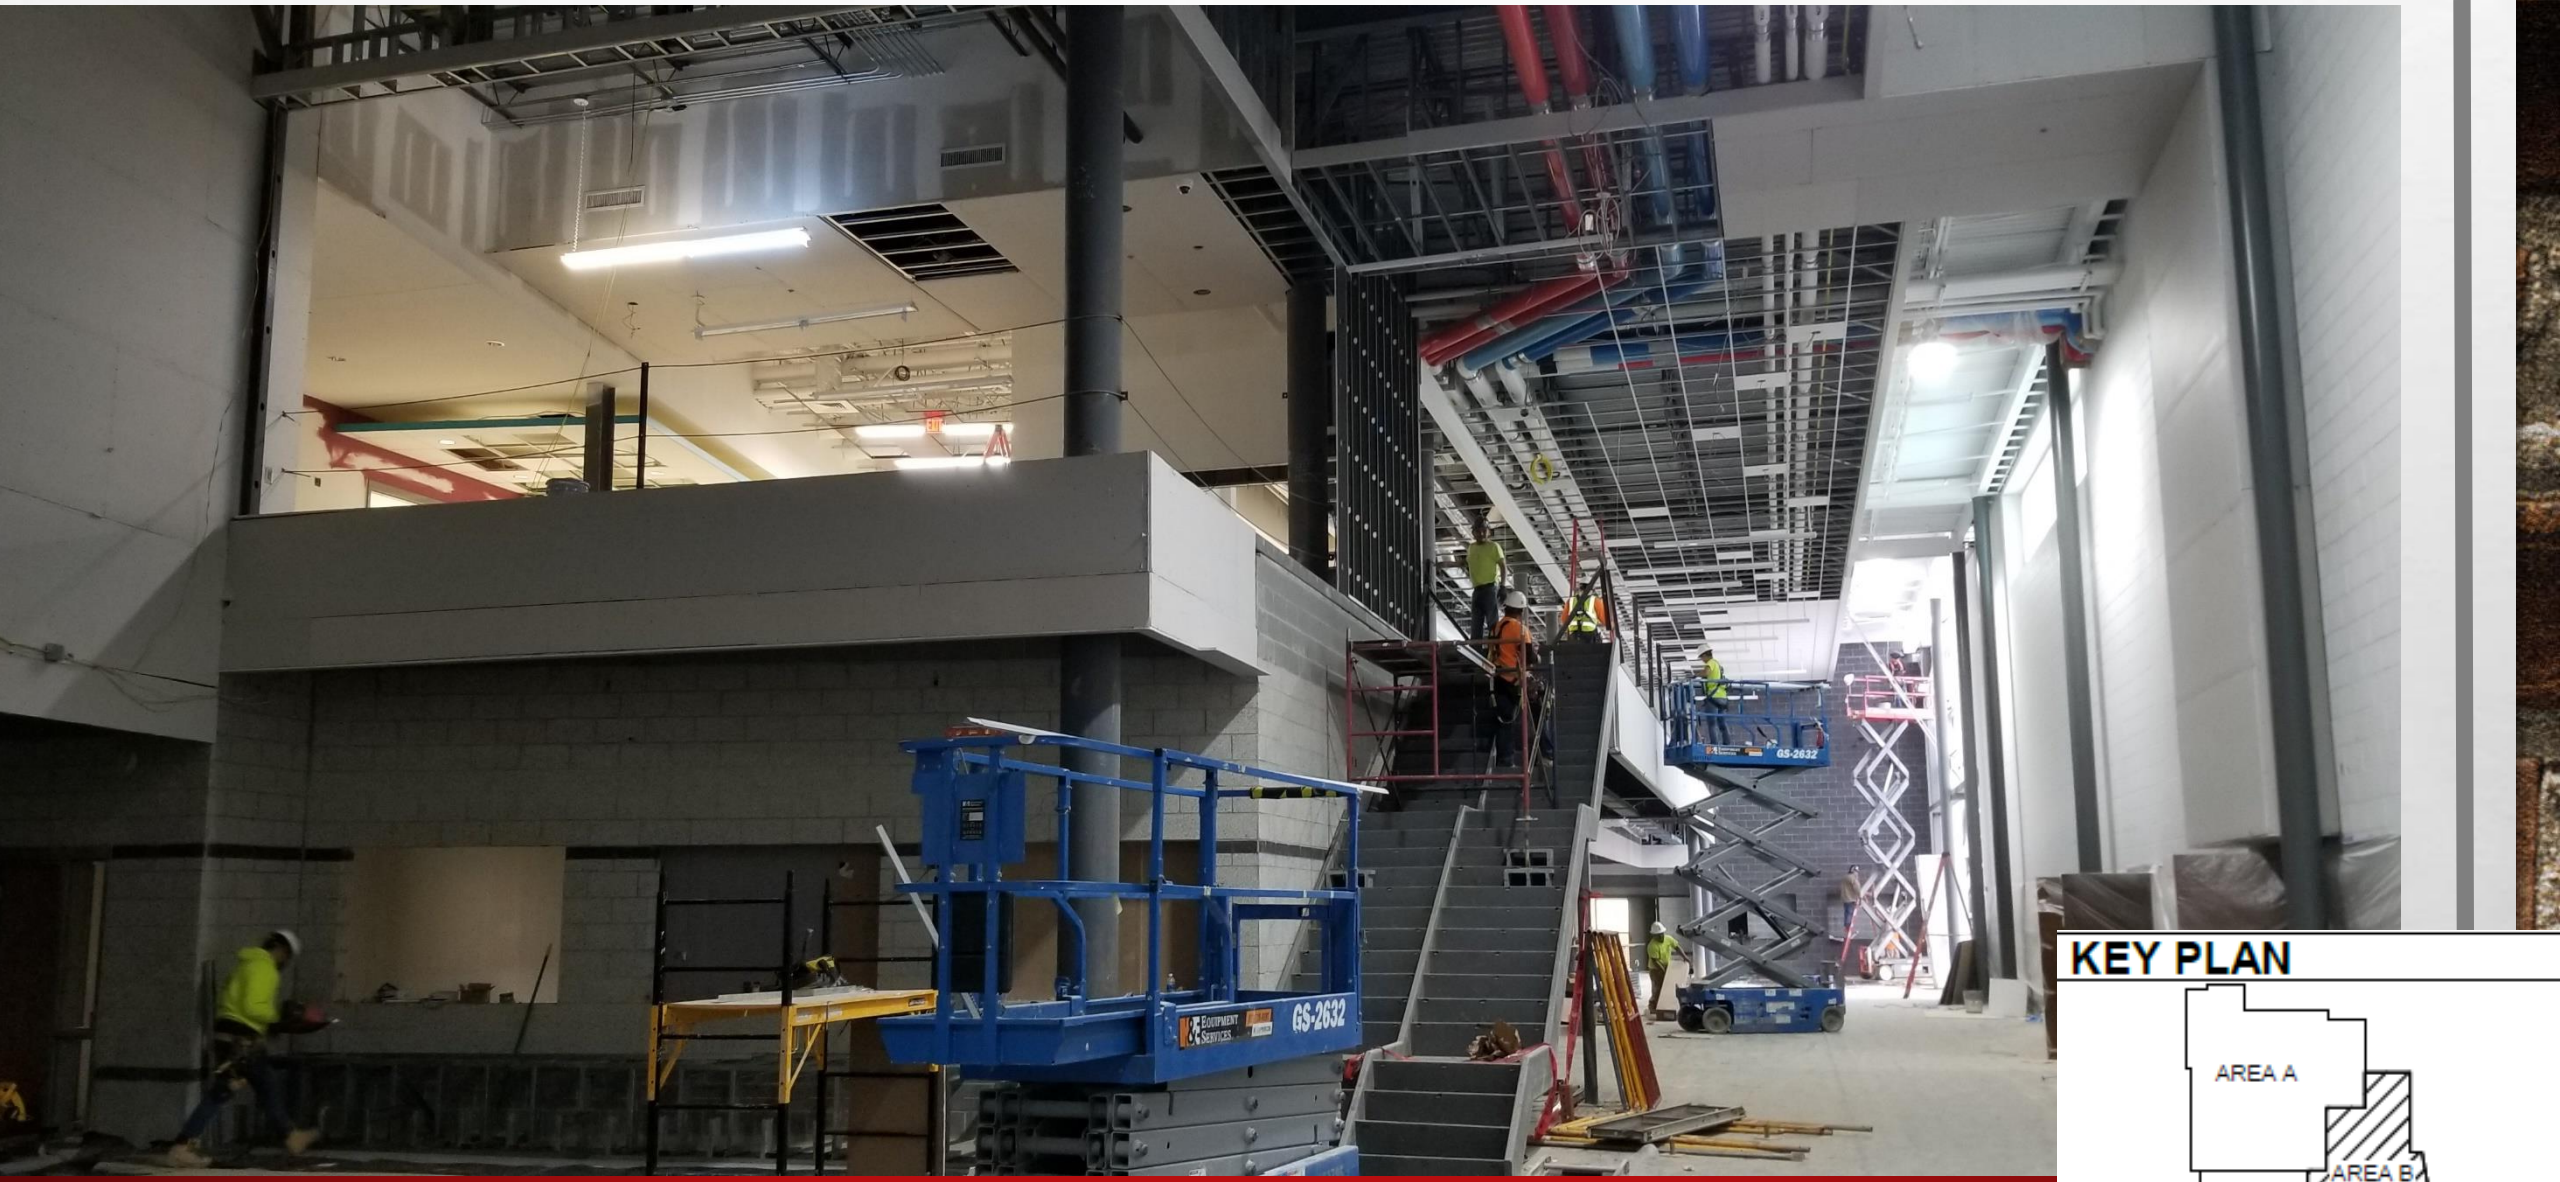


Area B – View down Main Corridor 4/30/2020

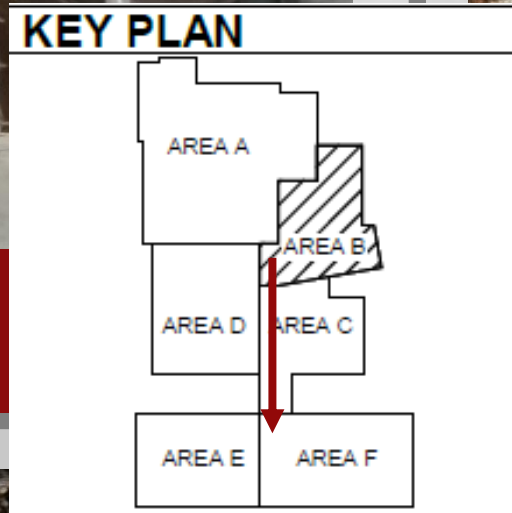


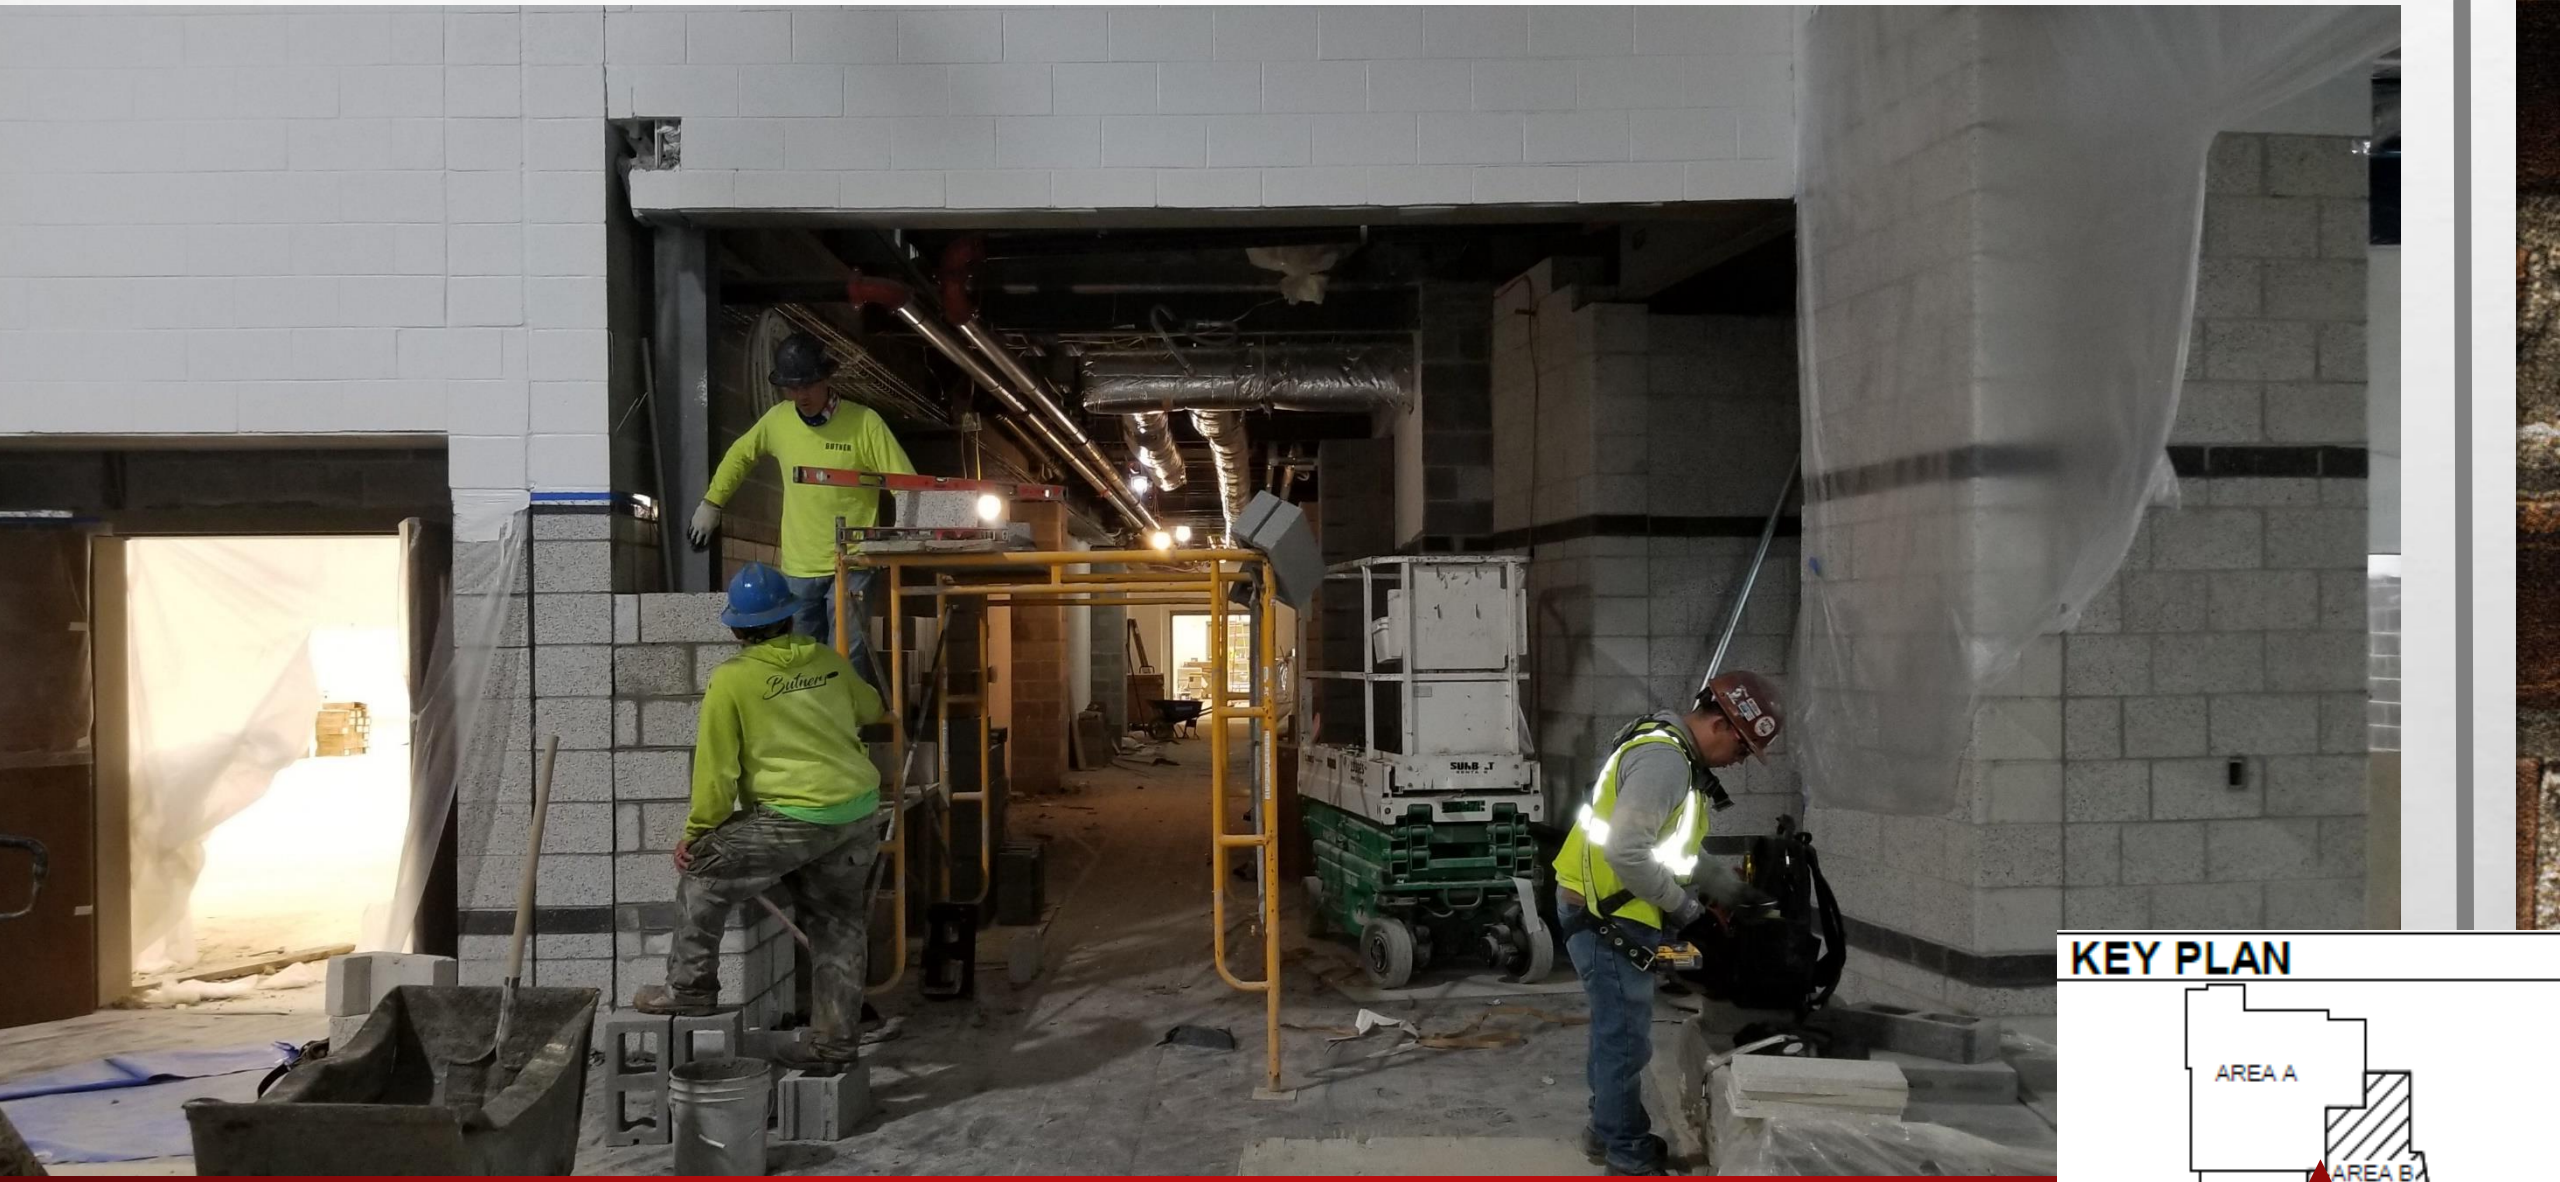


Area B – View down JROTC/Health Room Corridor

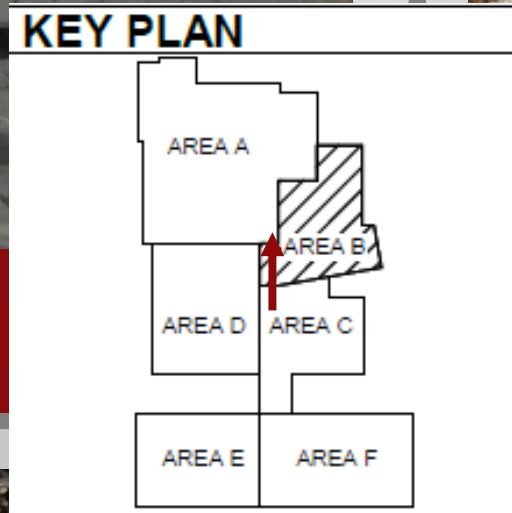


Area C 1st Floor – Main Entrance – Reception – SRO Office

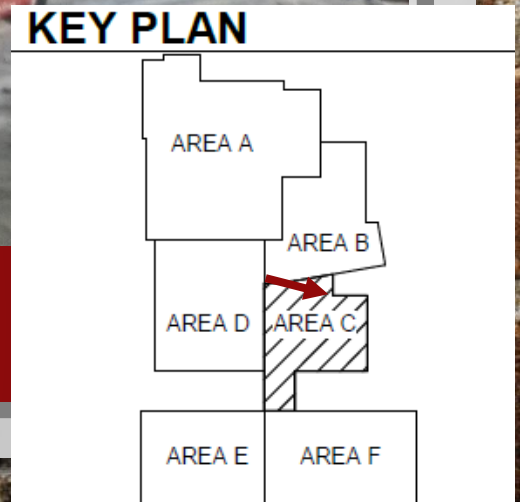


Area C 1st Floor – Office Area – 1322 PLC

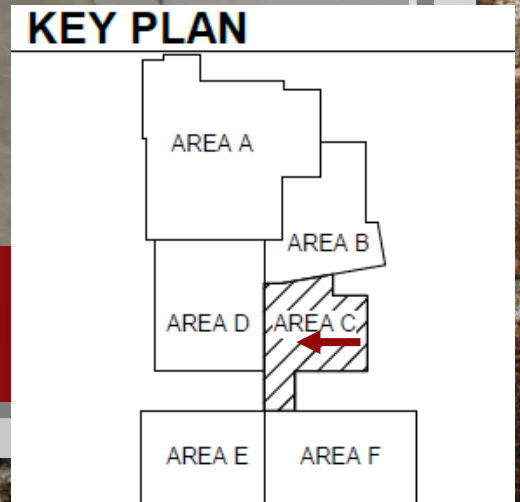


Area C 1st Floor – Main Corridor 1326

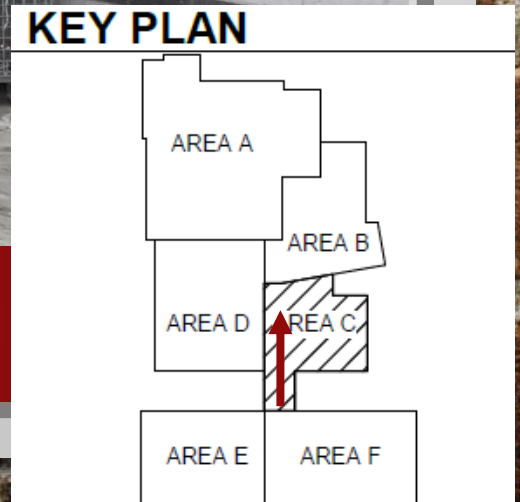

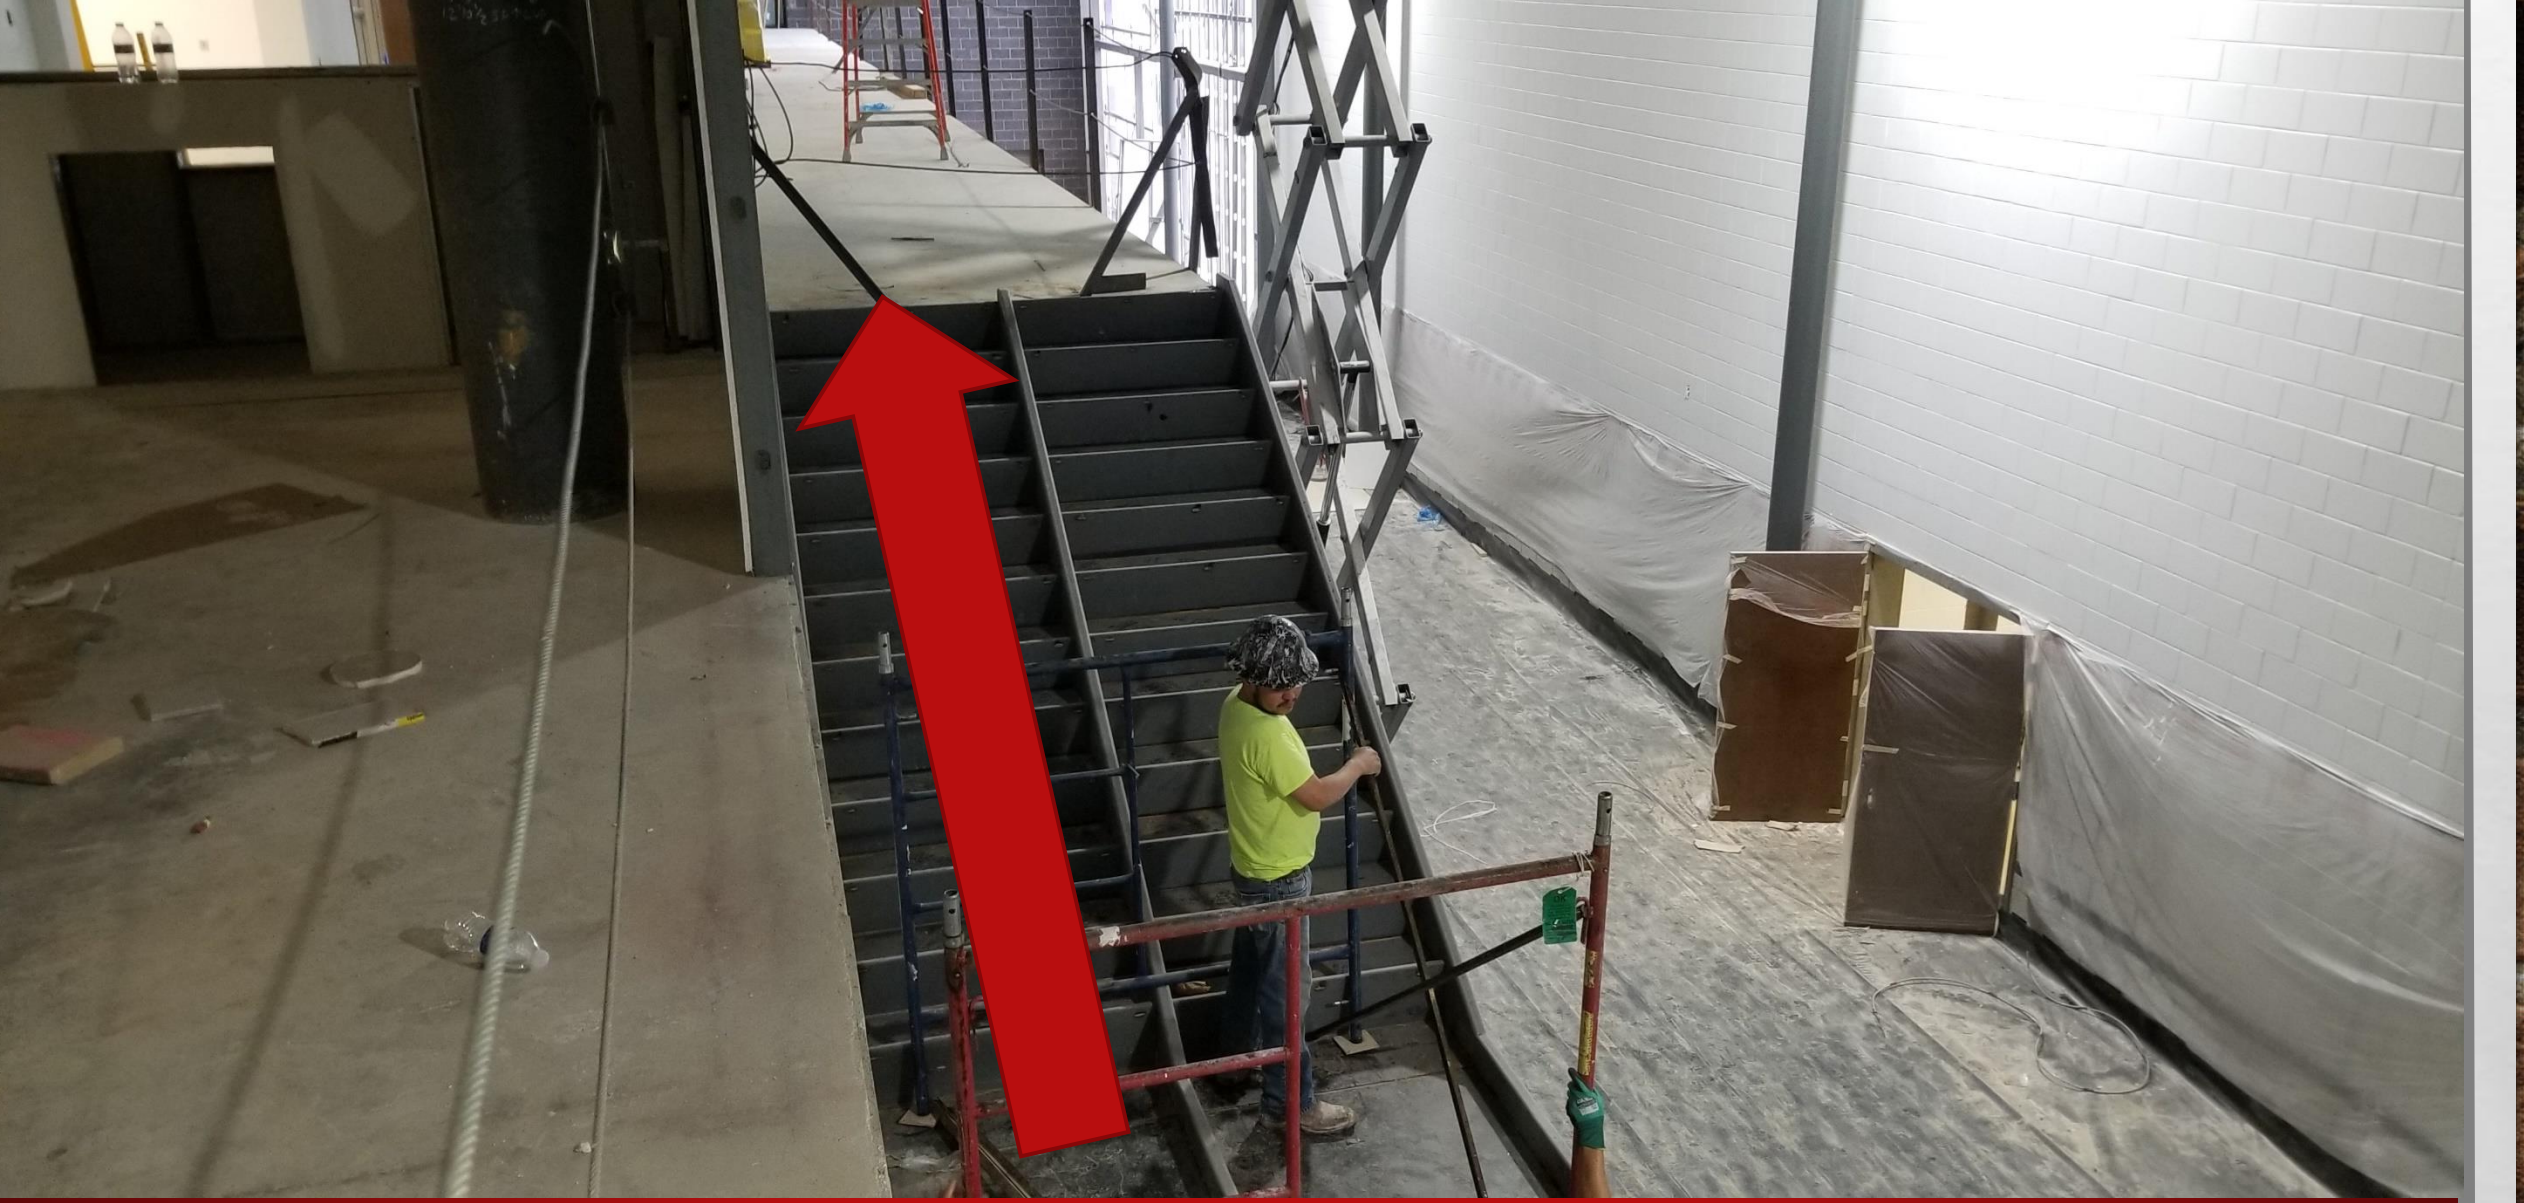


Up The Steps and Through the Wire


Area C 2nd Floor – Media Center

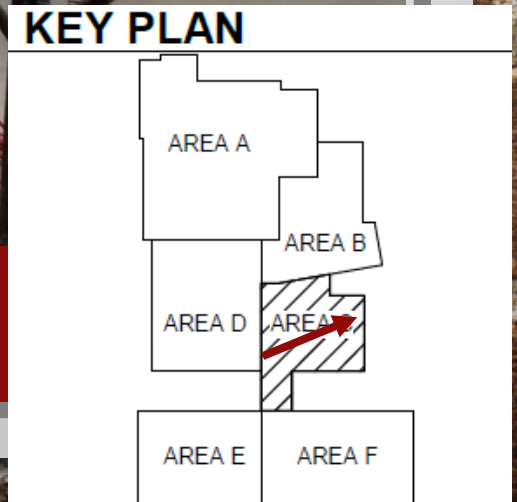

Area C 2nd Floor – Media Center – Sky Fold Door Location

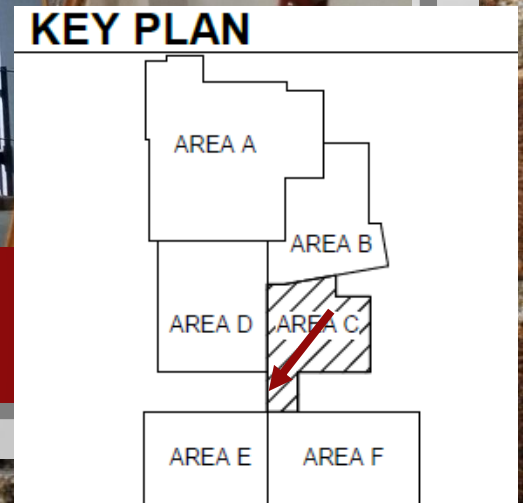


Dan with Branch – working hard

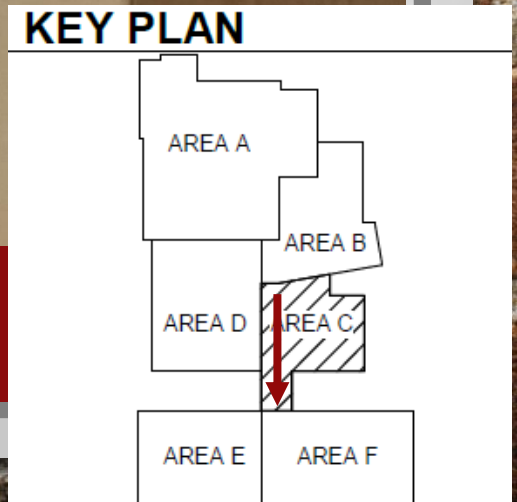



Back Down the Steps – Headed to Performing Arts Area D

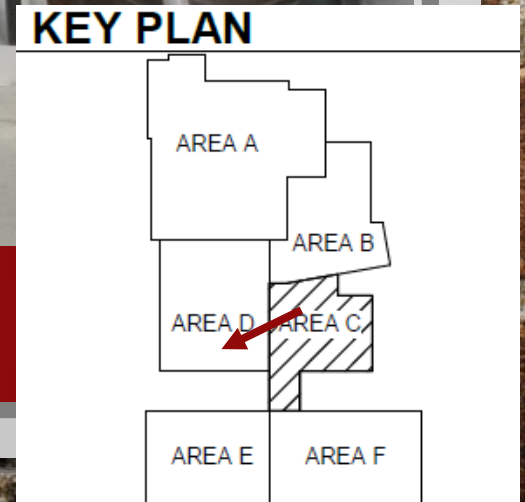


Area D -1432 Drama




KEY PLAN


Area D -1430 Dance

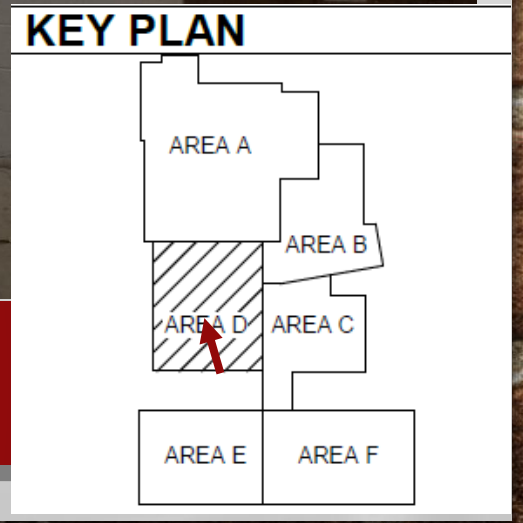


Area D -1424 Band/Chorus

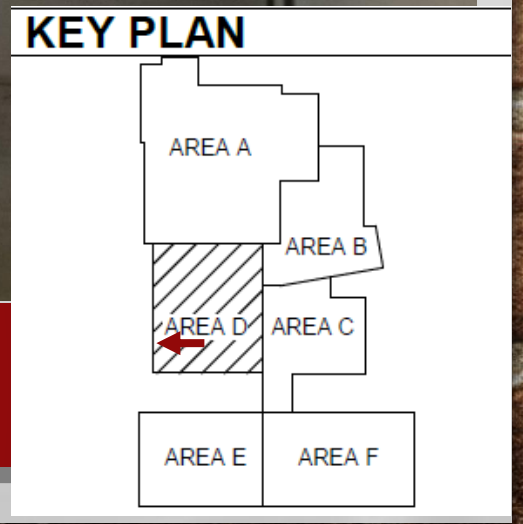

Area D -1427 Instrument Storage

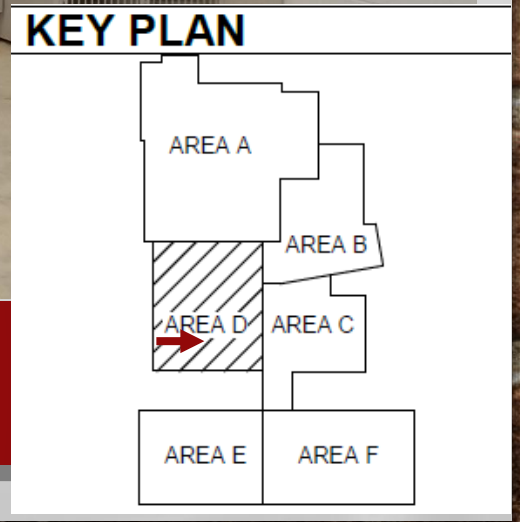

Area D – Auditorium – March BOE Report

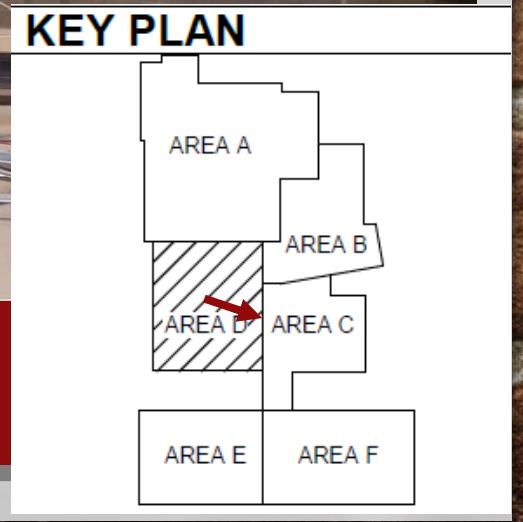




Area D – Auditorium – 4/30/2020




Area D – Auditorium – 4/08/2020

Area D – Auditorium – Stage Lighting

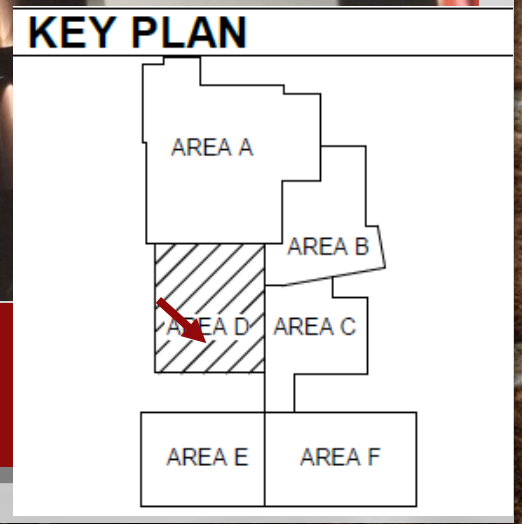




Area C 1st Floor – Main Stairwell In Progress – We're headed to E/F Instructional Wing

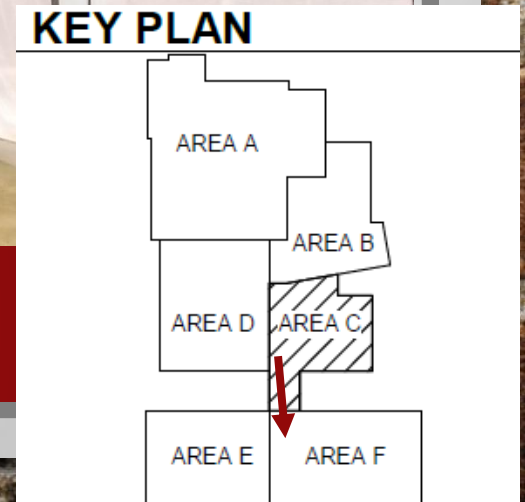




Area F 1st Floor – Locker


Area F 1st Floor – 1544 Commons 1534 Teacher Workroom

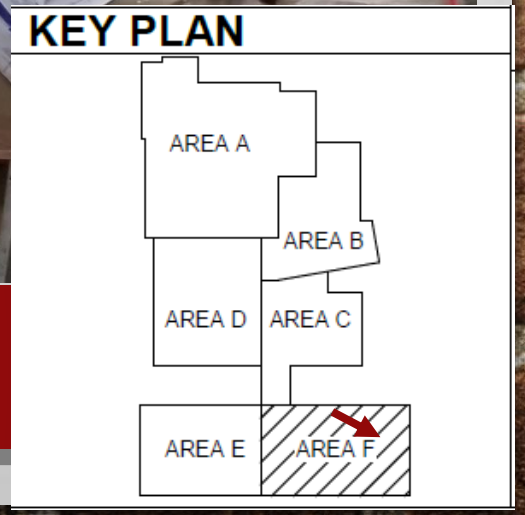

Area F 1st Floor – 1535 Classroom VCT in Progress

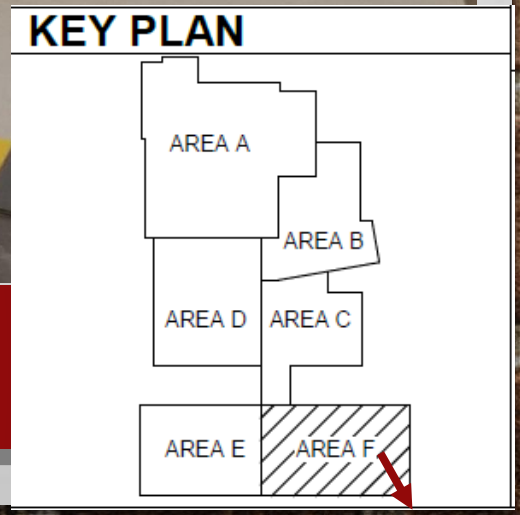


Area F 1st Floor – 1561 Corridor

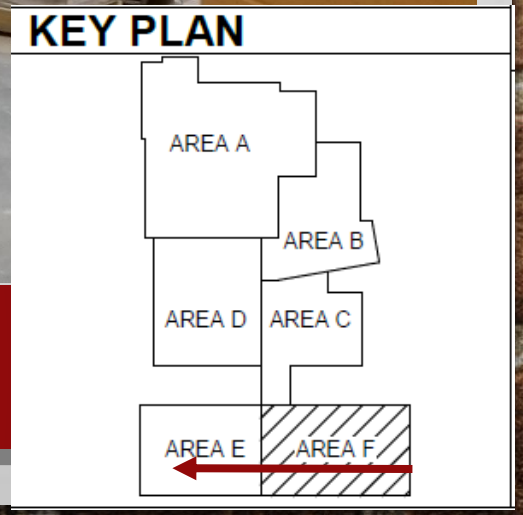




Up the steps…and yes….I did help him with the cart


Area F 2nd Floor – 2555 Computer Lab

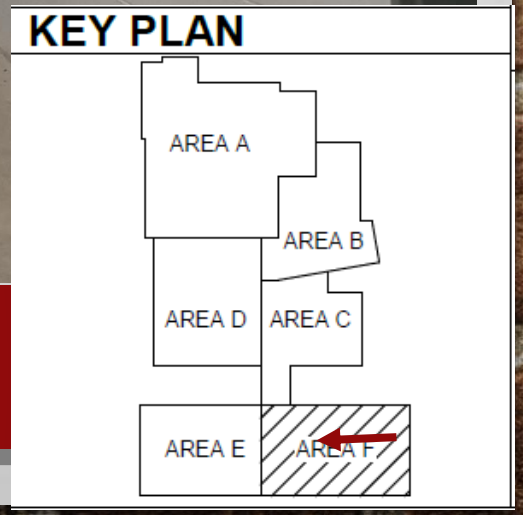


Area F 2nd Floor – 2538 Science

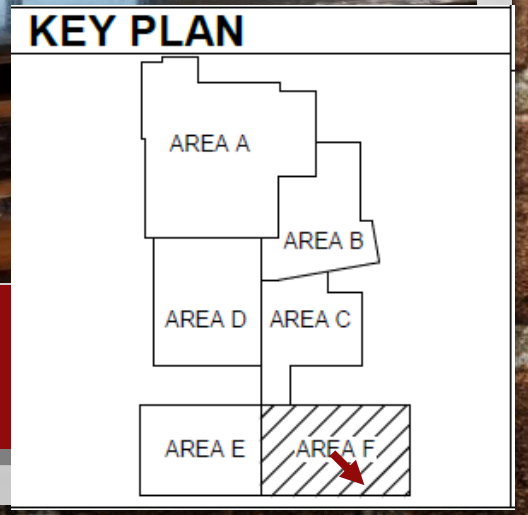

Area F 2nd Floor – 2538 Science Towards Front

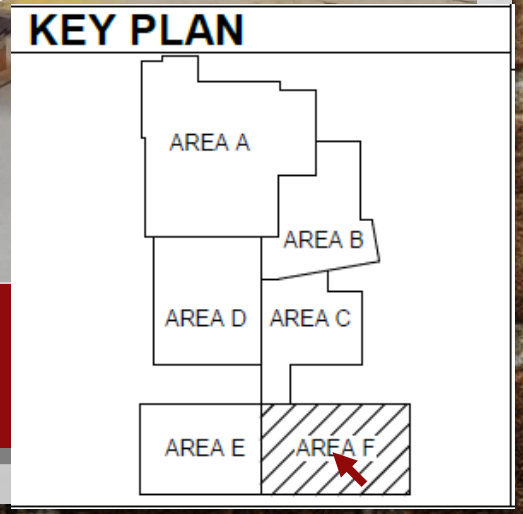


Area E 2nd Floor – 2542 Science

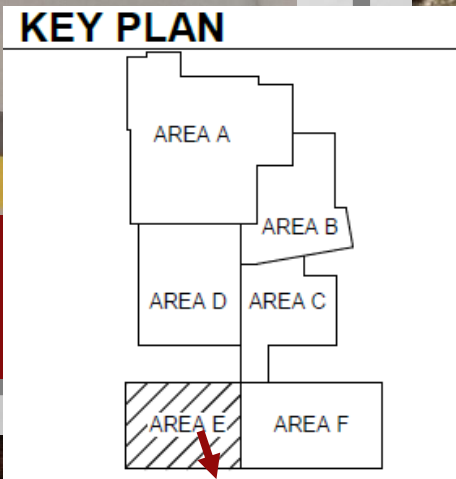




END SLIDE – QUESTIONS???


KEY PLAN

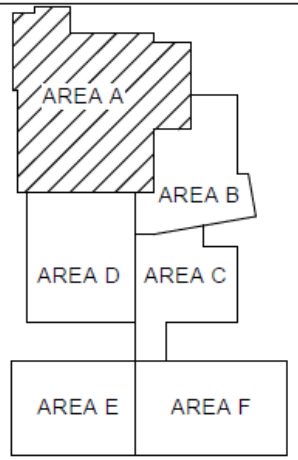


KEY PLAN

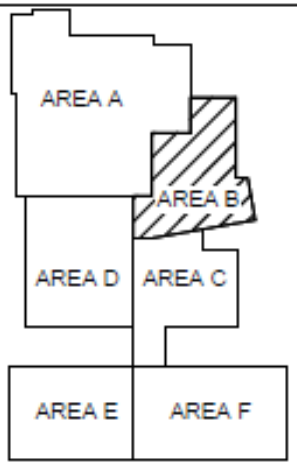


KEY PLAN

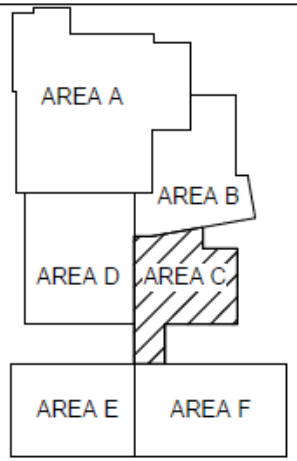


KEY PLAN

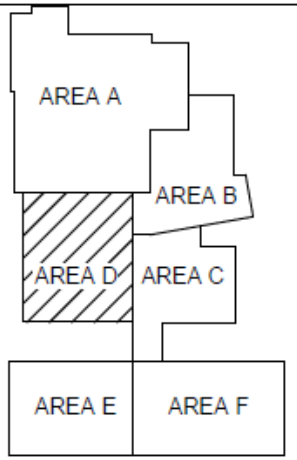

KEY PLAN

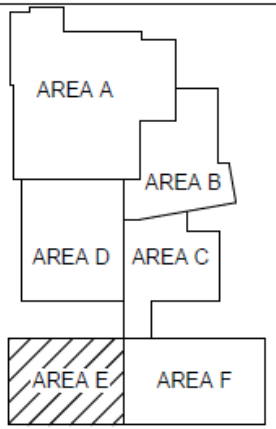


KEY PLAN

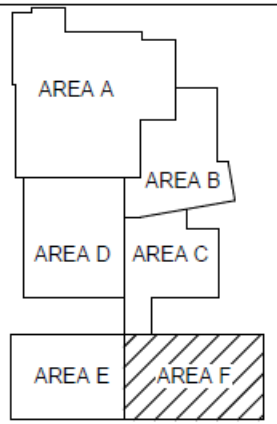


KEY PLAN



KEY PLAN



SITE KEY PLAN

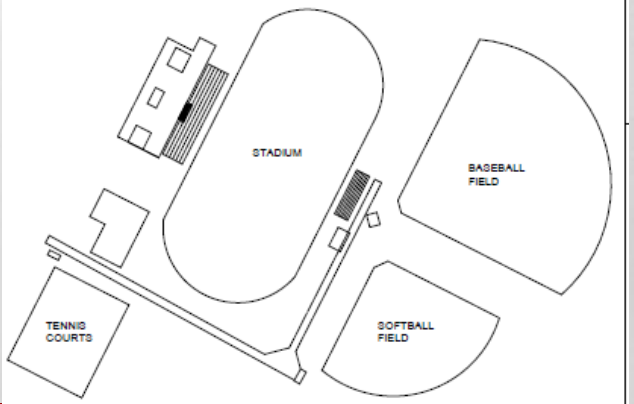

KEY BLOCK – DO NOT DELETE
