construction ECKLES services, inc.

Chicora Elementary School

Construction Project Update

Construction Report for September 09, 2024, Board Meeting

Cafeteria and serving line entrances

construction ECKLES services, inc.

Updates by Prime Contractors

Average workforce per day leading up to School Opening was averaging around 110 workers on site each day.

- **Vendrick Construction (General Contractor)**
  - Admin, Area B Cafeteria & Kitchen substantially complete
  - Loading dock complete, including approach apron
  - Sidewalks extended from teachers' parking areas to front entrance.
  - Flooring complete in classrooms and nearly complete in corridors
  - Paint is complete in all occupied areas.
  - Structural steel and deck at bus entrance side of connector erected.
  - Loading Dock Canopy steel erected
  - Parents' drop-off roadway is ready for asphalt.

- **Lugaila Mechanical (HVAC Contractor)**
  - Continuing controls installation & Programming
  - All Rooftop Air Handlers Started up and connected.
  - Grilles, registers, and diffusers are installed throughout the building.

- **Vrabel Plumbing (Plumbing Contractor)**
  - Gas line for Kitchen & Cafeteria installed across connector.
  - All fixtures in Areas B&C are installed.
  - gas lines connected to RTU's.
  - Temporary water lines installed to supply water to Kitchen until roof structure is installed at connector.
  - Hot Water heaters connected and started up.

- **Right Electric (Electrical Contractor)**
  - Generator started up and tested.
  - Continuing to switch areas over from old service to new
  - Connected kitchen equipment.
  - Lighting
  - Emergency circuits
  - Wiring for electronic access
  - Connected HVAC and Plumbing equipment.

- **Northeast Interior (Architectural Casework Contractor)**
  - Classroom/Admin Casework completed.
  - Library casework completed.
  - Millwork installed in Reception and Workroom
  - Countertops installed in Cafeteria.

- **Breckenridge Equipment (Foodservice Equipment)**
  - Kitchen equipment installed.
  - Health Department inspection passed 8/30.
  - Kitchen equipment full startup 9/06
  - Kitchen training 9/10
  - Custom Fabricated equipment to be installed starting 8/16.

Partial Occupancy was granted by the building Inspector.

construction ECKLES services, inc.

Financial Payment Application Summary as of 8/31/2024

Contractor	Vendrick	Lugaila	Vrabel	Right Electric	Breckenridge Kitchen	Northeast Interior	
Construction Contract	General Construction	HVAC Construction	Plumbing Construction	Electrical Construction	Food Service Construction	Casework	All Contracts
Original Contract Sum	$14,372,200.00	$3,631,000.00	$2,007,400.00	$3,120,600.00	$601,500.00	$839,000.00	$24,571,700.00
Change orders this period	$55,566.00	$0.00	$0.00	$0.00	$0.00	$0.00	$55,566.00
Previous Change Orders	$366,146.01	$528.21	$122,904.00	$23,198.20	$0.00	$0.00	$512,776.42
Change Order Total	$421,712.01	$528.21	$122,904.00	$23,198.20	$0.00	$0.00	$568,342.42
Contract Sum to Date	$14,793,912.01	$3,631,528.21	$2,130,304.00	$3,143,798.20	$601,500.00	$839,000.00	$25,140,042.42
Total Work Completed to date	$12,408,324.13	$3,373,044.71	$2,071,744.00	$2,925,210.57	$542,487.89	$777,130.00	$22,097,941.30
Total Retention Being Held	$620,416.21	$168,652.25	$207,174.00	$146,260.54	$54,248.79	$77,713.00	$1,274,464.79
Total earned net of Retainage	$11,787,907.92	$3,204,392.46	$1,864,570.00	$2,778,950.03	$488,239.10	$699,417.00	$20,823,476.51
Work Completed this period*	$1,408,704.68	$75,735.00	$149,163.60	$206,808.32	$179,203.00	$424,080.00	$2,443,694.60
Retention Held This Period	$70,435.24	$3,786.75	$14,916.00	$10,340.41	$17,920.30	$42,408.00	$159,806.70
Balance to Finish including Retainage	$3,006,004.09	$427,135.75	$265,734.00	$364,848.17	$113,260.90	$139,583.00	$4,316,565.91
Percent Complete	83.87%	92.88%	97.25%	93.05%	90.19%	92.63%	87.90%
Pay Application Amount (net of Retainage)							
April 2023		$71,302.50	$138,600.00	$104,400.00			$314,302.50
May 2023	$686,734.19	$9,022.50	$0.00	$0.00			$695,756.69
June 2023	$978,242.40	$457,661.25	$45,540.00	$105,784.20			$1,587,227.85
July 2023	$781,663.10	$120,816.00	$323,928.00	$151,188.75			$1,377,595.85
August 2023	$1,380,607.14	$901,143.00	$224,302.00	$332,932.95	$3,960.00	$201,690.00	$3,044,635.09
September 2023	$518,094.45	$54,855.00	$162,162.00	$178,947.00			$914,058.45
October 2023	$505,011.86	$65,396.25	$28,710.00	$328,845.60		$4,977.00	$932,940.71
November 2023	$371,209.50	$60,037.42	$60,264.00	$152,800.00			$644,310.92
December 2023	$483,818.46	$52,962.75	$22,020.00	$123,673.50	$26,676.90	$59,553.00	$768,704.61
January 2024	$209,514.60	$28,854.00	$28,134.00	$116,795.47	$226,681.10		$609,979.17
February 2024	$474,469.36	$87,619.50	$45,243.00	$40,040.99			$647,372.85
March 2024	$504,458.80	$138,709.58	$117,449.00	$105,724.13	$61,522.20		$927,863.71
April 2024	$1,016,763.44	$483,788.13	$134,247.60	$196,467.91	$8,116.20	$51,525.00	$1,890,908.28
May 2024	$805,379.00	$101,259.98	$119,331.00	$245,408.22	$0.00	$0.00	$1,271,378.20
June 2024	$1,087,171.10	$186,900.00	$92,745.00	$99,842.93			$1,466,659.03
July 2024	$646,491.09	$312,116.33	$220,850.40	$323,826.93			$1,503,284.75
August 2024	$1,338,269.44	$71,948.25	$134,247.60	$196,467.91	$161,282.70	$128,457.00	$2,030,672.90
September 2024							$0.00
October 2024							$0.00
November 2024							$0.00
December 2024							$0.00
TOTAL PAID TO DATE	**$11,787,897.93**	**$3,204,392.44**	**$1,897,773.60**	**$2,803,146.49**	**$488,239.10**	**$446,202.00**	**$20,627,651.56**

*** Negative Retention Figures indicate Retention Reduction per Contract at 50% completion of project.**

construction
ECKLES
services, inc.

Change Order Summary as of 8/31/2024.

Contractor	Contract	PCO/COR/RFCO #	Topic	Status	Resolution	Amount Submitted	Approved/Paid	Potential/Pending	NOTES
Right	EC	COR-EC-002	Bleacher Power	Executed	CO EC-001	$4,868.76	$ 4,868.76	$ -	
Right	EC	COR-EC-003	ASI #7 Changes	Executed	CO EC-002	$18,329.44	$ 18,329.44	$ -	Originally Submitted at $29K
Right	EC	COR-EC-001	BPI Power	Obsolete	Rejected	$10,674.67	$ -	$ -	This additional work not requied
Vendrick	GC	PCO GC-048	Area B Interior Connector Joist & Deck removal and reinstallation	Pending	CCD GC-003R	$ 27,150.00	$ -	$ 27,150.00	
Vendrick	GC	PCO GC-060	Cost for Breckenridge floor work as per CRA interpretation	Pending	CCD GC-006	$ 4,314.00	$ -	$ 4,314.00	
Vendrick	GC	Credit Letter PCO GC-001	Roller Shade VE Credit	Executed	CO GC-001	$ (6,300.00)	$ (6,300.00)	$ -	
Vendrick	GC	Additional Scope Letter	Summer 2023 Roofing	Executed	CO GC-002	$0.00	$0.00	$0.00	
Vendrick	GC	PCO GC-003	Added Brakemetal Closures	Executed	CO GC-003	$ 9,084.18	$ 9,084.18	$ -	
Vendrick	GC	PCO GC-004	Additional Wedge Curbs	Executed	CO GC-004	$ 679.25	$ 679.25	$ -	
Vendrick	GC	PCO GC-005	Added bulkhead at 122 & 125	Executed	CO GC-005	$ 975.66	$ 975.66	$ -	
Vendrick	GC	PCO GC-008	storefronts	Executed	CO GC-006	$ 2,268.40	$ 2,268.40	$ -	
Vendrick	GC	PCO GC-002	Relocate Inlet DI-030	Executed	CO GC-007	$ 3,849.62	$ 3,849.62	$ -	
Vendrick	GC	PCO GC-011	Reinforce existing inlet to make it traffic-bearing	Executed	CO GC-008	$ 9,378.00	$ 9,378.00	$ -	
Vendrick	GC	PCO GC-012	Raise Structure DI-01 8"	Executed	CO GC-009	$ 450.25	$ 450.25	$ -	
Vendrick	GC	PCO GC-015	Encase existing too-shallow electrical duct bank in concrete	Executed	CO GC-010	$ 4,831.00	$ 4,831.00	$ -	
Vendrick	GC	PCO GC-016	Replace Terracotta Pipe and DI-EX1B	Executed	CO GC-011	$ 6,678.26	$ 6,678.26	$ -	
Vendrick	GC	PCO GC-013	Final Cleaning Credit	Executed	CO GC-012	$ (3,300.00)	$ (3,300.00)	$ -	
Vendrick	GC	PCO GC-018	Temp pull off parking area	Executed	CO GC-013	$ 4,140.00	$ 4,140.00	$ -	
Vendrick	GC	PCO GC-019	Add ACT clg in room A110	Executed	CO GC-014	$ 445.41	$ 445.41	$ -	
Vendrick	GC	PCO GC-017	plywood for A/C in windows	Executed	CO GC-015	$ 754.07	$ 754.07	$ -	
Vendrick	GC	PCO GC-021	CMU Piers per RFI #53	Executed	CO GC-016	$ 1,315.00	$ 1,315.00	$ -	
Vendrick	GC	PCO GC-023	Trade Wall Graphics for Floor Graphics	Executed	CO GC-017	$ 954.45	$ 954.45	$ -	
Vendrick	GC	PCO GC-014	Signage Submittal Changes Incides PCO GC-020	Executed	CO GC-018	$ 791.38	$ 791.38	$ -	
Vendrick	GC	PCO GC-024	Area A Addition Also Includes rest of project (PCO GC-025)	Executed	CO GC-019	$ 1,838.00	$ 1,838.00	$ -	
Vendrick	GC	PCO GC-026	Relocate Red Maples	Executed	CO GC-020	$ 348.00	$ 348.00	$ -	
Vendrick	GC	PCO GC-027	Upgrade to Epoxy Paint in Corridors for rest of Project	Executed	CO GC-021	$ 2,655.00	$ 2,655.00	$ -	
Vendrick	GC	PCO GC-031	ASI #7 Changes	Executed	CO GC-022	$ 293.00	$ 293.00	$ -	
Vendrick	GC	PCO GC-035	Eliminate F1 Window	Executed	CO GC-023	$ (2,158.02)	$ (2,158.02)	$ -	
Vendrick	GC	PCO GC-032	accommodate HVAC and Sprinkler piping	Executed	CO GC-024	$ 1,696.00	$ 1,696.00	$ -	CRA/Tower/ECS find costs reasonable
Vendrick	GC	PCO GC-009E	Add Taper to Garland Roof Area	Executed	CO GC-025	$ 43,586.55	$ 43,586.55	$ -	
Vendrick	GC	PCO GC-029	Additional Chain Like Fence	Executed	CO GC-026	$ 37,980.00	$ 37,980.00	$ -	
Vendrick	GC	PCO GC-036	Room Windows	Executed	CO GC-027	$ 6,271.00	$ 6,271.00	$ -	
Vendrick	GC	PCO GC-034R1 CCD GC-002	Furring and Drywall and Laminating walls Combination of PCO's 033 & 034	Executed	CO GC-028	$ 19,343.10	$ 19,343.10	$ -	Original Price was $28,392.00
Vendrick	GC	PCO GC-037	Single-Occupant Restroom Privacy Indicators	Executed	CO GC-029	$ 9,061.00	$ 9,061.00	$ -	
Vendrick	GC	PCO GC-022R1 CCD GC-001	Storage Room Shoring	Executed	CO GC-030	$23,839.00	$ 23,839.00	$ -	Originally submitted at >$75,000
Vendrick	GC	PCO GC-041	Reconfigure Storefront Framing at Library Clerestory	Executed	CO GC-031	$ 1,102.00	$ 1,102.00	$ -	
Vendrick	GC	PCO GC-043	Asbestos-containing Transite Fascia removal	Executed	CO GC-032	$ 8,936.00	$ 8,936.00	$ -	
Vendrick	GC	PCO GC-042	Additional Bulkhead at B105	Executed	CO GC-033	$ 950.00	$ 1,102.00	$ -	
Vendrick	GC	PCO GC-028	Plaque Dimension Changes	Executed	CO GC-034	$ 896.00	$ 896.00	$ -	
Vendrick	GC	PCO GC-046	Partition reduction due to urinals in Gang Restrooms instead of all toilets	Executed	CO GC-035	$ (2,955.00)	$ (2,955.00)	$ -	
Vendrick	GC	PCO GC-040R1	Changes at Courtyards per ASI #6	Executed	CO GC-036	$ 105,105.00	$ 105,105.00	$ -	
Vendrick	GC	PCO GC-049	Remove Retaining Wall, infill louvers with brick	Executed	CO GC-037	$ 1,218.00	$ 1,218.00	$ -	
Vendrick	GC	PCO GC-050	Additional Courtyard Selective Demolition	Executed	CO GC-038	$ 1,431.00	$ 1,431.00	$ -	
Vendrick	GC	PCO GC-044R1	Playground Alterations (revised)	Executed	CO GC-039	$ 45,162.45	$ 45,162.45	$ -	
Vendrick	GC	PCO GC-039	Mortar Stain Repair Credit	Executed	CO GC-040	$ (5,350.00)	$ (5,350.00)	$ -	
Vendrick	GC	PCO GC-051	Credit to not paint Mechancial Rooms C160, C161, & C162	Executed	CO GC-041	$ (3,500.00)	$ (3,500.00)	$ -	
Vendrick	GC	CCD GC-005 RPCO GC-047R1	Rebuild Courtyard Fascia Support	Executed	CO GC-042	$ 21,353.00	$ 21,353.00	$ -	NTE Pricing Submitted at $ 34,122
Vendrick	GC	PCO GC-045	Grade changes	Executed	CO GC-043	$ 1,422.00	$ 1,422.00	$ -	
Vendrick	GC	PCO GC-052	Pipe Tunnel abatement and infill	Executed	CO GC-044 CCD GC-004	$ 17,056.00	$ 17,056.00	$ -	Being Done on T&M
Vendrick	GC	PCO GC-053	Unforeseen T&M Drywall work in "Remaining" area B	Executed	CO GC-045	$ 28,244.00	$ 28,244.00	$ -	

construction ECKLES services, inc.

Change Order Summary as of 8/12/2024 pg2.

Contractor	Contract	PCO/COR/RFCO #	Topic	Status	Resolution	Amount Submitted	Approved/Paid	Potential/Pending	NOTES
Vendrick	GC	PCO GC-055	Gym Acoustial Panel Demolition	Executed	CO GC-046	$ 1,908.00	$ 1,908.00	$ -	
Vendrick	GC	PCO GC-056	Corrective work at DI #29	Executed	CO GC-047	$ 5,238.00	$ 5,238.00	$ -	
Vendrick	GC	PCO GC-057	Changes necessary to meet Existing Gym Floor Elevation	Executed	CO GC-048	$ 1,698.00	$ 1,698.00	$ -	
Vendrick	GC	PCO GC-059	Out of sequence work in Connector	In Dispute	In Dispute	$ 12,817.00	$ -	$ -	
~~Vendrick~~	~~GC~~	~~PCO GC-020~~	~~Credit to change cast AL letters to acrylic (amount is included with PCO GC-014~~	~~Obsolete~~	~~Obsolete~~	~~$ -~~	~~$ -~~	$ -	
~~Vendrick~~	~~GC~~	~~PCO GC-025~~	~~Add Plumbing Chase Access Doors for rest of Project~~	~~Obsolete~~	~~Obsolete~~	~~$ -~~	~~$ -~~	$ -	
~~Vendrick~~	~~GC~~	~~PCO GC-044~~	~~Playground Alterations~~	~~Obsolete~~	~~Obsolete~~	~~$ 49,857.00~~	~~$ -~~	~~$ -~~	
Lugalia	HC	PCO HC-001	Delete Roof Vents not required as per rebid requirements	Executed	CO HC-001	$ (761.92)	$ (761.92)	$ -	
Lugalia	HC	PCO HC-004	Changes as per ASI#7	Executed	CO HC-002	$ 1,290.13	$ 1,290.13	$ -	
~~Lugalia~~	~~HC~~	~~PCO HC-002~~	~~Patch roof at deleted HVAC locations and flash in new HVAC equipment at Garland Roof area~~	~~Rejected~~	~~Rejected~~	~~$ 47,155.92~~	~~$ -~~	~~$ -~~	Cost per contract is a $40,000.00 add for seam taping & tapered insulation. Cost to keep Garland Roof is $ 46,000 credit, no extra $ 40,000 for taper, and CO to HC for $ 47,155.92. Net savings = $38,844.08
~~Lugalia~~	~~HC~~	~~PCO HC-003~~	~~Upcharge for custom Color on Fabric Ducts~~	~~Rejected~~	~~Rejected~~	~~$ 3,326.40~~	~~$ -~~	~~$ -~~	Fabric ducts will be white, as specified.
Vrabel	PC	PCO-PC-001	Raise Existing Manhole to new Grade	Executed	CO PC-001	$ 4,676.00	$ 4,676.00	$ -	
Vrabel	PC	PCO-PC-002	Install casing/piping for future concession stand at Athletic Field	Executed	CO PC-002	$ 8,935.00	$ 8,935.00	$ -	
Vrabel	PC	PCO-PC-003	that was supposed to be removed in	Executed	CO PC-003	$ 4,505.00	$ 4,505.00	$ -	
Vrabel	PC	PCO-PC-007	Cost for ASI #7	Executed	CO PC-004	$ 1,633.00	$ 1,633.00	$ -	
Vrabel	PC	PCO-PC-006	Credit for leaving Showers in locker rooms as-is	Executed	CO PC-005	$ (5,000.00)	$ (5,000.00)	$ -	
Vrabel	PC	PCO PC-004A	Locker Room Sanitary tie-in	Executed	CO PC-006	$ 18,801.00	$ 18,801.00	$ -	
Vrabel	PC	PCO PC-009	Relocate Waterline and Sprinkler Lines	Executed	CO PC-007	$ 16,232.00	$ 16,232.00	$ -	
~~Vrabel~~	~~PC~~	~~CCD PC-001 PCO PC-004~~	~~Locker Room Sanitary tie-in~~	~~Rejected~~	~~Obsolete~~	~~$ 26,884.00~~	~~$ -~~	~~$ -~~	
Vrabel	PC	CCD PC-002 PCO PC-005	Area B Storm Line	Executed	CO PC-008	$ 26,659.00	$ 26,659.00	$ -	
Vrabel	PC	PCO PC-008	Classroom Subsidence & Roof Drain piping repair	Executed	CO PC-009	$ 18,220.00	$ 18,220.00	$ -	
Vrabel	PC	PCO PC-010	Replace Art Room Sinks	Executed	CO PC-010	$ 1,696.00	$ 1,696.00	$ -	
Vrabel	PC	PCO PC-011	Reconfigure Courtyard drainage	Executed	CO PC-011	$ 23,688.00	$ 23,688.00	$ -	
Vrabel	PC	PCO PC-012	Mechanical Room Piping repairs	Pending	CCD PC-003	$ 8,525.91	$ -	$ 8,525.91	PCO PC-012 & PC-013 are both included in
Vrabel	PC	PCO PC-013	Mechanical Room Mop Basins	Pending	CCD PC-003	$ 4,778.37	$ -	$ 4,778.37	
Vrabel	PC	PCO PC-014	Change Toilets to Urinals in New Area C & existing A Boys' Gang Restrooms	Executed	CO PC-012	$ 2,859.00	$ 2,859.00	$ -	
Vendrick	GC	PCO GC-054	Cost to install Walk-In Cooler Roof Curbs out of sequence	Pending	Pending	$ 2,596.00	$ -	$ 2,596.00	This will be offset by a credit CO to FSE Contractor.
Vendrick	GC	PCO GC-058	Planter modificatiosn at Bud Entrance	Pending	Pending	$ 10,924.00	$ -	$ 10,924.00	
Vendrick	GC	PCO GC-061	Attitional Paving at Kittaning St.	Pending	Pending	$ 1,886.00	$ -	$ 1,886.00	
Vendrick	GC	PCO GC-062	Change Block soundproofing from foam to sand	Pending	Pending	$ (439.40)	$ -	$ (439.40)	
~~Vendrick~~	~~GC~~	~~PCO GC 006~~	~~VCT Flooring Change to LVT~~	~~Rejected~~	~~Rejected~~	~~$ 6,590.02~~	~~$ -~~	~~$ -~~	
~~Vendrick~~	~~GC~~	~~PCO GC-007~~	~~Additional Roof Frames~~	~~Rejected~~	~~Rejected~~	~~$ 5,582.89~~	~~$ -~~	~~$ -~~	
~~Vendrick~~	~~GC~~	~~PCO GC-009a~~	~~1/4" Tapered Overlay on Area B Roof~~	~~Rejected~~	~~Rejected~~	~~$ 238,400.00~~	~~$ -~~	~~$ -~~	
~~Vendrick~~	~~GC~~	~~PCO GC-009b~~	~~1/8" Tapered Overlay on Area B Roof~~	~~Rejected~~	~~Rejected~~	~~$ 191,420.00~~	~~$ -~~	~~$ -~~	
~~Vendrick~~	~~GC~~	~~PCO GC-009c~~	~~Double-Flash Seams on Area b Roof~~	~~Rejected~~	~~Rejected~~	~~$ 50,373.00~~	~~$ -~~	~~$ -~~	
~~Vendrick~~	~~GC~~	~~PCO GC-009d~~	~~Credit for Area B Library roof to remain in place: 10 years left on warranty~~	~~Rejected~~	~~Rejected~~	~~$ (46,200.00)~~	~~$ -~~	~~$ -~~	
Lugaila	HC	PCO HC-005	Cost to evacuate existing walk in refrigertant, and remove kitchen equipment	Pending	Pending	$ 3,562.05	$ -	$ 3,562.05	FSE Contractor refused to do tehis work that was determined to be within their scope.
Vrabel	PC	PCO PC-016	Temporary Water Lines to Open Area	Pending	Pending	$ 12,694.00	$ -	$ 12,694.00	
Vrabel	PC	PCO PC-015	Add Water Make-up for HVAC	Pending	Pending	$ 2,250.00	$ -	$ 2,250.00	
Breckenridge	FSEC	PCO FSE-001	HC Kitchen Demo Backcharges	Pending	Pending	$ (3,562.05)	$ -	$ (3,562.05)	
Breckenridge	FSEC	PCO FSE-002	GC out of sequence Roof work for Walk-In curbs deliverd late	Pending	Pending	$ (2,596.00)	$ -	$ (2,596.00)	
Breckenridge	FSEC	B/C KCASD-001	Cost for District Fire Sefety Vendor to decomission existign Ansul System	Pending	Pending	$ -	$ -	$ -	unknown cost at this time
~~Vendrick~~	~~GC~~	~~PCO GC 010a~~	~~Rock at Toe of Athletic Field~~	~~Rejected~~	~~Rejected~~	~~$ 38,072.00~~	~~$ -~~	$ -	
~~Vendrick~~	~~GC~~	~~PCO GC-010b~~	~~Rock at Toe of Athletic Field~~	~~Rejected~~	~~Rejected~~	~~$ 40,086.00~~	~~$ -~~	$ -	
~~Vendrick~~	~~GC~~	~~PCO GC 038~~	~~Add Bulletin Board cabinet at~~	~~Rejected~~	~~Rejected~~	~~$ 4,427.00~~	~~$ -~~	~~$ -~~	
~~Vendrick~~	~~GC~~	~~PCO GC 040~~	~~Changes at Courtyards per ASI #6~~	~~Rejected~~	~~Rejected~~	~~$ 139,134.00~~	~~$ -~~	~~$ -~~	
~~Vendrick~~	~~GC~~	~~PCO GC-030~~	~~Extra Piping for Relocated Downspout~~	~~Rescinded~~	~~Rescinded~~	~~$ 1,351.00~~	~~$ -~~	~~$ -~~	
~~Vendrick~~	~~GC~~	~~PCO GC 033~~	~~Furring and Drywall at bare CMU walls and under sills~~	~~Rejected~~	~~Under Review~~	~~$ 23,522.00~~	~~$ -~~	~~$ -~~	Plan is to proceed with these on T&M, NTE total submitted. GC to provide credit for contract patching.
~~Vendrick~~	~~GC~~	~~PCO GC-034~~	~~Laminate walls and change infills to metal studs~~	~~Rejected~~	~~Under Review~~	~~$ 13,012.00~~	~~$ -~~	~~$ -~~	Plan is to proceed with these on T&M, NTE total submitted. GC to provide credit for contract patching.
							$ -	$ -	
							$ -	$ -	
							$ -	$ -	
						TOTALS	**$ 558,444.42**	**$ 72,082.88**	
							Approved/Paid	**Potential/Pending**	
							2.27%	**0.29%**	
								2.57%	
								Percent of Total Contracts	

construction
ECKLES
services, inc.

The first students being served breakfast in the new Cafeteria

construction
ECKLES
services, inc.

Entrance to Guidance area from classroom side of building.

construction
ECKLES
services, inc.

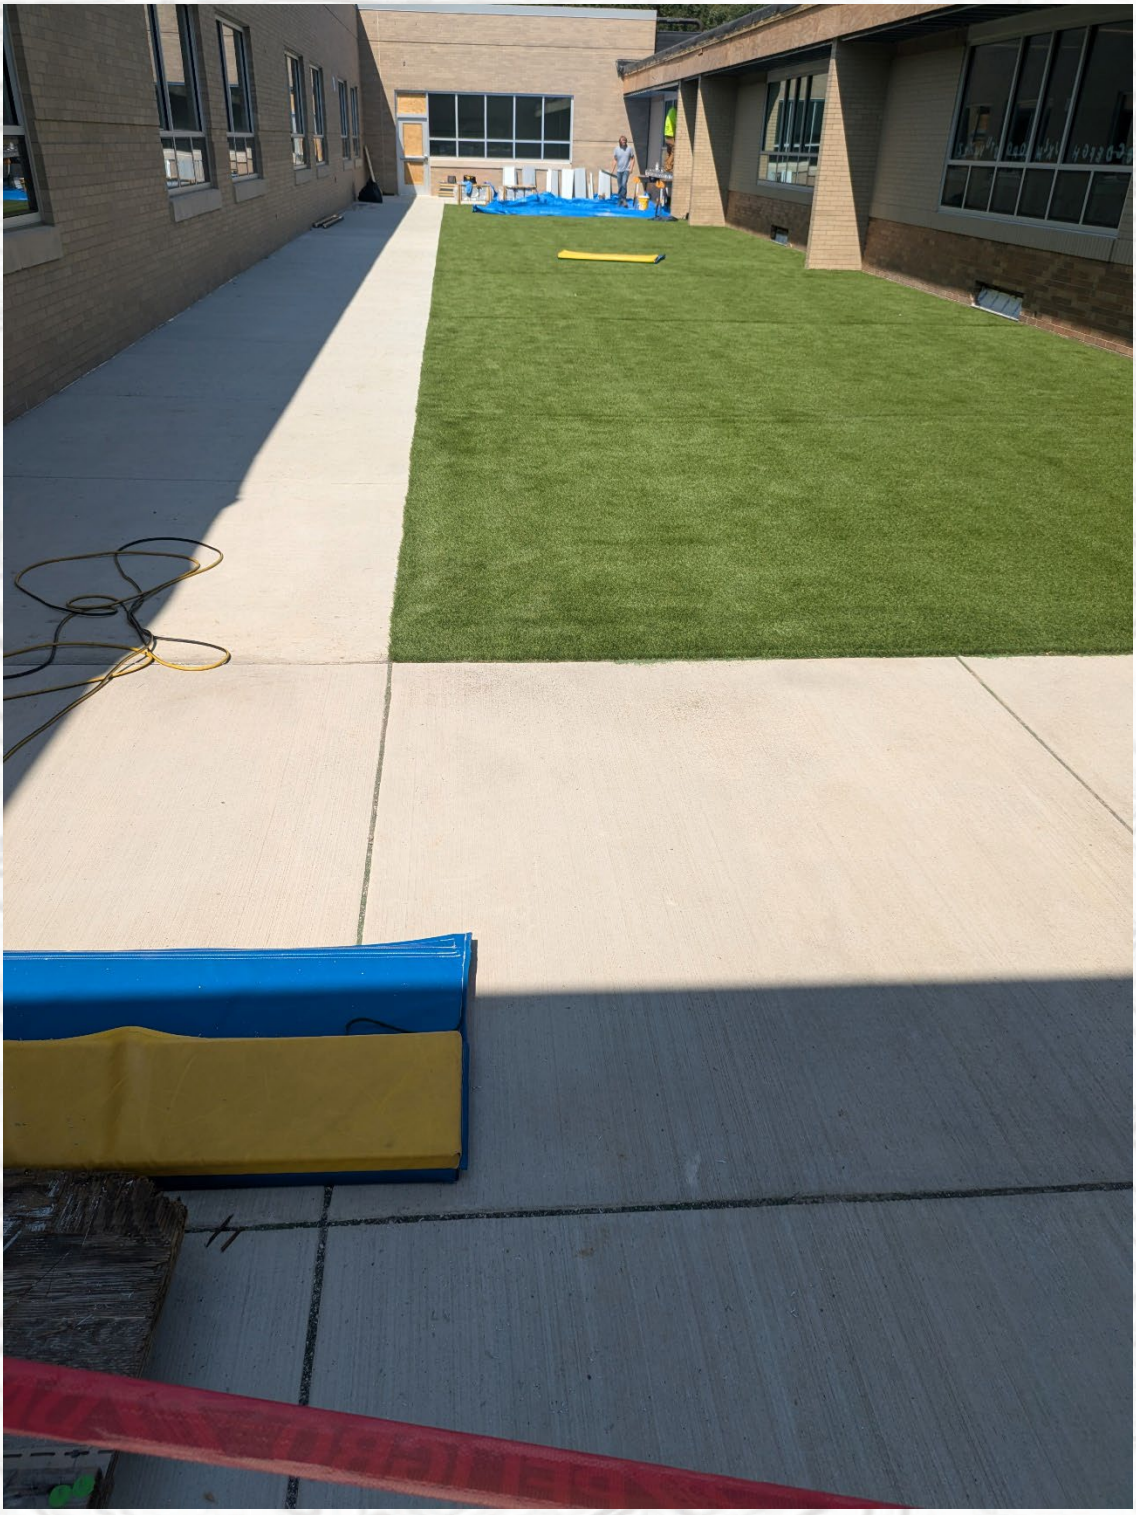

Courtyard with artifical turf flexible outdoor learning space.
New kindergarten wing is on the left.

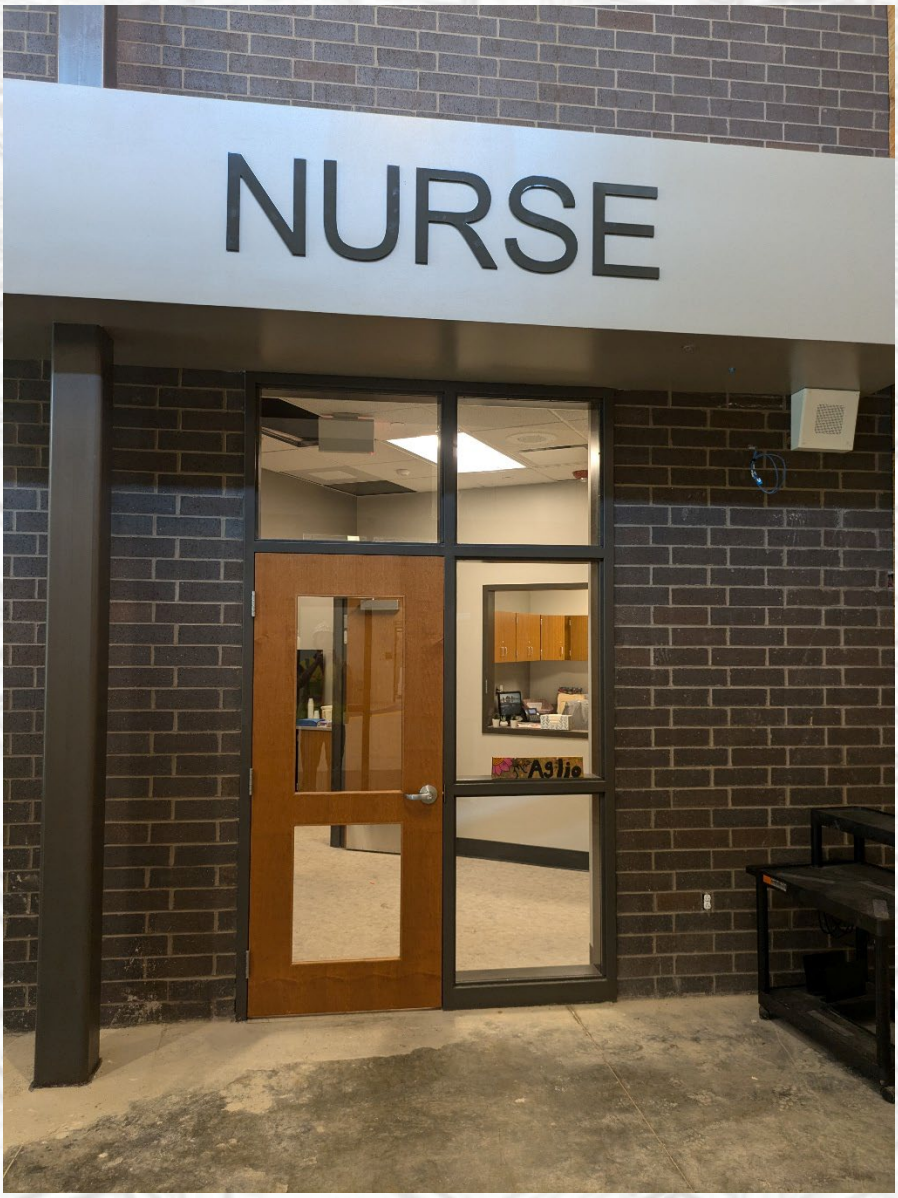

Nurse's suite entrance from main entry corridor.

construction
ECKLES
services, inc.

Learning Commons at end of Kindergarten corridor..

construction
ECKLES
services, inc.

Steamer and tilting braiser under hood in kitchent.

construction
ECKLES
services, inc.

New Standing Seam roof being installed..

construction
ECKLES
services, inc.

Bus Drop-off entrance.
Structural steel and roof deck in place.

construction
ECKLES
services, inc.

Parent Drop-off entrance with building signage installed.

construction
ECKLES
services, inc.

Concrete placed at Loading Dock apron

construction
ECKLES
services, inc.

Turnaround/Roundabout at top of Parent Drop Off.

construction
ECKLES
services, inc.

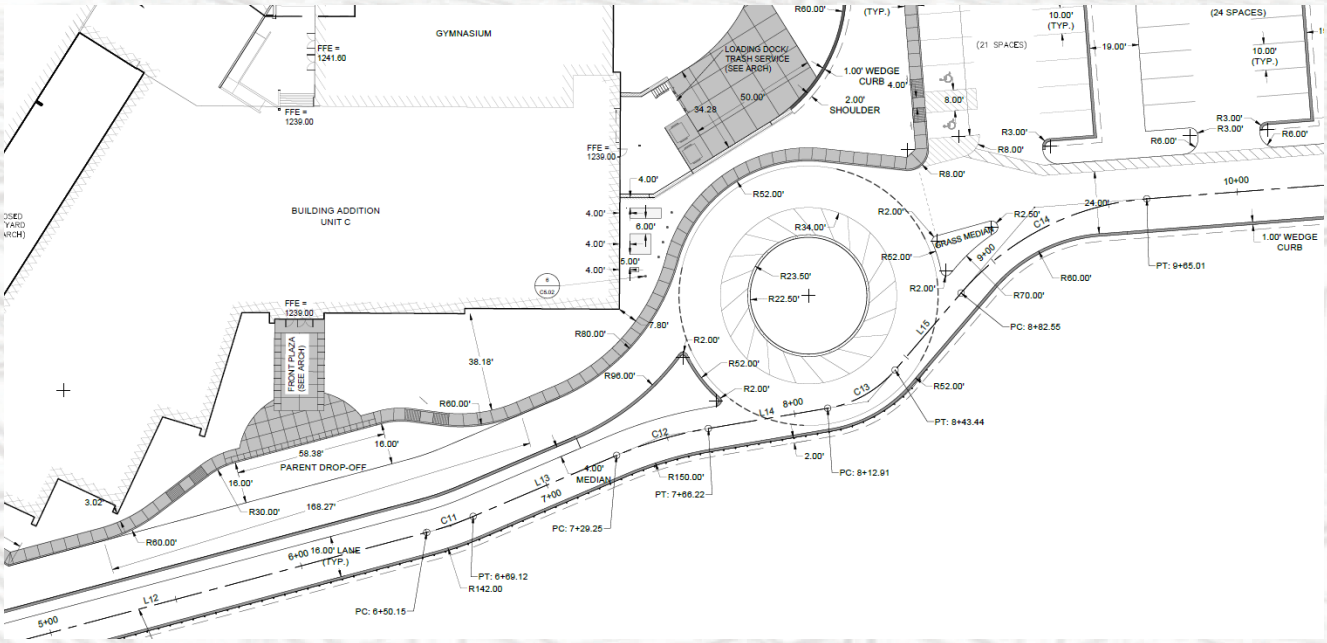

Plan view of turnaround/roundabout, loading dock apron, and Prent Drop off entrance.

construction
ECKLES
services, inc.

Parent Drop-Off Roadway, looking toward Kittanning St.
Roadway is ready for asphalt.

construction
ECKLES
services, inc.

Aerial view of Parent Drop-Off roadway

construction
ECKLES
services, inc.

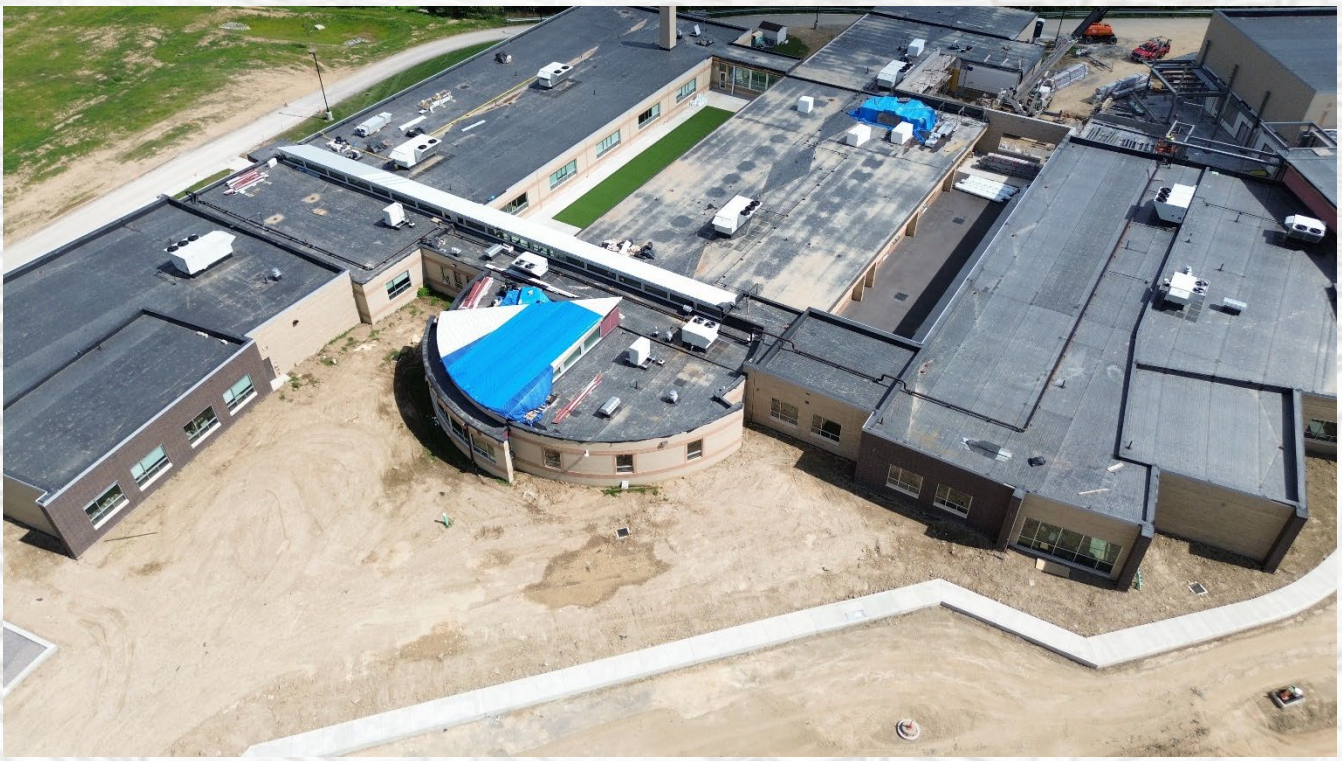

Aerial view of Academic areas. New standing seam roof over corridor and library is visible, as well as turf in north courtyard.

construction
ECKLES
services, inc.

Aerial view of "connector area under construction. Bus drop-off vestibule structural steel is under construction in this picture.

construction
ECKLES
services, inc.

Success Through Management

www.ecklesgroup.com

201 South Main Street
Suite 103
Zelienople, PA 16063
724-473-0485
