JEFFCO PUBLIC SCHOOLS

CAAC Design and Construction Update

11-21-24



Fletcher Miller Special School
New Facility @ Current Site

Construction

MOA – Crossland




JEFFCO PUBLIC SCHOOLS

Chatfield HS – Secure Entry

Construction


MOA - Mark Young Construction

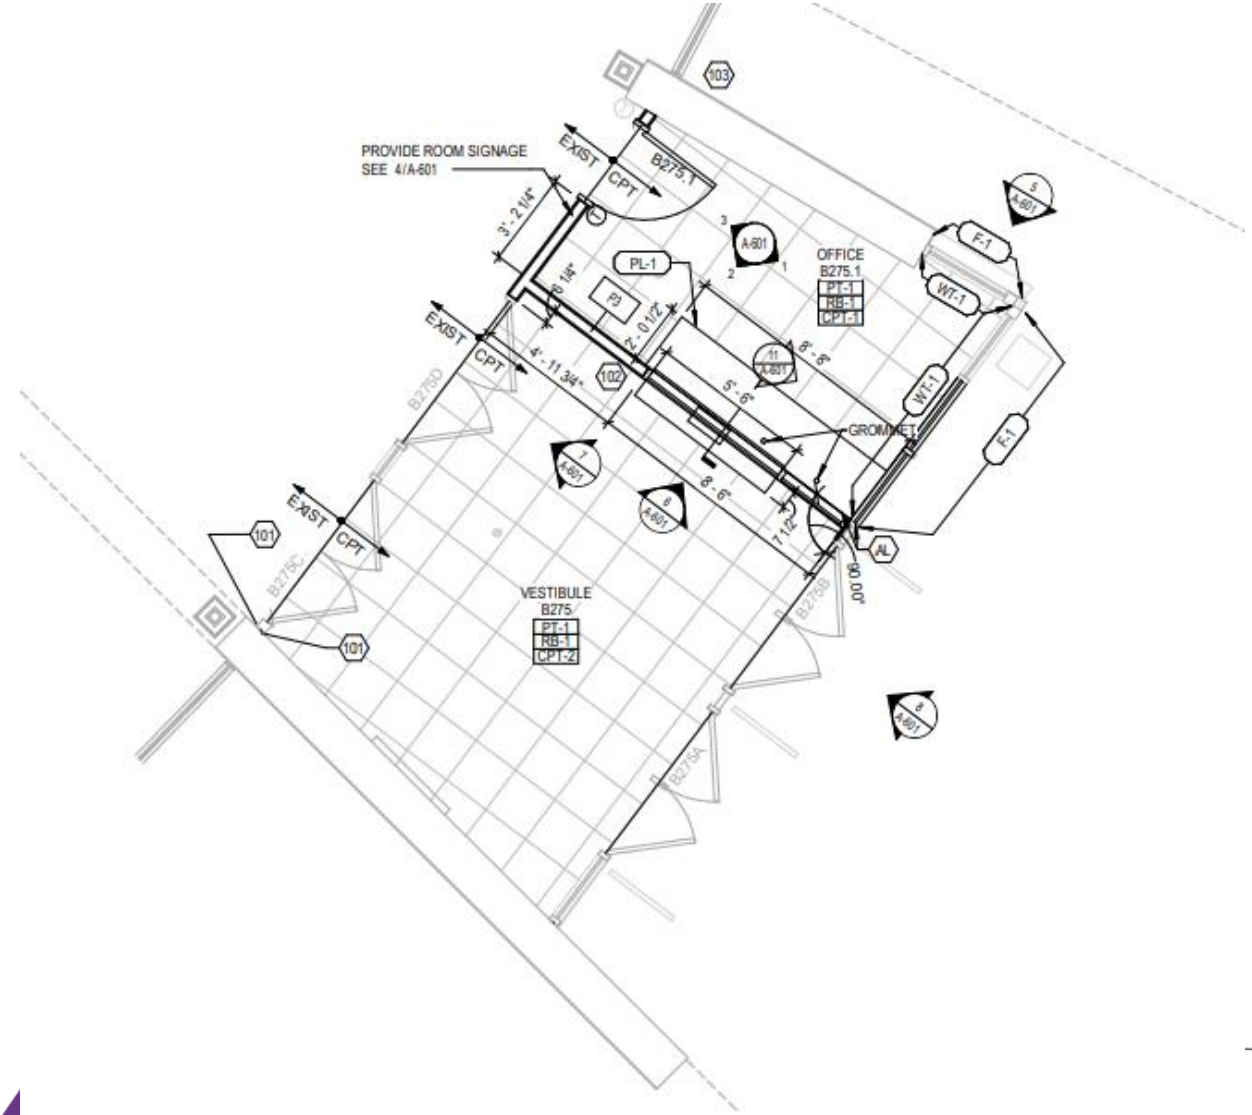

JEFFCO PUBLIC SCHOOLS

Blue Heron ES – Fire Alarm Upgrade

TLH – Odin Electric

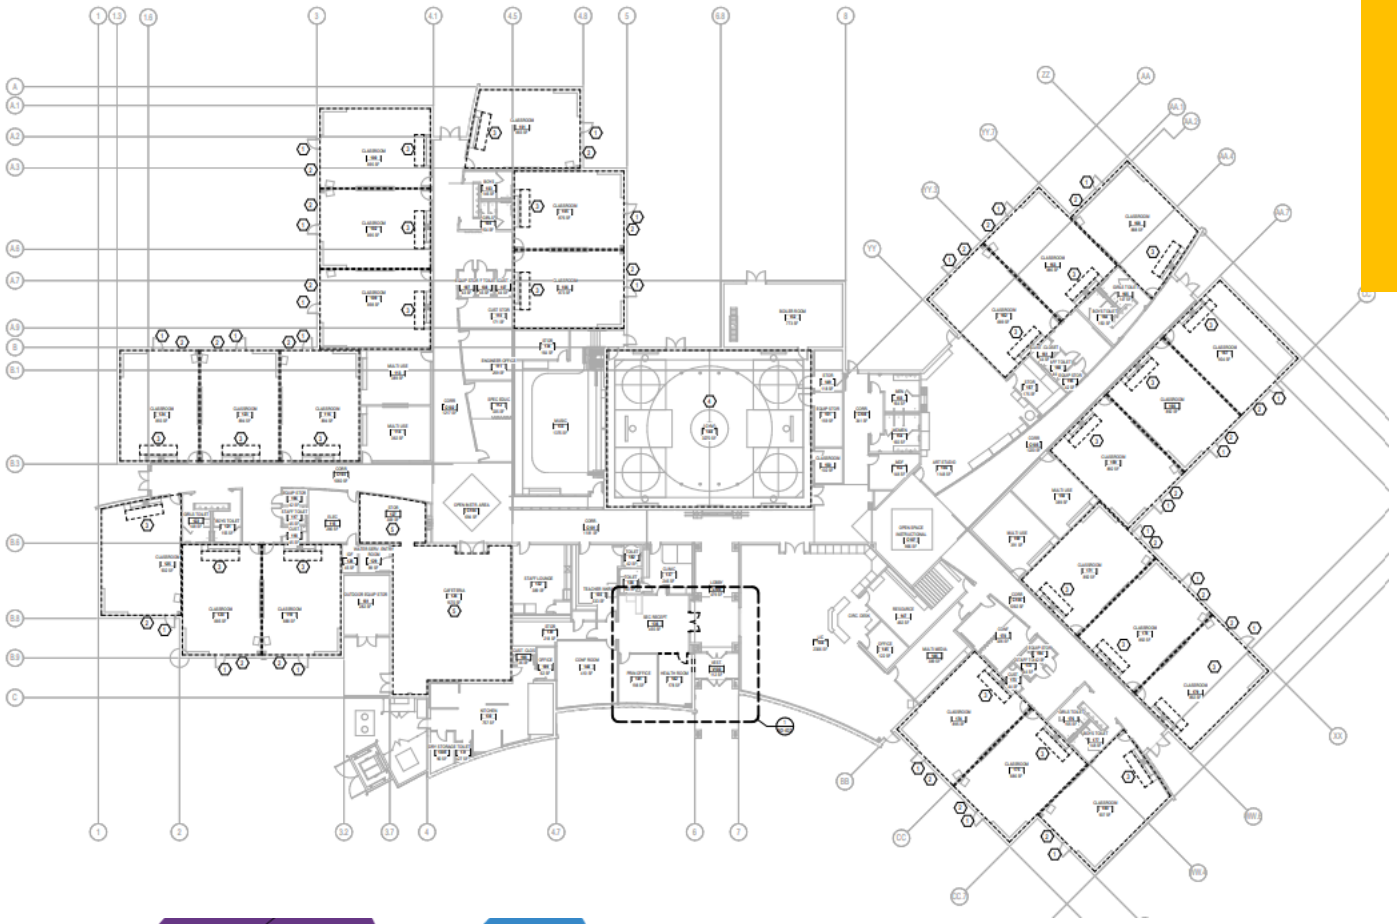

Bid
$247,437


Budget
$268,288

$ 20,851
Below Budget

JEFFCO PUBLIC SCHOOLS

Dakota Ridge HS – Chiller

Columbine – US Engineering

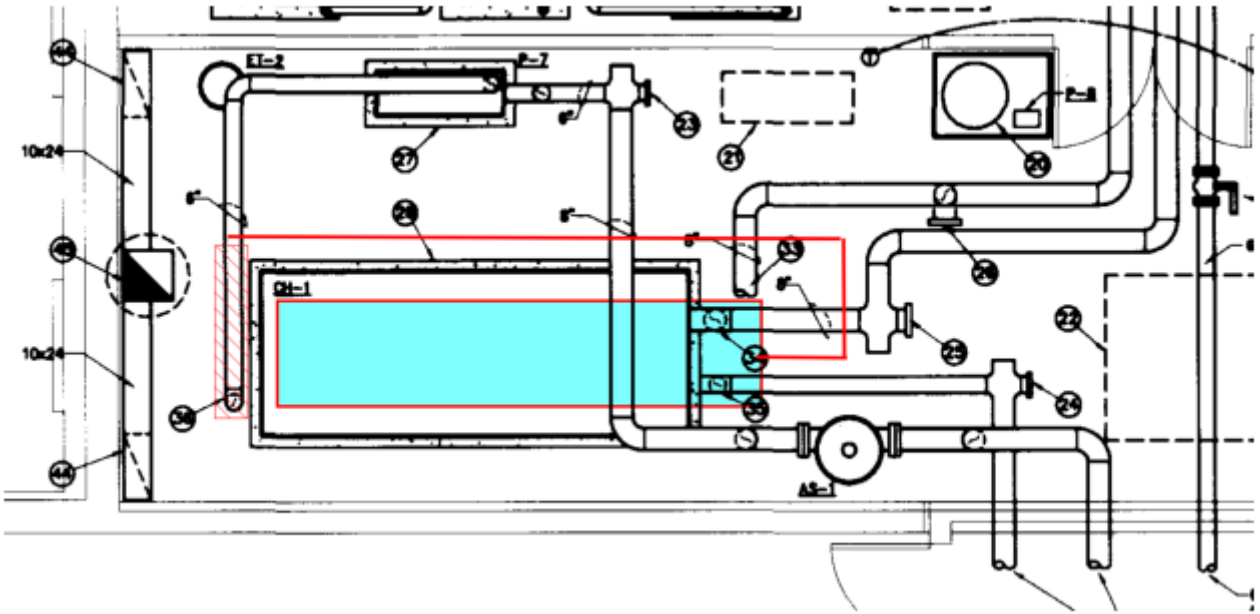

Bid
$978,165

Budget
$798,250


$179,915
Above Budget

JEFFCO PUBLIC SCHOOLS

Alameda HS – Gym Roof & Mechanical

Cator Ruma - TBD

Bids December 5

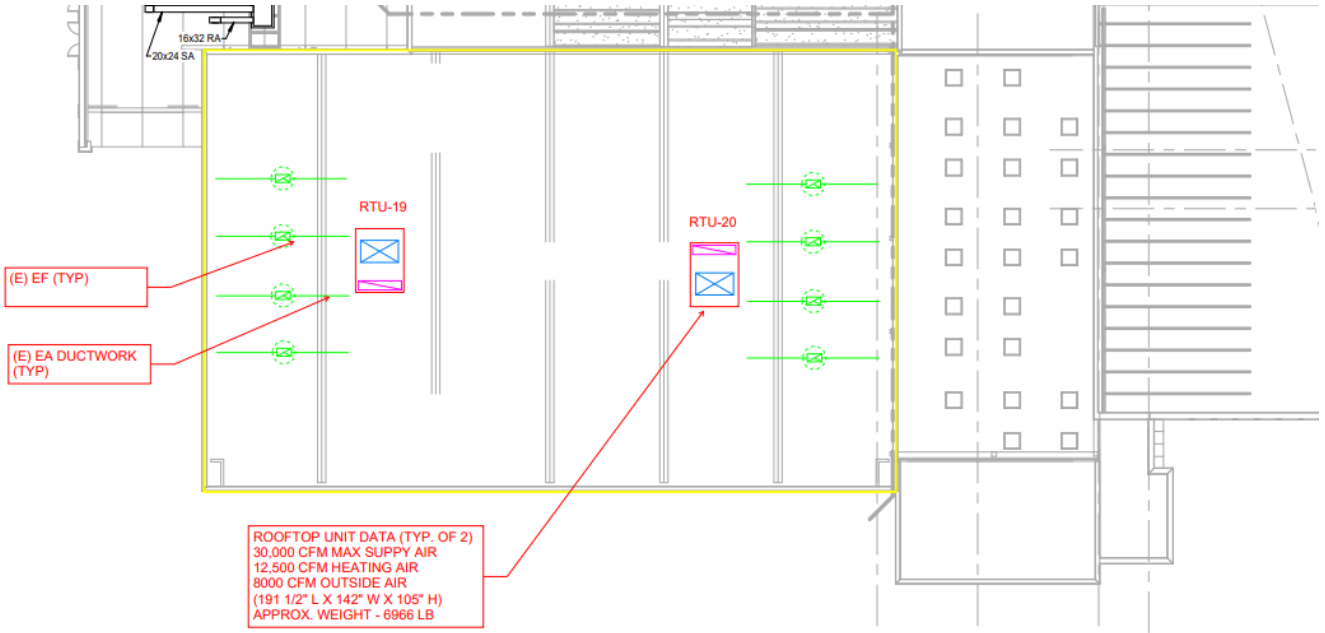

OPTION 1: (2) 30K CFM ROOFTOP UNITS

MECHANICAL ROOF PLAN
SCALE: 1" = 20'-0"

JEFFCO PUBLIC SCHOOLS

RVHS – Paving

JVA - TBD



Bids
December 17

JEFFCO PUBLIC SCHOOLS

District Wide – Roofing


Bids December


Evergreen HS gym, Jefferson HS (repair), Jeffco stadium east side press box (repair)
Jeffco driver training, Lakewood HS (repair)


SR+dk - TBD





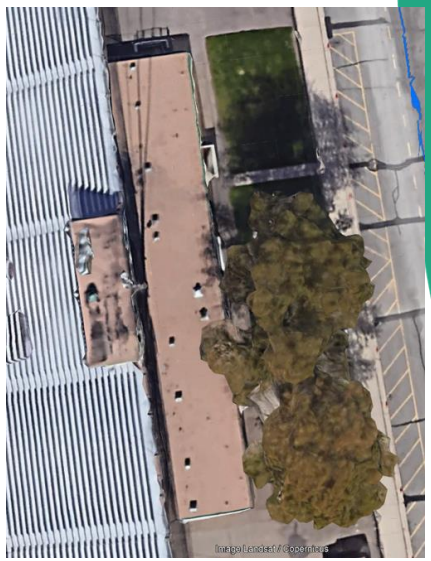



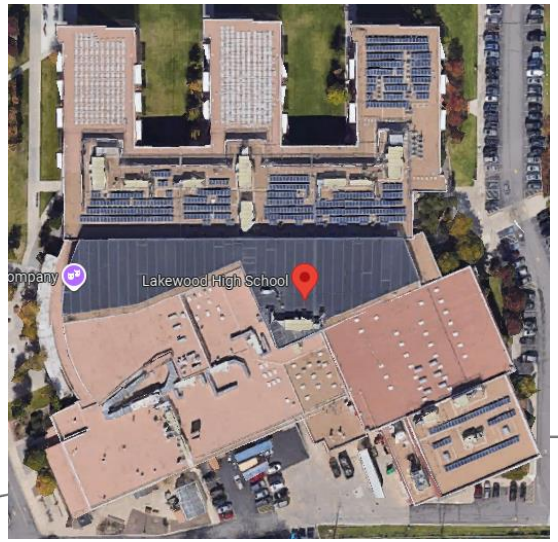



JEFFCO PUBLIC SCHOOLS

Wheat Ridge HS Phase II


Construction Documents

Eidos – GTC

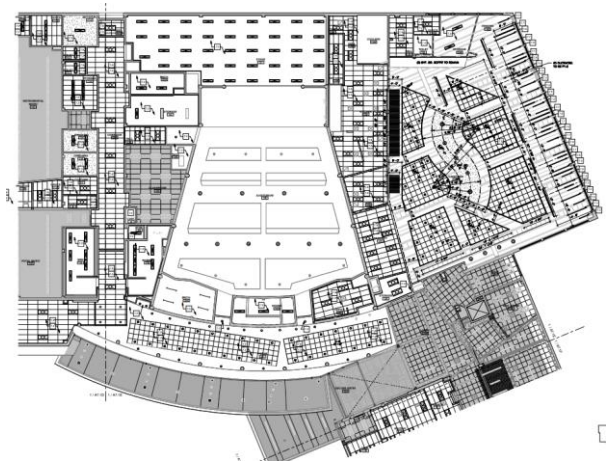


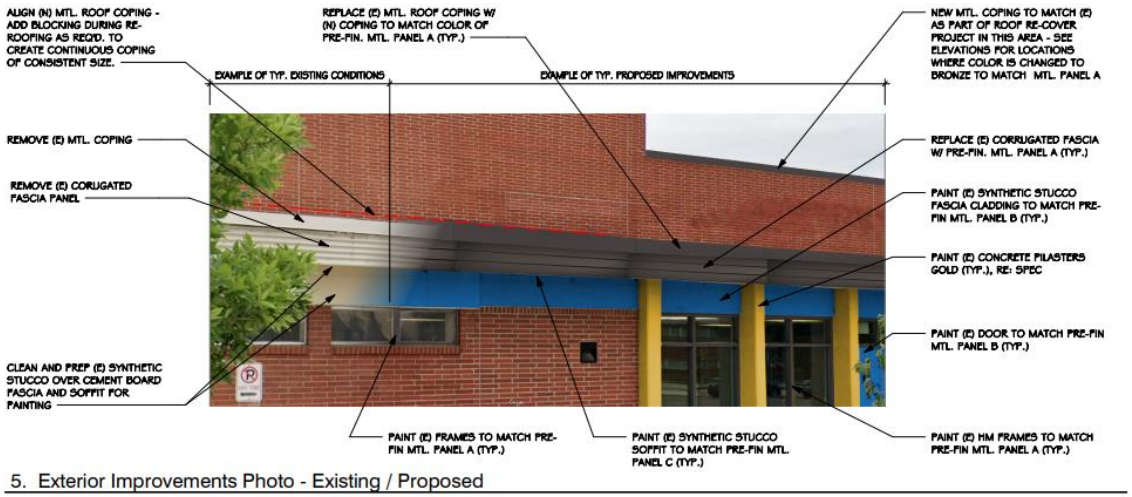

5. Exterior Improvements Photo - Existing / Proposed

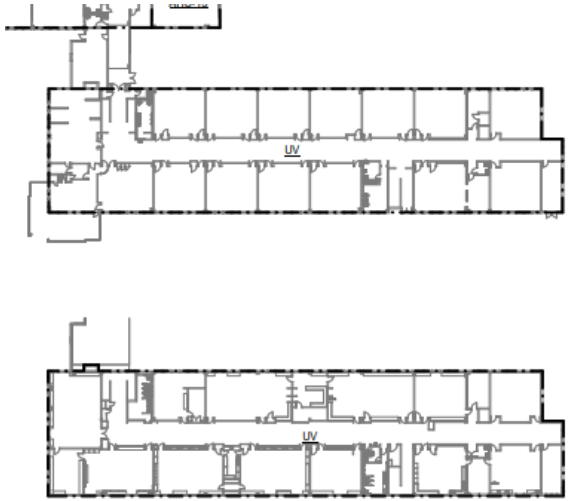


UPPER LEVEL HVAC ZONING PLAN

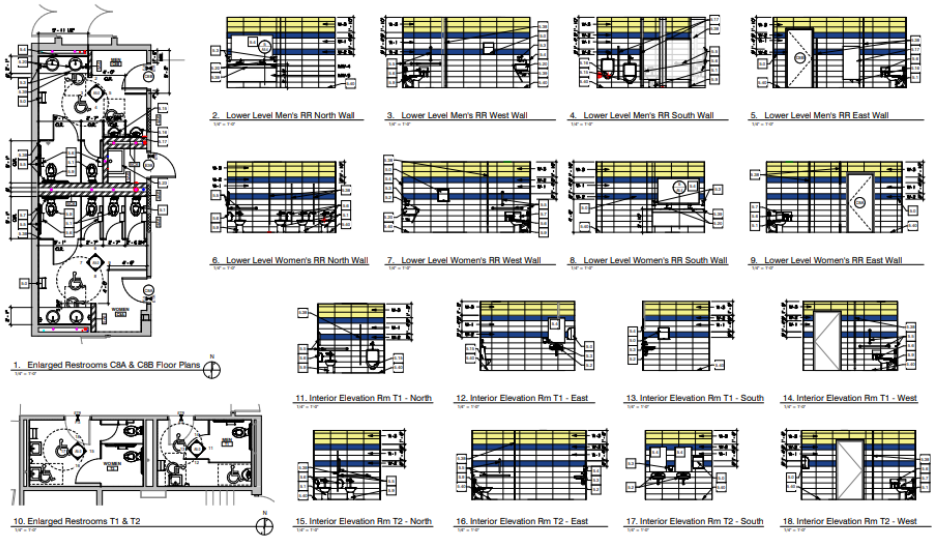

West Woods – RTU Repairs
Equipment Failure

Construction Documents

Columbine - TBD

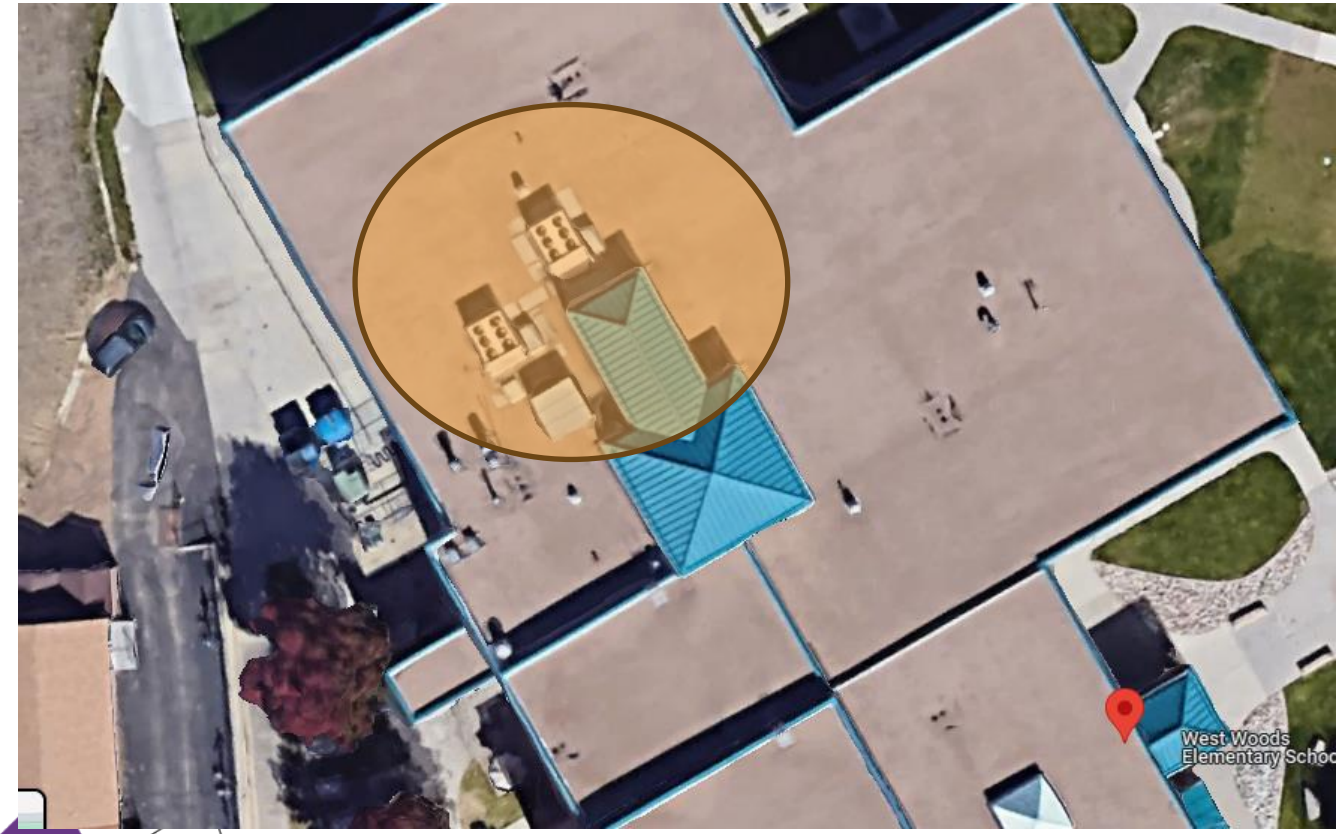

JEFFCO PUBLIC SCHOOLS

Edgewater ES Playground

City of Edgewater & Recreation Plus

Schematic Design



JEFFCO PUBLIC SCHOOLS

District Wide – Bleachers
GMHS & Chatfield

Solicitation




JEFFCO PUBLIC SCHOOLS

West Jefferson MS – Secure Entry

Design Development

Eidos - TBD

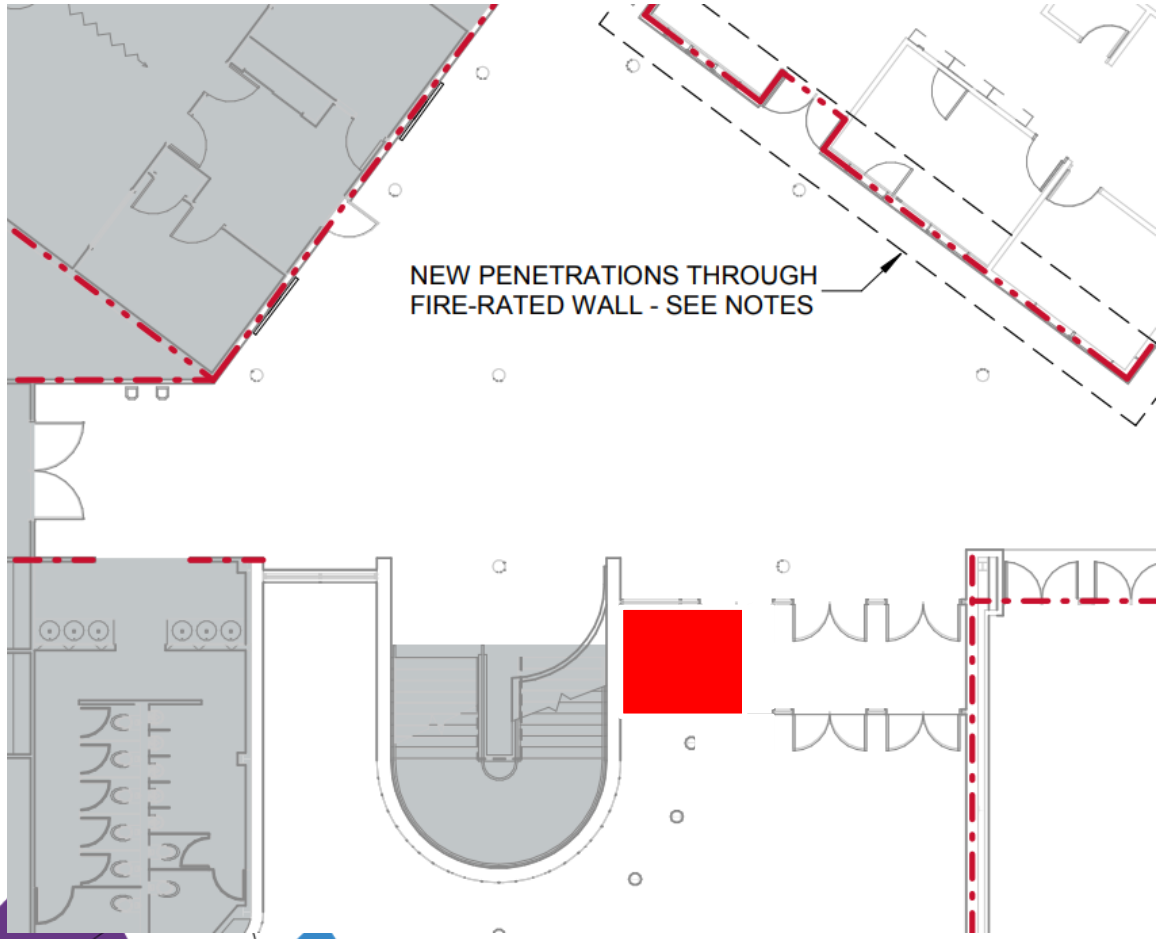


JEFFCO PUBLIC SCHOOLS

Devinny Retaining Wall wall failure

JVA – TBD

Construction Documents

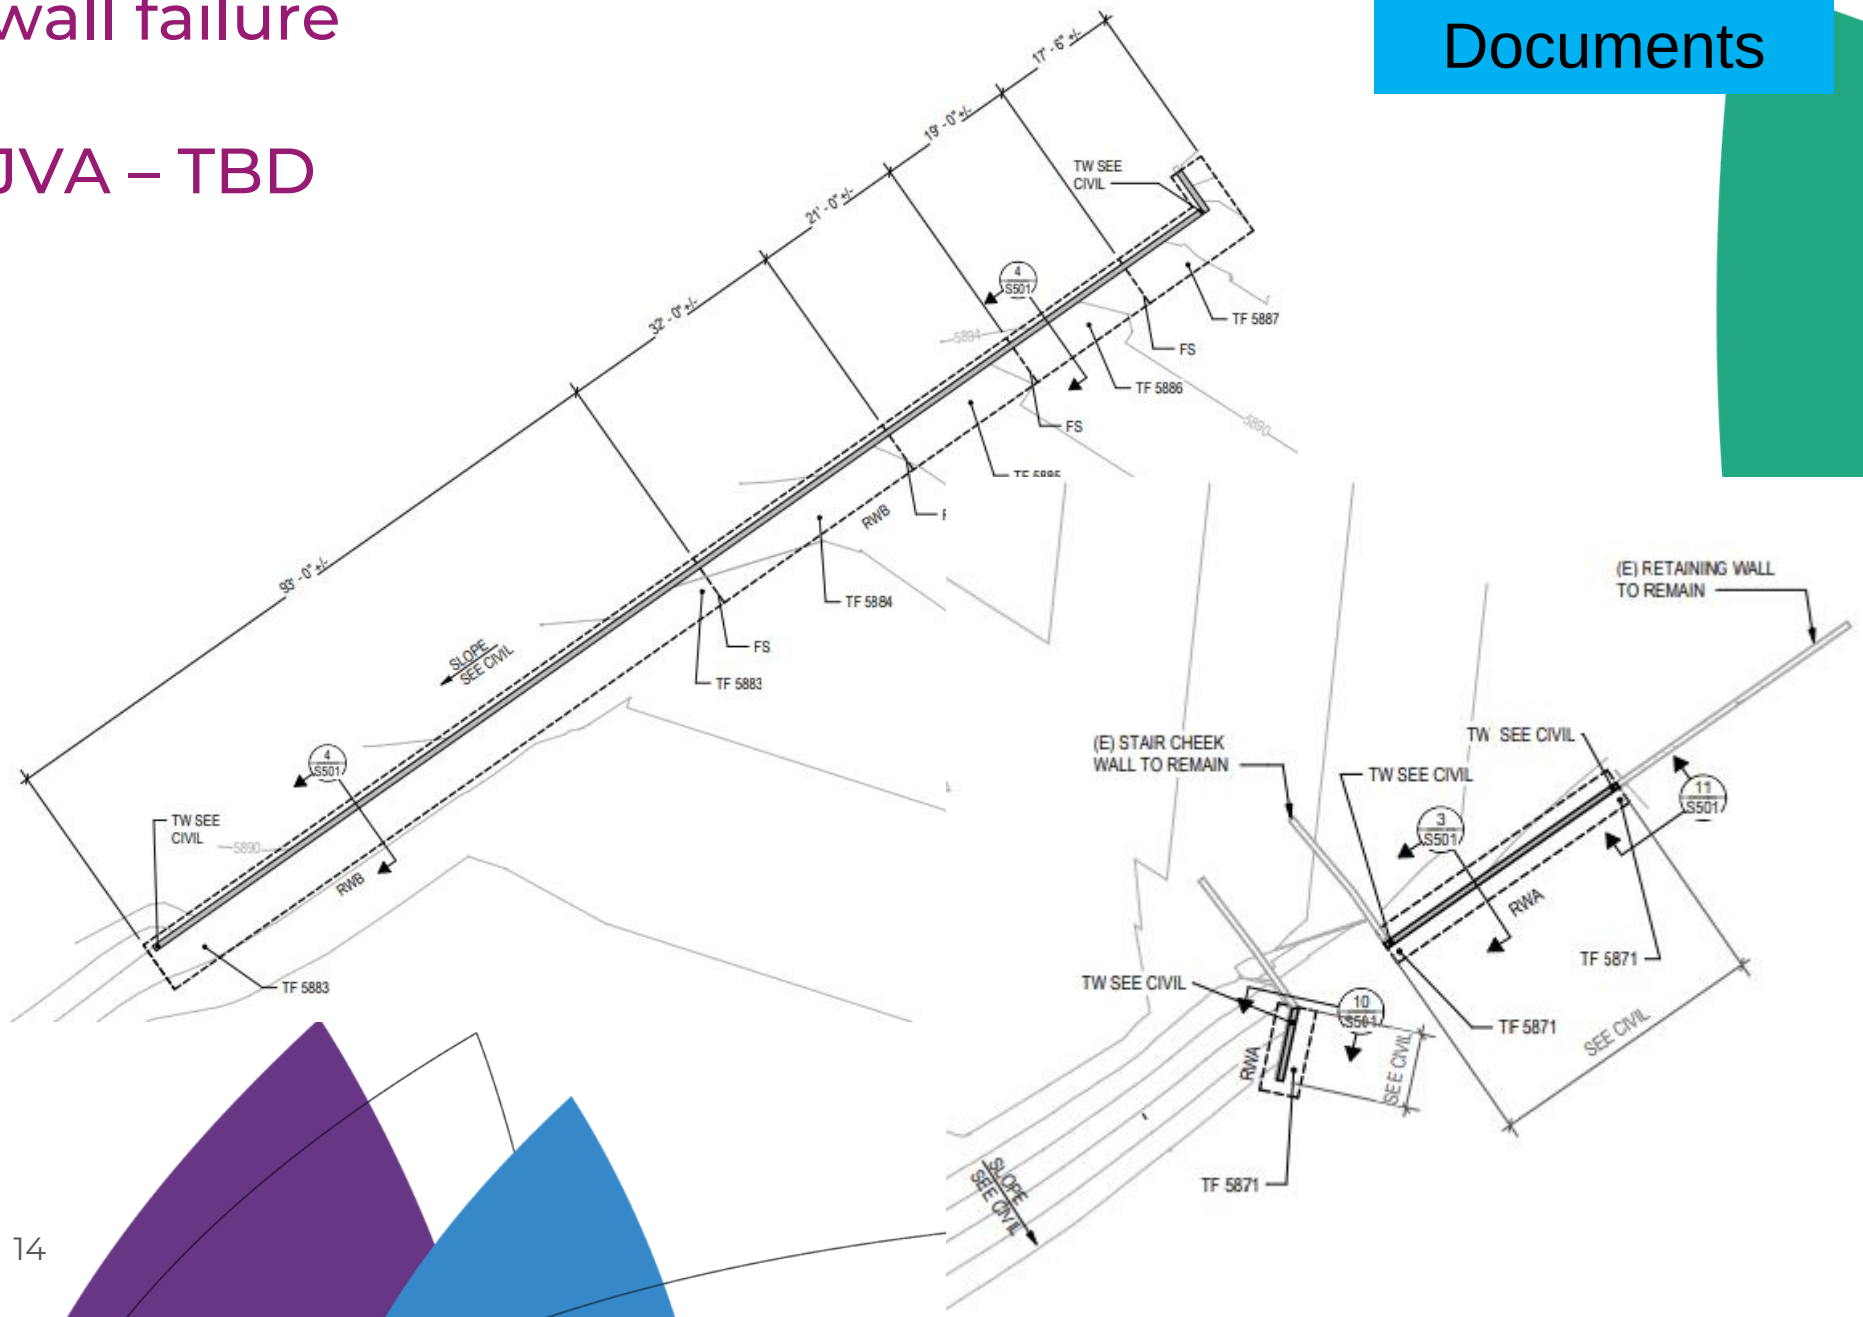

Columbine Hills – RTU-3 Replacement Equipment Failure

Schematic Design

IMEG - TBD

IMC 2021 VENTILATION RATE PROCEDURE CALCULATIONS - EXISTING UNIT EVALUATION

Unit: RTU-3 — **Existing Air Handling Unit % Outside Air (NOTE 3) : 13%** — **IEBC EVALUATION**

UNIT	ROOM NUMBER	ROOM NAME	ZONE TYPE	AREA SQ FT	OCCUPANT OUTDOOR AIRFLOW RATE CFM/PER	AREA OUTDOOR AIRFLOW RATE CFM/SQ FT	OCCUPANT DENSITY PEOPLE PER 1000 SQ FT	OCCUPANT QUANTITY	OVER-VENTILATION PERCENTAGE	BREATHING ZONE OUTDOOR AIRFLOW RATE CFM	TABLE 6-2 ZONE AIR DISTRIBUTION EFFECTIVENESS (Ez)	TOTAL SUPPLY AIR TO ZONE AT CONDITION ANALYZED CFM - NOTE 1	ZONE VENTILATION EFFICIENCY (Evz)	SYSTEM VENTILATION EFFICIENCY NOTE 2 (Ev)	ACTUAL OSA CFM REQUIRED AT UNIT FOR ZONE	MINIMUM PERCENTAGE AIRFLOW AT UNIT	MINIMUM OUTSIDE AIRFLOW AT UNIT AT UNIT FOR SCOPE	IEBC OUTDOOR AIR REQUIRED NOTE 4	MEETS REQUIREMENTS OF IEBC NOTE 4
RTU-3	137	CLINIC RR	Corridors	88	0.0	0.06	0	0	0%	5	0.8	50	1.01	0.83	6	-	-	0	Yes
	135	PRINCIPAL	Office space	225	5.0	0.06	5	4	0%	34	0.8	360	1.03	0.83	40	-	-	20	Yes
	138	CLINIC	Office space	236	5.0	0.06	5	3	0%	29	0.8	150	0.90	0.83	35	-	-	15	Yes
	139B	RECEPTIONIST & SECRETARY	Office space	335	5.0	0.06	5	5	0%	45	0.8	240	0.91	0.83	54	-	-	25	Yes
	136	CONFERENCE	Conference/meeting	186	5.0	0.06	50	8	0%	51	0.8	380	0.97	0.83	62	-	-	40	Yes
	141	STORAGE	Storage rooms	105	0.0	0.12	0	0	0%	13	0.8	50	0.83	0.83	15	-	-	0	Yes
	A359	OFFICE	Office space	95	5.0	0.06	5	2	0%	16	1.0	120	1.01	0.83	19	-	-	10	Yes
RTU-3	TOTALS FOR SCOPE OF WORK AREA											1350	-	0.83	233	17%	233		


SPECIFIC NOTES:

1. TOTAL SUPPLY AIR AT CONDITION ANALYZED USES THE MAXIMUM AIRFLOW PROVIDED TO THE ZONE DURING THE HEATING OR COOLING MODE, WHICHEVER IS THE CURRENT CONDITION BEING ANALYZED.
2. AS DETERMINED USING THE ASHRAE 62.1-2019 "62 MZ Calc" SPREADSHEET. SYSTEM VENTILATION EFFICIENCY IS EQUAL TO THE LOWEST ZONE VENTILATION EFFICIENCY OF ALL ROOMS SERVED BY THE UNIT AREA UNDER THE CURRENT SCOPE OF WORK.
3. EXISTING AIR HANDLING UNIT % OUTSIDE AIR PER THE BUILDING/PROPERTY MANAGER.
4. CALCULATIONS SHOW COMPLIANCE WITH INTERNATIONAL EXISTING BUILDING CODE (IEBC) SECTION 809 MECHANICAL ALTERATIONS WHICH ALLOW FOR 5 CFM/PERSON IN EXISTING SPACES.
5. OCCUPANT QUANTITY MAY VARY FROM OCCUPANT DENSITY FROM IMC. IN THOSE CASES OCCUPANT QUANTITY IS ADJUSTED TO MEET DATA PROVIDED BY THE CLIENT. THIS IS ACCEPTABLE PER IMC 403.3 EXCEPTION. OCCUPANCY RATES GREATER THAN CODE NOTED WITH A BOLD UNDERLINE. OCCUPANCY RATES LESS THAN CODE NOTED WITH A BOLD DOUBLE UNDERLINE.

TOTAL - Unit Outside Airflow Balance Setpoint [cfm], Note 3	270
TOTAL - Unit Supply Airflow Balance Setpoint [cfm], Note 3	2100
Scope - Percentage of Unit Flow	64.29%
Scope Associated - Unit Outside Airflow Balance Setpoint [cfm]	174
Unit Meets ASHRAE 62.1 Requirements	**No**

JEFFCO PUBLIC SCHOOLS

FF&E



Drake MS	FF&E
Normandy ES	FF&E
Pennington ES	FF&E
Secrest ES	FF&E
Swanson ES	FF&E
Ute Meadows ES	FF&E
Van Arsdale ES	FF&E
Warder ES	FF&E
Westgate ES	FF&E
West Woods ES	FF&E

JEFFCO PUBLIC SCHOOLS

Small Projects - 30 Day Activity

South Artic Areas	Central / Mountain Artic Areas	North Artic Areas
Chatfield Columbine Dakota Ridge Alameda Bear Creek	Conifer Evergreen Golden Green Mountain Jefferson Lakewood	Arvada Arvada West Pomona Ralston Valley Standley Lake Wheat Ridge
+27 Requests	+13 Requests	+21 Requests

JEFFCO PUBLIC SCHOOLS

Next Meeting 12-19-24
