JACKSON
PUBLIC SCHOOLS

Transforming lives through excellent education

JPS Board of Trustees Bond Update

1.7.2020

JPS Bond Construction Program Facts:

Bond Program Phase I Schools

High Schools

- Callaway High School*
- Forest Hill High School*
- Jim Hill High School*
- Lanier High School
- Murrah High School
- Provine High School*
- Wingfield High School*

Middle Schools

- Bailey APAC Middle School*
- Hardy Middle School

- **Requesting Clearance Approval From MDE**

JPS Bond Construction Program Facts:

Bond Program Phase I Schools

Elementary Schools

- Boyd Elementary School*
- Green Elementary School
- Wilkins Elementary School*
- Van Winkle Elementary School*

Other Academic Facilities

- Career Development Center
- Capital City Alternative School
- Performing Arts Center
- JROTC

* Mississippi Department of Education Corrective Action Plan (CAP)

- **Requesting Clearance Approval From MDE**

Projects Completed to Date

- 42 -

(42 – Total projects completed to date including 12 projects completed since December 3, 2019 Board meeting update)

School	Project
Green Elementary	27 spaces added for employee parking.
Wilkins Elementary	Front entrance and walkway were repaired to complete the requirements of the Mississippi Department of Education ‘s Corrective Action Plan (CAP). Handicap ramp was repaired to meet ADA requirements.
Hardy Middle	Drainage pipe scanned in preparation for site drainage improvements in the courtyard and exterior of the school.

Projects Completed to Date

School	Project
Callaway High	Science lab decommissioned to complete the requirements of the Mississippi Department of Education's Corrective Action Plan.
Callaway High	Phase I of exterior improvements completed which included building pressure washing in preparation for building façade upgrade.
Callaway High	Sewer line replaced in preparation of restroom renovations.
Callaway High	Courtyard fencing replaced to provide a more secured environment between buildings "B" and "C."
Forest Hill High	Science lab decommissioned to complete the requirements of the Mississippi Department of Education's Corrective Action Plan.
Forest Hill High	Phase I of parking lot improvements completed. Phase II to be completed by Summer 2020.
Forest Hill High	Sewer line replaced in preparation of restroom renovations.
Jim Hill High	Phase I of parking lot improvements completed. Phase II to be completed by Summer 2020.
Jim Hill High	Phase I of exterior and interior improvements were completed.

Projects Completed to Date

School	Project
Provine High	Science lab decommissioned to complete the requirements of the Mississippi Department of Education's Corrective Action Plan.
Provine High	Drainage pipe scanned in preparation of drainage and plumbing repairs underneath the building.
Wingfield High	Science lab decommissioned to complete the requirements of the Mississippi Department of Education's Corrective Action Plan.
Hardy Middle	Courtyard drainage improvements were completed.
Obama Magnet	Parking lot improvements were completed.
Forest Hill High	Building Signage has been completed.
Timberlawn Elementary	Parking lot improvements Phase I have been completed.
Siwell Middle	Exterior lighting upgraded to LED lighting has been completed.
Provine High	Exterior lighting upgraded to LED lighting Phase I of II has been completed.

Projects Completed to Date

School	Project
Wingfield High	Exterior lighting upgraded to LED lighting has been completed.
Brinkley Middle	Exterior lighting upgraded to LED lighting has bee completed.
Wingfield High	2nd Floor restroom upgrades have been completed.
Murrah High	Translucent panel cleaning Phase I of II has been completed.
Murrah High	Exterior door replacement has been completed.
Provine High	Gymnasium roof drain rerouting in preparation for gymnasium and locker room renovations has been completed.
CDC	Carpet removal has been completed.
Provine High	Exterior lighting upgraded to LED lighting Phase II of II has been completed.
Van Winkle Elementary	Interior painting has been completed.

Projects Completed to Date

(Since December 3, 2019 Bond Update)

School	Project
Van Winkle Elementary	Electrical upgrades have been completed.
Van Winkle Elementary	Upgrade exterior lighting Phase I of II has been completed.
Van Winkle Elementary	Interior door repairs and replacement have been completed.
Obama Magnet	Door canopies at auditorium exits have been completed.
Obama Magnet	Playground canopy has been completed.
Boyd Elementary	Upgrade exterior and interior lighting Phase I of II has been completed.
CDC	Repair building entrance brick pavers has been completed.
Chastain Middle	Exterior lighting upgrades have been completed.

Projects Completed to Date

(Since December 3, 2019 Bond Update)

School	Project
Forest Hill High	Exterior lighting upgrades (Phase I) have been completed.
Hardy Middle	Removal of carpet in office has been completed.
Lanier High	Sewer line repair in preparation for restroom renovations has been completed.
Jim Hill	Electrical upgrade has been completed.

Projects Under Construction (21)

School	Project	Completion Date
Spann	Restroom upgrades	**Revised** January 30, 2020
Obama Magnet Elementary	Multi-purpose room renovations	March 30, 2020
Callaway High	Gym floor replacement	TBD
Callaway High	Gym bleacher replacement	Bleachers arrive on December 5, 2019 to be stored until gym floor is completed
Callaway High	Exterior lighting upgrades	March 30, 2020
Powell Middle	Exterior lighting upgrades	January 15, 2020
Boyd Elementary	Window replacement & library renovations	Construction Starts Spring Break March 7 - 13, 2020

Projects Under Construction

School	Project	Completion Date
CDC	Exterior lighting upgrades	**Revised** January 30, 2020
Timberlawn Elementary	Parking lot improvement Phase II	**Revised** February 3, 2020
Van Winkle Elementary	Improve back parking lot surface (Bus staging)	February 28, 2020
Van Winkle Elementary	Interior and exterior lighting improvements	February 28, 2020
Chastain Middle	Site drainage underneath building investigation	**Revised** February 28, 2020
Chastain Middle	North egress portico and walkway repairs	January 30, 2020
Brinkley Middle	HVAC upgrades Phase I and II of III	February 28, 2020
Casey Elementary	Restroom upgrades	**Revised** March 31, 2020

Projects Under Construction

School	Project	Completion Date
Jim Hill High	Exterior lighting upgrades	**Revised** February 28, 2020
Northwest Middle	Exterior lighting upgrades	January 15, 2020
Forest Hill High	Repair gymnasium floor	June 30, 2020
Forest Hill High	Heating, ventilation, and air conditioning system (HVAC) in gymnasium	June 30, 2020
Forest Hill High	Restroom renovations	June 30, 2020
Hardy Middle	Site drainage in courtyard	June 30, 2020

Projects Under Construction

Please Note that during construction, adjustments may take place i.e., revised completion dates and other factors due to latent conditions, weather conditions, availability of materials, and industry market changes and increases.

Projects Scheduled to Bid (20)

School	Lanier High	Hardy Middle	Green Elementary
Architect	**JBHM**	**Duvall Decker**	**Eley Guild Hardy**
Project	Window Restoration	Windows, Infills and Exterior Doors	Restroom & Classroom Renovations, and Exterior Door Replacement, and Front Entry Improvement
	Date	Date	Date
Bid Ad #1	TBD	November 22, 2019	December 10, 2019
Bid Ad #2	TBD	November 29, 2019	December 17, 2019
Bid Opening	**Will Require Rebidding** (Previous Date November 8, 2019)	**December 20, 2019 (New Bid Date)**	**January 24, 2020**
Board Approval	TBD	January 21, 2020	March 3, 2020

Projects Scheduled to Bid

School	Callaway High	Provine High	Murrah High
Architect	**Dale Partners**	**Duvall Decker**	**M3A Architecture**
Project	Site, Roof, HVAC, Restroom Renovations, and Interior	Restroom and Locker Room Renovations	Restroom Renovations
	Date	Date	Date
Bid Ad #1	TBD	TBD	December 16, 2019
Bid Ad #2	TBD	TBD	December 23, 2019
Bid Opening	**Will Require Rebidding** (Previous Date November 11, 2019)	**Will Require Rebidding** (Previous Date December 10, 2019)	**January 29, 2020**
Board Approval	TBD	TBD	February 18, 2020

Projects Scheduled to Bid

School	Jim Hill High	Lanier High	Callaway High
Architect	**Durrell Design Group, LLC**	**Durrell Designer Group, LLC**	**Dale Partners**
Project	Restroom Renovations	Restroom Renovations	Reroof Gymnasium and Gymnasium Floor Replacement
	Date	Date	Date
Bid Ad #1	December 2, 2019	December 2, 2019	December 12, 2019
Bid Ad #2	December 9, 2019	December 9, 2019	December 19, 2019
Bid Opening	**January 14, 2020** **Extended Bid Date** (Previous Date January 7, 2020)	**January 14, 2020** **Extended New Bid Date** (Previous Date January 7, 2020)	**January 16, 2020**
Board Approval	February 18, 2020	February 18, 2020	February 18, 2020

JPS Bond Construction Program
Phase II Schools

12 Elementary Schools	6 Middle Schools
Baker Elementary	Brinkley Middle
Bates Elementary	Cardozo Middle
Casey Elementary	Chastain Middle
John Hopkins Elementary	Northwest Middle
Johnson Elementary	Powell Middle
Oak Forest Elementary	Whitten Middle
Pecan Park Elementary	
Power APAC Elementary	
Raines Elementary	
Spann Elementary	
Timberlawn Elementary	
Watkins Elementary	




CDC Front Entrance Brick Pavers Removal







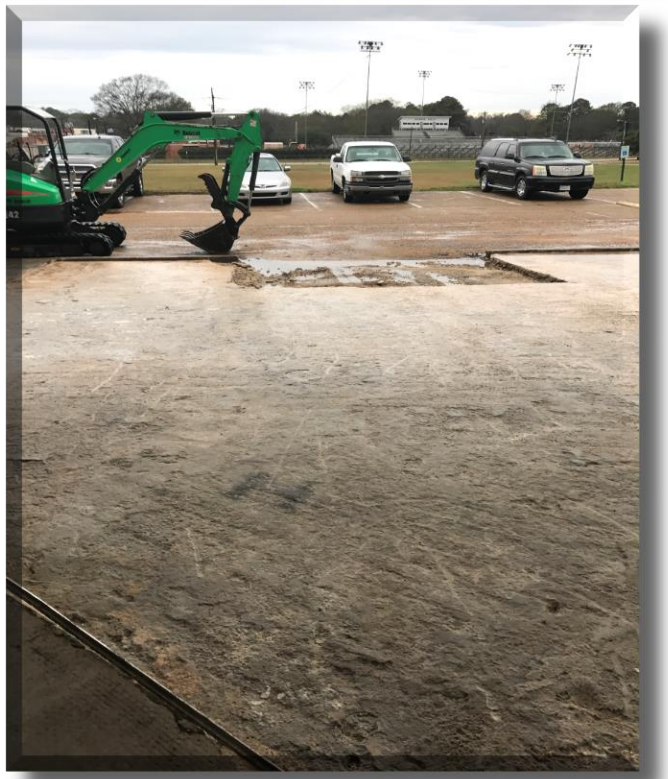



CDC Carpet Removal











Obama Magnet Door Canopies and Playground Canopy











JACKSON
PUBLIC SCHOOLS

Transforming lives through excellent education

Thank You

We Welcome Any Questions
