JACKSON
PUBLIC SCHOOLS

Transforming lives through excellent education

JPS Board of Trustees Bond Update

12.3.2019

JPS Bond Construction Program Facts:

Bond Program Phase I Schools

High Schools

- Callaway High School*
- Forest Hill High School*
- Jim Hill High School*
- Lanier High School
- Murrah High School
- Provine High School*
- Wingfield High School*

Middle Schools

- Bailey APAC Middle School*
- Hardy Middle School

- **Requesting Clearance Approval From MDE**

JPS Bond Construction Program Facts:

Bond Program Phase I Schools

Elementary Schools

- Boyd Elementary School*
- Green Elementary School
- Wilkins Elementary School*
- Van Winkle Elementary School*

Other Academic Facilities

- Career Development Center
- Capital City Alternative School
- Performing Arts Center
- JROTC

* Mississippi Department of Education Corrective Action Plan (CAP)

- **Requesting Clearance Approval From MDE**

Projects Completed to Date (31)

School	Project	Vendor
Green Elementary	27 spaces added for employee parking.	R & L Unlimited (MBE)
Wilkins Elementary	Front entrance and walkway were repaired to complete the requirements of the Mississippi Department of Education ‘s Corrective Action Plan (CAP). Handicap ramp was repaired to meet ADA requirements.	Heritage Landscape (MBE)
Hardy Middle	Drainage pipe scanned in preparation for site drainage improvements in the courtyard and exterior of the school.	J. L. Roberts Plumbing
Callaway High	Science lab decommissioned to complete the requirements of the Mississippi Department of Education’s Corrective Action Plan.	Advance Environmental Consultants (MBE)
Callaway High	Phase I of exterior improvements completed which included building pressure washing in preparation for building façade upgrade.	Home and Business Services (MBE)
Callaway High	Sewer line replaced in preparation of restroom renovations.	Buford Plumbing
Callaway High	Courtyard fencing replaced to provide a more secured environment between buildings “B” and “C.”	Calhoun Fencing (MBE)

Projects Completed to Date

School	Project	Vendor
Forest Hill High	Science lab decommissioned to complete the requirements of the Mississippi Department of Education's Corrective Action Plan.	Advance Environmental Consultants (MBE)
Forest Hill High	Phase I of parking lot improvements completed. Phase II to be completed by Summer 2020.	Four Seasons Enterprises, LLC (MBE)
Forest Hill High	Sewer line replaced in preparation of restroom renovations.	Buford Plumbing
Jim Hill High	Phase I of parking lot improvements completed. Phase II to be completed by Summer 2020.	R & L Unlimited (MBE)
Jim Hill High	Phase I of exterior and interior improvements were completed.	JPS
Provine High	Science lab decommissioned to complete the requirements of the Mississippi Department of Education's Corrective Action Plan.	Advance Environmental Consultants (MBE)
Provine High	Drainage pipe scanned in preparation of drainage and plumbing repairs underneath the building.	J. L. Roberts Plumbing
Wingfield High	Science lab decommissioned to complete the requirements of the Mississippi Department of Education's Corrective Action Plan.	Advance Environmental Consultants (MBE)

Projects Completed to Date

School	Project	Vendor
Hardy Middle	Courtyard drainage improvements were completed.	J. L. Roberts Plumbing
Obama Magnet	Parking lot improvements were completed.	R & L Unlimited (MBE)
Forest Hill High	Building Signage	Budget Signs
Timberlawn Elementary	Parking lot improvements	R & L Unlimited (MDE
Siwell Middle	Exterior lighting upgraded to LED lights	JPS Electrical Dept. Staff
Provine High	Exterior lighting upgraded to LED lights	JPS Electrical Dept. Staff
Wingfield High	Exterior lighting upgraded to LED lights	JPS Electrical Dept. Staff
Brinkley Middle	Exterior lighting upgraded to LED lights	JPS Electrical Dept. Staff
Wingfield High	2nd Floor restroom upgrades	Business and Office Konnextions (MDE)

Projects Completed to Date

School	Project	Vendor
Murrah High	Translucent panel cleaning – Phase I of II	Associated Architectural, Inc.
Murrah High	Exterior door replacement	Target Door and Supply
Provine High	Gymnasium roof drain rerouting in preparation for gymnasium and locker room renovations	McClain Plumbing
CDC	Carpet removal	Dixon Interiors (MBE)
Van Winkle Elementary	Interior painting	Conerly Construction
Provine High	Exterior lighting upgraded to LED lights – Phase I of II	JPS Electrical Dept. Staff
Obama Magnet	Door Canopies	Aluminum Contractors

Projects Scheduled to Start in December (20)

School	Project	Vendor	Completion Date
Spann	Restroom Upgrades	JPS Plumbing Dept. Staff and Contractor (TBD)	December 30, 2019
Obama Magnet Elementary	Playground Canopy	PO Issued to Business and Office Konnextions (MBE)	TBD - Waiting on completion of roof under construction
Obama Magnet Elementary	Multi-Purpose Room Renovations	PO Issued to Dixon Interior Finishing (MBE)	TBD - Waiting on completion of roof under construction
Callaway High	Gym Floor Replacement	Rebidding Phase	TBD
Callaway High	Gym Bleacher Replacement	Innovative Performance (MBE)	Bleachers arrive on December 5, 2019 to be stored until gym floor is completed
Powell Middle	Exterior Lighting Upgrades	JPS Electrical Dept. Staff and Contractor (TBD)	January 15, 2020

Projects Scheduled to Start in December

School	Project	Vendor	Completion Date
Boyd Elementary	Window Replacement & Library Renovations	Robertson Construction Contractors, LLC	Construction Starts Spring Break March 7 - 13, 2020
Callaway High	Exterior Lighting Upgrades	JPS Staff and Contractor (TBD)	January 15, 2020
CDC	Exterior Lighting Upgrades	JPS Staff	December 30, 2019
Timberlawn Elementary	Parking Lot Improvement II	R & L Unlimited (MBE)	**Revised** Completion - December 14, 2019
Van Winkle Elementary	Interior and Exterior Improvements	Conerly Construction, Inc.	February 28, 2020
Jim Hill High	Exterior Lighting Upgrades	JPS Electrical Dept. Staff	December 30, 2019

Projects Scheduled to Start in December

School	Project	Vendor	Completion Date
Boyd Elementary	Exterior Lighting Upgrades	JPS Electrical Dept. Staff and Contractor (TBD)	December 30, 2019
Chastain Middle	Site Drainage Underneath Building Investigation	JPS Plumbing Dept. Staff and Contractor (TBD)	December 30, 2019
Chastain Middle	Exterior Lighting Upgrades	JPS Electrical Dept. Staff and Contractor (TBD)	January 15, 2020
Chastain Middle	North Egress Portico and walkway Repairs	JPS Carpentry Dept. Staff and Contractor (TBD)	January 30, 2020
Brinkley Middle	HVAC Upgrades Phase I and II of III	Contractor (TBD)	February 28, 2020
Casey Elementary	Restroom Upgrades	JPS Plumbing Dept. Staff and Contractor (TBD)	January 30, 2020
Lanier High	Exterior Door Replacement Phase I of II	Contractor (TBD)	January 30, 2020
Northwest Middle	Exterior Lighting Upgrades	JPS Electrical Dept. Staff and Contractor (TBD)	January 15, 2020

Projects Scheduled to Bid (28)

Architect	JBHM	CDFL	CDFL	Eley Guild Hardy
School	**Lanier High**	**Forest Hill High**	**Forest Hill High**	**Green Elementary**
Project	Window Restoration	Coliseum Renovation	Restroom Renovations	Restroom & Classroom Renovations, Exterior Door Replacement, and Front Entry Improvement
	Date	Date	Date	Date
Bid Ad #1	October 10, 2019	October 24, 2019	October 29, 2019	December 10, 2019
Bid Ad #2	October 17, 2019	October 31, 2019	November 5, 2019	December 17, 2019
Bid Opening	**November 8, 2019 Will Require Rebidding**	**November 22, 2019**	**December 17, 2019**	**January 24, 2020**
Board Approval		December 17, 2019	January 7, 2020	March 3, 2020

Projects Scheduled to Bid

Architect	Dale Partners	Duvall Decker	Duvall Decker	M3A Architecture	M3A Architecture
School	**Callaway High**	**Hardy Middle**	**Provine High**	**South Jackson Field**	**Murrah High**
Project	Site, Roof, HVAC, Restroom Renovations, and Interior	Window, Infill and Exterior Doors	Restroom and Locker Room Renovations	Visitor Restrooms and Concession Stands	Restroom Renovations
	Date	Date	Date	Date	Date
Bid Ad #1	September 30, 2019	September 23, 2019	October 29, 2019	December 16, 2019	December 16 2019
Bid Ad #2	October 4 , 2019	September 30, 2019	November 5, 2019	December 23, 2019	December 23, 2019
Bid Opening	**November 11, 2019 Will Require Rebidding**	**October 23, 2019 Will Require Rebidding**	**December 10, 2019**	**January 29, 2019**	**January 29, 2020**
Board Approval	December 17, 2019		January 7, 2020	February 18, 2020	February 18, 2020

Projects Scheduled to Bid

Architect	Durrell Design Group, LLC	Durrell Designer Group, LLC	Eley Guild Hardy	Dale Partners
School	**Jim Hill High**	**Lanier High**	**Wingfield High**	**Callaway High**
Project	Restroom Renovations	Restroom Renovations	Building Entry Façade Upgrade	Reroof Gymnasium and Gymnasium Floor Replacement
	Date	Date	Date	Date
Bid Ad #1	December 2, 2019	December 2, 2019	December 9, 2019	December 12, 2019
Bid Ad #2	December 9, 2019	December 9, 2019	December 16, 2019	December 19, 2019
Bid Opening	**January 7, 2020**	**January 7, 2020**	**January 10, 2020**	**January 16, 2020**
Board Approval	February 18, 2020	February 18, 2020	February 18, 2020	February 18, 2020

JPS Bond Construction Program
Team Staffing Update

Jackson Public Schools Staff

- Executive Director of Facilities and Operations
- Interim Construction Director
- Bond Project Coordinator – Approved at the November 19 Board
- Bond Procurement Specialist – Approved at the November 5 Board
- Interim Architectural Designer – Position Being Advertised

Consulting Services

- Bond Staff Support – Engineering Firm Under Consideration

JPS Bond Construction Program
Phase II Schools

12 Elementary Schools	6 Middle Schools
Baker Elementary	Brinkley Middle
Bates Elementary	Cardozo Middle
Casey Elementary	Chastain Middle
John Hopkins Elementary	Northwest Middle
Johnson Elementary	Powell Middle
Oak Forest Elementary	Whitten Middle
Pecan Park Elementary	
Power APAC Elementary	
Raines Elementary	
Spann Elementary	
Timberlawn Elementary	
Watkins Elementary	












Murrah High Exterior Door Replacements



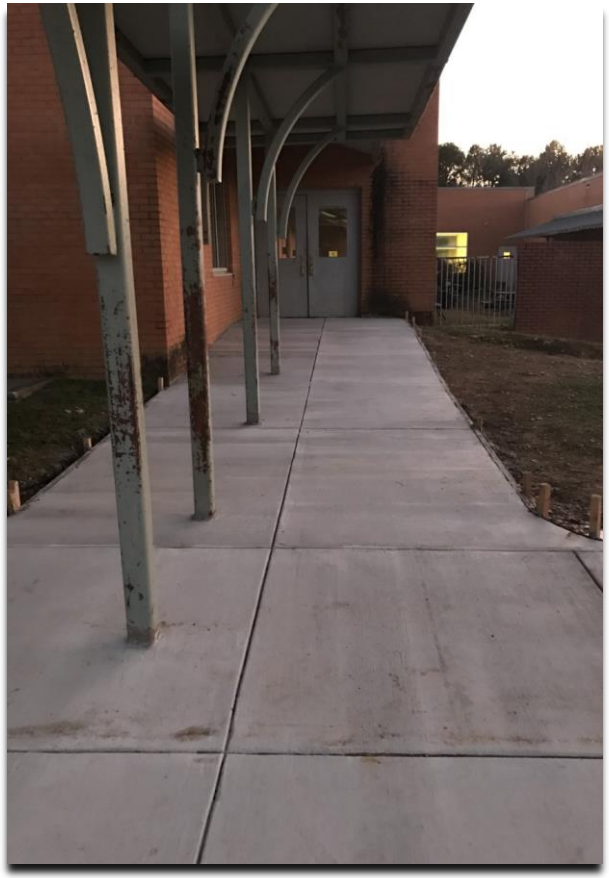

Van Winkle Site Improvements



JACKSON
PUBLIC SCHOOLS

Transforming lives through excellent education

Thank You

We Welcome Any Questions
