Market & Johnson
Adding Value to Everything We Do

ECASD North HS Media Center Alterations

 # 1

Week of: 6/2/2025

WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- M&J completed CMU wall opening demolition.
- Subs continued MEP demolition.
- M&J started floor demolition.
- M&J masons layed in openings.
- Cutting Edge completed saw cutting CMU wall openings.
- North High Schools last day was 6/6.

Upcoming Week

Market & Johnson to supervise and coordinate with trades.

- Subs to continue MEP demolition.
- M&J to continue floor demolition.
- Aerofoil to install structural steel members.
- Aerofoil to frame metal stud walls & HM frames.

Priority RFI's

- RFI #3: Electrical Panel BP-R Existing Conditions
- RFI #4: Ceiling & Wall Added Demolition

Priority Submittals

- Submittal #09 66 10-2 Revision 0: Terrazzo Patching
- Submittal #09 91 00-2 Revision 0: Painting - Sample
- Submittal #26 28 16-1 Revision 0: Enclosed Switches & Circuit Breaker

Project Manager:	Jordan Lieffring	(715) 579-0176	jlieffring@market-johnson.com
Superintendent:	Jeremy Hollister	(715) 579-7991	jhollister@market-johnson.com


Market & Johnson
Adding Value to Everything We Do

ECASD North HS Media Center Alterations

 # 1

Week of: 6/2/2025

Weekly Photos

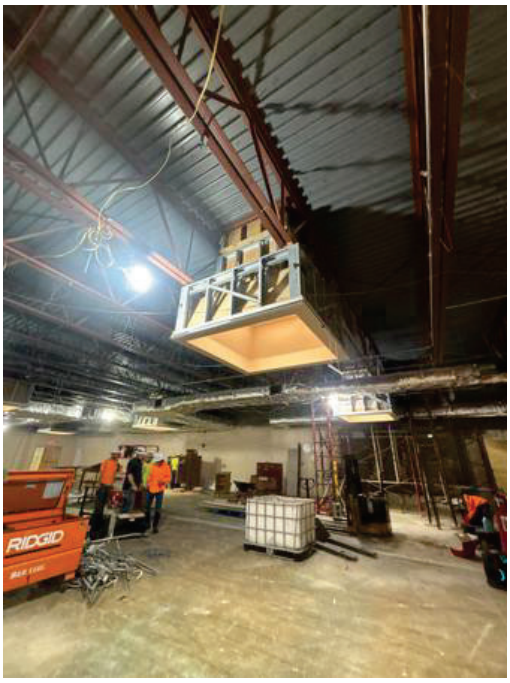




Market & Johnson
Adding Value to Everything We Do

ECASD North HS Media Center Alterations

 # 1

Week of: 6/2/2025



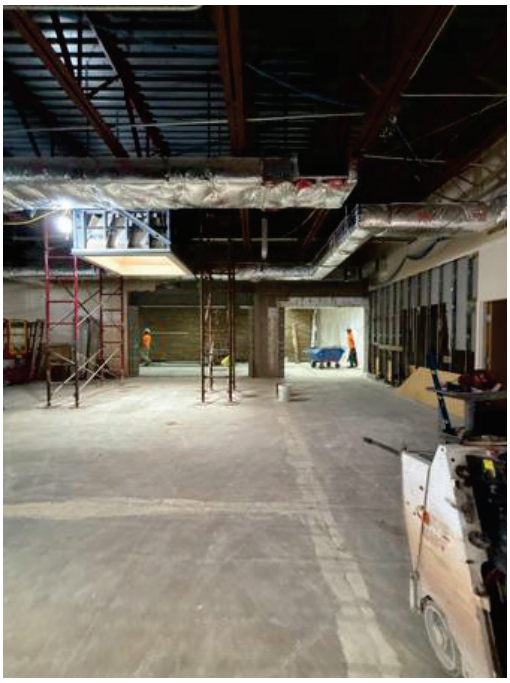

Market & Johnson
Adding Value to Everything We Do

ECASD North HS Media Center Alterations

 # 1

Week of: 6/2/2025

