WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

July 14th, 2025

Last 5 Days:

- Segment C (Tec Ed, Art, and B&G Club Areas)
  - Underground Plumbing Continued
  - Overhead MEP Rough-ins Continued
  - Slab Removals for Underground Work
  - Structural Steel Columns at Masonry Firewall Locations
  - Finished Masonry Firewall and Prep for Final Brick Veneer.
  - Cold Form Framing and Densglass Install at Clerestory.
  - Interior Stud Framing at B&G Club Areas South of GYM 177 (B&G Club Gym)
  - Slab-on-Grade Infills
- Exterior Site Improvements
  - Playground Equipment Install
  - Asphalt Paving at Multiple Locations
  - 200M Playground Walking Track Paved and Striped.
  - Exterior Concrete Sidewalks and Paving at New Bus Drop Off.
  - Main Parking Lot Paving Completed
  - Added Therapy Swing Installed.

Next 5 Days

- Segment C (Tec Ed, Art, and B&G Club Areas)
  - Underground Plumbing will continue.
  - Overhead MEP Rough-ins to continue.
  - Further Slab Removals for Plumbing Underground
  - GYM 177 Wood Gym Floor Installation to begin (Boys and Girls Club)
  - Final Brick Veneer on the West Side Elevation.
  - Continue Interior Stud Framing
- Exterior Site Improvements
  - Playground Equipment Install
  - Asphalt Paving at Multiple Locations
  - 200M Playground Walking Track Paved and Striped.
  - Exterior Concrete Sidewalks and Paving at New Bus Drop Off.

WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

July 14th, 2025



Northwest Site – 200 M Track and Basketball Courts Installed



Exterior Site – Main Parking Lot Paving Completed


WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

July 14th, 2025



Segment C – West Elevation Exterior Masonry Veneer Install In-Progress

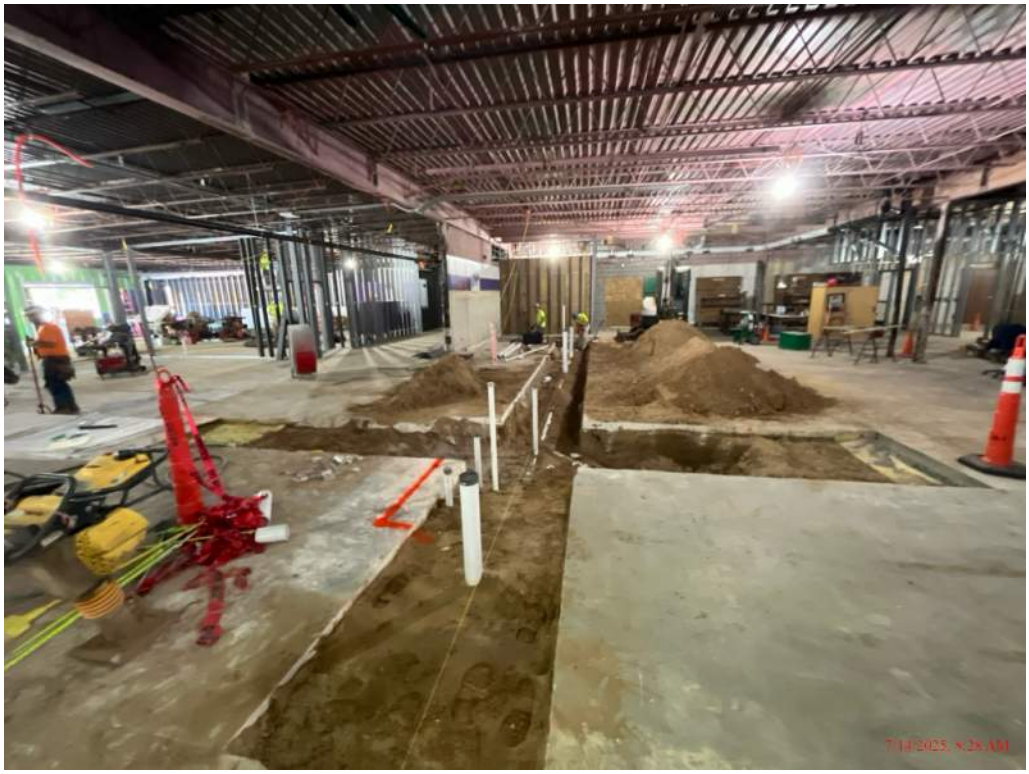

Segment C – Interior Slab Removal and Underground Plumbing Ongoing

WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

July 14th, 2025



Segment C Slab-on-Grade Infills for Underground Plumbing Work



Segment C – Interior Stud Framing

WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

July 14th, 2025



Exterior South Site – Concrete Sidewalk at New Bus Drop Off



Segment A – Choir Room Ceiling Grid Installation and Interior Painting
