ORANGEBURG
COUNTY SCHOOL DISTRICT
We Are **One**

OPERATIONS UPDATE



Orangeburg-Wilkinson High School

KAHN

SAFETY	
Incidents to Date	1
First Aids to Date	0

WEATHER	
Working Days	308
Weather Days	46
Activities Delayed	2

MANPOWER	
Number of Trades	11
Average Workers *(per day)*	135

SCHEDULE MILESTONES	
Job Start	5/5/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continued.
- Roofing at the low roof of the cafeteria nears completion.
- CMU nears completion in classroom wings A1 & A2.
- Press box retaining wall footing is 90% complete. The wall begins 7/28/25.
- Exterior insulation continued at E2 & D.
- Brick continued in area E2.
- Metal decking was installed at the Field House.
- Paving continued at the football parking lot.
- Joists were completed at the practice gym.

Upcoming Activities

- Press box retaining wall will begin.







Orangeburg-Wilkinson High School

SAFETY	
Incidents to Date	1
First Aids to Date	0
WEATHER	
Working Days	313
Weather Days	46
Activities Delayed	2
MANPOWER	
Number of Trades	11
Average Workers *(per day)*	151
SCHEDULE MILESTONES	
Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continued.
- Roofing at the gym began.
- CMU nears completion in classroom wings A1 & A2.
- The press box retaining wall has begun.
- Exterior insulation continued at F1 & was completed at the BB/SB building.
- Brick continued in area E2 & D.
- Paving continued at the football parking lot.
- Roof joists in A1 began.

Upcoming Activities

- Press box retaining wall will begin.
- Brick at the gym will begin.
- Brick at the SB/BB will begin.







East Lake Elementary School



727.520.8181
www.aerophoto.com

OCSD East Elementary School

Image # 23
Date 07.24.25



727.520.8181
www.aerophoto.com

OCSD East Elementary School

Image # 22
Date 07.24.25

East Lake Elementary School



727.520.8181
www.aerophoto.com

OCSD East Elementary School

Image # 22
Date 07.24.25



727.520.8181
www.aerophoto.com

OCSD East Elementary School

Image # 24
Date 07.24.25


EAST LAKE
ELEMENTARY SCHOOL

Robert E. Howard Elementary School

ROBERT E. HOWARD ELEMENTARY SCHOOL

SAFETY	
Incidents to Date	0
First Aids to Date	0
WEATHER	
Working Days	49
Weather Days	0
Activities Delayed	0
MANPOWER	
Number of Trades	3
Average Workers *(per day)*	20
SCHEDULE MILESTONES	
Job Start	5/27/2025
Contract Completion	12/14/2026

Top Activities This Week

- Abatement in area 3 in progress
- Demolition of area 2 in progress
- Clearing, striping, grading
- Water and sewer installation
- Building pad in progress

Upcoming Activities

- Demolition of Area 2 & 3
- Storm Drainage continuing
- Aggregate Piers installation to start 8/11







Week of **July 21st , 2025**

Robert E. Howard Elementary School

ROBERT E. HOWARD ELEMENTARY SCHOOL

SAFETY	
Incidents to Date	0
First Aids to Date	0
WEATHER	
Working Days	55
Weather Days	0
Activities Delayed	0
MANPOWER	
Number of Trades	3
Average Workers *(per day)*	20
SCHEDULE MILESTONES	
Job Start	5/27/2025
Contract Completion	12/14/2026

Top Activities This Week

- Abatement in area 3
- Demolition of area 2 & 3 in progress
- Clearing, striping, grading
- Water and sewer installation
- Building pad in progress

Upcoming Activities

- Demolition of area 2 & 3
- Storm Drainage continuing
- Aggregate Piers installation to start 8/11
- Concrete mobilizing 8/25







Week of **July 28th, 2025**

Summer Projects











Summer Projects





Summer Projects

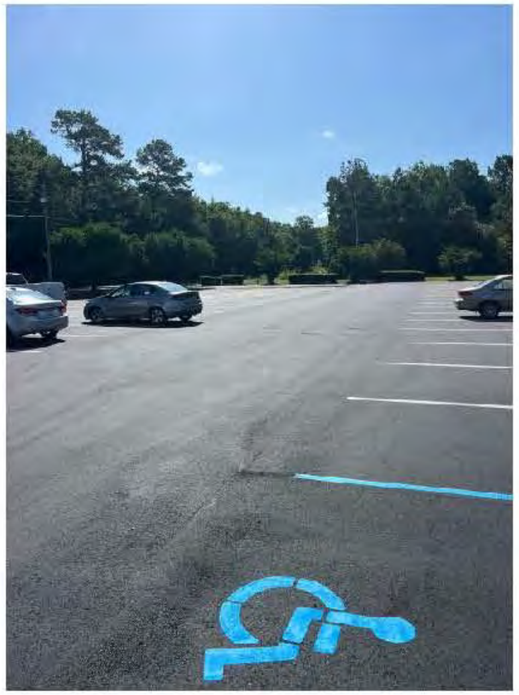

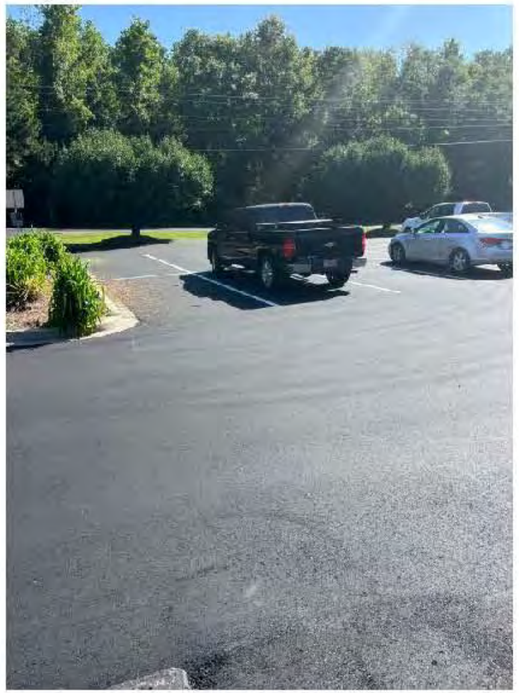





Summer Projects

