Market & Johnson
Adding Value to Everything We Do

ECASD North HS Weight Room Addition & Alterations

47

Week of: 8/4/2025

WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- Forum/Old Weight Room
  - M&J carpenters completed install of HM doors & hardware.
  - Subs started MEP finishes.
  - Verhalen completed dropping ceiling tiles.
- Art Rooms
  - M&J started casework, marker board, & TV install.
  - Kumplete Dec. continued tape, finish, & paint.
  - Concrete Treatments finished epoxy flooring touch ups.
  - Esser Glass started aluminum window frames/glazing install.
  - Subs started MEP finishes.
- Dog House/Gym Corridor
  - Kumplete Dec. completed tape, finish, & paint.
  - Verhalen dropped full ceiling tiles.

Upcoming Week

Market & Johnson to supervise and coordinate with trades.

- Forum/Old Weight Room
  - Subs to complete MEP finishes.
  - Esser Glass to complete HM glazing install.
  - Grazzini to start carpet & base install.
- Art Rooms
  - M&J to continue casework, marker board, & TV install.
  - Wynn Jones to start epoxy top install.
  - Esser Glass to complete aluminum window frames/glazing install.
  - Subs to complete MEP finishes.

Project Manager:	Jordan Lieffring	(715) 579-0176	jlieffring@market-johnson.com
Superintendent:	Jeremy Hollister	(715) 579-7991	jhollister@market-johnson.com


Market & Johnson
Adding Value to Everything We Do


ECASD North HS Weight Room Addition & Alterations

47

Week of: 8/4/2025

Weekly Photos

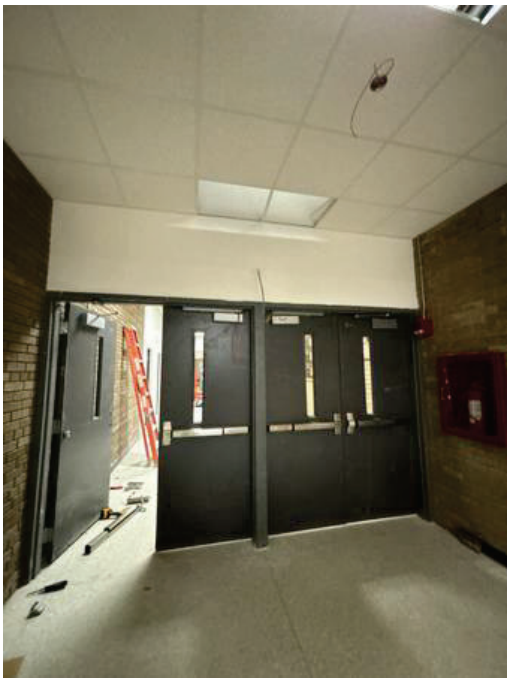

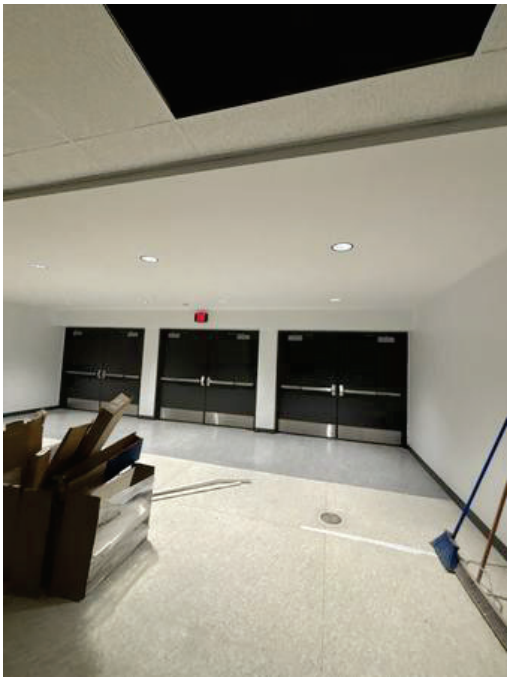


Market & Johnson
Adding Value to Everything We Do

ECASD North HS Weight Room Addition & Alterations

47

Week of: 8/4/2025

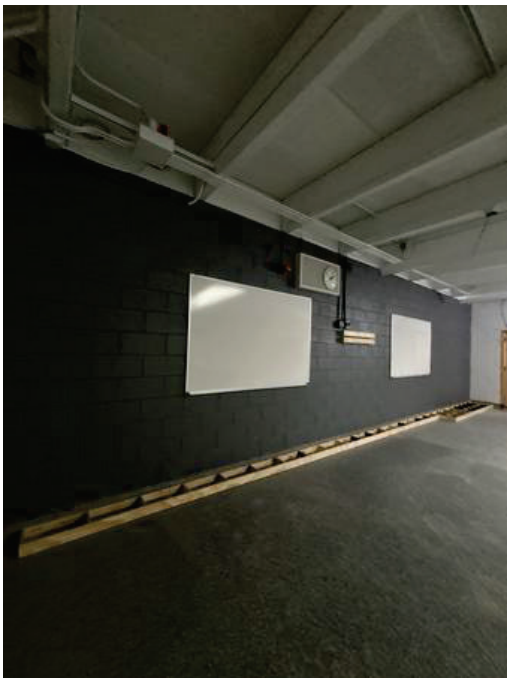



Market & Johnson
Adding Value to Everything We Do

ECASD North HS Weight Room Addition & Alterations

47

Week of: 8/4/2025





Market & Johnson
Adding Value to Everything We Do

ECASD North HS Weight Room Addition & Alterations

47

Week of: 8/4/2025





Market & Johnson
Adding Value to Everything We Do

ECASD North HS Media Center Alterations

10

Week of: 8/4/2025

WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- M&J continued casework install.
- M&J started specialties install.
- RJP completed tape, finish, & paint.
- VerHalen completed ceiling grid install.
- Erskine Interiors completed flooring install.
- Subs completed MEPF finishes.

Upcoming Week

Market & Johnson to supervise and coordinate with trades.

- M&J to continue specialties install.
- M&J to complete doors & hardware install.
- Verhalen to drop ceiling tiles.
- Verhalen to install ceiling clouds
- Fast Signs to install acrylic signage.

Project Manager: Jordan Lieffring (715) 579-0176 jlieffring@market-johnson.com

Superintendent:


Market & Johnson
Adding Value to Everything We Do

ECASD North HS Media Center Alterations

10

Week of: 8/4/2025

Weekly Photos

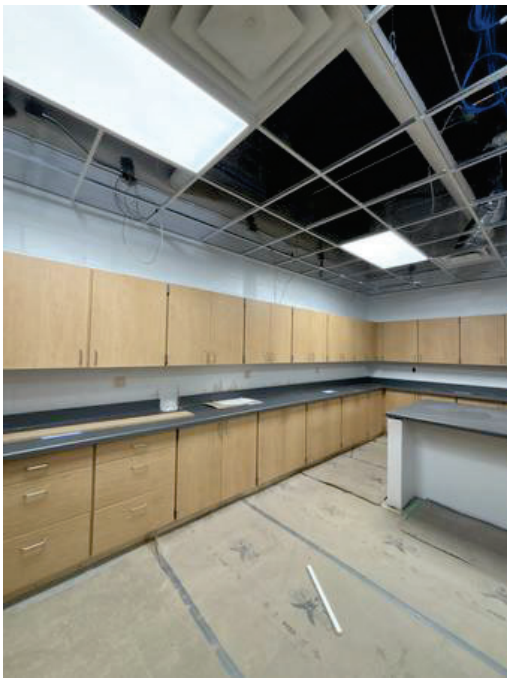




Market & Johnson
Adding Value to Everything We Do

ECASD North HS Media Center Alterations

10

Week of: 8/4/2025



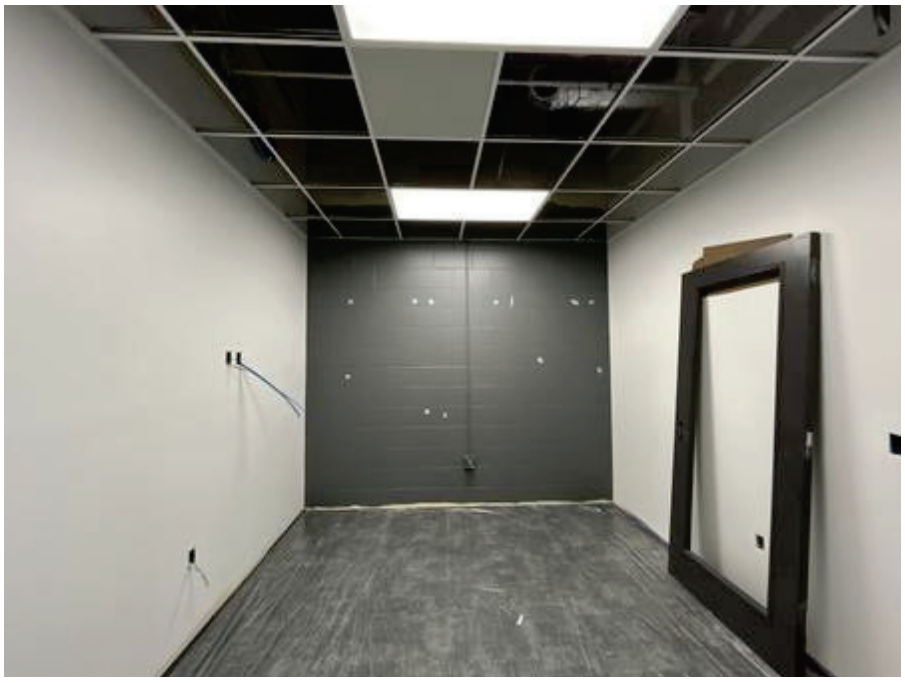

Market & Johnson
Adding Value to Everything We Do

ECASD North HS Media Center Alterations

10

Week of: 8/4/2025



