Bond Oversight Committee Report

June 4, 2025



Topics

01

Bond Cost Projection Updates

02

2017 Bond Projects

03

2022 Bond Projects


04

2025 Bond Projects

05

Board Decisions

01

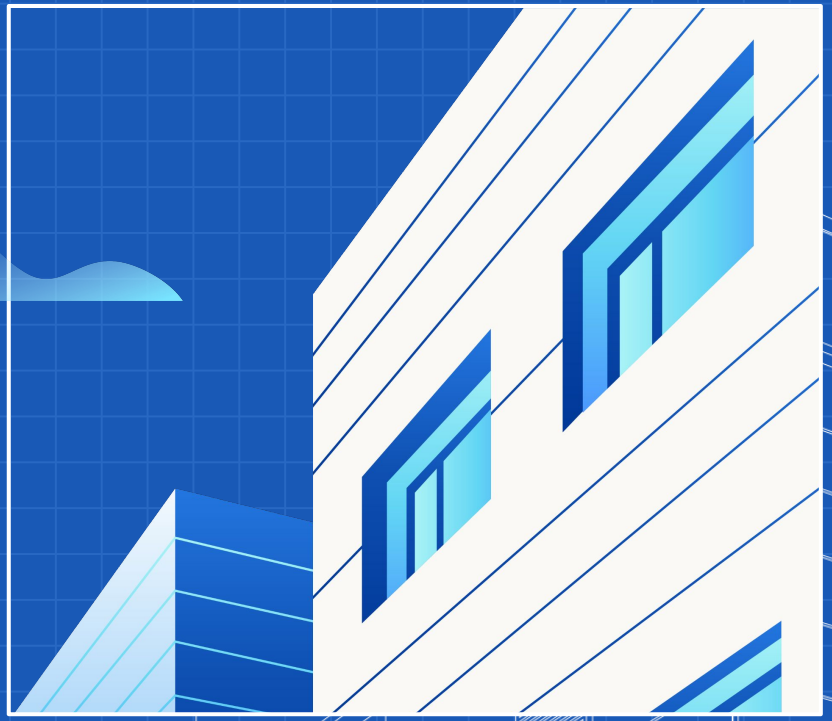

Bond Cost Update

2017 Bond Budget Update

Bond Expenses Summary	Bond Issue #	Original Bond Plan	Adjustment	Updated Bond Plan	Cost to Complete	Over/(Under) Updated Estimate
Intermediate Renovations	#3	4,100,000		4,100,000	6,597,674	$ 2,497,674.25
Elementary #3	#3	35,900,000	-827,590	35,020,183	30,573,650	$ (4,446,533.00)
Administration Building	#2	5,000,000	817,554	5,817,554	5,893,760	$ 76,206.00
Transportation Center	#3	4,000,000		4,000,000	4,266,787	$ 266,787.00
Technology	#2	3,000,000		3,000,000	2,882,232	$ (117,768.00)
AHS Phase 3 Parking Expansion		-		-	2,436,623	$ 2,436,623.00
Closed Projects		$ 114,000,000.00		$ 114,062,263.00	$ 113,083,699.00	$ (978,564.00)
Sixth Grade Center Fire Lane		-			1,196,618	$ 1,196,617.75
Hilltop HVAC replacement and irrigation upgrades		-			446,435	$ 446,435.00
Future project		-				$ -
Unallocated Interest Earnings		-		3,875,364		$ (3,875,364.00)
Total		**166,000,000**		**169,875,364**	**167,377,478**	**$ (2,497,886.00)**


2022 Bond Budget Update - Prop A

Bond Expenses Summary	Original Bond Plan	Cost to Complete	Over/(Under) Updated Estimate
Elementary #4	39,435,000	46,520,744	$ 7,085,744.00
HS Orchestra Shell	350,000	282,096	$ (67,903.81)
Hilltop Playground	500,000	354,422	$ (145,578.00)
Tech Infrastructure	300,000	300,000	$ -
Busses	4,490,000	4,490,000	$ -
Land Acquisition	20,000,000	20,000,000	$ -
Middle School #1	103,520,000	102,165,688	$ (1,354,312.00)
Elementary #5	44,515,000	54,954,248	$ 10,439,248.00
Furniture Refresh	2,000,000	2,000,000	$ -
Safety and Security updates	1,000,000	1,000,000	$ -
Middle School #2 Design (partial cost only)	4,975,000	0	$ (4,975,000.00)
Total Prop A (before interest)			**$ 10,982,198.19**
Interest Earnings (through May 2025)	-		$ (14,527,561.00)
Arbitrage rebate(allowance only)			$ 3,768,037.00
Total Prop A	**221,085,000**	**232,067,198**	**$ 222,674.19**



2022 Bond Budget Update - Props B & C

Stadium	26,915,000	28,624,650	$ 1,709,650.00
Interest Earnings (through May 2025)			$ (3,367,019.00)
Arbitrage rebate (allowance only)			$ 884,230.00
Total Prop B			**$ (773,139.00)**
IAC	19,885,000	21,145,639	$ 1,260,639.00
Interest Earnings (through May 2025)			$ (2,487,833.00)
Arbitrage rebate(allowance only)			$ 761,793.00
Total Prop C			**$ (465,401.00)**

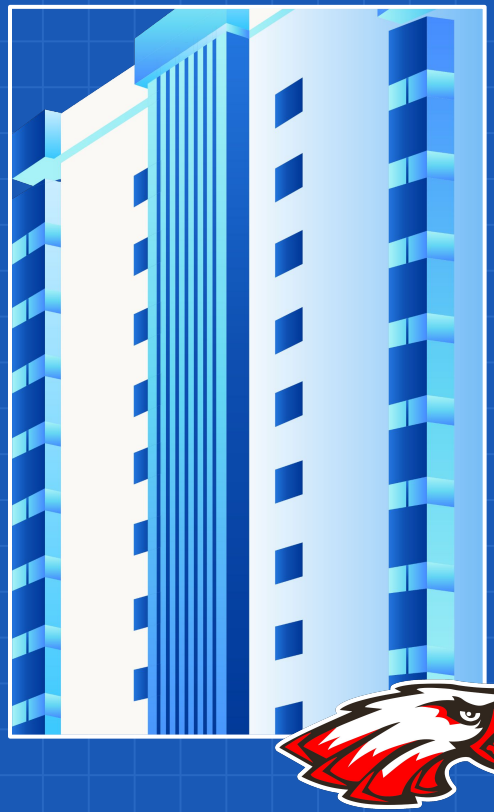


2024 Bond Budget Update - Prop C

Bond Expenses Summary	Original Bond Plan	Expenditures	Cost to Complete	Over/(Under) Updated Estimate
Technology	6,500,000		5,714,600	
Pending Board Action in April				
1:1 refresh for grades 6, 7 and 9		785,400	785,400	
Total Prop C (before interest)				$ -
Interest Earnings (through ??? 2025)	-	-		
Arbitrage rebate(allowance only)				
Total Prop C	**6,500,000**	**785,400**	**6,500,000**	$ -



2025 Bond Budget Update - Prop A

Bond Expenses Summary	Original Bond Plan	Cost to Complete	Over/(Under) Updated Estimate
MS # 2	129,080,000	129,080,000	$ -
ES # 6	65,645,000	65,645,000	$ -
CF Connector	6,930,000	6,930,000	$ -
ES # 5 Escalation	15,000,000	15,000,000	$ -
Hilltop CI Projects	2,760,000	2,760,000	$ -
377 Campus CI Projects	33,580,000	33,580,000	$ -
SGC CI Projects	11,940,000	11,940,000	$ -
MS # 3 Planning & Design Only	12,300,000	12,300,000	$ -
Buses	9,000,000	9,000,000	$ -
Technology	7,500,000	7,500,000	$ -
Land and offsite costs	100,000,000	100,000,000	$ -
Total Prop A (before interest)			$ -
Interest Earnings	-		
Arbitrage rebate(allowance only)			
Total Prop A	**393,735,000**	**393,735,000**	$ -

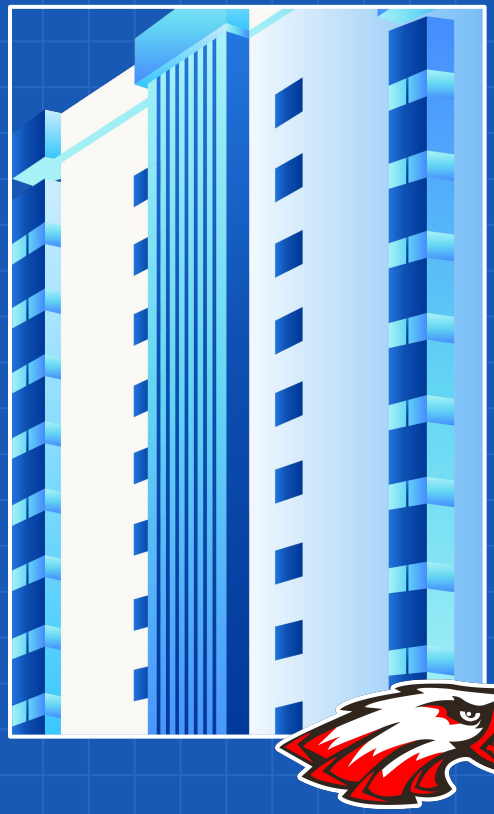


2025 Bond Budget Update - Prop B

BB/SB Complex at CF	29,435,000	29,435,000	$ -
Interest Earnings	0		
Arbitrage rebate (allowance only)			
Total Prop B	**29,435,000**	**29,435,000**	**$ -**




02

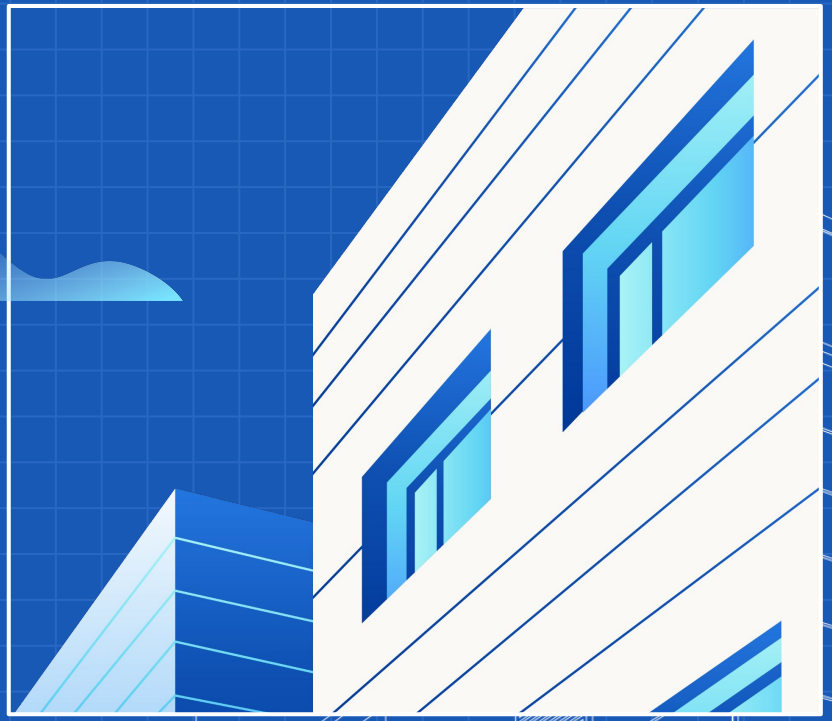

2017 Bond Projects

03

2022 Bond Projects

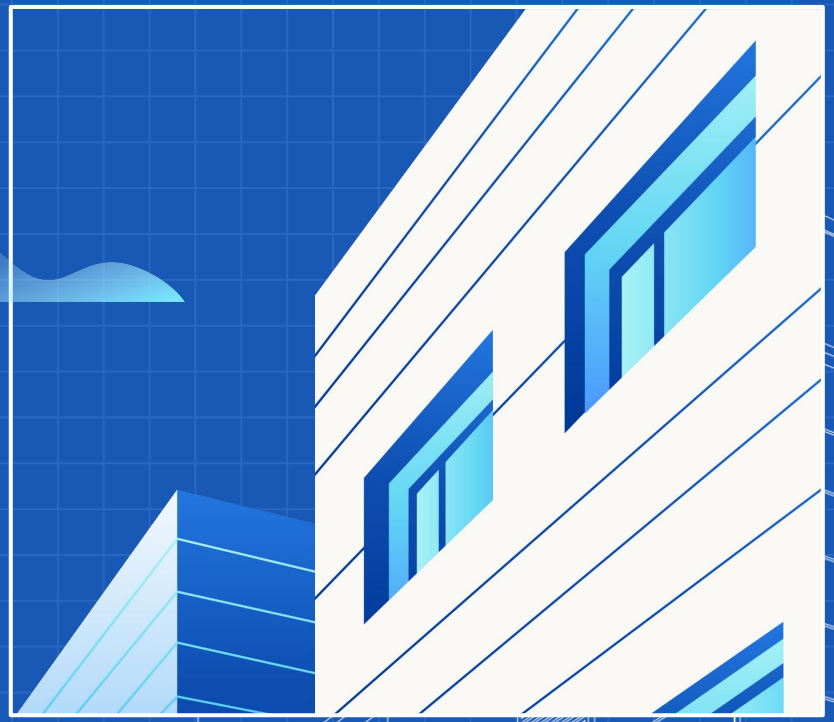

Stadium and IAC



- Architect: VLK Architects
- Contractor: Pogue Construction
- Contract Method: CSP
- Start Date: September 2024
- Completion Date: December 2025
- Cost: $ 45,823,500

Stadium and IAC



- Grass practice field has been top dressed
- Area around the practice field has been hydro-mulched
- Construction trailer will be moved out this week and construction fences taken down in this area

Stadium and IAC



- Fire lane being poured
- PEMB assembly is ongoing

Stadium and IAC



- Visitor side grandstands in progress
- Concession stand construction in progress
- All parking has been poured

Stadium and IAC



- Pressbox steel erection continues
- Grandstand columns in progress
- Concession stand D roof deck installation

Stadium and IAC





Middle School #1

- Architect: Corgan
- Contractor: Pogue Construction
- Contract Method: CMaR
- Start Date: September 2024
- Completion Date: Aug. 2026
- GMP: $87,392,415



Middle School #1



- All paving is complete

Middle School #1



- Masonry walls in locker room areas
- Interior masonry walls at the storm shelter in progress
- Steel erection in the band area is in progress
- Exterior metal stud framing in progress in the band area

Middle School #1



- Air barrier is installed on the gym and brick veneer is in progress

Middle School #1



- Pads for the tennis courts

Middle School #1



- Track surfacing installation is in progress

Elementary School #5

- Architect: Corgan
- Contractor: Pogue Construction
- Contract Method: CMaR
- Start Date: TBD
- Completion Date: Aug. 2027
- Construction Budget Available: $ 38,680,281



Elementary School #5

- Development plans are under review at the Town
- Building plans are under review at the Town
- Plan / Specification review




Miscellaneous Projects

Hilltop ES & 377 Campus Furniture Refresh

- Scheduled for the upcoming summer break
  - 6/23 through 7/8

04

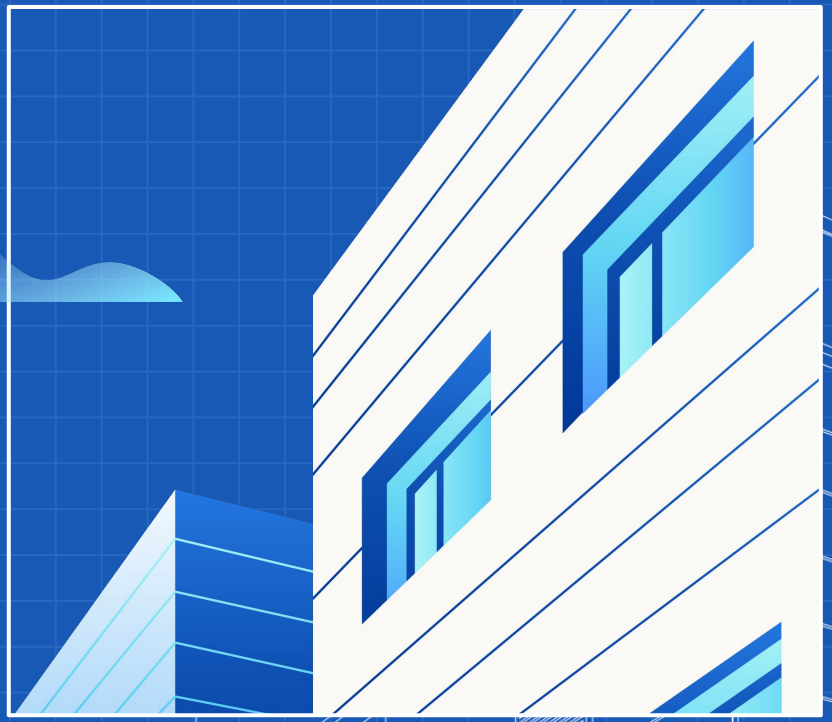

2025 Bond Projects

Projected Project Starts - 12 Months or Less

Capital Improvements at Hilltop and 377 Campus

Canyon Falls Campus Connector


New Middle School # 2

Baseball / Softball Complex at Canyon Falls Campus

Transportation parking

05

Board Decisions

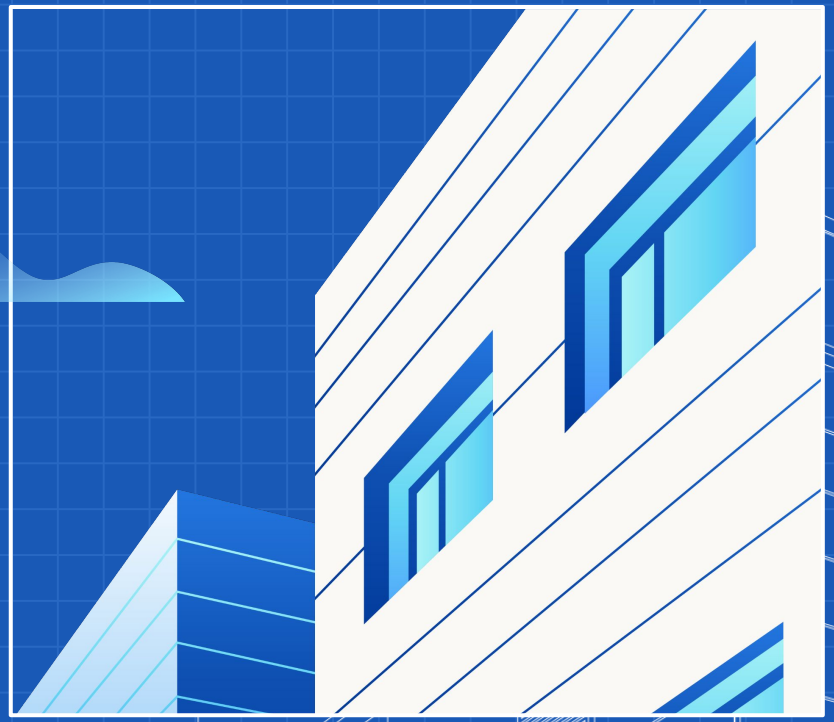

Last Months Board Approvals



Upcoming Board Approval Items



- ES#5 guaranteed maximum price (anticipated in September / October)
- Materials testing services for ES#5 (anticipated in September / October)
- Contract increase to Stadium (June)
- Architectural services for projects
- Construction procurement method for projects
