Prepared for:

Kyrene Elementary School District
8700 South Kyrene Road
Tempe, Arizona 85284

AHERA ASBESTOS INSPECTION REPORT

FOR

KYRENE DEL PUEBLO MIDDLE SCHOOL
360 SOUTH TWELVE OAKS BOULEVARD
CHANDLER, ARIZONA 85226

PURCHASE ORDER NO. 251702

Prepared by:

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue, Building 7
Phoenix, Arizona 85027
(623) 516-1415

Dominion Project Number: AZ1418.59

AHERA Re-Inspection Date: June 20, 2025 & June 23, 2025 – June 24, 2025

TABLE OF CONTENTS

LIMITATIONS ..... SECTION 1

INSPECTION PROCESS ..... SECTION 2

EXECUTIVE SUMMARY ..... SECTION 3

SITE PLANS ..... SECTION 4

HOMOGENEOUS MATERIALS INVENTORY LISTS ..... SECTION 5

PLM BULK SAMPLE SHEETS ..... SECTION 6

PLM BULK SAMPLE LOCATION MAPS ..... SECTION 7

PHYSICAL ASSESSMENT INFORMATION SHEETS ..... SECTION 8

LABORATORY REPORTS ..... SECTION 9

ASSUMED ACBM LOCATION MAPS ..... SECTION 10

INSPECTOR ACCREDITATION ..... SECTION 11

LABORATORY ACCREDITATION ..... SECTION 12

SECTION 1

♦

LIMITATIONS

LIMITATIONS

The conclusions and results contained herein are based solely on the information presented in this report. The sampling, testing, and observations described in the report represent conditions only at the specified times and locations. Additional materials or information which were hidden, undiscovered, inaccessible, or not a part of the findings presented herein, would result in the modification of the conclusions and recommendations made herein. Any response action guidelines are based solely on the findings contained herein. The response action guidelines are presented as a courtesy and are not to be considered a complete or detailed set of specifications. Dominion performed this survey as directed by the client and in compliance with applicable regulations.

Dominion is not responsible for the accuracy of information provided by others, or for conditions or consequences arising from relevant facts that were withheld, concealed, undiscovered, or not fully disclosed. Dominion is not a law firm, and therefore, makes no representations regarding any potential liability of any person or entity for site conditions. Further, Dominion is not qualified to present medical advice. If any present or future health issues are in question, it is recommended that the findings in this report be presented to a qualified medical professional for evaluation.

Kyrene Del Pueblo is currently being used daily, therefore, to avoid conspicuous damage and a possible trip and fall hazard, Dominion was only able to check for secondary flooring layers in the corners of each room. Therefore, if the carpets are to be replaced, additional investigation should be performed under other areas of the flooring to assure that an undetected second layer of flooring does not exist. Any necessary samples should be collected by a certified inspector prior to the disturbance of any discovered unsampled flooring.

Additional materials or information which were hidden, undiscovered, inaccessible, or are not a part of the finding presented herein, would result in the modification of the conclusions and recommendations made herein. Changes over which Dominion has no control, including but not limited to, the passage of time, manifestation of latent conditions, or occurrence of future events, require reevaluation of the findings, observations, and conclusions expressed in the report.

The limited sampling, testing, and observations described in the report represent conditions only at specified times and locations. These limited sampling methods, techniques, and scope of services were not comprehensive or to be considered all inclusive. Dominion is not responsible for the accuracy of information or services provided by others, including but not limited to other consultants, analytical laboratories, or public records. Dominion is not liable for conditions or consequences arising from relevant facts that were withheld, concealed, undiscovered, or not fully disclosed. Dominion performed this survey in a specific area as directed by the Client and in compliance with applicable regulations.

Dominion's scope of service for this report did not include the inspection for, or identification of fungi, lead paint, or any other hazardous or controlled substances not specifically identified herein. This report presents professional opinions and findings of a scientific or technical nature.

SECTION 2

♦

INSPECTION PROCESS

INSPECTION PROCESS

The Environmental Protection Agency (EPA) in 40 CFR 763, the Asbestos Hazard Emergency Response Act (AHERA), requires Local Education Agencies (LEAs) to identify friable and non-friable asbestos-containing building material (ACBM) in public and private elementary and secondary schools by visually inspecting school buildings for such materials and by sampling all identified suspect materials if they are not assumed to be ACBM. Those samples are then to be analyzed using appropriate analysis techniques, by a qualified laboratory, as referred to in the regulations. AHERA requires LEAs to only utilize accredited personnel when conducting inspections, re-inspections, developing management plans, or performing response actions. This regulation also includes record-keeping requirements. LEAs may contractually delegate their duties under this rule, but they remain responsible for the proper performance of those duties. LEAs are encouraged to consult with EPA Regional Asbestos Coordinators, or if applicable a State's lead agency designated by the State Governor, for assistance in complying with this rule.

This report complies with AHERA based protocols outlined in 40 CFR 763.85, specifically:

- The campus was visually inspected to identify the locations of all suspected ACBM.
- All suspect materials were touched to determine friability and condition.
- Bulk samples were collected of all homogeneous areas of friable suspected ACBM and all homogeneous areas of non-friable suspected ACBM.
- The date of the inspection, the name and signature of the person making the inspection, State of accreditation, his or her accreditation number and any changes in the condition of known or assumed ACBM are included in this report, if applicable.
- The exact locations where samples were collected during the inspection are marked, as well as a description of the manner used to determine sampling locations, the name and signature of each accredited inspector who collected the samples, State of accreditation and if applicable, his or her accreditation number.
- Also included within the report are any assessments or reassessments made of friable material, the name and signature of the accredited inspector making the assessments, State of accreditation and if applicable, his or her accreditation number.

The sampling protocol outlined in 40 CFR 763.86 is as follows:

Surfacing material is material in a school building that is sprayed-on, troweled-on, or otherwise applied to surfaces, such as acoustical plaster on ceilings and fireproofing materials on structural members, or other materials on surfaces for acoustical, fireproofing, or other purposes. Surfacing materials are collected in a statistically random manner as follows:

- At least three (3) bulk samples shall be collected from each homogeneous area that is one thousand (1,000) square feet.

- At least five (5) bulk samples shall be collected from each homogeneous area that is greater than one thousand (1,000) square feet but less than or equal to five thousand (5,000) square feet.

- At least seven (7) bulk samples shall be collected from each homogeneous area that is greater than five thousand (5,000) square feet.

Thermal system insulation (TSI) in a school building means materials applied to pipes, fittings, boilers, breeching, tanks, ducts, or other interior structural components to prevent heat loss or gain, or water condensation, or for other purposes. TSI samples are collected in a randomly distributed manner as follows:

- A minimum of three (3) bulk samples are collected from each homogeneous area of TSI that is not assumed to be ACBM.

- Collect at least one (1) bulk sample from each homogeneous area of patched TSI that is not assumed to be ACBM if the patched section is less than six (6) linear or square feet.

- In a manner sufficient to determine whether the material is ACBM or not ACBM, collect bulk samples from each insulated mechanical system that is not assumed to be ACBM where cement or plaster is used on fittings such as tees, elbows, or valves.

- Bulk samples are not required to be collected from any homogeneous area where the accredited inspector has determined that the TSI is fiberglass, foam glass, rubber, or other non-ACBM.

  Miscellaneous material is sampled in a manner sufficient to determine whether the material is ACBM or not ACBM. An accredited inspector shall collect bulk samples from each homogeneous area of friable miscellaneous material that is not "assumed" to be ACBM. Therefore, Dominion will collect a minimum of three (3) samples of each miscellaneous material, as a matter of industry standards.

ASSESSMENT OF MATERIALS

In compliance with 40 CFR 763.88, Dominion inspectors have classified the ACBM and suspected ACBM in the school buildings into one of the following categories:

(1) Damaged or significantly damaged Thermal System Insulation ACBM
(2) Damaged friable surfacing ACBM
(3) Significantly damaged friable surfacing ACBM
(4) Damaged or significantly damaged friable miscellaneous ACBM
(5) ACBM with potential for damage
(6) ACBM with potential for significant damage
(7) Any remaining friable ACBM or friable suspected ACBM

As part of the assessment, the following issues have been taken into consideration:

i. Location and the amount of the material, both in total quantity and as a percentage of the functional space.
ii. The type of damage or significant damage (e.g., flaking, blistering, water damage, or other signs of physical damage).
iii. The severity of damage (e.g., major flaking, severely torn jackets, as opposed to occasional flaking, minor tears to jackets).
iv. Extent or spread of damage over large areas or large percentages of the homogeneous area.
v. Whether the material is accessible.
vi. The material's potential for disturbance.
vii. Known or suspected causes of damage or significant damage (e.g., air erosion, vandalism, vibration, water).
viii. Preventive measures might eliminate the reasonable likelihood of undamaged ACBM from becoming significantly damaged.

SECTION 3

♦

EXECUTIVE SUMMARY

EXECUTIVE SUMMARY

INTRODUCTION

Dominion Environmental Consultants, Inc. (Dominion) was authorized, by Mr. Mason Meade with the Kyrene Elementary School District (KESD), to perform the Initial AHERA Asbestos Inspection of Kyrene Del Pueblo Middle School, located at 360 South Twelve Oaks Boulevard, Chandler, Arizona, via a written Purchase Order #251702, dated February 4, 2025.

Due to budgetary constraints, Dominion was directed by Mr. Meade to first sample the accessible building materials inside the building until a pre-determined number of samples were collected. Once the allotted number of samples per building had been collected, Dominion was then directed to "assume as asbestos-containing" the remaining suspect building materials. Pursuant to Mr. Meade's directions, the sampling order of importance was determined first on materials with the largest square footage, then least accessible materials, ceramic tiles, and materials least likely to be disturbed.

Dominion was also instructed to utilize Dominion's pervious Limited Asbestos Reports, Project Numbers AZ0959.2668 dated January 15, 2021, AZ0959.3108 dated July 12, 2022 and AZ1418.11 dated March 13, 2024. Per the direction of Mr. Meade, Dominion was instructed to utilize the information from these previous reports and to only collect additional bulk samples of any previously unsampled building materials.

Kyrene Del Pueblo Middle School campus consists of seven (7) single story, slab on grade, block structure. No below grade levels were observed for any building on campus.

BACKGROUND INFORMATION

INITIAL LIMITED AHERA ASBESTOS SURVEY – JANUARY 2021

Dominion's Limited Asbestos Inspections of the Kyrene Del Pueblo Middle School Main Office, Lounge, Work Room, D-1, Restroom, and Storage of Building 500 was conducted on January 15, 2021, by Mr. Basilio Marcos, an AHERA accredited Asbestos Building Inspector (State of Arizona #ON-53933-1419-061620, expiration date June 16, 2021).

2022 LIMITED AHERA ASBESTOS SURVEY – JULY 2022

Dominion's Limited Asbestos Inspections of the Kyrene Del Pueblo Middle School Janitor's Closet of Building 300 was conducted on July 12, 2022, by Mr. Nick Marcos, an AHERA accredited Asbestos Building Inspector (State of Arizona #ON-4644-8873-032422, expiration date March 24, 2023).

2024 AHERA ASBESTOS INSPECTION – MARCH 2024

Dominion's Limited Asbestos Inspections of the Kyrene Del Pueblo Middle School the Restrooms in Building 200 and Kitchen and Stage of Building 600 were conducted on March 11,

2024, by Mrs. Tracey Carpenter, an AHERA accredited Asbestos Building Inspector (State of Arizona #ON-4644-14588-091422, expiration date September 14, 2023).

2025 AHERA ASBESTOS RE-INSPECTION – JUNE 2025

Dominion's AHERA Asbestos Inspection, of the Kyrene Del Pueblo Middle School was conducted on June 20, 2025 and June 23, 2025 – June 24, 2025, by Mr. Nick Marcos, an AHERA accredited Asbestos Building Inspector. (State of Arizona #ON-188748-8873-031325, expiration date March 13, 2026).

COLLECTION OF BULK SAMPLES

Initial Limited AHERA Asbestos Survey – January 2021

A total of twenty-four (24) bulk samples were collected from seventeen (17) homogeneous building materials within the Main Office, Lounge, Work Room, D-1, Restroom, and Storage of Building 500.

Identified in the following list are the seventeen (17) suspect homogeneous building materials sampled during the January 15, 2021 limited asbestos inspection.

Building 500 – Office, Lounge, Work Room, D-1, Restroom, & Storage - 17 Materials, 0 ACBM

- Black Cove Base
- Cream Mastic for Black Cove Base
- Brown Cove Base
- Yellow Mastic for Brown Cove Base
- Blue Cove Base
- Cream Mastic for Blue Cove Base
- Orange Peel Drywall System - Cream Paint
- White Texture
- Pink Mesh
- White Joint Compound
- White/Tan Drywall
- Multicolored Blue Carpet
- Dark Yellow Mastic for Multicolored Blue Carpet
- Brown Wallpaper
- Cream Mastic for Brown Wallpaper
- Orange Peel Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)
- Smooth Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)

2022 Limited AHERA Asbestos Survey – July 2022

A total of eighteen (18) bulk samples were collected from nine (9) homogeneous building materials within the Janitor's Closet of Building 300.

Identified in the following list are the nine (9) suspect homogeneous building materials sampled during the July 12, 2022 limited asbestos inspection.

Building 300 – Janitor's Closet - 9 Materials – 0 ACBM

- Smooth Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)
- White Fiberglass Reinforced Plastic (FRP)
- Off-White Mastic for White Fiberglass Reinforced Plastic (FRP)
- Gray Cove Base
- Yellow Mastic for Gray Cove Base
- White Mop Sink Caulking
- Orange Peel Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)
- Blue Cove Base
- Yellow Mastic for Blue Cove Base

2024 AHERA Asbestos Inspection– March 2024

A total of twelve (12) bulk samples were collected from twelve (12) homogeneous building materials within the Restrooms in Building 200 and Kitchen and Stage of Building 600.

Identified in the following list are the twelve (12) suspect homogeneous building materials sampled during the March 13, 2024 limited asbestos inspection.

Building 200 - Restrooms – 6 Materials – 0 ACBM

- Brown Restroom Wall Tile
- Brown Grout for Brown Restroom Wall Tile
- Tan Mastic for Brown Restroom Wall Tile
- 2" x 2" Tan Restroom Floor Tile
- Brown Grout for 2" x 2" Tan Restroom Floor Tile
- Tan Mastic for 2" x 2" Tan Restroom Floor Tile

Building 600 – Kitchen and Stage – 6 Materials – 0 ACBM

- Red 6" x 6" Floor Tile
- Red-Brown Grout for Red 6" x 6" Floor Tile
- Gray Thinset for Red 6" x 6" Floor Tile
- White Mastic for Red 6" x 6" Floor Tile
- Brown Cove Base
- Yellow Mastic for Brown Cove Base

2025 AHERA Asbestos Re-Inspection - June 2025

During the 2025 AHERA Asbestos Re-inspection, a total of one hundred and twenty-six (126) bulk samples were collected from sixty (60) homogeneous building materials (multiple layers) throughout the Kyrene Del Pueblo Buildings 100, 200, 300, 400, 500, 600, and 700. Identified in

the following list are the sixty (60) suspect homogeneous materials Dominion sampled during the 2025 AHERA inspection.

Building 100 – Pod A/B – 9 Materials – 0 ACBM

- Gray Multicolored Carpet Square
- Orange Mastic for Gray Multicolored Carpet Square
- Blue Cove Base
- Cream Mastic for Blue Cove Base
- Orange Peel Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)
- New 2' x 2' Gray Ceiling Tile
- Old 2' x 2' Gray Ceiling Tile
- Red-Brown Brick
- Red Mortar for Red-Brown Brick

Building 200 – Pod G/H – 9 Materials – 0 ACBM

- Gray Multicolored Carpet Square
- Yellow Mastic for Gray Multicolored Carpet Square
- Blue Cove Base
- Cream Mastic for Blue Cove Base
- Orange Peel Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)
- New 2' x 2' Gray Ceiling Tile
- Old 2' x 2' Gray Ceiling Tile
- Red Brick
- Red Mortar for Red Brick

Building 300 – Administration Office – 9 Materials – 0 ACBM

- Gray Multicolored Carpet Square
- Tan Mastic for Gray Multicolored Carpet Square
- Blue Cove Base
- Cream Mastic for Blue Cove Base
- Black Carpet Square
- Yellow Mastic for Black Carpet Square
- New 2' x 2' Gray Ceiling Tile
- Old 2' x 2' Gray Ceiling Tile
- Orange Peel Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)

Building 400 – Pod E – 9 Materials – 0 ACBM

- Gray Multicolored Carpet Square
- Tan Mastic for Gray Multicolored Carpet Square
- Blue Carpet

- Yellow Mastic for Blue Carpet
- Blue Cove Base
- Off-White Mastic for Blue Cove Base
- New 2' x 2' Gray Ceiling Tile
- Old 2' x 2' Gray Ceiling Tile
- Orange Peel Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)

Building 500 – Pod D – 8 Materials – 0 ACBM

- Gray Multicolored Carpet Square
- Yellow Mastic for Gray Multicolored Carpet Square
- Blue Cove Base
- Cream Mastic for Blue Cove Base
- 2' x 2' Gray Ceiling Tile
- 2' x 4' Gray Ceiling Tile
- Orange Peel Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)
- Lightly Textured 2' x 2' Gray Ceiling Tile

Building 600 – Pod C – 8 Materials – 0 ACBM

- Gray Multicolored Carpet Square
- Tan Mastic for Gray Multicolored Carpet Square
- Blue Cove Base
- Off-White Mastic for Blue Cove Base
- New 2' x 2' Gray Ceiling Tile
- Old 2' x 2' Gray Ceiling Tile
- 2' x 4' Gray Ceiling Tile
- Orange Peel Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)

Building 700 – Pod I/J – 8 Materials – 0 ACBM

- Gray Multicolored Carpet Square
- Yellow Mastic for Gray Multicolored Carpet Square
- Blue Cove Base
- Cream Mastic for Blue Cove Base
- Orange Peel Drywall System (Paint, Texture, Tape, Joint Compound, & Drywall)
- New 2' x 2' Gray Ceiling Tile
- Old 2' x 2' Gray Ceiling Tile
- Textured 2' x 2' Gray Ceiling Tile

All the suspect bulk samples collected from Kyrene Del Pueblo School were submitted to EMLab P&K (EMLab) in Phoenix, Arizona for analysis using Polarized Light Microscopy (PLM) methods. EMLab used the methods prescribed in Method 40 CFR, Part 763, in the Code of Federal Register in analyzing bulk samples. EMLab is certified by the National *Institute of*

Standards and Technology as a National Voluntary Laboratory Accreditation Program (NVLAP), Number 500031-0. The suspect asbestos bulk samples were collected and submitted to the laboratory using established chain-of-custody procedures.

Bulk samples were collected utilizing safety and health practices as required by the Occupational Safety and Health Administration (OSHA). At the time of sample collection, the buildings were not occupied by students. Only limited administrative and custodial staff were present on campus.

ASSUMED ACBM – June 20 & June 23, 2025 – June 24, 2025

Due to budgetary constraints, KESD instructed Dominion to assume any unsampled suspect building materials as asbestos containing until further asbestos bulk sampling can be budgeted and conducted. Therefore, listed below, separated by building, are the two hundred and twenty-one (221) building materials that were assumed to contain greater than one percent (>1%) asbestos.

Building 100 – Pod A/B – 39 Assumed ACBM

- Interior Caulking
- Exterior Caulking
- Tackboard
- Black Sink Coating
- Black Countertops
- Fume Hood Panel
- Tan 12" x 12" Vinyl Floor Tile (VCT)
- Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)
- Brown Cove Base
- Mastic for Brown Cove Base
- Tan 4" x 6" Ceramic Wall Tile
- Brown 4" x 6" Ceramic Wall Tile
- Dark Brown 4" x 4" Replacement Ceramic Wall Tile
- Gray 4" x 4" Replacement Ceramic Wall Tile
- Grout for Ceramic Wall Tiles
- Mastic for Ceramic Wall Tiles
- Tan 2" x 2" Ceramic Floor Tile
- Grout for Tan 2" x 2" Ceramic Floor Tile
- Thinset for Tan 2" x 2" Ceramic Floor Tile
- Fixture Caulking
- Divider Wall
- Smooth Drywall System
- Fiberglass Reinforced Plastic (FRP)
- Mastic for Fiberglass Reinforced Plastic (FRP)
- Gray 5" x 5" Ceramic Floor Tile

- Grout for Gray 5" x 5" Ceramic Floor Tile
- Thinset for Gray 5" x 5" Ceramic Floor Tile
- Gray 5" x 5" Ceramic Wall Tile
- Grout for Gray 5" x 5" Ceramic Wall Tile
- Mortar for Gray 5" x 5" Ceramic Wall Tile
- Exterior Plaster Overhang
- White Duct Tape
- Mastic for White Duct Tape
- Unfinished Drywall System
- Gray Flex Duct Wrap

Building 200 – Pod G/H – 35 Assumed ACBM

- Interior Caulking
- Exterior Caulking
- Tackboard
- Gray 6" x 6" Ceramic Floor Tile
- Grout for Gray 6" x 6" Ceramic Floor Tile
- Thinset for Gray 6" x 6" Ceramic Floor Tile
- Gray 4" x 6" Ceramic Wall Tile
- Grout for Gray 4" x 6" Ceramic Wall Tile
- Mastic for Gray 4" x 6" Ceramic Wall Tile
- Tan 4" x 6" Ceramic Wall Tile
- Grout for Tan 4" x 6" Ceramic Wall Tile
- Mortar for Tan 4" x 6" Ceramic Wall Tile
- Fixture Caulking
- Blue 12" X 12" Vinyl Floor Tile (VCT)
- Mastic for Blue 12" X 12" Vinyl Floor Tile (VCT)
- Black Sink Coating
- Fiberglass Reinforced Plastic (FRP)
- Mastic for Fiberglass Reinforced Plastic (FRP)
- Old Black Cove Base
- Mastic for Old Black Cove Base
- Tan 12" x 12" Vinyl Floor Tile (VCT)
- Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)
- Brown Cove Base
- Mastic for Brown Cove Base
- Black Countertops
- Fume Hood Panel
- Divider Wall
- Exterior Plaster Overhang
- Unfinished Drywall
- White Duct Tape

- Mastic for White Duct Tape
- White Pipe Wrap
- Mastic for White Pipe Wrap

Building 300 – Administration Office – 20 Assumed ACBM

- Interior Caulking
- Exterior Caulking
- Black Sink Coating
- Glass Block Mortar
- Brick
- Mortar for Brick
- Tackboard
- Tan 12" x 12" Vinyl Floor Tile (VCT)
- Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)
- Brown Cove Base
- Mastic for Brown Cove Base
- Fixture Caulking
- White Duct Tape
- Mastic for White Duct Tape
- Gray Duct Mastic
- Silver Flex Duct Wrap
- Gray Flex Duct Wrap
- Silver Duct Tape
- Unfinished Drywall
- Silver Duct Wrap

Building 400 – Pod E – 20 Assumed ACBM

- Interior Caulking
- Exterior Caulking
- Tan 12" x 12" Vinyl Floor Tile (VCT)
- Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)
- Fixture Caulking
- Wallpaper
- Tackboard
- Black Sink Coating
- Gray Cove Base
- Mastic for Gray Cove Base
- Brick
- Mortar for Brick
- White Duct Seam Tape
- Mastic for White Duct Seam Tape

- Silver Flex Duct Wrap
- Gray Flex Duct Wrap
- White Pipe Wrap
- Mastic for White Pipe Wrap
- Unfinished Drywall System
- Skylight Insulation Panel

Building 500 – Pod D – 26 Assumed ACBM

- Interior Caulking
- Exterior Caulking
- Black Sink Coating
- Tackboard
- Black 12" x 12" Vinyl Floor Tile (VCT)
- Mastic for Black 12" x 12" Vinyl Floor Tile (VCT)
- Divider Wall
- Gray Sink Coating
- Polished Concrete
- Tan 12" x 12" Vinyl Floor Tile (VCT)
- Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)
- Brown Carpet
- Mastic for Brown Carpet
- Rubber Flooring
- Fiberglass Reinforced Plastic
- Mastic for Fiberglass Reinforced Plastic
- Brick
- Mortar for Brick
- Silver Duct Wrap
- Silver Flex Duct Wrap
- White Duct Seam Tape
- Mastic for White Duct Seam Tape
- Silver Duct Tape
- Gray Duct Mastic
- Skylight Insulation Panel
- Unfinished Drywall System

Building 600 – Pod C – 46 Assumed ACBM

- Polished Concrete
- Floor Expansion Joint
- Interior Caulking
- Exterior Caulking
- Black Stair Tread

- Mastic for Black Stair Tread
- Red Ramp Tread
- Mastic for Red Ramp Tread
- Red 6" x 6" Ceramic Wall Tile
- Grout for Red 6" x 6" Ceramic Wall Tile
- Mortar for Red 6" x 6" Ceramic Wall Tile
- 2' x 4' Drywall Ceiling Tile
- Tan 12" x 12" Vinyl Floor Tile (VCT)
- Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)
- Fiberglass Reinforced Plastic (FRP)
- Mastic for Fiberglass Reinforced Plastic (FRP)
- Silver Kitchen Caulking
- White 4" x 4" Ceramic Wall Tile
- Beige 4" x 4" Ceramic Wall Tile
- Maroon 4" x 4" Ceramic Wall Tile
- Grout for 4" x 4" Ceramic Wall Tiles
- Mastic for 4" x 4" Ceramic Wall Tiles
- Gray Floor Caulking
- Fixture Caulking
- Black L-Shaped Cove Base
- Mastic for Black L-Shaped Cove Base
- Tan 2" x 2" Ceramic Floor Tile
- Grout for Tan 2" x 2" Ceramic Floor Tile
- Thinset for Tan 2" x 2" Ceramic Floor Tile
- Beige 4" x 6" Ceramic Wall Tile
- Brown 4" x 6" Ceramic Wall Tile
- Grout for 4" x 6" Ceramic Wall Tiles
- Mastic for 4" x 6" Ceramic Wall Tiles
- Black Carpet Square
- Mastic for Black Carpet Square
- Wallpaper
- Black Sink Coating
- Unfinished Drywall System
- White Duct Seam Tape
- Mastic for White Duct Seam Tape
- Silver Flex Duct Wrap
- Gray Flex Duct Wrap
- Silver Duct Wrap
- Brick
- Mortar for Brick
- Exterior Plaster Overhang

Building 700 – Pod I/J – 35 Assumed ACBM

- Interior Caulking
- Exterior Caulking
- Tackboard
- Beige Streak 12" x 12" Vinyl Floor Tile (VCT)
- Mastic for Beige Streak 12" x 12" Vinyl Floor Tile (VCT)
- Gray Cove Base
- Mastic for Gray Cove Base
- Tan 12" x 12" Vinyl Floor Tile (VCT)
- Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)
- White 2" x 2" Ceramic Floor Tile
- Grout for White 2" x 2" Ceramic Floor Tile
- Thinset for White 2" x 2" Ceramic Floor Tile
- White 4" x 4" Ceramic Wall Tile
- Black 2" x 2" Ceramic Wall Tile
- Grout for Ceramic Wall Tiles
- Mastic for Ceramic Wall Tiles
- Fixture Caulking
- Black Sink Coating
- Divider Wall
- Fiberglass Reinforced Plastic (FRP)
- Mastic for Fiberglass Reinforced Plastic (FRP)
- Soundboard Wrap
- Mastic for Soundboard Wrap
- Brick
- Mortar for Brick
- Exterior Plaster Overhang
- Unfinished Drywall System
- White Duct Tape
- Mastic for White Duct Tape
- White Pipe Wrap
- Mastic for White Pipe Wrap
- Gray Duct Mastic
- Silver Flex Duct Wrap
- Silver Duct Wrap
- Black Foam Pipe Insulation

INSPECTION FINDINGS

INITIAL LIMITED AHERA ASBESTOS SURVEY – January 15, 2021

All twenty-two (22) of the homogeneous building materials sampled during the January 2021 inspection within the Main Office, Lounge, Work Room, D1, Restroom, and Storage of Building

500 were reported by the laboratory using the PLM analysis method to be “none detected” for asbestos content.

2020 LIMITED AHERA ASBESTOS SURVEY – July 12, 2022

All twelve (12) of the homogeneous building materials sampled during the July 2022 inspection within the Janitor’s Closet of Building 300 were reported by the laboratory using the PLM analysis method to be “none detected” for asbestos content.

2024 AHERA ASBESTOS INSPECTION – March 13, 2024

The twelve (12) homogeneous building materials sampled during the March 2024 inspection within the Restrooms in Building 200 and Kitchen and Stage of Building 600 were reported by the laboratory using the PLM analysis method to be “none detected” for asbestos content.

2025 AHERA ASBESTOS RE-INSPECTION – June 20 & June 23, 2025 – June 24, 2025

All sixty (60) of the homogeneous building materials sampled during the June 2025 inspection were reported by the laboratory using the PLM analysis method to be “none detected” for asbestos content.

As shown above, two hundred and twenty-one (221) suspect homogeneous building materials were *assumed* to contain greater than one percent (>1%) asbestos.

RECOMMENDATIONS

Any building material within the Kyrene Del Pueblo Middle School campus not identified in this inspection report that is not wood, glass, or metal, is a suspect ACBM and should not be removed, sanded, ground, abraded, or otherwise disturbed by any person without being first properly trained as per 40 CFR 763.92 and, or 29 CFR 1926.1101. For detailed recommendations, please refer to the Kyrene Del Pueblo Middle School AHERA Management Plan.

The ACBM or assumed ACBM located within the structures of the Kyrene Del Pueblo Middle School campus can be managed in compliance with the Kyrene Elementary School District AHERA Management Plan until such a time as these building materials become degraded, have become friable, or will be disturbed by ongoing maintenance, renovation, or a demolition activity. Prior to a renovation or demolition activity, the previously listed assumed ACBM should be sampled by an AHERA Certified Building Inspector to determine the presence of asbestos.


At least once every six (6) months after a management plan is in effect, the KESD should conduct periodic surveillance in each building that it leases, owns, or otherwise uses as a school building that contains ACBM.

At least once every three (3) years after a management plan is in effect, the KESD should conduct an inspection of all ACBM on the school campus.

The AHERA inspection is limited to only the interior of the buildings and the underside of any covered walkways. This would mean that the additional suspect building materials found on the exterior of the buildings or structures, that are not regulated by AHERA are regulated by EPA NESHAP and OSHA. Therefore, prior to any disturbance of these un-sampled or newly installed suspect building materials, Dominion recommends that these suspect materials be sampled by an AHERA Certified Building Inspector and analyzed for asbestos content by a qualified laboratory prior to any disturbance.

The property owner or his representatives should retain the services of an independent asbestos consulting firm to monitor the performance of any asbestos abatement activities. The consulting firm should oversee the completeness of any asbestos removal and verify the quality of the air during the removal work and perform final clearance air sampling in accordance with the AHERA guidelines.

All documentation is being provided to the Kyrene Elementary School District and must be retained as a permanent record. Should you have any questions regarding the procedures that were followed on this project, please contact Dominion at any time. Thank you for the opportunity to provide these environmental consulting services.



2025 AHERA Building Inspector
Nick Marcos
AHERA Certificate Number: ON-188748-8873-031325
Expires: March 13, 2026

Historical Information:

2024 AHERA Building Inspector
Tracey Carpenter
AHERA Certificate Number: ON-4644-14588-091422
Expired: September 14, 2023


2022 AHERA Building Inspector
Nick Marcos
AHERA Certificate Number: ON-4644-8873-032422
Expired: March 24, 2023

2021 AHERA Building Inspector
Basilio Marcos
AHERA Certificate Number: ON-53933-1419-061620
Expired: June 16, 2021

SECTION 4

♦

SITE MAPS

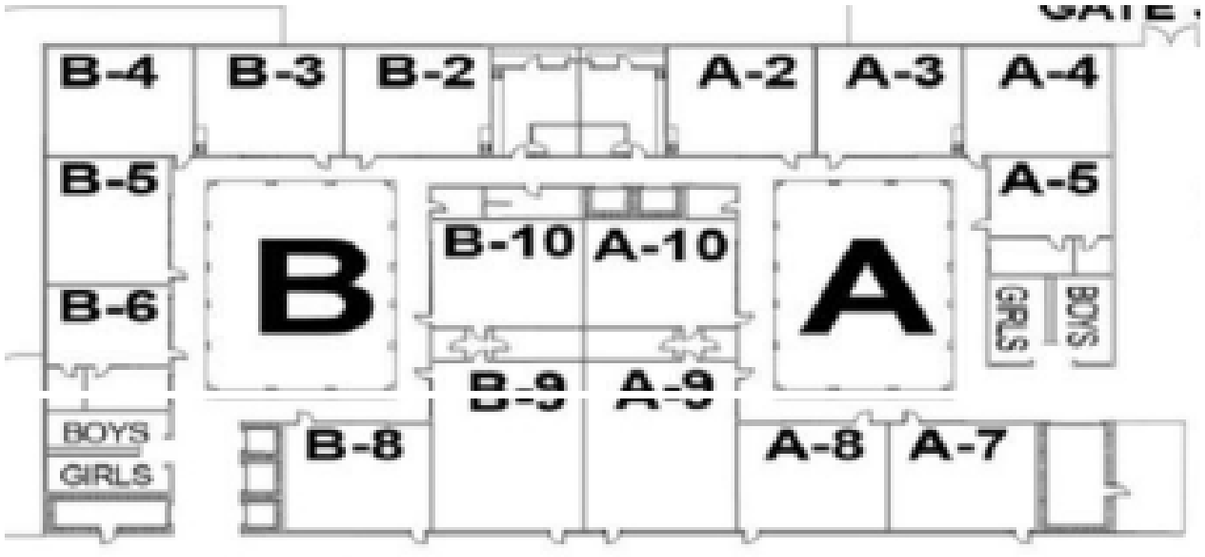

Site Plan (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 100 - Pod A/B

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415




Site Plan (2)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 200 - Pod G/H


Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

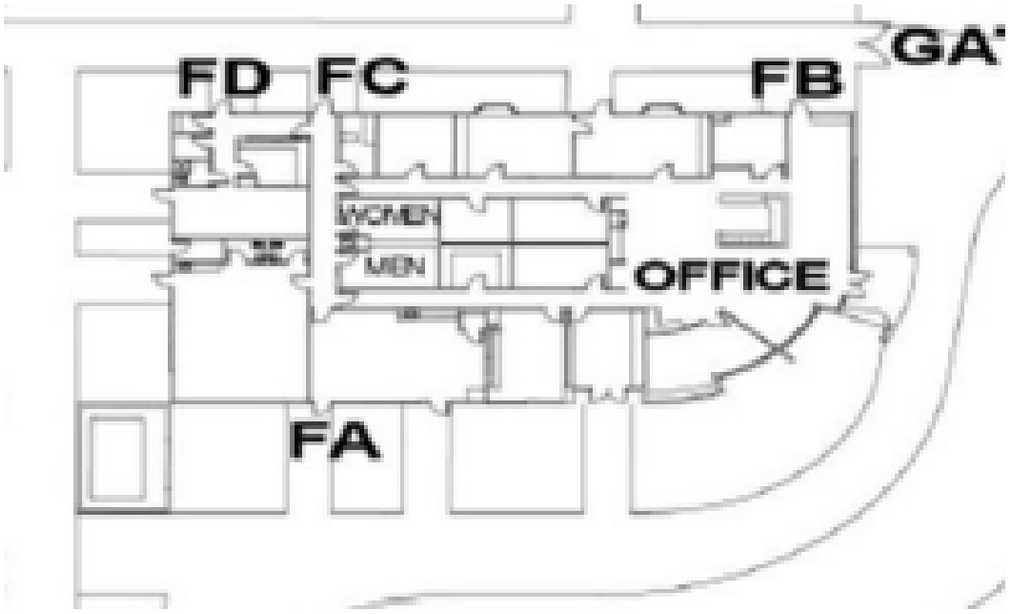

Site Plan (3)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59
Building 300 - Administration Office

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

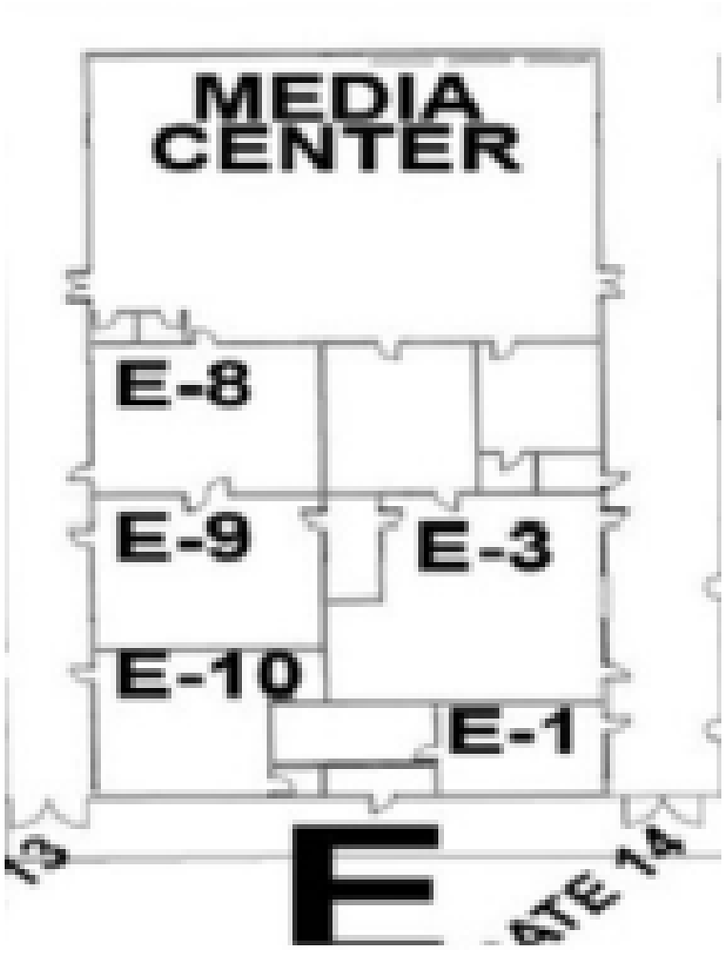


Site Plan (4)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 400 - Pod E

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

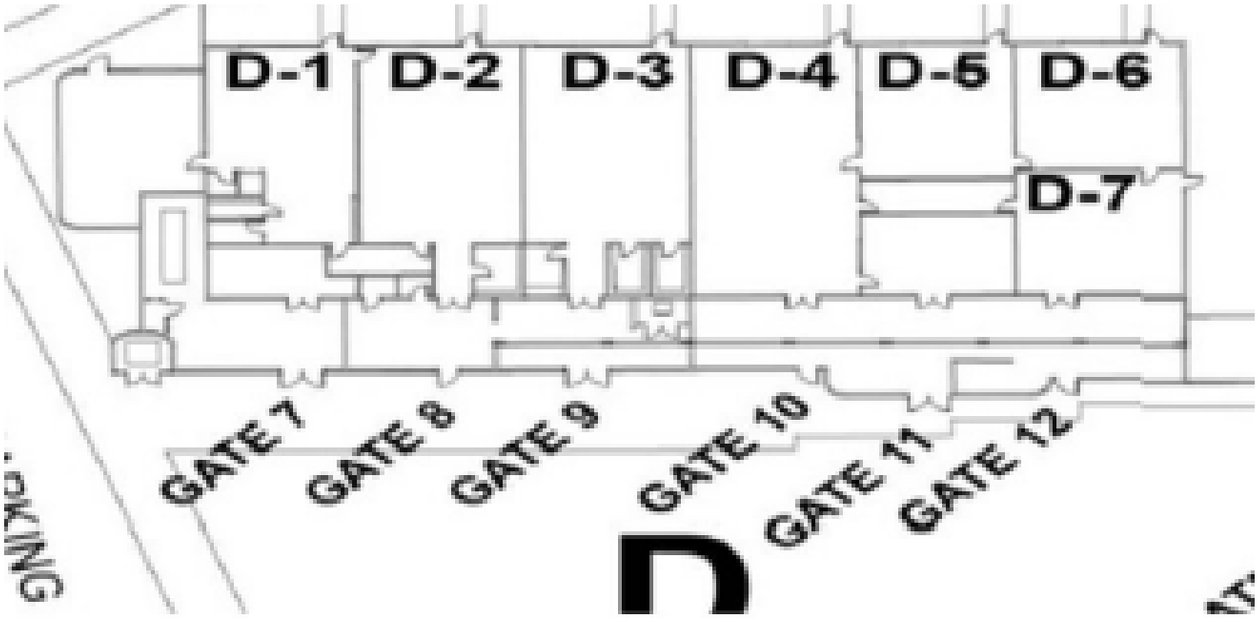


Site Plan (5)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 500 - Pod D

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

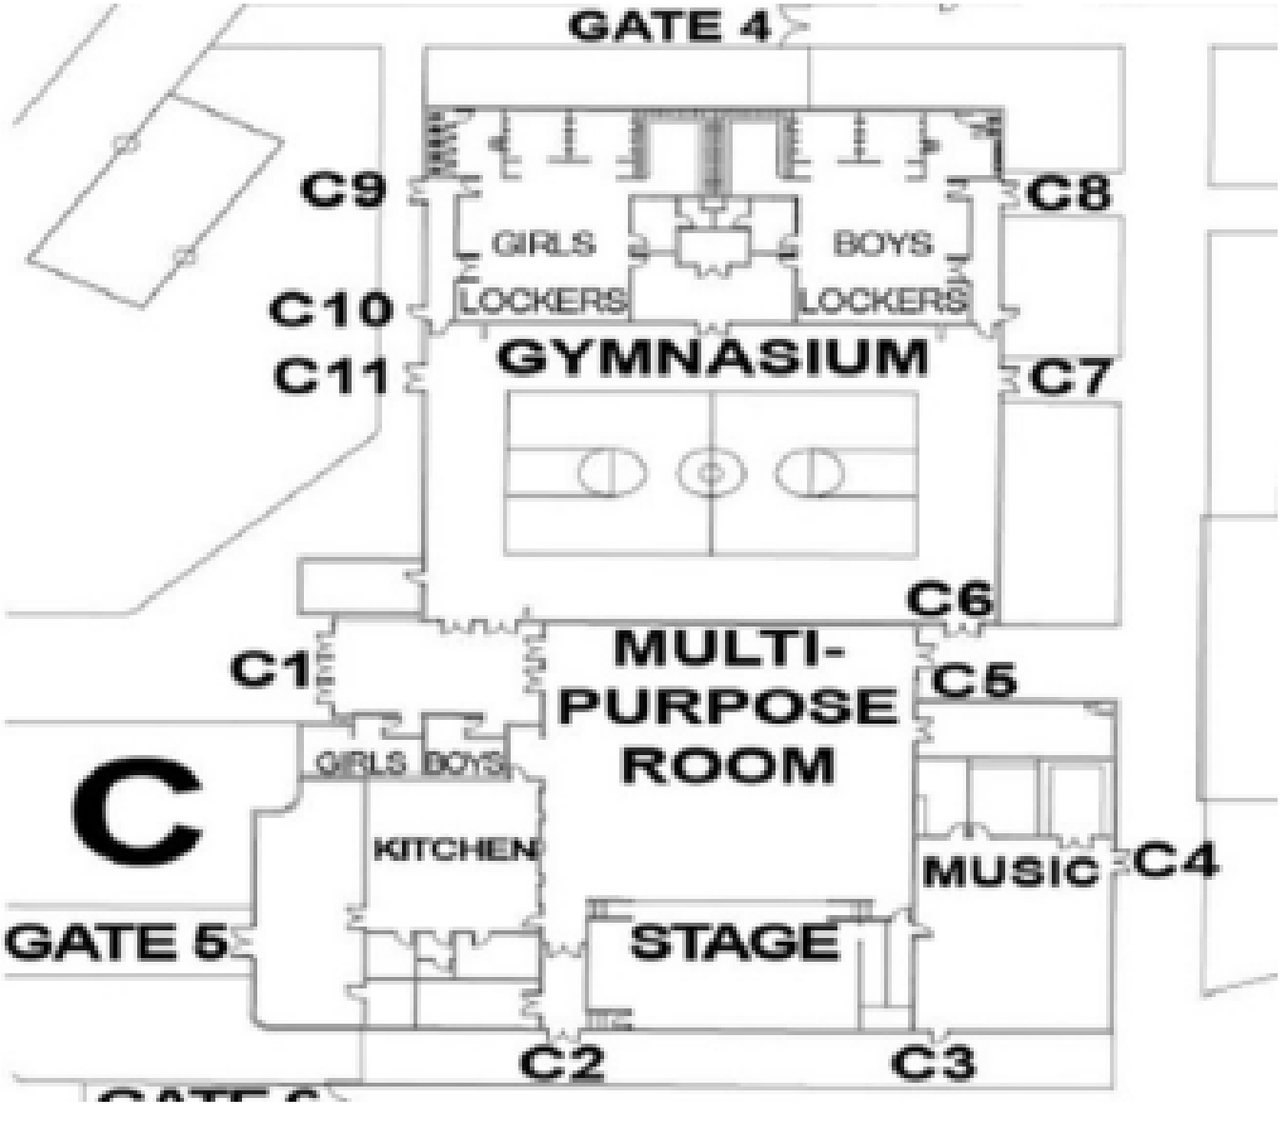


Site Plan (6)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 600 - Pod C

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

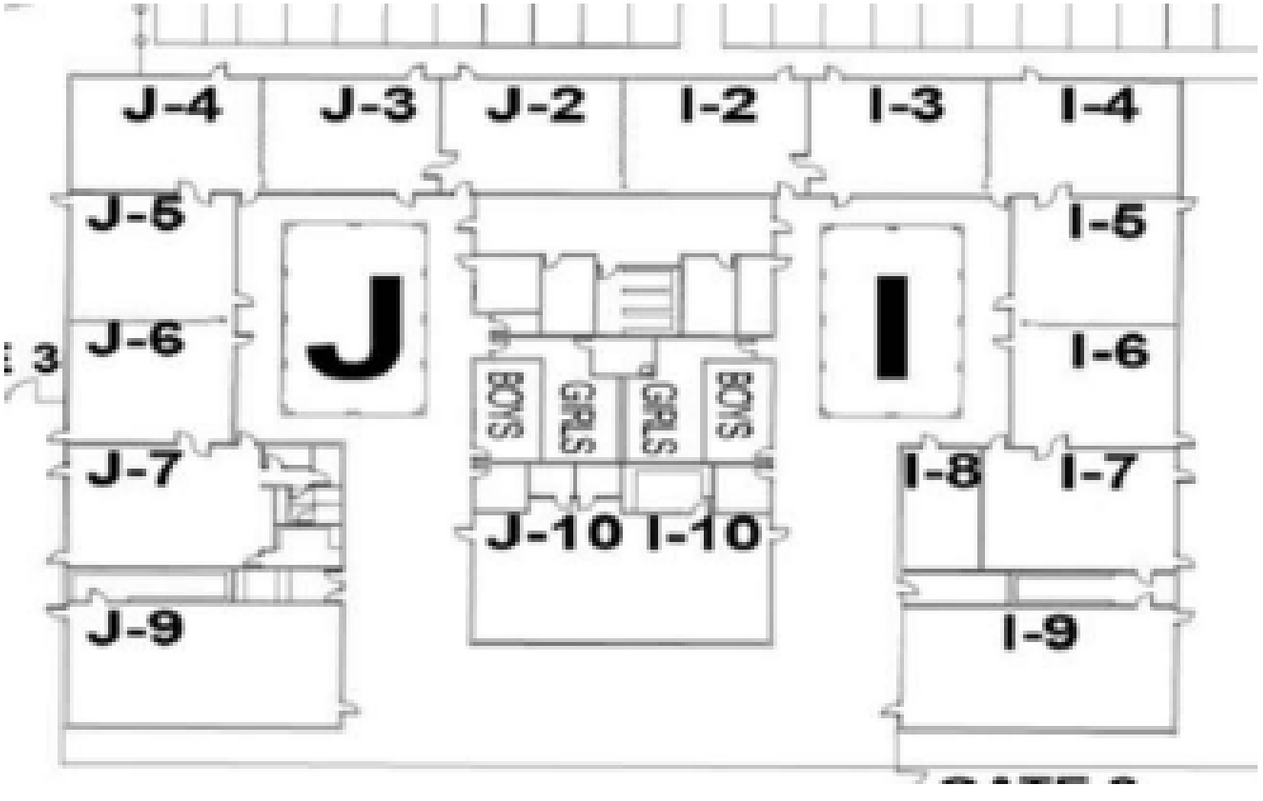

Site Plan (7)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 700 - Pod I/J

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

SECTION 5

♦

HOMOGENEOUS MATERIALS INVENTORY LISTS

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): June 24,2025	Site: Kyrene Del Pueblo Middle School - Building 100 - Pod A/B

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
Inspection Date: June 24, 2025- AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)						
1	Gray Multicolored Carpet Square	Throughout	No	No	M	20,000
2	Orange Mastic for Gray Multicolored Carpet Square		No	No	M	
3	Blue Cove Base	Throughout	No	No	M	600
4	Cream Mastic for Blue Cove Base		No	No	M	
5	Orange Peel Drywall System - Beige Paint	Throughout	No	No	M	30,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	Whtie Joint Compound		No	No	M	
	White Drywall with Brown Paper		No	No	M	
6	New 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	5,000
7	Old 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	15,000
8	Red-Brown Brick	Throughout	No	No	M	100,000
9	Red Mortar for Red-Brown Brick		No	No	M	
Assumed ACBM						
10	Interior Caulking	Throughout	Assumed	No	M	100
11	Exterior Caulking	Throughout	Assumed	No	M	100
12	Tackboard	Throughout	Assumed	No	M	10,000
13	Black Sink Coating	Throughout	Assumed	No	M	100
14	Black Countertops	Rooms A-9 and B-9	Assumed	No	M	2,000
15	Fume Hood Panel		Assumed	No	M	100
16	Tan 12" x 12" Vinyl Floor Tile (VCT)	Rooms A-9 Storage and B-9 Storage, Storages, and Workroom	Assumed	No	M	3,000
17	Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
18	Brown Cove Base	Rooms A-9 Storage and B-9 Storage, Storages, and Workroom	Assumed	No	M	100
19	Mastic for Brown Cove Base		Assumed	No	M	
20	Tan 4" x 6" Ceramic Wall Tile	Restrooms	Assumed	No	M	3,000
23	Brown 4" x 6" Ceramic Wall Tile	Restrooms	Assumed	No	M	2,000
24	Dark Brown 4" x 4" Replacement Ceramic Wall Tile	Restrooms (Pod A)	Assumed	No	M	150

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): June 24,2025	Site: Kyrene Del Pueblo Middle School - Building 100 - Pod A/B

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
25	Gray 4" x 4" Replacement Ceramic Wall Tile	Restrooms (Pod A)	Assumed	No	M	150
21	Grout for Ceramic Wall Tiles	Restrooms	Assumed	No	M	530
22	Mastic for Ceramic Wall Tiles	Restrooms	Assumed	No	M	5,300
26	Tan 2" x 2" Ceramic Floor Tile	Restrooms	Assumed	No	M	2,000
27	Grout for Tan 2" x 2" Ceramic Floor Tile		Assumed	No	M	200
28	Thinset for Tan 2" x 2" Ceramic Floor Tile		Assumed	No	M	2,000
29	Fixture Caulking	Restrooms	Assumed	No	M	40
30	Divider Wall	Workroom	Assumed	No	M	1,000
31	Smooth Drywall System	Electrical	Assumed	No	M	1,500
32	Fiberglass Reinforced Plastic (FRP)	Pod B Janitor Closet	Assumed	No	M	100
33	Mastic for Fiberglass Reinforced Plastic (FRP)		Assumed	No	M	
34	Gray 5" x 5" Ceramic Floor Tile	Pod B Maintenance	Assumed	No	M	750
35	Grout for Gray 5" x 5" Ceramic Floor Tile		Assumed	No	M	75
36	Thinset for Gray 5" x 5" Ceramic Floor Tile		Assumed	No	M	750
37	Gray 5" x 5" Ceramic Wall Tile	Pod B Maintenance	Assumed	No	M	200
38	Grout for Gray 5" x 5" Ceramic Wall Tile		Assumed	No	M	20
39	Mortar for Gray 5" x 5" Ceramic Wall Tile		Assumed	No	M	200
40	Exterior Plaster Overhang	Exterior Throughout	Assumed	No	M	25,000
41	White Duct Tape	Above Ceiling	Assumed	No	M	500
42	Mastic for White Duct Tape		Assumed	No	M	
43	Unfinished Drywall System	Above Ceiling	Assumed	No	M	10,000
44	Gray Flex Duct Wrap	Above Ceiling	Assumed	No	M	500

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.11 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): March 13, 2024 + June 23, 2025	Site: Kyrene Del Pueblo Middle School - Building 200 - Pod G/H

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
Inspection Date: March 13, 2024 - AHERA Building Inspector: Tracey Carpenter (Certification #ON-4644-14588-091422)						
1	Brown Restroom Wall Tile	Restrooms	No	No	M	2,000
2	Brown Grout for Brown Restroom Wall Tile		No	No	M	200
3	Tan Mastic for Brown Restroom Wall Tile		No	No	M	2,000
4	2" x 2" Tan Restroom Floor Tile	Restrooms	No	No	M	2,000
5	Brown Grout for 2" x 2" Tan Restroom Floor Tile		No	No	M	200
6	Tan Mastic for 2" x 2" Tan Restroom Floor Tile		No	No	M	2,000
Inspection Date: June 23, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)						
7	Gray Multicolored Carpet Square	Throughout	No	No	M	20,000
8	Yellow Mastic for Gray Multicolored Carpet Square		No	No	M	
9	Blue Cove Base	Throughout	No	No	M	600
10	Cream Mastic for Blue Cove Base		No	No	M	
11	Orange Peel Drywall System - Tan Paint	Throughout	No	No	M	30,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	White Drywall with Brown Paper		No	No	M	
12	New 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	5,000
13	Old 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	15,000
14	Red Brick	Throughout	No	No	M	100,000
15	Red Mortar for Red Brick		No	No	M	
Assumed ACBM						
16	Interior Caulking	Throughout	Assumed	No	M	100
17	Exterior Caulking	Throughout	Assumed	No	M	100
18	Tackboard	Throughout	Assumed	No	M	10,000
19	Gray 6" x 6" Ceramic Floor Tile	Maintenance	Assumed	No	M	750
20	Grout for Gray 6" x 6" Ceramic Floor Tile		Assumed	No	M	75
21	Thinset for Gray 6" x 6" Ceramic Floor Tile		Assumed	No	M	750

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.11 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): March 13, 2024 + June 23, 2025	Site: Kyrene Del Pueblo Middle School - Building 200 - Pod G/H

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
22	Gray 4" x 6" Ceramic Wall Tile	Maintenance	Assumed	No	M	200
23	Grout for Gray 4" x 6" Ceramic Wall Tile		Assumed	No	M	20
24	Mastic for Gray 4" x 6" Ceramic Wall Tile		Assumed	No	M	200
25	Tan 4" x 6" Ceramic Wall Tile	Restrooms	Assumed	No	M	3,000
26	Grout for Tan 4" x 6" Ceramic Wall Tile		Assumed	No	M	300
27	Mortar for Tan 4" x 6" Ceramic Wall Tile		Assumed	No	M	3,000
28	Fixture Caulking	Restrooms	Assumed	No	M	40
29	Blue 12" X 12" Vinyl Floor Tile (VCT)	Room G-6 Storage	Assumed	No	M	250
30	Mastic for Blue 12" X 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
31	Black Sink Coating	Throughout	Assumed	No	M	100
32	Fiberglass Reinforced Plastic (FRP)	Janitor's Closet	Assumed	No	M	100
33	Mastic for Fiberglass Reinforced Plastic (FRP)		Assumed	No	M	
34	Old Black Cove Base	Janitor's Closet	Assumed	No	M	30
35	Mastic for Old Black Cove Base		Assumed	No	M	
36	Tan 12" x 12" Vinyl Floor Tile (VCT)	Rooms G-8 and H-8 Storages	Assumed	No	M	3,000
37	Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
38	Brown Cove Base	Rooms G-8 and H-8 Storages	Assumed	No	M	75
39	Mastic for Brown Cove Base		Assumed	No	M	
40	Black Countertops	Rooms G-8 and H-8	Assumed	No	M	2,000
41	Fume Hood Panel		Assumed	No	M	100
42	Divider Wall	Workroom	Assumed	No	M	1,000
43	Exterior Plaster Overhang	Exterior Throughout	Assumed	No	M	25,000
44	Unfinished Drywall	Above Ceiling	Assumed	No	M	10,000
45	White Duct Tape	Above Ceiling	Assumed	No	M	500
46	Mastic for White Duct Tape		Assumed	No	M	
47	White Pipe Wrap	Above Ceiling	Assumed	No	M	1,000
48	Mastic for White Pipe Wrap		Assumed	No	M	

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ0959.3108 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): July 12, 2022 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 300 - Administration Office

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
Inspection Date: July 12, 2022 - AHERA Building Inspector: Nick Marcos (Certification #ON-4644-8873-032422)						
1	Smooth Drywall System - Off-White Paint	Janitor's Closet	No	No	M	5,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	White Drywall with Brown Paper		No	No	M	
2	White Fiberglass Reinforced Plastic (FRP)	Janitor's Closet	No	No	M	150
3	Off-White Mastic for White Fiberglass Reinforced Plastic (FRP)		No	No	M	
4	Gray Cove Base	Janitor's Closet	No	No	M	150
5	Yellow Mastic for Gray Cove Base		No	No	M	
6	White Mop Sink Caulking	Janitor's Closet	No	No	M	3
7	Orange Peel Drywall System - Off-White Paint	Throughout	No	No	M	20,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	White Drywall with Brown Paper		No	No	M	
8	Blue Cove Base	Janitor's Closet	No	No	M	400
9	Yellow Mastic for Blue Cove Base		No	No	M	
Inspection Date: June 20, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)						
10	Gray Multicolored Carpet Square	Throughout	No	No	M	10,000
11	Tan Mastic for Gray Multicolored Carpet Square		No	No	M	
12	Blue Cove Base	Throughout	No	No	M	400
13	Cream Mastic for Blue Cove Base		No	No	M	
14	Black Carpet Square	Throughout	No	No	M	200
15	Yellow Mastic for Black Carpet Square		No	No	M	

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ0959.3108 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): July 12, 2022 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 300 - Administration Office

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
16	New 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	5,000
17	Old 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	10,000
18	Orange Peel Drywall System - Beige Paint	Throughout	No	No	M	20,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	White Drywall with Brown Paper		No	No	M	
Assumed ACBM						
19	Interior Caulking	Throughout	Assumed	No	M	100
20	Exterior Caulking	Throughout	Assumed	No	M	100
21	Black Sink Coating	Throughout	Assumed	No	M	20
22	Glass Block Mortar	Throughout	Assumed	No	M	200
23	Brick	Throughout	Assumed	No	M	25,000
24	Mortar for Brick		Assumed	No	M	
25	Tackboard	Throughout	Assumed	No	M	5,000
26	Tan 12" x 12" Vinyl Floor Tile (VCT)	Nurse's Restroom, M/IN Restrooms & Janitor's Closet	Assumed	No	M	5,000
27	Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
28	Brown Cove Base	M/IN Restrooms	Assumed	No	M	100
29	Mastic for Brown Cove Base		Assumed	No	M	
30	Fixture Caulking	Restrooms	Assumed	No	M	30
31	White Duct Tape	Above Ceiling	Assumed	No	M	500
32	Mastic for White Duct Tape		Assumed	No	M	
33	Gray Duct Mastic	Above Ceiling	Assumed	No	M	200
34	Silver Flex Duct Wrap	Above Ceiling	Assumed	No	M	2,000
35	Gray Flex Duct Wrap	Above Ceiling	Assumed	No	M	1,000
36	Silver Duct Tape	Above Ceiling	Assumed	No	M	300
37	Unfinished Drywall	Above Ceiling	Assumed	No	M	8,000
38	Silver Duct Wrap	Above Ceiling	Assumed	No	M	3,000

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 400 - Pod E

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
Inspection Date: June 20, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)						
1	Gray Multicolored Carpet Square	Throughout	No	No	M	20,000
2	Tan Mastic for Gray Multicolored Carpet Square		No	No	M	
3	Blue Carpet	Media Center	No	No	M	1,500
4	Yellow Mastic for Blue Carpet		No	No	M	
5	Blue Cove Base	Throughout	No	No	M	650
6	Off-White Mastic for Blue Cove Base		No	No	M	
7	New 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	10,000
8	Old 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	10,000
9	Orange Peel Drywall System - Tan Paint	Throughout	No	No	M	30,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	White Drywall with Brown Paper		No	No	M	
Assumed ACBM						
10	Interior Caulking	Throughout	Assumed	No	M	100
11	Exterior Caulking	Throughout	Assumed	No	M	100
12	Tan 12" x 12" Vinyl Floor Tile (VCT)	Throughout	Assumed	No	M	3,000
13	Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
14	Fixture Caulking	Restrooms	Assumed	No	M	50
15	Wallpaper	Throughout	Assumed	No	M	600
16	Tackboard	Throughout	Assumed	No	M	3,000
17	Black Sink Coating	Throughout	Assumed	No	M	50
18	Gray Cove Base	Room E-10 Restroom	Assumed	No	M	20
19	Mastic for Gray Cove Base		Assumed	No	M	
20	Brick	Throughout	Assumed	No	M	100,000
21	Mortar for Brick		Assumed	No	M	
22	White Duct Seam Tape	Above Ceiling	Assumed	No	M	500
23	Mastic for White Duct Seam Tape	Above Ceiling	Assumed	No	M	

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 400 - Pod E

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
24	Silver Flex Duct Wrap	Above Ceiling	Assumed	No	M	2,000
25	Gray Flex Duct Wrap	Above Ceiling	Assumed	No	M	1,000
26	White Pipe Wrap	Above Ceiling	Assumed	No	M	3,000
27	Mastic for White Pipe Wrap		Assumed	No	M	
28	Unfinished Drywall System	Above Ceiling	Assumed	No	M	10,000
29	Skylight Insulation Panel	Above Ceiling	Assumed	No	M	2,000

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ0959.2668 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): January 15, 2021 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 500 - Pod D

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
Inspection Date: January 15, 2021 - AHERA Building Inspector: Basilio Marcos (Certification #ON-53933-1419-061620)						
1	Black Cove Base	Rooms D-1, D-4, D-5, and Dressing Room	No	No	M	75
2	Cream Mastic for Black Cove Base		No	No	M	
3	Brown Cove Base	Rooms D-3	No	No	M	30
4	Yellow Mastic for Brown Cove Base		No	No	M	
5	Blue Cove Base	Throughout	No	No	M	100
6	Cream Mastic for Blue Cove Base		No	No	M	
7	Orange Peel Drywall System - Cream Paint	Throughout	No	No	M	12,000
	White Texture		No	No	M	
	Pink Mesh		No	No	M	
	White Joint Compound		No	No	M	
	White/Tan Drywall		No	No	M	
8	Multicolored Blue Carpet	Room D-1	No	No	M	150
9	Dark Yellow Mastic for Multicolored Blue Carpet		No	No	M	
10	Brown Wallpaper	Workroom	No	No	M	500
11	Cream Mastic for Brown Wallpaper		No	No	M	
12	Orange Peel Drywall System - Cream Paint	Throughout	No	No	M	12,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	Brown/Tan/Green Drywall		No	No	M	
13	Smooth Drywall System - Off-White/Cream Paint	Bldg. - Main Office	No	No	M	750
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	White/Tan Drywall		No	No	M	
Inspection Date: June 20, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)						
14	Gray Multicolored Carpet Square	Throughout	No	No	M	3,000
15	Yellow Mastic for Gray Multicolored Carpet Square		No	No	M	

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ0959.2668 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): January 15, 2021 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 500 - Pod D

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
16	Blue Cove Base	Throughout	No	No	M	100
17	Cream Mastic for Blue Cove Base		No	No	M	
18	2' x 2' Gray Ceiling Tile	Throughout	No	No	M	3,000
19	2' x 4' Gray Ceiling Tile	Throughout	No	No	M	4,000
20	Orange Peel Drywall System - Beige Paint	Throughout	No	No	M	12,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	White Drywall with Brown Paper		No	No	M	
21	Lightly Textured 2' x 2' Gray Ceiling Tile	Room D-2	No	No	M	2,000
Assumed ACBM						
22	Interior Caulking	Throughout	Assumed	No	M	100
23	Exterior Caulking	Throughout	Assumed	No	M	100
24	Black Sink Coating	Throughout	Assumed	No	M	50
25	Tackboard	Throughout	Assumed	No	M	3,000
26	Black 12" x 12" Vinyl Floor Tile (VCT)	Rooms D-4 and D-5, Dressing Room	Assumed	No	M	2,000
27	Mastic for Black 12" x 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
28	Divider Wall	Rooms D-4 and D-5, Dressing Room	Assumed	No	M	1,000
29	Gray Sink Coating	Rooms D-4 and D-5, Dressing Room	Assumed	No	M	10
30	Polished Concrete	Room D-2 and D-4 Costume	Assumed	No	M	3,000
31	Tan 12" x 12" Vinyl Floor Tile (VCT)	Room D-1 Office	Assumed	No	M	1,500
32	Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
33	Brown Carpet	Room D-3 Office	Assumed	No	M	500
34	Mastic for Brown Carpet		Assumed	No	M	
35	Rubber Flooring	Room D-1	Assumed	No	M	2,000
36	Fiberglass Reinforced Plastic	Room D-1	Assumed	No	M	1,000
37	Mastic for Fiberglass Reinforced Plastic		Assumed	No	M	

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ0959.2668 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): January 15, 2021 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 500 - Pod D

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
38	Brick	Throughout	Assumed	No	M	75,000
39	Mortar for Brick		Assumed	No	M	
40	Silver Duct Wrap	Above Ceiling	Assumed	No	M	2,000
41	Silver Flex Duct Wrap	Above Ceiling	Assumed	No	M	1,000
42	White Duct Seam Tape	Above Ceiling	Assumed	No	M	500
43	Mastic for White Duct Seam Tape		Assumed	No	M	
44	Silver Duct Tape	Above Ceiling	Assumed	No	M	300
45	Gray Duct Mastic	Above Ceiling	Assumed	No	M	200
46	Skylight Insulation Panel	Above Ceiling	Assumed	Yes	M	2,000
47	Unfinished Drywall System	Above Ceiling	Assumed	No	M	10,000

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.11 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): March 13, 2024 + June 24, 2025	Site: Kyrene Del Pueblo Middle School - Building 600 - Pod C

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
Inspection Date: March 13, 2024 - AHERA Building Inspector: Tracey Carpenter (Certification #ON-4644-14588-091422)						
1	Red 6" x 6" Floor Tile	Kitchen	No	No	M	5,000
2	Red-Brown Grout for Red 6" x 6" Floor Tile		No	No	M	500
3	Gray Thinset for Red 6" x 6" Floor Tile		No	No	M	5,000
4	White Mastic for Red 6" x 6" Floor Tile		No	No	M	5,000
5	Brown Cove Base	Stage	No	No	M	75
6	Yellow Mastic for Brown Cove Base		No	No	M	
Inspection Date: June 24, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)						
7	Gray Multicolored Carpet Square	Room C-1	No	No	M	2,000
8	Tan Mastic for Gray Multicolored Carpet Square		No	No	M	
9	Blue Cove Base	Throughout	No	No	M	400
10	Off-White Mastic for Blue Cove Base		No	No	M	
11	New 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	6,000
12	Old 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	6,000
13	2' x 4' Gray Ceiling Tile	Throughout	No	Yes	M	2,000
14	Orange Peel Drywall System - Off-White Paint	Throughout	No	No	M	50,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	White Drywall with Brown Paper		No	No	M	
Assumed ACBM						
15	Polished Concrete	Cafeteria/Multi-Purpose Room	Assumed	No	M	12,000
16	Floor Expansion Joint		Assumed	No	M	100
17	Interior Caulking	Throughout	Assumed	No	M	100
18	Exterior Caulking	Throughout	Assumed	No	M	100
19	Black Stair Tread	Stage	Assumed	No	M	100
20	Mastic for Black Stair Tread		Assumed	No	M	
21	Red Ramp Tread	Stage	Assumed	No	M	250
22	Mastic for Red Ramp Tread		Assumed	No	M	

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.11 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): March 13, 2024 + June 24, 2025	Site: Kyrene Del Pueblo Middle School - Building 600 - Pod C

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
23	Red 6" x 6" Ceramic Wall Tile	Kitchen	Assumed	No	M	1,000
24	Grout for Red 6" x 6" Ceramic Wall Tile		Assumed	No	M	100
25	Mortar for Red 6" x 6" Ceramic Wall Tile		Assumed	No	M	1,000
26	2' x 4' Drywall Ceiling Tile	Kitchen	Assumed	Yes	M	5,000
27	Tan 12" x 12" Vinyl Floor Tile (VCT)	Kitchen Office, Storage Rooms, Locker Rooms Entry, and Locker Rooms Offices	Assumed	No	M	1,500
28	Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
29	Fiberglass Reinforced Plastic (FRP)	Kitchen	Assumed	No	M	3,000
30	Mastic for Fiberglass Reinforced Plastic (FRP)		Assumed	No	M	
31	Silver Kitchen Caulking	Kitchen	Assumed	No	M	50
32	White 4" x 4" Ceramic Wall Tile	Restrooms	Assumed	No	M	2,000
33	Beige 4" x 4" Ceramic Wall Tile	Restrooms	Assumed	No	M	200
34	Maroon 4" x 4" Ceramic Wall Tile	Restrooms	Assumed	No	M	200
35	Grout for 4" x 4" Ceramic Wall Tiles	Restrooms	Assumed	No	M	40
36	Mastic for 4" x 4" Ceramic Wall Tiles		Assumed	No	M	2,400
37	Gray Floor Caulking	Restrooms	Assumed	No	M	1,500
38	Fixture Caulking	Restrooms	Assumed	No	M	30
39	Black L-Shaped Cove Base	Gymnasium	Assumed	No	M	200
40	Mastic for Black L-Shaped Cove Base		Assumed	No	M	
41	Tan 2" x 2" Ceramic Floor Tile	Locker Rooms	Assumed	No	M	3,000
42	Grout for Tan 2" x 2" Ceramic Floor Tile		Assumed	No	M	300
43	Thinset for Tan 2" x 2" Ceramic Floor Tile		Assumed	No	M	3,000
44	Beige 4" x 6" Ceramic Wall Tile	Locker Rooms	Assumed	No	M	4,000
45	Brown 4" x 6" Ceramic Wall Tile	Locker Rooms	Assumed	No	M	1,000
46	Grout for 4" x 6" Ceramic Wall Tiles	Locker Rooms	Assumed	No	M	500
47	Mastic for 4" x 6" Ceramic Wall Tiles		Assumed	No	M	5,000

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.11 / AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): March 13, 2024 + June 24, 2025	Site: Kyrene Del Pueblo Middle School - Building 600 - Pod C

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
48	Black Carpet Square	Gymnasium Entries	Assumed	No	M	150
49	Mastic for Black Carpet Square		Assumed	No	M	
50	Wallpaper	Room C-1 Office	Assumed	No	M	1,000
51	Black Sink Coating	Room C-1	Assumed	No	M	10
52	Unfinished Drywall System	Above Ceiling	Assumed	No	M	10,000
53	White Duct Seam Tape	Above Ceiling	Assumed	No	M	500
54	Mastic for White Duct Seam Tape		Assumed	No	M	
55	Silver Flex Duct Wrap	Above Ceiling	Assumed	No	M	2,000
56	Gray Flex Duct Wrap	Above Ceiling	Assumed	No	M	1,000
57	Silver Duct Wrap	Above Ceiling	Assumed	No	M	2,000
58	Brick	Throughout	Assumed	No	M	150,000
59	Mortar for Brick		Assumed	No	M	
60	Exterior Plaster Overhang	Exterior	Assumed	No	M	10,000

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): June 23, 2025	Site: Kyrene Del Pueblo Middle School - Building 700 - Pod I/J

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
Inspection Date: June 23, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)						
1	Gray Multicolored Carpet Square	Throughout	No	No	M	20,000
2	Yellow Mastic for Gray Multicolored Carpet Square		No	No	M	
3	Blue Cove Base	Throughout	No	No	M	600
4	Cream Mastic for Blue Cove Base		No	No	M	
5	Orange Peel Drywall System - White Paint	Throughout	No	No	M	30,000
	White Texture		No	No	M	
	Cream Tape		No	No	M	
	White Joint Compound		No	No	M	
	White Drywall with Brown Paper		No	No	M	
6	New 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	5,000
7	Old 2' x 2' Gray Ceiling Tile	Throughout	No	Yes	M	15,000
8	Textured 2' x 2' Gray Ceiling Tile	Room J-10	No	Yes	M	2,000
Assumed ACBM						
9	Interior Caulking	Throughout	Assumed	No	M	100
10	Exterior Caulking	Throughout	Assumed	No	M	100
11	Tackboard	Throughout	Assumed	No	M	10,000
12	Beige Streak 12" x 12" Vinyl Floor Tile (VCT)	Room J-7, J-8, and J-9 Storage	Assumed	No	M	3,000
13	Mastic for Beige Streak 12" x 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
14	Gray Cove Base	Room J-8, and J-9 Storage	Assumed	No	M	100
15	Mastic for Gray Cove Base		Assumed	No	M	
16	Tan 12" x 12" Vinyl Floor Tile (VCT)	Room J-7 Closet	Assumed	No	M	500
17	Mastic for Tan 12" x 12" Vinyl Floor Tile (VCT)		Assumed	No	M	
18	White 2" x 2" Ceramic Floor Tile	Restrooms	Assumed	No	M	2,000
19	Grout for White 2" x 2" Ceramic Floor Tile		Assumed	No	M	200
20	Thinset for White 2" x 2" Ceramic Floor Tile		Assumed	No	M	2,000

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

Dominion Environmental Consultants, Inc.
AHERA Suspect ACBM Homogeneous Building Materials Inventory List

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Inspection Date(s): June 23, 2025	Site: Kyrene Del Pueblo Middle School - Building 700 - Pod I/J

Homogeneous Material #	Material Description	Location(s)	ACBM Yes/No/ Assumed	Friable Yes/No	Material Category	Approximate Quantity (sq. ft.)
21	White 4" x 4" Ceramic Wall Tile	Restrooms	Assumed	No	M	5,000
22	Black 2" x 2" Ceramic Wall Tile	Restrooms	Assumed	No	M	1,000
23	Grout for Ceramic Wall Tiles	Restrooms	Assumed	No	M	600
24	Mastic for Ceramic Wall Tiles		Assumed	No	M	6,000
25	Fixture Caulking	Restrooms	Assumed	No	M	40
26	Black Sink Coating	Restrooms	Assumed	No	M	100
27	Divider Wall	Rooms J-2 - J-6 and I-2 - I-6	Assumed	No	M	5,000
28	Fiberglass Reinforced Plastic (FRP)	Throughout	Assumed	No	M	100
29	Mastic for Fiberglass Reinforced Plastic (FRP)		Assumed	No	M	
30	Soundboard Wrap	Room J-10	Assumed	No	M	5,000
31	Mastic for Soundboard Wrap		Assumed	No	M	
32	Brick	Throughout	Assumed	No	M	100,000
33	Mortar for Brick		Assumed	No	M	
34	Exterior Plaster Overhang	Exterior Throughout	Assumed	No	M	25,000
35	Unfinished Drywall System	Above Ceiling	Assumed	No	M	10,000
36	White Duct Tape	Above Ceiling	Assumed	No	M	500
37	Mastic for White Duct Tape		Assumed	No	M	
38	White Pipe Wrap	Above Ceiling	Assumed	No	M	1,000
39	Mastic for White Pipe Wrap		Assumed	No	M	
40	Gray Duct Mastic	Above Ceiling	Assumed	No	M	200
41	Silver Flex Duct Wrap	Above Ceiling	Assumed	No	M	2,000
42	Silver Duct Wrap	Above Ceiling	Assumed	No	M	2,000
43	Black Foam Pipe Insulation	Above Ceiling	Assumed	No	M	200

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

KEY:
S = Surfacing
M = Miscellaneous
TSI = Thermal System Insulation

SECTION 6

♦

PLM BULK
SAMPLE SHEETS

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): June 24,2025	Site: Kyrene Del Pueblo Middle School - Building 100 - Pod A/B

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
Sample Date: June 24, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)					
AZ1418.59- PLM-1	1	Gray Multicolored Carpet Square	Room B-4 - Northeast	Convenient	None Detected
	2	Orange Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59- PLM-2	1	Gray Multicolored Carpet Square	Room A-3 - Northeast	Convenient	None Detected
	2	Orange Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59- PLM-3	1	Gray Multicolored Carpet Square	Room A-8 - Northwest	Convenient	None Detected
	2	Orange Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59- PLM-4	3	Blue Cove Base	Room B-2 - Southwest	Convenient	None Detected
	4	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59- PLM-5	3	Blue Cove Base	Room B-6 - East	Convenient	None Detected
	4	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59- PLM-6	3	Blue Cove Base	Room A-5 - Northwest Corner	Convenient	None Detected
	4	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59- PLM-7	5	Orange Peel Drywall System - Beige Paint	Workroom - Northwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		Whtie Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59- PLM-8	5	Orange Peel Drywall System - Beige Paint	Room A-10 Southeast Storage - East	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		Whtie Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59- PLM-9	5	Orange Peel Drywall System - Beige Paint	Room B-10 Southwest Storage - West	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		Whtie Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): June 24,2025	Site: Kyrene Del Pueblo Middle School - Building 100 - Pod A/B

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ1418.59- PLM-10	6	New 2' x 2' Gray Ceiling Tile	Room B-10 - Northwest	Convenient	None Detected
AZ1418.59- PLM-11		New 2' x 2' Gray Ceiling Tile	Room A-2 - Southeast	Convenient	None Detected
AZ1418.59- PLM-12		New 2' x 2' Gray Ceiling Tile	Room A-9 - West	Convenient	None Detected
AZ1418.59- PLM-13	7	Old 2' x 2' Gray Ceiling Tile	Room B-8 - Southeast	Convenient	None Detected
AZ1418.59- PLM-14		Old 2' x 2' Gray Ceiling Tile	Room B-5 - Southwest	Convenient	None Detected
AZ1418.59- PLM-15		Old 2' x 2' Gray Ceiling Tile	Room B-3 - Northeast	Convenient	None Detected
AZ1418.59- PLM-16	8	Red-Brown Brick	Room A-10 North - Northeast Corner	Convenient	None Detected
	9	Red Mortar for Red-Brown Brick		Convenient	None Detected
AZ1418.59- PLM-17	8	Red-Brown Brick	Open Room B - Northwest	Convenient	None Detected
	9	Red Mortar for Red-Brown Brick		Convenient	None Detected
AZ1418.59- PLM-18	8	Red-Brown Brick	Open Room A - Southeast	Convenient	None Detected
	9	Red Mortar for Red-Brown Brick		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.11 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): March 13, 2024 + June 23, 2025	Site: Kyrene Del Pueblo Middle School - Building 200 - Pod G/H

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
Sample Date: March 13, 2024 - AHERA Building Inspector: Tracey Carpenter (Certification #ON-4644-14588-091422)					
AZ1418.11- PLM-1	1	Brown Restroom Wall Tile	Pod G Girl's Restroom - Northwest Corner	Convenient	None Detected
	2	Brown Grout for Brown Restroom Wall Tile		Convenient	None Detected
	3	Tan Mastic for Brown Restroom Wall Tile		Convenient	None Detected
AZ1418.11- PLM-2	1	Brown Restroom Wall Tile	Pod G Boy's Restroom - North	Convenient	None Detected
	2	Brown Grout for Brown Restroom Wall Tile		Convenient	None Detected
	3	Tan Mastic for Brown Restroom Wall Tile		Convenient	None Detected
AZ1418.11- PLM-3	1	Brown Restroom Wall Tile	Pod H Boy's Restroom - Northwest Corner	Convenient	None Detected
	2	Brown Grout for Brown Restroom Wall Tile		Convenient	None Detected
	3	Tan Mastic for Brown Restroom Wall Tile		Convenient	None Detected
AZ1418.11- PLM-4	4	2" x 2" Tan Restroom Floor Tile	Pod G Boy's Restroom - Northwest Corner	Convenient	None Detected
	5	Brown Grout for 2" x 2" Tan Restroom Floor Tile		Convenient	None Detected
	6	Tan Mastic for 2" x 2" Tan Restroom Floor Tile		Convenient	None Detected
AZ1418.11- PLM-5	4	2" x 2" Tan Restroom Floor Tile	Pod G Girl's Restroom - West	Convenient	None Detected
	5	Brown Grout for 2" x 2" Tan Restroom Floor Tile		Convenient	None Detected
	6	Tan Mastic for 2" x 2" Tan Restroom Floor Tile		Convenient	None Detected
AZ1418.11- PLM-6	4	2" x 2" Tan Restroom Floor Tile	Pod H Girl's Restroom - Center	Convenient	None Detected
	5	Brown Grout for 2" x 2" Tan Restroom Floor Tile		Convenient	None Detected
	6	Tan Mastic for 2" x 2" Tan Restroom Floor Tile		Convenient	None Detected
Sample Date: June 23, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)					
AZ1418.59-PLM-1	7	Gray Multicolored Carpet Square	Room G-6 - Northwest Corner	Convenient	None Detected
	8	Yellow Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-2	7	Gray Multicolored Carpet Square	Room H-3 - West	Convenient	None Detected
	8	Yellow Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-3	7	Gray Multicolored Carpet Square	Room H-6 - Southeast	Convenient	None Detected
	8	Yellow Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-4	9	Blue Cove Base	Room H-5 - South	Convenient	None Detected
	10	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-5	9	Blue Cove Base	Workroom - Northwest Corner	Convenient	None Detected
	10	Cream Mastic for Blue Cove Base		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.11 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): March 13, 2024 + June 23, 2025	Site: Kyrene Del Pueblo Middle School - Building 200 - Pod G/H

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ1418.59-PLM-6	9	Blue Cove Base	Room G-7 - Southeast	Convenient	None Detected
	10	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-7	11	Orange Peel Drywall System - Multicolored Paint	Workroom - Northeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59-PLM-8	11	Orange Peel Drywall System - Tan Paint	Room Between H-8 and H-9 - Northwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59-PLM-9	11	Orange Peel Drywall System - Tan Paint	Room Between G-8 and G-9 - Southeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59-PLM-10	12	New 2' x 2' Gray Ceiling Tile	Room H-8 - Southeast	Convenient	None Detected
AZ1418.59-PLM-11		New 2' x 2' Gray Ceiling Tile	Room H-4 - Southwest	Convenient	None Detected
AZ1418.59-PLM-12		New 2' x 2' Gray Ceiling Tile	Room G-2 - Northwest	Convenient	None Detected
AZ1418.59-PLM-13	13	Old 2' x 2' Gray Ceiling Tile	Room G-3 - Northwest	Convenient	None Detected
AZ1418.59-PLM-14		Old 2' x 2' Gray Ceiling Tile	Room G-5 - South	Convenient	None Detected
AZ1418.59-PLM-15		Old 2' x 2' Gray Ceiling Tile	Room H-7 - South	Convenient	None Detected
AZ1418.59-PLM-16	14	Red Brick	Open Room G - Northeast	Convenient	None Detected
	15	Red Mortar for Red Brick		Convenient	None Detected
AZ1418.59-PLM-17	14	Red Brick	Open Room G - Southwest	Convenient	None Detected
	15	Red Mortar for Red Brick		Convenient	None Detected
AZ1418.59-PLM-18	14	Red Brick	Open Room H - South	Convenient	None Detected
	15	Red Mortar for Red Brick		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ0959.3108 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): July 12, 2022 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 300 - Administration Office

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
Sample Date: July 12, 2022 - AHERA Building Inspector: Nick Marcos (Certification #ON-4644-8873-032422)					
AZ0959.3108- PLM-1	1	Smooth Drywall System - Off-White Paint	Janitor's Closet - Southeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ0959.3108- PLM-2	1	Smooth Drywall System - Off-White Paint	Janitor's Closet - Southwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ0959.3108- PLM-3	1	Smooth Drywall System - Off-White Paint	Janitor's Closet - Southwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ0959.3108- PLM-4	2	White Fiberglass Reinforced Plastic (FRP)	Janitor's Closet - Southeast	Convenient	None Detected
	3	Off-White Mastic for White Fiberglass Reinforced Plastic (FRP)		Convenient	None Detected
AZ0959.3108- PLM-5	2	White Fiberglass Reinforced Plastic (FRP)	Janitor's Closet - Southeast	Convenient	None Detected
	3	Off-White Mastic for White Fiberglass Reinforced Plastic (FRP)		Convenient	None Detected
AZ0959.3108- PLM-6	2	White Fiberglass Reinforced Plastic (FRP)	Janitor's Closet - South	Convenient	None Detected
	3	Off-White Mastic for White Fiberglass Reinforced Plastic (FRP)		Convenient	None Detected
AZ0959.3108- PLM-7	4	Gray Cove Base	Janitor's Closet - East	Convenient	None Detected
	5	Yellow Mastic for Gray Cove Base		Convenient	None Detected
AZ0959.3108- PLM-8	4	Gray Cove Base	Janitor's Closet - Center - Southeast	Convenient	None Detected
	5	Yellow Mastic for Gray Cove Base		Convenient	None Detected
AZ0959.3108- PLM-9	4	Gray Cove Base	Janitor's Closet - Southeast Corner	Convenient	None Detected
	5	Yellow Mastic for Gray Cove Base		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ0959.3108 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): July 12, 2022 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 300 - Administration Office

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ0959.3108- PLM-10	6	White Mop Sink Caulking	Janitor's Closet - Southeast Corner	Convenient	None Detected
AZ0959.3108- PLM-11		White Mop Sink Caulking	Janitor's Closet - Southeast	Convenient	None Detected
AZ0959.3108- PLM-12		White Mop Sink Caulking	Janitor's Closet - South	Convenient	None Detected
AZ0959.3108- PLM-13	7	Orange Peel Drywall System - Off-White Paint	Janitor's Closet - Southwest	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ0959.3108- PLM-14	7	Orange Peel Drywall System - Off-White Paint	Janitor's Closet - Southwest	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ0959.3108- PLM-15	7	Orange Peel Drywall System - Off-White Paint	Janitor's Closet - South	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ0959.3108- PLM-16	8	Blue Cove Base	Janitor's Closet - South	Convenient	None Detected
	9	Yellow Mastic for Blue Cove Base		Convenient	None Detected
AZ0959.3108- PLM-17	8	Blue Cove Base	Janitor's Closet - South	Convenient	None Detected
	9	Yellow Mastic for Blue Cove Base		Convenient	None Detected
AZ0959.3108- PLM-18	8	Blue Cove Base	Janitor's Closet - Southwest	Convenient	None Detected
	9	Yellow Mastic for Blue Cove Base		Convenient	None Detected
Sample Date: June 20, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)					
AZ1418.59-PLM-1	10	Gray Multicolored Carpet Square	Lounge - Northwest	Convenient	None Detected
	11	Tan Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-2	10	Gray Multicolored Carpet Square	ISS - Northwest	Convenient	None Detected
	11	Tan Mastic for Gray Multicolored Carpet Square		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ0959.3108 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): July 12, 2022 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 300 - Administration Office

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ1418.59-PLM-3	10	Gray Multicolored Carpet Square	North of Office - Northwest Corner	Convenient	None Detected
	11	Tan Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-4	12	Blue Cove Base	Lounge - Northwest	Convenient	None Detected
	13	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-5	12	Blue Cove Base	ISS - Northwest	Convenient	None Detected
	13	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-6	12	Blue Cove Base	North of Office - Northwest Corner	Convenient	None Detected
	13	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-7	14	Black Carpet Square	North of Office - Northwest	Convenient	None Detected
	15	Yellow Mastic for Black Carpet Square		Convenient	None Detected
AZ1418.59-PLM-8	14	Black Carpet Square	East of Office - East	Convenient	None Detected
	15	Yellow Mastic for Black Carpet Square		Convenient	None Detected
AZ1418.59-PLM-9	14	Black Carpet Square	East of Office - East	Convenient	None Detected
	15	Yellow Mastic for Black Carpet Square		Convenient	None Detected
AZ1418.59-PLM-10	16	New 2' x 2' Gray Ceiling Tile	West of Office - Northwest	Convenient	None Detected
AZ1418.59-PLM-11		New 2' x 2' Gray Ceiling Tile	North of Office - Northeast	Convenient	None Detected
AZ1418.59-PLM-12		New 2' x 2' Gray Ceiling Tile	South of Office - Southeast	Convenient	None Detected
AZ1418.59-PLM-13	17	Old 2' x 2' Gray Ceiling Tile	South Hall - Center	Convenient	None Detected
AZ1418.59-PLM-14		Old 2' x 2' Gray Ceiling Tile	South of Office - Southeast	Convenient	None Detected
AZ1418.59-PLM-15		Old 2' x 2' Gray Ceiling Tile	ISS - Southwest	Convenient	None Detected
AZ1418.59-PLM-16	18	Orange Peel Drywall System - Beige Paint	North of Office - Northwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59-PLM-17	18	Orange Peel Drywall System - Beige Paint	Lounge - Southwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ0959.3108 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): July 12, 2022 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 300 - Administration Office

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ1418.59-PLM-18	18	Orange Peel Drywall System - Beige Paint	West of Office - Northwest	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 400 - Pod E

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
Sample Date: June 20, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)					
AZ1418.59- PLM-1	1	Gray Multicolored Carpet Square	Media Center - Southeast	Convenient	None Detected
	2	Tan Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59- PLM-2	1	Gray Multicolored Carpet Square	Room E-9 - Southwest	Convenient	None Detected
	2	Tan Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59- PLM-3	1	Gray Multicolored Carpet Square	Room E-3 - Northeast	Convenient	None Detected
	2	Tan Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59- PLM-4	3	Blue Carpet	Media Center - Northwest	Convenient	None Detected
	4	Yellow Mastic for Blue Carpet		Convenient	None Detected
AZ1418.59- PLM-5	3	Blue Carpet	Media Center - North	Convenient	None Detected
	4	Yellow Mastic for Blue Carpet		Convenient	None Detected
AZ1418.59- PLM-6	3	Blue Carpet	Media Center - East	Convenient	None Detected
	4	Yellow Mastic for Blue Carpet		Convenient	None Detected
AZ1418.59- PLM-7	5	Blue Cove Base	Room South of Media Center - Southwest Corner	Convenient	None Detected
	6	Off-White Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59- PLM-8	5	Blue Cove Base	Rooms E-3 and E-9 Storage - Southwest Corner	Convenient	None Detected
	6	Off-White Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59- PLM-9	5	Blue Cove Base	Room E-10 - Southwest Corner	Convenient	None Detected
	6	Off-White Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59- PLM-10	7	New 2' x 2' Gray Ceiling Tile	Room Southeast of Media Center - Northwest Corner	Convenient	None Detected
AZ1418.59- PLM-11		New 2' x 2' Gray Ceiling Tile	Media Center - Southwest	Convenient	None Detected
AZ1418.59- PLM-12		New 2' x 2' Gray Ceiling Tile	Room South of Media Center - Center - North	Convenient	None Detected
AZ1418.59- PLM-13	8	Old 2' x 2' Gray Ceiling Tile	Rooms E-3 and E-9 Storage - Northwest	Convenient	None Detected
AZ1418.59- PLM-14		Old 2' x 2' Gray Ceiling Tile	Media Center - South	Convenient	None Detected
AZ1418.59- PLM-15		Old 2' x 2' Gray Ceiling Tile	Room E-3 - Southeast	Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 400 - Pod E

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ1418.59- PLM-16	9	Orange Peel Drywall System - Tan Paint	Room Southeast of Media Center - Southwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59- PLM-17	9	Orange Peel Drywall System - Tan Paint	Room E-10 - Northeast	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59- PLM-18	9	Orange Peel Drywall System - Tan Paint	Room E-8 - Northeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ0959.2668 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): January 15, 2021 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 500 - Pod D

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
Sample Date: January 15, 2021 - AHERA Building Inspector: Basilio Marcos (Certification #ON-53933-1419-061620)					
AZ0959.2668- PLM-1	1	Black Cove Base	Room D-1 - Southeast	Convenient	None Detected
	2	Cream Mastic for Black Cove Base		Convenient	None Detected
AZ0959.2668- PLM-2	1	Black Cove Base	Room D-1 - East	Convenient	None Detected
	2	Cream Mastic for Black Cove Base		Convenient	None Detected
AZ0959.2668- PLM-3	1	Black Cove Base	Room D-1 - Northeast	Convenient	None Detected
	2	Cream Mastic for Black Cove Base		Convenient	None Detected
AZ0959.2668- PLM-4	3	Brown Cove Base	Room D-1 - Lounge - North	Convenient	None Detected
	4	Yellow Mastic for Brown Cove Base		Convenient	None Detected
AZ0959.2668- PLM-5	3	Brown Cove Base	Room D-1 - Lounge - Northeast Corner	Convenient	None Detected
	4	Yellow Mastic for Brown Cove Base		Convenient	None Detected
AZ0959.2668- PLM-6	3	Brown Cove Base	Room D-1 - Lounge - East	Convenient	None Detected
	4	Yellow Mastic for Brown Cove Base		Convenient	None Detected
AZ0959.2668- PLM-7	5	Blue Cove Base	Workroom - Southwest Corner	Convenient	None Detected
	6	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ0959.2668- PLM-8	5	Blue Cove Base	Workroom - Southeast Corner	Convenient	None Detected
	6	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ0959.2668- PLM-9	5	Blue Cove Base	Workroom - Southeast	Convenient	None Detected
	6	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ0959.2668- PLM-10	7	Orange Peel Drywall System - Cream Paint	Room D-1 - Northeast	Convenient	None Detected
		White Texture		Convenient	None Detected
		White/Tan Drywall		Convenient	None Detected
AZ0959.2668- PLM-11	7	Orange Peel Drywall System - Cream Paint	Room D-1 - Northeast	Convenient	None Detected
		White Texture		Convenient	None Detected
		Pink Mesh		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White/Tan Drywall		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ0959.2668 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): January 15, 2021 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 500 - Pod D

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ0959.2668- PLM-12	7	Orange Peel Drywall System - Cream Paint	Workroom - Southeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Pink Mesh		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White/Tan Drywall		Convenient	None Detected
AZ0959.2668- PLM-13	8	Multicolored Blue Carpet	Workroom - Southwest Corner	Convenient	None Detected
	9	Dark Yellow Mastic for Multicolored Blue Carpet		Convenient	None Detected
AZ0959.2668- PLM-14	8	Multicolored Blue Carpet	Workroom - Southeast	Convenient	None Detected
	9	Dark Yellow Mastic for Multicolored Blue Carpet		Convenient	None Detected
AZ0959.2668- PLM-15	8	Multicolored Blue Carpet	Workroom - Southeast	Convenient	None Detected
	9	Dark Yellow Mastic for Multicolored Blue Carpet		Convenient	None Detected
AZ0959.2668- PLM-16	10	Brown Wallpaper	Workroom - Southeast	Convenient	None Detected
	11	Cream Mastic for Brown Wallpaper		Convenient	None Detected
AZ0959.2668- PLM-17	10	Brown Wallpaper	Workroom - Southeast	Convenient	None Detected
	11	Cream Mastic for Brown Wallpaper		Convenient	None Detected
AZ0959.2668- PLM-18	10	Brown Wallpaper	Workroom - East	Convenient	None Detected
	11	Cream Mastic for Brown Wallpaper		Convenient	None Detected
AZ0959.2668- PLM-19	12	Orange Peel Drywall System - Cream Paint	Room D-1 - Lounge - East	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		Brown/Tan/Green Drywall		Convenient	None Detected
AZ0959.2668- PLM-20	12	Orange Peel Drywall System - Cream Paint	Room D-1 - Lounge - Northeast	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		Brown/Tan/Green Drywall		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ0959.2668 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): January 15, 2021 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 500 - Pod D

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ0959.2668- PLM-21	12	Orange Peel Drywall System - Cream Paint	Room D-1 - Lounge - Northeast	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		Brown/Tan/Green Drywall		Convenient	None Detected
AZ0959.2668- PLM-22	13	Smooth Drywall System - Off-White Paint	Pod D - Bldg. Main Office - Southwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White/Tan Drywall		Convenient	None Detected
AZ0959.2668- PLM-23	13	Smooth Drywall System - Off-White Paint	Pod D - Bldg. Main Office - Southwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White/Tan Drywall		Convenient	None Detected
AZ0959.2668- PLM-24	13	Smooth Drywall System - Off-White/Cream Paint	Pod D - Bldg. Main Office - West	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White/Tan Drywall		Convenient	None Detected
Sample Date: June 20, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)					
AZ1418.59-PLM-1	14	Gray Multicolored Carpet Square	Room D-7 - Southeast	Convenient	None Detected
	15	Yellow Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-2	14	Gray Multicolored Carpet Square	Room D-6 - Northwest Corner	Convenient	None Detected
	15	Yellow Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-3	14	Gray Multicolored Carpet Square	Room D-5 - Northwest	Convenient	None Detected
	15	Yellow Mastic for Gray Multicolored Carpet Square		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ0959.2668 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): January 15, 2021 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 500 - Pod D

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ1418.59-PLM-4	16	Blue Cove Base	Room D-6 - Southwest Corner	Convenient	None Detected
	17	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-5	16	Blue Cove Base	Room D-7 - Northeast	Convenient	None Detected
	17	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-6	16	Blue Cove Base	Room D-4 - North	Convenient	None Detected
	17	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-7	18	2' x 2' Gray Ceiling Tile	Room D-7 - Northeast	Convenient	None Detected
AZ1418.59-PLM-8		2' x 2' Gray Ceiling Tile	Room D-4 Storage - Southwest	Convenient	None Detected
AZ1418.59-PLM-9		2' x 2' Gray Ceiling Tile	Room South of D-4 - Center - East	Convenient	None Detected
AZ1418.59-PLM-10	19	2' x 4' Gray Ceiling Tile	Room D-5 - South	Convenient	None Detected
AZ1418.59-PLM-11		2' x 4' Gray Ceiling Tile	Room D-7 - East	Convenient	None Detected
AZ1418.59-PLM-12		2' x 4' Gray Ceiling Tile	Room D-6 - Center - North	Convenient	None Detected
AZ1418.59-PLM-13	20	Orange Peel Drywall System - Beige Paint	Room South of D-4 - South	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59-PLM-14	20	Orange Peel Drywall System - Beige Paint	Room D-4 - Southeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59-PLM-15	20	Orange Peel Drywall System - Beige Paint	Room D-1 - Lounge - Northwest Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ0959.2668 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): January 15, 2021 + June 20, 2025	Site: Kyrene Del Pueblo Middle School - Building 500 - Pod D

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ1418.59-PLM-16	21	Lightly Textured 2' x 2' Gray Ceiling Tile	Room D-2 - Northwest	Convenient	None Detected
AZ1418.59-PLM-17		Lightly Textured 2' x 2' Gray Ceiling Tile	Room D-2 - Center - Northwest	Convenient	None Detected
AZ1418.59-PLM-18		Lightly Textured 2' x 2' Gray Ceiling Tile	Room D-2 - South	Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.11 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): March 13, 2024 + June 24, 2025	Site: Kyrene Del Pueblo Middle School - Building 600 - Pod C

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
Sample Date: March 13, 2024 - AHERA Building Inspector: Tracey Carpenter (Certification #ON-4644-14588-091422)					
AZ1418.11- PLM-1	1	Red 6" x 6" Floor Tile	Kitchen - Southwest Corner	Convenient	None Detected
	2	Red-Brown Grout for Red 6" x 6" Floor Tile		Convenient	None Detected
	3	Gray Thinset for Red 6" x 6" Floor Tile		Convenient	None Detected
	4	White Mastic for Red 6" x 6" Floor Tile		Convenient	None Detected
AZ1418.11- PLM-2	1	Red 6" x 6" Floor Tile	Kitchen - West	Convenient	None Detected
	2	Red-Brown Grout for Red 6" x 6" Floor Tile		Convenient	None Detected
	3	Gray Thinset for Red 6" x 6" Floor Tile		Convenient	None Detected
	4	White Mastic for Red 6" x 6" Floor Tile		Convenient	None Detected
AZ1418.11- PLM-3	1	Red 6" x 6" Floor Tile	Girl's Restroom - Southeast	Convenient	None Detected
	2	Red-Brown Grout for Red 6" x 6" Floor Tile		Convenient	None Detected
	3	Gray Thinset for Red 6" x 6" Floor Tile		Convenient	None Detected
	4	White Mastic for Red 6" x 6" Floor Tile		Convenient	None Detected
AZ1418.11- PLM-4	5	Brown Cove Base	Stage - East	Convenient	None Detected
	6	Yellow Mastic for Brown Cove Base		Convenient	None Detected
AZ1418.11- PLM-5	5	Brown Cove Base	Stage - Southeast	Convenient	None Detected
	6	Yellow Mastic for Brown Cove Base		Convenient	None Detected
AZ1418.11- PLM-6	5	Brown Cove Base	Stage - Southeast	Convenient	None Detected
	6	Yellow Mastic for Brown Cove Base		Convenient	None Detected
Sample Date: June 24, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)					
AZ1418.59-PLM-1	7	Gray Multicolored Carpet Square	Room C-1 - East	Convenient	None Detected
	8	Tan Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-2	7	Gray Multicolored Carpet Square	Room Northeast of C-1 - Northeast Corner	Convenient	None Detected
	8	Tan Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-3	7	Gray Multicolored Carpet Square	Room Northwest of C-1 - West	Convenient	None Detected
	8	Tan Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59-PLM-4	9	Blue Cove Base	Cafeteria/Multi-Purpose Room - Southwest	Convenient	None Detected
	10	Off-White Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-5	9	Blue Cove Base	Cafeteria/Multi-Purpose Room - North	Convenient	None Detected
	10	Off-White Mastic for Blue Cove Base		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.11 / AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): March 13, 2024 + June 24, 2025	Site: Kyrene Del Pueblo Middle School - Building 600 - Pod C

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ1418.59-PLM-6	9	Blue Cove Base	Room C-1 - West	Convenient	None Detected
	10	Off-White Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59-PLM-7	11	New 2' x 2' Gray Ceiling Tile	Cafeteria/Multi-Purpose Room - Southwest	Convenient	None Detected
AZ1418.59-PLM-8		New 2' x 2' Gray Ceiling Tile	Cafeteria/Multi-Purpose Room - Northwest	Convenient	None Detected
AZ1418.59-PLM-9		New 2' x 2' Gray Ceiling Tile	Room C-1 - Southeast	Convenient	None Detected
AZ1418.59-PLM-10	12	Old 2' x 2' Gray Ceiling Tile	Room C-1 - Southeast	Convenient	None Detected
AZ1418.59-PLM-11		Old 2' x 2' Gray Ceiling Tile	Room Northeast of C-1 - Northeast Corner	Convenient	None Detected
AZ1418.59-PLM-12		Old 2' x 2' Gray Ceiling Tile	Room North of C-1 - North	Convenient	None Detected
AZ1418.59-PLM-13	13	2' x 4' Gray Ceiling Tile	Cafeteria/Multi-Purpose Room - Northeast	Convenient	None Detected
AZ1418.59-PLM-14		2' x 4' Gray Ceiling Tile	Cafeteria/Multi-Purpose Room - Southeast	Convenient	None Detected
AZ1418.59-PLM-15		2' x 4' Gray Ceiling Tile	Hall North of Restrooms - Center - East	Convenient	None Detected
AZ1418.59-PLM-16	14	Orange Peel Drywall System - Off-White Paint	Room Northeast of C-1 - Northeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59-PLM-17	14	Orange Peel Drywall System - Off-White Paint	Room Northwest of C-1 - Northeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59-PLM-18	14	Orange Peel Drywall System - Off-White Paint	PE Girl's Locker Room - Center - Northeast	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): June 23, 2025	Site: Kyrene Del Pueblo Middle School - Building 700 - Pod I/J

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
Sample Date: June 23, 2025 - AHERA Building Inspector: Nick Marcos (Certification #ON-188748-8873-031325)					
AZ1418.59- PLM-1	1	Gray Multicolored Carpet Square	Room I-4 - Northwest	Convenient	None Detected
	2	Yellow Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59- PLM-2	1	Gray Multicolored Carpet Square	Room J-2 - Northwest	Convenient	None Detected
	2	Yellow Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59- PLM-3	1	Gray Multicolored Carpet Square	Room I-8 - North	Convenient	None Detected
	2	Yellow Mastic for Gray Multicolored Carpet Square		Convenient	None Detected
AZ1418.59- PLM-4	3	Blue Cove Base	Room I-3 - Southeast	Convenient	None Detected
	4	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59- PLM-5	3	Blue Cove Base	Room J-4 - Northwest Corner	Convenient	None Detected
	4	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59- PLM-6	3	Blue Cove Base	Room J-6 - Southeast	Convenient	None Detected
	4	Cream Mastic for Blue Cove Base		Convenient	None Detected
AZ1418.59- PLM-7	5	Orange Peel Drywall System - White Paint	Room J-9 - Southeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59- PLM-8	5	Orange Peel Drywall System - White Paint	Workroom - Northeast Corner	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected
AZ1418.59- PLM-9	5	Orange Peel Drywall System - White Paint	Room South of Workroom - East	Convenient	None Detected
		White Texture		Convenient	None Detected
		Cream Tape		Convenient	None Detected
		White Joint Compound		Convenient	None Detected
		White Drywall with Brown Paper		Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

Dominion Environmental Consultants, Inc.
AHERA PLM Bulk Sample Summary

Dominion Project Number(s): AZ1418.59	Client: Kyrene Elementary School District
Sample Date(s): June 23, 2025	Site: Kyrene Del Pueblo Middle School - Building 700 - Pod I/J

Sample Number	HM#	Material Description	Sample Location	Manner of Sampling	Asbestos Content
AZ1418.59- PLM-10	6	New 2' x 2' Gray Ceiling Tile	Room I-5 - Northwest	Convenient	None Detected
AZ1418.59- PLM-11		New 2' x 2' Gray Ceiling Tile	Room J-5 - Northwest	Convenient	None Detected
AZ1418.59- PLM-12		New 2' x 2' Gray Ceiling Tile	Room J-3 - Southwest Corner	Convenient	None Detected
AZ1418.59- PLM-13	7	Old 2' x 2' Gray Ceiling Tile	Room J-7 - Southeast	Convenient	None Detected
AZ1418.59- PLM-14		Old 2' x 2' Gray Ceiling Tile	Room I-5 - Northwest	Convenient	None Detected
AZ1418.59- PLM-15		Old 2' x 2' Gray Ceiling Tile	Room I-9 - Southwest Corner	Convenient	None Detected
AZ1418.59- PLM-16	8	Textured 2' x 2' Gray Ceiling Tile	Room J-10 - Northwest Corner	Convenient	None Detected
AZ1418.59- PLM-17		Textured 2' x 2' Gray Ceiling Tile	Room I-10 - Northeast Corner	Convenient	None Detected
AZ1418.59- PLM-18		Textured 2' x 2' Gray Ceiling Tile	Room I-10 - Southeast Corner	Convenient	None Detected

Inspector: Nick Marcos
Certificate # : ON-188748-8873-031325
State: Arizona

DOMINION

SECTION 7

♦

PLM BULK SAMPLE LOCATION MAPS




PLM Bulk Sample Location Map
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 100 - Pod A/B

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

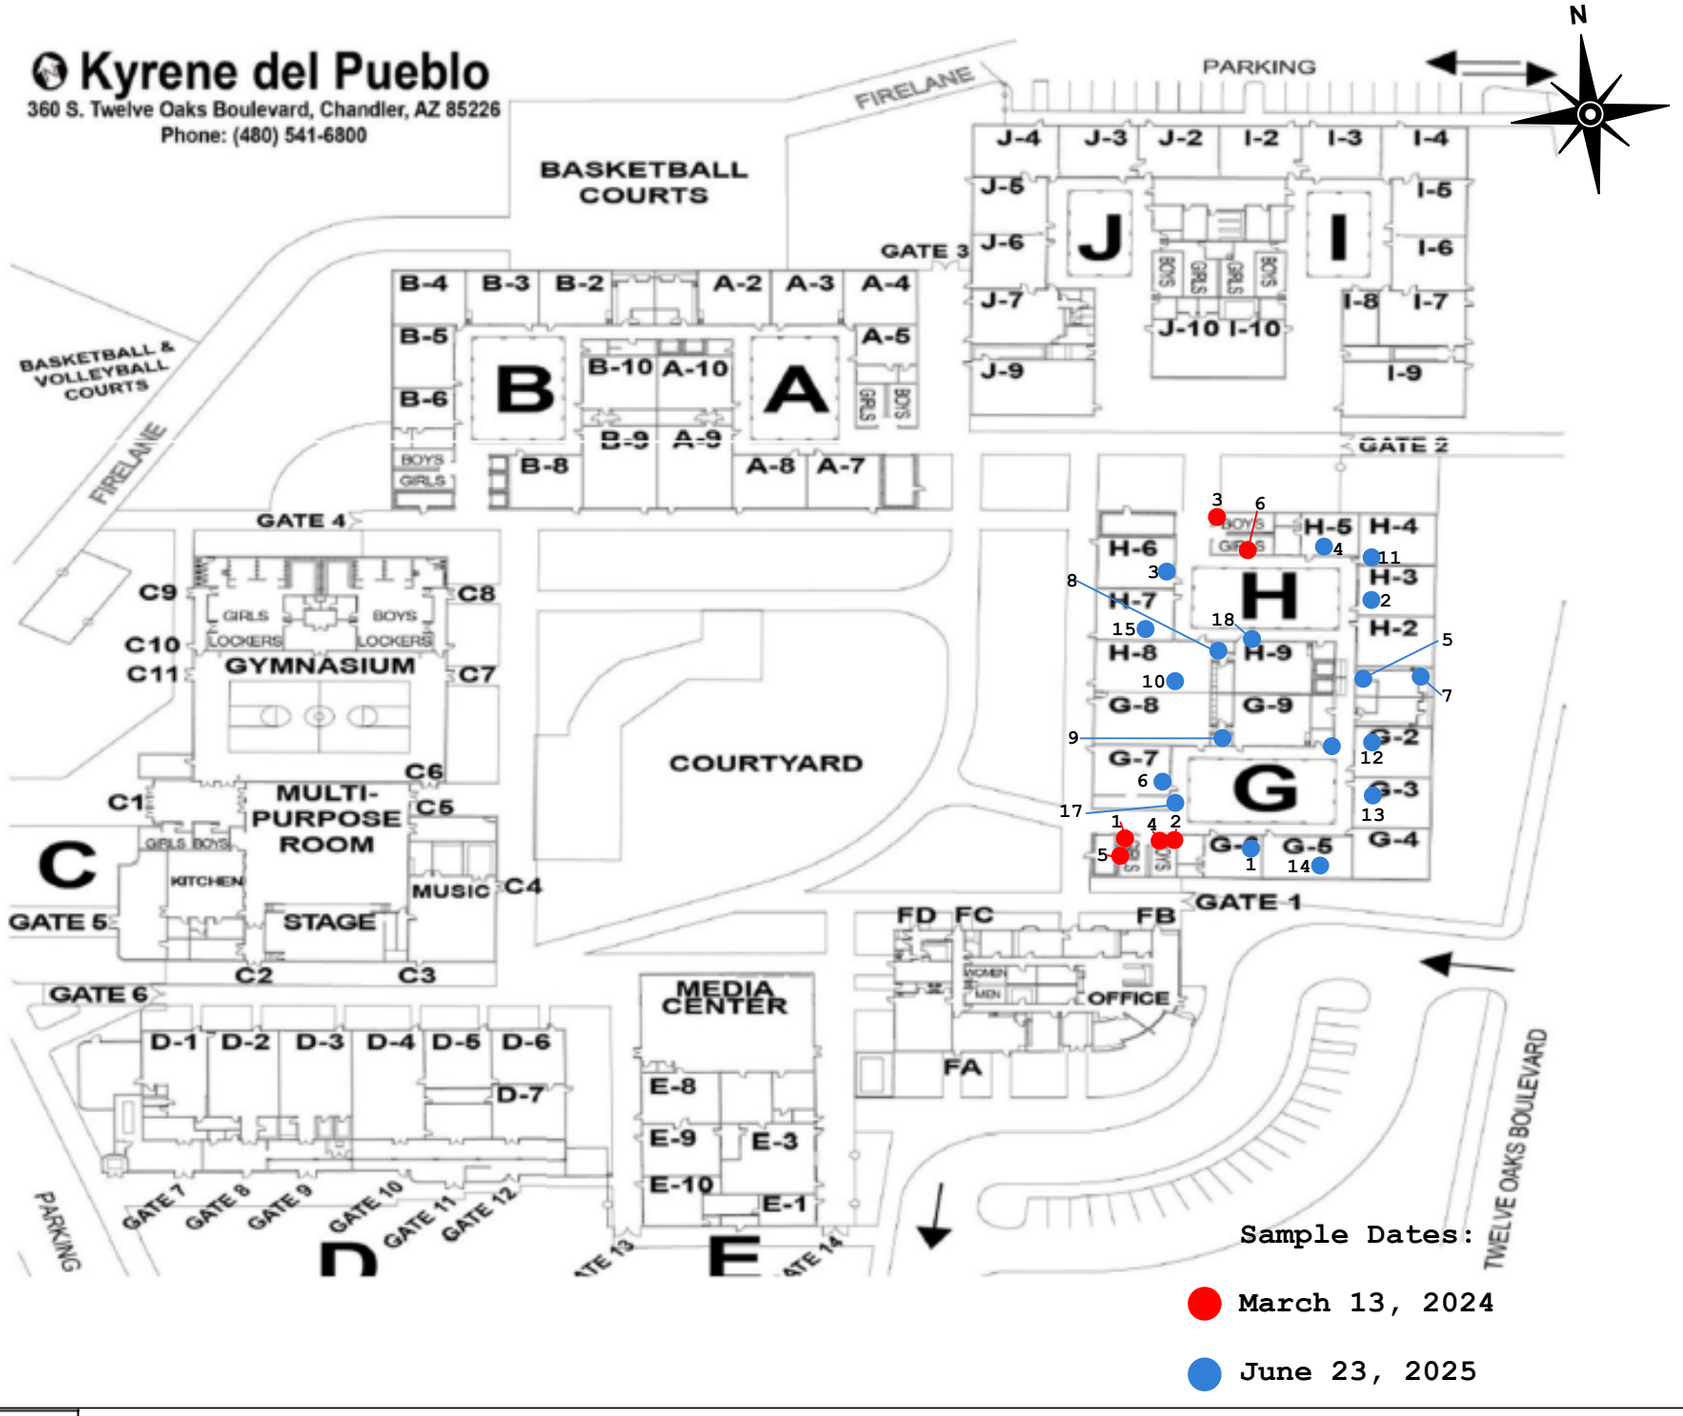


PLM Bulk Sample Location Map
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.11/AZ1418.59

Building 200 - Pod G/H

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

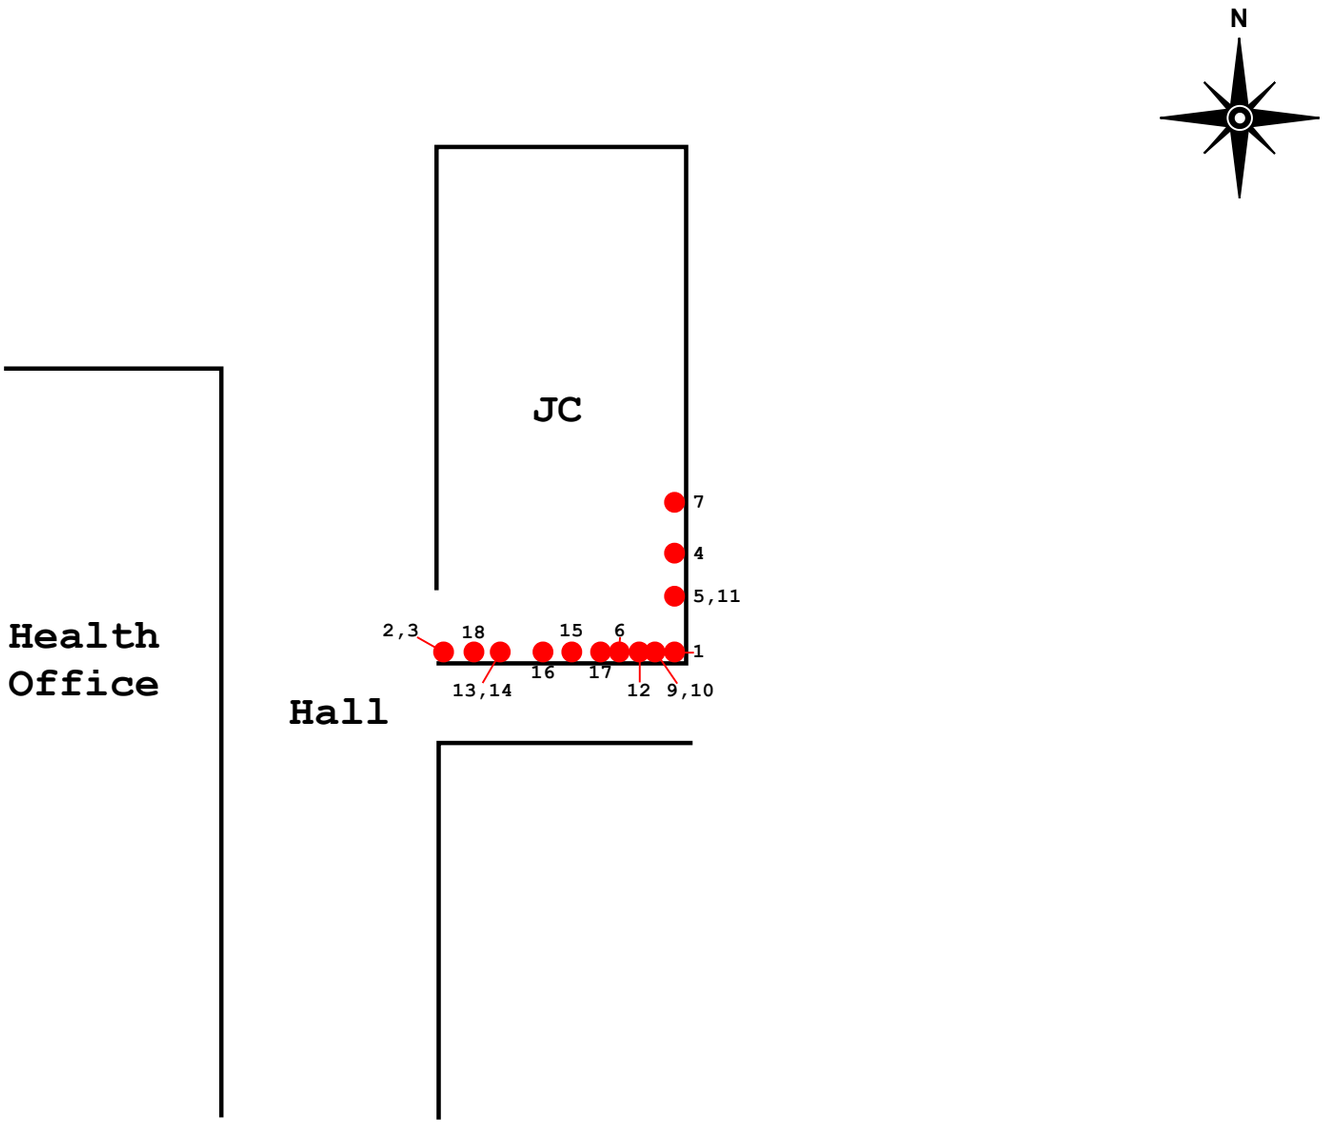

Sample Date:

July 12, 2022

PLM Bulk Sample Location Map (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ0959.3108/AZ1418.59

Building 300 - Administration Office

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415



PLM Bulk Sample Location Map (2)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ0959.3108/AZ1418.59

Building 300 - Administration Office

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415




PLM Bulk Sample Location Map
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 400 - Pod E

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

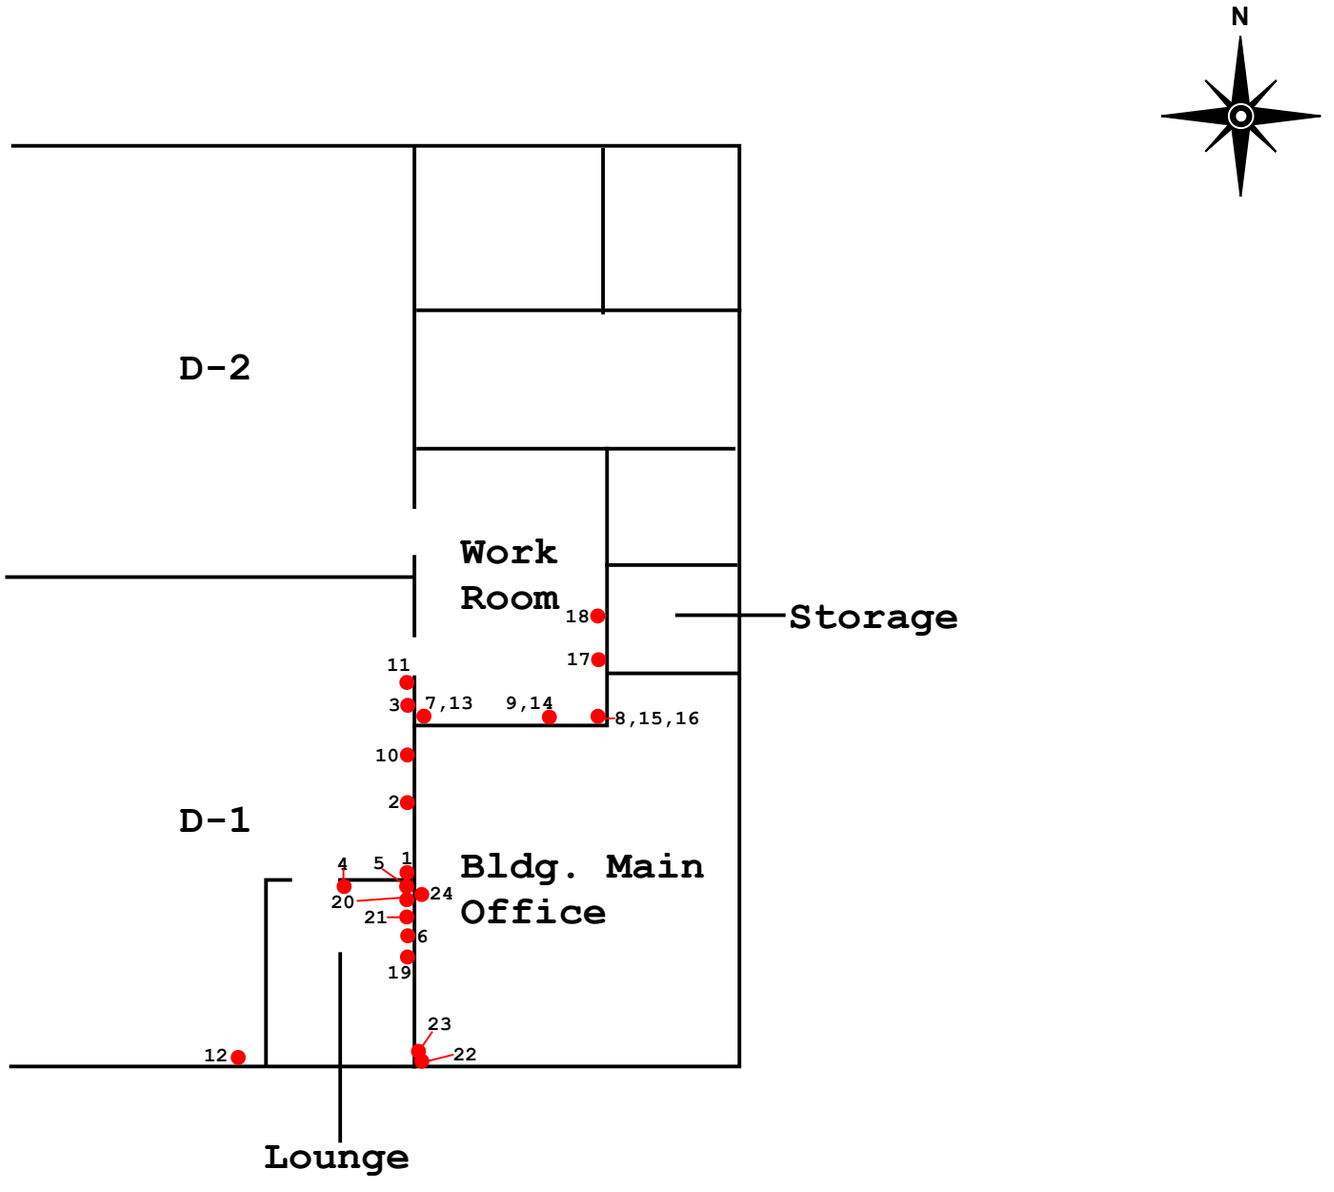

Sample Date:

January 15, 2021

PLM Bulk Sample Location Map (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ0959.2668/AZ1418.59

Building 500 - Pod D

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415




PLM Bulk Sample Location Map (2)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ0959.2668/AZ1418.59

Building 500 - Pod D

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

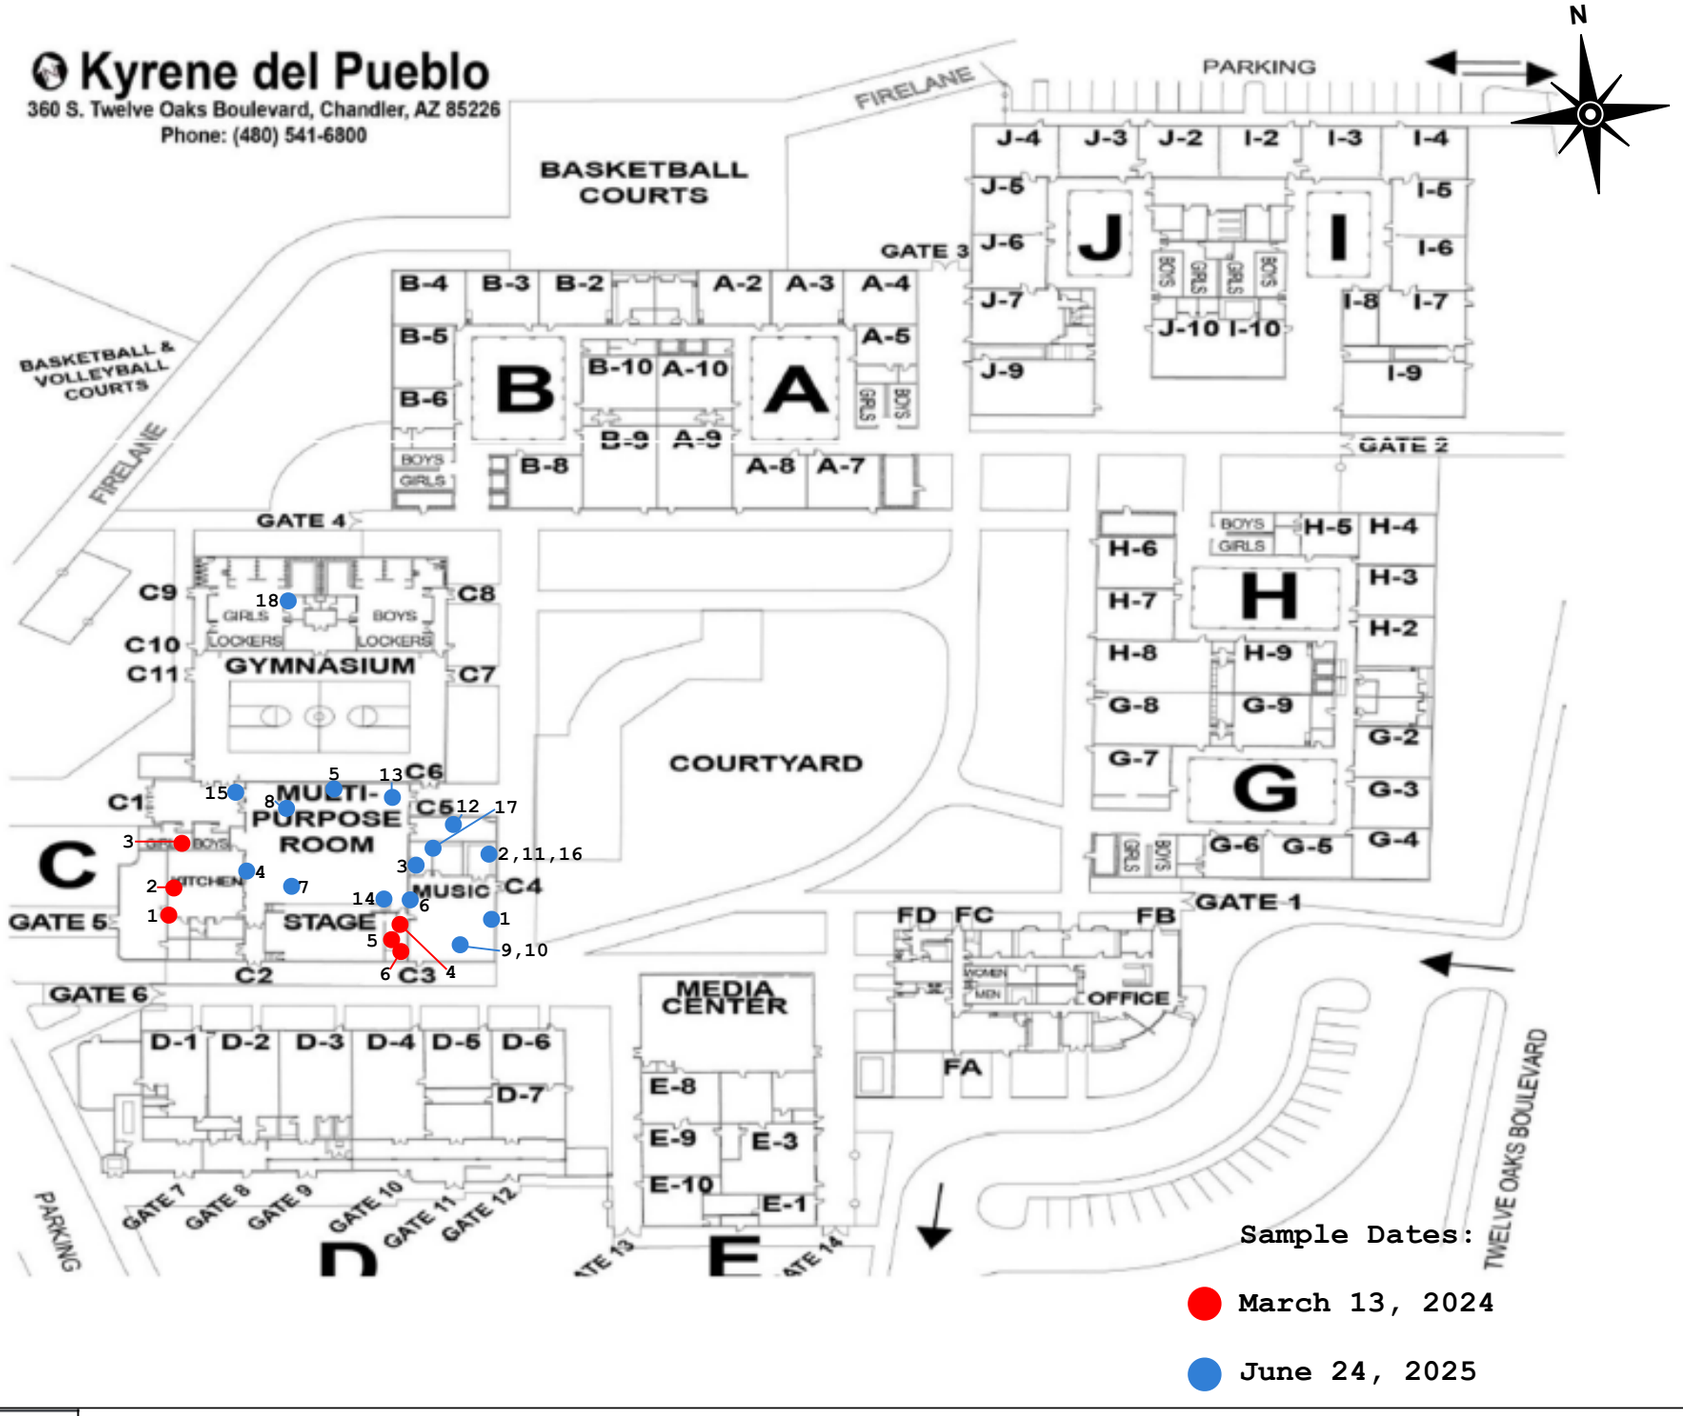


PLM Bulk Sample Location Map
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.11/AZ1418.59

Building 600 - Pod C

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

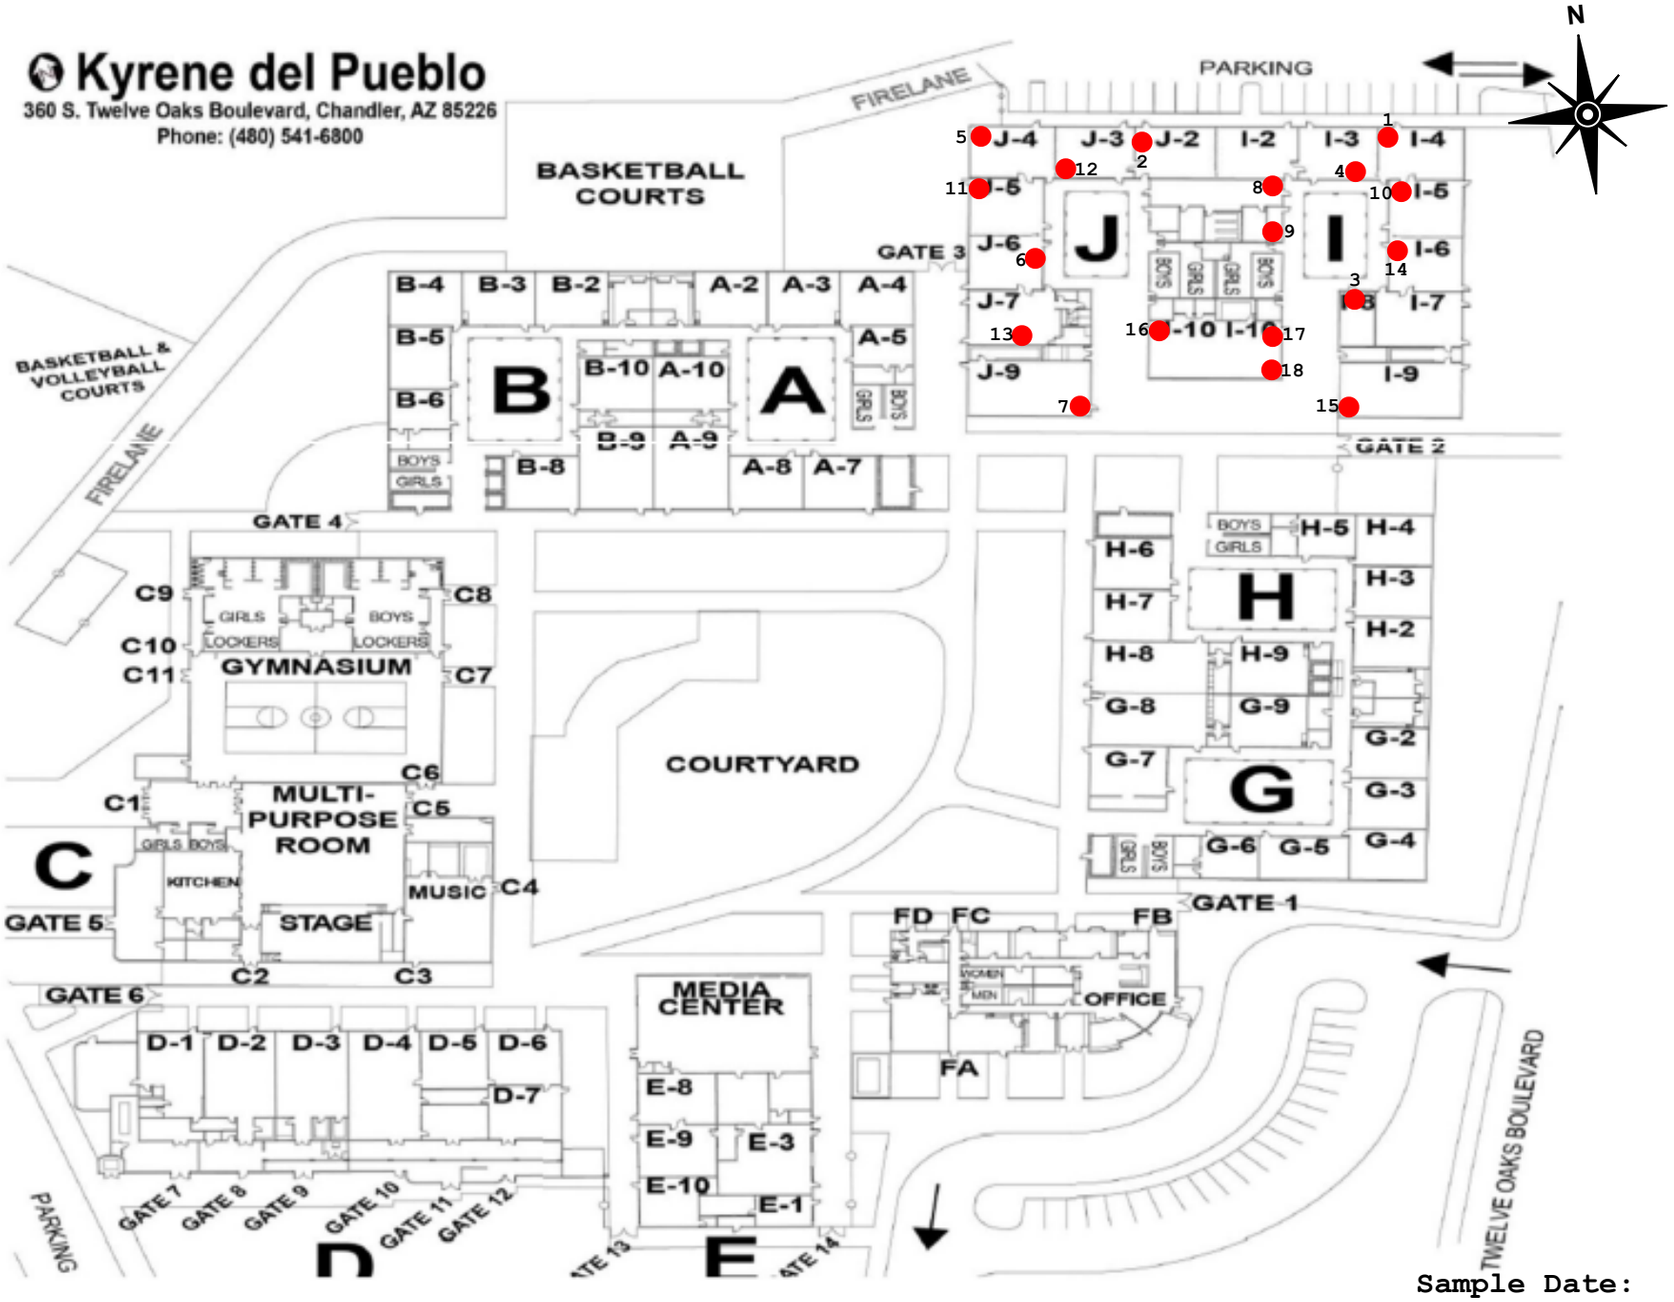

PLM Bulk Sample Location Map
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 700 - Pod I/J

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

SECTION 8

♦

PHYSICAL ASSESSMENT INFORMATION SHEETS

BUILDING MATERIAL PHYSICAL ASSESSMENT INFORMATION SHEET

Project #: AZ1418.59 **Client:** Kyrene Elementary School District **Site:** Kyrene Del Pueblo Middle School **Bldg. #:** 400 – Pod E

(HM) Material #: 29 **Quantity of Material:** 2,000 sq. ft . **Material in Air Plenum?** Yes No

Material Description: Skylight Insulation Panel **Material Location(s):** Above Ceiling

Material Type: TSI Surfacing
Miscellaneous (Circle One)

Physical Assessment Categories

G	1) Damaged or significantly damaged TSI ACBM	G	5) ACBM with potential for damage
G	2) Damaged friable surfacing ACBM	G	6) ACBM with potential for significant damage
G	3) Significantly damaged friable surfacing ACBM	■	7) Any remaining friable ACBM or friable suspect ACBM
G	4) Damaged or significantly damaged friable misc. ACBM		

Material Condition

Damage Type: G Physical G Vandalism G Water G Vibration G Air Erosion ■ None G Other

Damage Extent: ■ Low <1% evenly; 10% locally G Moderate <10% evenly; 10% - 25% locally G High >10% evenly; >25% locally

Description of Damage: None, Assumed ACBM

Exposure Factors

Accessibility:	■	Low	**Occupancy:**	G	Low	**Potential for Contact:**	■	Low	**Potential for Vibration:**	G	Low
	G	Moderate		■	Moderate		G	Moderate		■	Moderate
	G	High		G	High		G	High		G	High

Potential for Air Erosion:	G	Low									
	■	Moderate									
	G	High									

Preventative Measures: Low Potential for Disturbance

Hazard Classification/Assessment Categories

■	1) Good condition with low potential for disturbance damage	G	5) Damaged condition with potential for disturbance damage
G	2) Good condition with potential for disturbance damage	G	6) Damaged condition with potential for significant disturbance damage
G	3) Good condition with potential for significant disturbance damage	G	7) Significant damage with potential for any disturbance
G	4) Damaged condition with low potential for disturbance damage		

Inspector: Nick Marcos
Certificate #: ON-188748-8873-031325 **State:** Arizona
Signature: Nick Marcos **Exp Date:** March 13, 2026

Management Planner: Tracey Carpenter
Certificate #: ON-4651-14588-070625 **State:** Arizona
Signature: Tracey Carpenter **Exp Date:** July 6, 2026

BUILDING MATERIAL PHYSICAL ASSESSMENT INFORMATION SHEET

Project #: AZ1418.59 **Client:** Kyrene Elementary School District **Site:** Kyrene Del Pueblo Middle School **Bldg. #:** 500 – Pod D

(HM) Material #: 46 **Quantity of Material:** 2,000 sq. ft . **Material in Air Plenum?** Yes No

Material Description: Skylight Insulation Panel **Material Location(s):** Above Ceiling

Material Type: TSI Surfacing
Miscellaneous (Circle One)

Physical Assessment Categories

G	1) Damaged or significantly damaged TSI ACBM	G	5) ACBM with potential for damage
G	2) Damaged friable surfacing ACBM	G	6) ACBM with potential for significant damage
G	3) Significantly damaged friable surfacing ACBM	■	7) Any remaining friable ACBM or friable suspect ACBM
G	4) Damaged or significantly damaged friable misc. ACBM		

Material Condition

Damage Type: G Physical G Water G Air Erosion G Other
G Vandalism G Vibration ■ None

Damage Extent: ■ Low <1% evenly; 10% locally G Moderate <10% evenly; 10% - 25% locally G High >10% evenly; >25% locally

Description of Damage: None, Assumed ACBM

Exposure Factors

Accessibility:	■	Low	**Occupancy:**	G	Low	**Potential for Contact:**	■	Low	**Potential for Vibration:**	G	Low	**Potential for Air Erosion:**	G	Low
	G	Moderate		■	Moderate		G	Moderate		■	Moderate		■	Moderate
	G	High		G	High		G	High		G	High		G	High

Preventative Measures: Low Potential for Disturbance

Hazard Classification/Assessment Categories

■	1) Good condition with low potential for disturbance damage	G	5) Damaged condition with potential for disturbance damage
G	2) Good condition with potential for disturbance damage	G	6) Damaged condition with potential for significant disturbance damage
G	3) Good condition with potential for significant disturbance damage	G	7) Significant damage with potential for any disturbance
G	4) Damaged condition with low potential for disturbance damage		

Inspector: Nick Marcos
Certificate #: ON-188748-8873-031325 **State:** Arizona
Signature: Nick Marcos **Exp Date:** March 13, 2026

Management Planner: Tracey Carpenter
Certificate #: ON-4651-14588-070625 **State:** Arizona
Signature: Tracey Carpenter **Exp Date:** July 6, 2026

BUILDING MATERIAL PHYSICAL ASSESSMENT INFORMATION SHEET

Project #: AZ1418.59 **Client:** Kyrene Elementary School District **Site:** Kyrene Del Pueblo Middle School **Bldg. #:** 600 – Pod C

(HM) Material #: 26 **Quantity of Material:** 5,000 sq. ft. **Material in Air Plenum?** Yes No

Material Description: 2' x 4' Drywall Ceiling Tile **Material Location(s):** Kitchen

Material Type: TSI Surfacing
Miscellaneous (Circle One)

Physical Assessment Categories

G	1) Damaged or significantly damaged TSI ACBM	G	5) ACBM with potential for damage
G	2) Damaged friable surfacing ACBM	G	6) ACBM with potential for significant damage
G	3) Significantly damaged friable surfacing ACBM	■	7) Any remaining friable ACBM or friable suspect ACBM
G	4) Damaged or significantly damaged friable misc. ACBM		

Material Condition

Damage Type: G Physical G Water G Air Erosion G Other
G Vandalism G Vibration ■ None

Damage Extent: ■ Low <1% evenly; 10% locally G Moderate <10% evenly; 10% - 25% locally G High >10% evenly; >25% locally

Description of Damage: None, Assumed ACBM

Exposure Factors

Accessibility:	■	Low	**Occupancy:**	G	Low	**Potential for Contact:**	■	Low	**Potential for Vibration:**	G	Low	**Potential for Air Erosion:**	G	Low
	G	Moderate		■	Moderate		G	Moderate		■	Moderate		■	Moderate
	G	High		G	High		G	High		G	High		G	High

Preventative Measures: Low Potential for Disturbance

Hazard Classification/Assessment Categories

■	1) Good condition with low potential for disturbance damage	G	5) Damaged condition with potential for disturbance damage
G	2) Good condition with potential for disturbance damage	G	6) Damaged condition with potential for significant disturbance damage
G	3) Good condition with potential for significant disturbance damage	G	7) Significant damage with potential for any disturbance
G	4) Damaged condition with low potential for disturbance damage		

Inspector: Nick Marcos
Certificate #: ON-188748-8873-031325 **State:** Arizona
Signature: Nick Marcos **Exp Date:** March 13, 2026

Management Planner: Tracey Carpenter
Certificate #: ON-4651-14588-070625 **State:** Arizona
Signature: Tracey Carpenter **Exp Date:** July 6, 2026

SECTION 9

♦

LABORATORY REPORTS

eurofins | Built Environment Testing

Report for:

Nick Marcos
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Eurofins Aerotech Built Environment Testing, LLC
Project: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)
EML ID: 4122890

Approved by:



Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 06-26-2025

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EB-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins Aerotech Built Environment Testing, LLC ("the Company"), a member of the Eurofins Built Environment Testing group of companies, shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Total Samples Submitted:	18
Total Samples Analyzed:	18
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM-1, Gray Multi-Color Carpet Square and Mastic Lab ID-Version‡: 20584001-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Orange Mastic	ND
Composite Non-Asbestos Content:	60% Synthetic Fibers 2% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-2, Gray Multi-Color Carpet Square and Mastic Lab ID-Version‡: 20584002-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Orange Mastic	ND
Composite Non-Asbestos Content:	60% Synthetic Fibers 2% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-3, Gray Multi-Color Carpet Square and Mastic Lab ID-Version‡: 20584003-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Orange Mastic	ND
Composite Non-Asbestos Content:	60% Synthetic Fibers 2% Glass Fibers
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-4, Blue Cove Base and Mastic

Lab ID-Version‡: 20584004-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-5, Blue Cove Base and Mastic Lab ID-Version‡: 20584005-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-6, Blue Cove Base and Mastic Lab ID-Version‡: 20584006-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-7, Orange Peel D.W. (paint,tex,tape,j.c.,d.w.) Lab ID-Version‡: 20584007-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-8, Orange Peel D.W. (paint,tex,tape,j.c.,d.w.) Lab ID-Version‡: 20584008-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-9, Orange Peel D.W. (paint,tex,tape,j.c.,d.w.) Lab ID-Version‡: 20584009-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

Location: PLM-10, New 2'x2' Ceiling Tile Lab ID-Version‡: 20584010-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	60% Cellulose 20% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-11, New 2'x2' Ceiling Tile Lab ID-Version‡: 20584011-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	60% Cellulose 20% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-12, New 2'x2' Ceiling Tile Lab ID-Version‡: 20584012-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	60% Cellulose 20% Glass Fibers
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-13, Old 2'x2' Ceiling Tile

Lab ID-Version‡: 20584013-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-14, Old 2'x2' Ceiling Tile

Lab ID-Version‡: 20584014-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-15, Old 2'x2' Ceiling Tile

Lab ID-Version‡: 20584015-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-16, Brick and Mortar

Lab ID-Version‡: 20584016-1

Sample Layers	Asbestos Content
Red-Brown Brick	ND
Red Mortar	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-17, Brick and Mortar

Lab ID-Version‡: 20584017-1

Sample Layers	Asbestos Content
Red-Brown Brick	ND
Red Mortar	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-18, Brick and Mortar

Lab ID-Version‡: 20584018-1

Sample Layers	Asbestos Content
Red-Brown Brick	ND
Red Mortar	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built


Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

PROJECT ANALYST AND SIGNATORY REPORT

Project Analyst



Analyst: Kayla Heinen

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY

www.eurofinsus.com/Built

eurofins | Built Environment Testing

East:(866) 871-1984
West/Central:(800) 651-4802

WEATHER		Fog	Rain	Snow	Wind	Clear
LEVEL	None					
	Light					
	Moderate					
	Heavy					

CONTACT INFORMATION

Company:	Dominion Environmental Consultants	Address:	20045 N. 19th Ave., Phx, AZ 85027
Contact:	Nick Marcos	Special Instructions:	
Phone:	623-516-1415		

PROJECT INFORMATION

Project ID:	AZ1418.59		
Project Description:	Kyrene Del Pueblo M.S. - Bldg 100 (Pod A/B)		
Project Zip Code:		Sampling Date/Time:	6/24/2025
PO Number:	13753	Sampled By:	NM

TURN AROUND TIME CODES - (TAT)

STD - Standard (Default)
ND - Next Business Day
SD - Same Business Day
WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

REQUESTED SERVICES

Non-Culturable

Spore Tr | Tape,

Culturable

BioCassette™, Andersen, SAS, Swab, Water, Bulk, Dust, Soil,

Other Requests

004122890

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)	Spore Trap Analysis	Other biological particles - supplement	Direct Microscopic Exam (Qualitative)	Quantitative spore count direct exam	Dust Characterization	1-Media Surface Fungi (Genus ID + Asp. s	Culturable Air Fungi (Genus ID + Asp. spp.	Gram Stain and Counts (Culturable Air and	Legionella culture	Total Coliform, E.coli (Presence/Absence)	QuantiTray-Sewage Screen	OTHER: (please specify test)	Asbestos in Air - PCM Airborne Fiber Count (NIOSH 7400)	Asbestos Bulk - PLM (EPA method 600/R-93-116)	Lead (Pb) / Paint Chip	PCR (please specify test)	Allergens (please specify test)
PLM 1-3	Gray Multi-Color Carpet Square and Mastic	B	STD																X			
PLM 4-6	Blue Cove Base and Mastic	B	STD																X			
PLM 7-9	Orange Peel D.W. (paint,tex,tape,j.c.,d.w.)	B	STD																X			
PLM 10-12	New 2' X 2' Ceiling Tile	B	STD																X			
PLM 13-15	Old 2' X 2' Ceiling Tile	B	STD																X			
PLM 16-18	Brick and Mortar	B	STD																X			

SAMPLE TYPE CODES

BC - BioCassette™	**CP** - Contact Plate	**T** - Tape	**O** - Other:
A1S - Andersen	**ST** - Spore Trap	**SW** - Swab	
SAS - Surface Air Sampler	**B** - Bulk	**SO** - Soil	
NP - Non-potable Water	**P** - Potable Water	**D** - Dust	

RELINQUISHED BY	DATE & TIME	RECEIVED BY	DATE & TIME
Nick Marcos	6/24/2025	Lydia Custer	4:10PM 6/24/25

By submitting this Chain of Custody, you agree to be bound by the terms and conditions set forth at http://www.emlab.com/s/main/serviceterms.html

eurofins | Built Environment Testing

Report for:

Tracey Carpenter
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Eurofins Aerotech Built Environment Testing, Inc.
Project: AZ1418.11; Pueblo-Bldg G-H
EML ID: 3573119

Approved by:

Renee Luna-Trepczynski

Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 03-18-2024

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EM-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins Aerotech Built Environment Testing, Inc. ("the Company"), a member of the Eurofins Built Environment Testing group of companies, shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins Aerotech Built Environment Testing, Inc.
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Tracey Carpenter
Re: AZ1418.11; Pueblo-Bldg G-H

Date of Sampling: 03-13-2024
Date of Receipt: 03-14-2024
Date of Report: 03-18-2024

ASBESTOS PLM REPORT

Total Samples Submitted:	6
Total Samples Analyzed:	6
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM1, Brown RR wall Tile & Grout & Mastic Lab ID-Version‡: 17464572-1

Sample Layers	Asbestos Content
Brown Ceramic Tile	ND
Brown Grout	ND
Tan Mastic	ND
Sample Composite Homogeneity:	Poor

Location: PLM2, Brown RR wall Tile & Grout & Mastic Lab ID-Version‡: 17464573-1

Sample Layers	Asbestos Content
Brown Ceramic Tile	ND
Brown Grout	ND
Tan Mastic	ND
Sample Composite Homogeneity:	Poor

Location: PLM3, Brown RR wall Tile & Grout & Mastic Lab ID-Version‡: 17464574-1

Sample Layers	Asbestos Content
Brown Ceramic Tile	ND
Brown Grout	ND
Tan Mastic	ND
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, Inc.
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Tracey Carpenter
Re: AZ1418.11; Pueblo-Bldg G-H

Date of Sampling: 03-13-2024
Date of Receipt: 03-14-2024
Date of Report: 03-18-2024

ASBESTOS PLM REPORT

Location: PLM4, 2"x2" Tan RR Floor Tile & Grout & Thinset Lab ID-Version‡: 17464575-1

Sample Layers	Asbestos Content
Tan Floor Tile	ND
Brown Grout	ND
Tan Mastic	ND
Sample Composite Homogeneity:	Poor

Location: PLM5, 2"x2" Tan RR Floor Tile & Grout & Thinset Lab ID-Version‡: 17464576-1

Sample Layers	Asbestos Content
Tan Floor Tile	ND
Brown Grout	ND
Tan Mastic	ND
Sample Composite Homogeneity:	Poor

Location: PLM6, 2"x2" Tan RR Floor Tile & Grout & Thinset Lab ID-Version‡: 17464577-1

Sample Layers	Asbestos Content
Tan Floor Tile	ND
Brown Grout	ND
Tan Mastic	ND
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY eurofins | EMLab P&K

www.EMLabPK.com

Marlton, NJ: 3000 Lincoln Dr E, Ste. A, Marlton, NJ 08053 * (866) 871-1984
Phoenix, AZ: 1501 West Knudsen Drive, Phoenix, AZ 85027 * (800) 651-4802
SSF, CA: 6000 Shoreline Ct, Ste. 205, S. San Francisco, CA 94080 * (866) 888-6653

WEATHER	Fog	Rain	Snow	Wind	Clear
LEVEL None					
Light					
Moderate					
Heavy					

003573119

CONTACT INFORMATION

Company:	Dominion Environmental Consultants	Address: 20045 N. 19th Ave, Bldg 7, Phoenix, AZ 85027	
Contact:	Tracey Carpenter	Special Instructions: email results: tcarpenter@dominion-env.com	
Phone:	(602) 989-9992		

PROJECT INFORMATION

Project ID:	AZ1418.11		
Project Description:	Pueblo - Bldg 6-H		
Project Zip Code:	85044	Sampling Date/Time:	3/13/24 @
PO Number:	316309	Sampled By:	TLC 9:30AM

TURN AROUND TIME CODES - (TAT)

STD - Standard (Default)
ND - Next Business Day
SD - Same Business Day
WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)	Non-Culturable: Spore Trap: Spore Trap Analysis	Non-Culturable: Tape, Swab, Bulk: Other biological particles - supplement	Direct Microscopic Exam (Qualitative)	Quatitative spore count direct exam	Dust Characterization	1-Media Surface Fungi (Genus ID + *Asp.* spp.)	Culturable Air Fungi (Genus ID + *Asp.* spp.)	Gram Stain and Counts (Culturable Air and Surface Bact	*Legionella* culture	Total Coliform, *E.coli* (Presence/Absence)	QuantiTray-Sewage Screen	OTHER: (please specify test)	Asbestos in Air - PCM Airborne Fiber Count (NIOSH 740	Asbestos Bulk - PLM (EPA method 600/R-93-116)	Lead (Pb)	PCR (please specify test)	Allergens (please specify test)
PLM 1-3	Brown RR Wall	B	STD																X			
	Tile + Grout + Mastic	1	1																			
PLM 4-6	2" x 2" Tan RR Floor	B	STD																X			
	Tile + Grout + Thinset																					

SAMPLE TYPE CODES

BC - BioCassette™	CP - Contact Plate	T - Tape	O - Other:
A1S - Andersen	ST - Spore Trap	SW - Swab	
SAS - Surface Air Sampler	B - Bulk	SO - Soil	
NP - Non-potable Water	P - Potable Water	D - Dust	

RELINQUISHED BY	DATE & TIME	RECEIVED BY	DATE & TIME
Tracey Carp	3/14/24 @9:15 AM		3-14-24

eurofins | Built Environment Testing

Report for:

Nick Marcos
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Eurofins Aerotech Built Environment Testing, LLC
Project: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)
EML ID: 4121027

Approved by:



Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 06-24-2025

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EB-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins Aerotech Built Environment Testing, LLC ("the Company"), a member of the Eurofins Built Environment Testing group of companies, shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Total Samples Submitted:	18
Total Samples Analyzed:	18
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM-1, Gray Mulit-Color Carpet Square and Mastic Lab ID-Version‡: 20573921-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	50% Synthetic Fibers 2% Glass Fibers
Sample Composite Homogeneity:	Poor

Location: PLM-2, Gray Mulit-Color Carpet Square and Mastic Lab ID-Version‡: 20573922-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	50% Synthetic Fibers 2% Glass Fibers
Sample Composite Homogeneity:	Poor

Location: PLM-3, Gray Mulit-Color Carpet Square and Mastic Lab ID-Version‡: 20573923-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	50% Synthetic Fibers 2% Glass Fibers
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-4, Blue Cove Base and Mastic

Lab ID-Version‡: 20573924-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-5, Blue Cove Base and Mastic Lab ID-Version‡: 20573925-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-6, Blue Cove Base and Mastic Lab ID-Version‡: 20573926-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-7, Orange Peel D.W. (paint, tex, tape, j.c., d.w.) Lab ID-Version‡: 20573927-1

Sample Layers	Asbestos Content
Multicolored Paint Layers	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-8, Orange Peel D.W. (paint, tex, tape, j.c., d.w.) Lab ID-Version‡: 20573928-1

Sample Layers	Asbestos Content
Tan Paint	ND
White Texture	ND
Cream Tape	ND
Transparent Adhesive	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)
Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-9, Orange Peel D.W. (paint, tex, tape, j.c., d.w.) Lab ID-Version‡: 20573929-1

Sample Layers	Asbestos Content
Tan Paint	ND
White Texture	ND
Cream Tape	ND
Transparent Adhesive	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

Location: PLM-10, New 2'x2' Ceiling Tile Lab ID-Version‡: 20573930-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	60% Cellulose 20% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-11, New 2'x2' Ceiling Tile Lab ID-Version‡: 20573931-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	60% Cellulose 20% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-12, New 2'x2' Ceiling Tile Lab ID-Version‡: 20573932-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	60% Cellulose 20% Glass Fibers
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-13, Old 2''x2' Ceiling Tile

Lab ID-Version‡: 20573933-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 30% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-14, Old 2''x2' Ceiling Tile

Lab ID-Version‡: 20573934-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 30% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-15, Old 2''x2' Ceiling Tile

Lab ID-Version‡: 20573935-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 30% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-16, Brick and Mortar

Lab ID-Version‡: 20573936-1

Sample Layers	Asbestos Content
Red Brick	ND
Red Mortar	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-17, Brick and Mortar

Lab ID-Version‡: 20573937-1

Sample Layers	Asbestos Content
Red Brick	ND
Red Mortar	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-18, Brick and Mortar

Lab ID-Version‡: 20573938-1

Sample Layers	Asbestos Content
Red Brick	ND
Red Mortar	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)
Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

PROJECT ANALYST AND SIGNATORY REPORT

Project Analyst



Analyst: Michael Williams

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY

www.eurofinsus.com/Built

eurofins | Built Environment Testing

East:(866) 871-1984
West/Central:(800) 651-4802

WEATHER	Fog	Rain	Snow	Wind	Clear
LEVEL None					
Light					
Moderate					
Heavy					

CONTACT INFORMATION

Company:	Dominion Environmental Consultants	Address:20045 N. 19th Ave., Phx, AZ 85027	
Contact:	Nick Marcos	Special Instructions:	
Phone:	623-516-1415		

PROJECT INFORMATION

Project ID:	AZ1418.59		
Project Description:	Kyrene Del Pueblo M.S. - Bldg. 200 (Pod G/H)		
Project Zip Code:		Sampling Date/Time:	6/23/2025
PO Number:	13750	Sampled By:	NM

TURN AROUND TIME CODES - (TAT)

STD - Standard (Default)
ND - Next Business Day
SD - Same Business Day
WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

REQUESTED SERVICES

Non-Culturable | Culturable | Other Requests

004121027

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)	Spore Trap Analysis	Other biological particles - supplement	Direct Microscopic Exam (Qualitative)	Quantitative spore count direct exam	Dust Characterization	1-Media Surface Fungi (Genus ID + Asp. spp.)	Culturable Air Fungi (Genus ID + Asp. spp.)	Gram Stain and Counts (Culturable Air and S	*Legionella* culture	Total Coliform, *E.coli* (Presence/Absence)	QuantiTray-Sewage Screen	OTHER: (please specify test)	Asbestos in Air - PCM Airborne Fiber Count (NIOSH 7400)	Asbestos Bulk - PLM (EPA method 600/R-93-116)	Lead (Pb) / Paint Chip	PCR (please specify test)	Allergens (please specify test)
PLM 1-3	Gray Multi-Color Carpet Square and Mastic	B	STD																X			
PLM 4-6	Blue Cove Base and Mastic	B	STD																X			
PLM 7-9	Orange Peel D.W. (paint,tex,tape,j.c.,d.w.)	B	STD																X			
PLM 10-12	New 2' X 2' Ceiling Tile	B	STD																X			
PLM 13-15	Old 2" X 2' Ceiling Tile	B	STD																X			
PLM 16-18	Brick and Mortar	B	STD																X			

SAMPLE TYPE CODES

BC - BioCassette™	**CP** - Contact Plate	**T** - Tape	**O** - Other:
A1S - Andersen	**ST** - Spore Trap	**SW** - Swab	
SAS - Surface Air Sampler	**B** - Bulk	**SO** - Soil	
NP - Non-potable Water	**P** - Potable Water	**D** - Dust	

RELINQUISHED BY	DATE & TIME
Nick Marcos	6/23/2025

RECEIVED BY	DATE & TIME
Paddy Lugo	6/23/25 3:45pm

By submitting this Chain of Custody, you agree to be bound by the terms and conditions set forth at http://www.emlab.com/s/main/serviceterms.html

eurofins | EMLab P&K

Report for:

Mr. Nick Marcos
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Project: AZ0959.3108; Kyrene del Pueblo M.S.
EML ID: 2975027

Approved by:

Renee Luna-Trepczynski

Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 07-13-2022

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EM-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins EMLab P&K ("the Company") shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins EMLab P&K
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 Fax (623) 780-7695 www.emlab.com

Client: Dominion Environmental Consultants, Inc.
C/O: Mr. Nick Marcos
Re: AZ0959.3108; Kyrene del Pueblo M.S.

Date of Sampling: 07-12-2022
Date of Receipt: 07-12-2022
Date of Report: 07-13-2022

ASBESTOS PLM REPORT

Total Samples Submitted:	18
Total Samples Analyzed:	18
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM-1, Smooth D.W. (Paint, Tex, Tape, J.C., D.W.) Lab ID-Version‡: 14307806-1

Sample Layers	Asbestos Content
Off-White Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose < 1% Glass Fibers
Sample Composite Homogeneity:	Poor

Location: PLM-2, Smooth D.W. (Paint, Tex, Tape, J.C., D.W.) Lab ID-Version‡: 14307807-1

Sample Layers	Asbestos Content
Off-White Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose < 1% Glass Fibers
Sample Composite Homogeneity:	Poor

Location: PLM-3, Smooth D.W. (Paint, Tex, Tape, J.C., D.W.) Lab ID-Version‡: 14307808-1

Sample Layers	Asbestos Content
Off-White Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose < 1% Glass Fibers
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by any agency of the federal government. Eurofins EMLab P&K reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins EMLab P&K
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 Fax (623) 780-7695 www.emlab.com

Client: Dominion Environmental Consultants, Inc.
C/O: Mr. Nick Marcos
Re: AZ0959.3108; Kyrene del Pueblo M.S.

Date of Sampling: 07-12-2022
Date of Receipt: 07-12-2022
Date of Report: 07-13-2022

ASBESTOS PLM REPORT

Location: PLM-4, FRP & Mastic

Lab ID-Version‡: 14307809-1

Sample Layers	Asbestos Content
White Fiberglass Reinforced Plastic	ND
Off-White Mastic	ND
Composite Non-Asbestos Content:	25% Glass Fibers
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by any agency of the federal government. Eurofins EMLab P&K reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins EMLab P&K
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 Fax (623) 780-7695 www.emlab.com

Client: Dominion Environmental Consultants, Inc.
C/O: Mr. Nick Marcos
Re: AZ0959.3108; Kyrene del Pueblo M.S.

Date of Sampling: 07-12-2022
Date of Receipt: 07-12-2022
Date of Report: 07-13-2022

ASBESTOS PLM REPORT

Location: PLM-5, FRP & Mastic

Lab ID-Version‡: 14307810-1

Sample Layers	Asbestos Content
White Fiberglass Reinforced Plastic	ND
Off-White Mastic	ND
Composite Non-Asbestos Content:	25% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-6, FRP & Mastic

Lab ID-Version‡: 14307811-1

Sample Layers	Asbestos Content
White Fiberglass Reinforced Plastic	ND
Off-White Mastic	ND
Composite Non-Asbestos Content:	25% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-7, Gray Cove Base & Mastic

Lab ID-Version‡: 14307812-1

Sample Layers	Asbestos Content
Gray Baseboard	ND
Yellow Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-8, Gray Cove Base & Mastic

Lab ID-Version‡: 14307813-1

Sample Layers	Asbestos Content
Gray Baseboard	ND
Yellow Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by any agency of the federal government. Eurofins EMLab P&K reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins EMLab P&K
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 Fax (623) 780-7695 www.emlab.com

Client: Dominion Environmental Consultants, Inc.
C/O: Mr. Nick Marcos
Re: AZ0959.3108; Kyrene del Pueblo M.S.

Date of Sampling: 07-12-2022
Date of Receipt: 07-12-2022
Date of Report: 07-13-2022

ASBESTOS PLM REPORT

Location: PLM-9, Gray Cove Base & Mastic Lab ID-Version‡: 14307814-1

Sample Layers	Asbestos Content
Gray Baseboard	ND
Yellow Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-10, Mop Sink Caulking Lab ID-Version‡: 14307815-1

Sample Layers	Asbestos Content
White Caulk	ND
Sample Composite Homogeneity:	Good

Location: PLM-11, Mop Sink Caulking Lab ID-Version‡: 14307816-1

Sample Layers	Asbestos Content
White Caulk	ND
Sample Composite Homogeneity:	Good

Location: PLM-12, Mop Sink Caulking Lab ID-Version‡: 14307817-1

Sample Layers	Asbestos Content
White Caulk	ND
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by any agency of the federal government. Eurofins EMLab P&K reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins EMLab P&K
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 Fax (623) 780-7695 www.emlab.com

Client: Dominion Environmental Consultants, Inc.
C/O: Mr. Nick Marcos
Re: AZ0959.3108; Kyrene del Pueblo M.S.

Date of Sampling: 07-12-2022
Date of Receipt: 07-12-2022
Date of Report: 07-13-2022

ASBESTOS PLM REPORT

Location: PLM-13, Orange Peel D.W. (Paint, Tex, Tape, J.C., D.W.) Lab ID-Version‡: 14307818-1

Sample Layers	Asbestos Content
Off-White Paint Layers	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose < 1% Glass Fibers
Sample Composite Homogeneity:	Poor

Location: PLM-14, Orange Peel D.W. (Paint, Tex, Tape, J.C., D.W.) Lab ID-Version‡: 14307819-1

Sample Layers	Asbestos Content
Off-White Paint Layers	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose < 1% Glass Fibers
Sample Composite Homogeneity:	Poor

Location: PLM-15, Orange Peel D.W. (Paint, Tex, Tape, J.C., D.W.) Lab ID-Version‡: 14307820-1

Sample Layers	Asbestos Content
Off-White Paint Layers	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose < 1% Glass Fibers
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by any agency of the federal government. Eurofins EMLab P&K reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins EMLab P&K
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 Fax (623) 780-7695 www.emlab.com

Client: Dominion Environmental Consultants, Inc.
C/O: Mr. Nick Marcos
Re: AZ0959.3108; Kyrene del Pueblo M.S.

Date of Sampling: 07-12-2022
Date of Receipt: 07-12-2022
Date of Report: 07-13-2022

ASBESTOS PLM REPORT

Location: PLM-16, Blue Cove Base & Mastic

Lab ID-Version‡: 14307821-1

Sample Layers	Asbestos Content
Blue Baseboard	ND
Yellow Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by any agency of the federal government. Eurofins EMLab P&K reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins EMLab P&K
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 Fax (623) 780-7695 www.emlab.com

Client: Dominion Environmental Consultants, Inc.
C/O: Mr. Nick Marcos
Re: AZ0959.3108; Kyrene del Pueblo M.S.

Date of Sampling: 07-12-2022
Date of Receipt: 07-12-2022
Date of Report: 07-13-2022

ASBESTOS PLM REPORT

Location: PLM-17, Blue Cove Base & Mastic

Lab ID-Version‡: 14307822-1

Sample Layers	Asbestos Content
Blue Baseboard	ND
Yellow Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-18, Blue Cove Base & Mastic

Lab ID-Version‡: 14307823-1

Sample Layers	Asbestos Content
Blue Baseboard	ND
Yellow Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by any agency of the federal government. Eurofins EMLab P&K reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY

www.EMLabPK.com

eurofins | EMLab P&K

Marlton, NJ: 3000 Lincoln Dr E, Ste. A, Marlton, NJ 08053 * **(866) 871-1984**
Phoenix, AZ: 1501 West Knudsen Drive, Phoenix, AZ 85027 * **(800) 651-4802**
SSF, CA: 6000 Shoreline Ct, Ste. 205, S. San Francisco, CA 94080 * **(866) 888-6653**

WEATHER	Fog	Rain
None		
Light		
Moderate		
Heavy		

002975027

CONTACT INFORMATION

Company:	Dominion Environmental Consultants, Inc. (6285)	Address:	20045 N. 19th Ave, Bldg 7 Phoenix, AZ 85027
Contact:	Mr. Nick Marcos		
Phone:	623-516-1415	Special Instructions:	

PROJECT INFORMATION

Project ID:	AZ0959.3108		
Project Description:	Kyrene del Pueblo M.S.		
Project Zip Code:		Sampling Date/Time:	7/12/22
PO Number:	288290	Sampled By:	NM

TURN AROUND TIME CODES - (TAT)

STD - Standard (Default)
ND - Next Business Day
SD - Same Business Day
WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

REQUESTED SERVICES

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)
PLM 1	Smooth D.W. (paint, tex, tape,	B	ND		
2	↓ J.C., d.w.				
3					
4	FRP & Mastic				
5					
6	↓				
7	Gray Cove Base & Mastic				
8					
9	↓				
10	MOP Sink Caulking				
11					
12	↓				
13	Orange Peel d.w. (paint, tex,				
14	↓ tape, J.C., d.w)				
15					

Spore Trap Analysis	Other biological particles - supplement	Direct Microscopic Exam (Qualitative)	Quantitative spore count direct exam	Dust Characterization	1-Media Surface Fungi (Genus ID + Asp. spp.)	Culturable Air Fungi (Genus ID + Asp. spp.)	Gram Stain and Counts (Culturable Air and Surface Bacteria)	*Legionella* culture	Total Coliform, *E.coli* (Presence/Absence)	QuantiTray-Sewage Screen	OTHER: (please specify test)	Asbestos in Air - PCM Airborne Fiber Count (NIOSH 7400)	Asbestos Bulk - PLM	Lead (Pb) - Flame AA	PCR (please specify test)	Allergens (please specify test)
													X			

Culturable: ...ietle™ Andersen, SAS, Water, Bulk, Dust, Soil, Contact Plate

Other Requests

SAMPLE TYPE CODES

BC - BioCassette™	CP - Contact Plate	T - Tape	O - Other:
A1S - Andersen	ST - Spore Trap	SW - Swab	
SAS - Surface Air Sampler	B - Bulk	SO - Soil	
NP - Non-potable Water	P - Potable Water	D - Dust	

RELINQUISHED BY	DATE & TIME	RECEIVED BY	DATE & TIME
[signature]	7/12/22	Dyani Zamon	7/12/22
			2:30pm

By submitting this Chain of Custody, you agree to be bound by the terms and conditions set forth at http://www.emlab.com/terms-of-service
Copyright © 2019 Eurofins EMLab P&K

CHAIN OF CUSTODY

www.EMLabPK.com

EMLab P&K

ASBESTOS ANALYSIS

PAGE ___ of ___

PROJECT INFORMATION

Company:

Contact:

Project ID:

Project Desc.:

SAMPLE ID	DESCRIPTION	Sample Type	TAT	Total Volume	NOTES	PLM X
PLM 16	Blue Cove Base & Mastic	B	ND			
17		↓	↓			↓
18						

002975027

eurofins | Built Environment Testing

Report for:

Nick Marcos
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Eurofins Aerotech Built Environment Testing, LLC
Project: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 300 (Admin)
EML ID: 4121010

Approved by:



Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 06-25-2025

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EB-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins Aerotech Built Environment Testing, LLC ("the Company"), a member of the Eurofins Built Environment Testing group of companies, shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 300 (Admin)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Total Samples Submitted:	18
Total Samples Analyzed:	18
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM-1, Gray Mulit-Color Carpet Square and Mastic Lab ID-Version‡: 20574413-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Tan Mastic	ND
Composite Non-Asbestos Content:	80% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-2, Gray Mulit-Color Carpet Square and Mastic Lab ID-Version‡: 20574414-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Tan Mastic	ND
Composite Non-Asbestos Content:	80% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-3, Gray Mulit-Color Carpet Square and Mastic Lab ID-Version‡: 20574415-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Tan Mastic	ND
Composite Non-Asbestos Content:	80% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-4, Blue Cove Base and Mastic Lab ID-Version‡: 20574416-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 300 (Admin)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-5, Blue Cove Base and Mastic Lab ID-Version‡: 20574417-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-6, Blue Cove Base and Mastic Lab ID-Version‡: 20574418-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-7, Back Carpet Square and Mastic Lab ID-Version‡: 20574419-1

Sample Layers	Asbestos Content
Black Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	75% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-8, Back Carpet Square and Mastic Lab ID-Version‡: 20574420-1

Sample Layers	Asbestos Content
Black Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	75% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 300 (Admin)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-9, Back Carpet Square and Mastic Lab ID-Version‡: 20574421-1

Sample Layers	Asbestos Content
Black Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	75% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-10, New 2'x2' Ceiling Tile Lab ID-Version‡: 20574422-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	70% Cellulose 5% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-11, New 2'x2' Ceiling Tile Lab ID-Version‡: 20574423-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	70% Cellulose 5% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-12, New 2'x2' Ceiling Tile Lab ID-Version‡: 20574424-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	70% Cellulose 5% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 300 (Admin)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-13, Old 2'x2' Ceiling Tile Lab ID-Version‡: 20574425-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	70% Cellulose 5% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-14, Old 2'x2' Ceiling Tile Lab ID-Version‡: 20574426-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	70% Cellulose 5% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-15, Old 2'x2' Ceiling Tile Lab ID-Version‡: 20574427-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	70% Cellulose 5% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-16, Orange Peel D.W. (paint,tex, tape, j.c.,d.w.) Lab ID-Version‡: 20574428-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 300 (Admin)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-17, Orange Peel D.W. (paint,tex, tape, j.c.,d.w.) Lab ID-Version‡: 20574429-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

Location: PLM-18, Orange Peel D.W. (paint,tex, tape, j.c.,d.w.) Lab ID-Version‡: 20574430-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 300 (Admin)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

PROJECT ANALYST AND SIGNATORY REPORT

Project Analyst



Analyst: Jason Bosse

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY

www.eurofinsus.com/Built

eurofins | Built Environment Testing

East:(866) 871-1984
West/Central:(800) 651-4802

WEATHER		Fog	Rain	Snow	Wind	Clear
LEVEL	None					
	Light					
	Moderate					
	Heavy					

004121010

CONTACT INFORMATION

Company:	Dominion Environmental Consultants	Address:20045 N. 19th Ave., Phx, AZ 85027
Contact:	Nick Marcos	Special Instructions:
Phone:	623-516-1415	

PROJECT INFORMATION

Project ID:	AZ1418.59		
Project Description:	Kyrene Del Pueblo M.S. - Bldg. 300 (Admin)		
Project Zip Code:		Sampling Date/Time:	6/20/2025
PO Number:	13747	Sampled By:	NM

TURN AROUND TIME CODES - (TAT)

STD - Standard (Default)
ND - Next Business Day
SD - Same Business Day
WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

REQUESTED SERVICES

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)	Spore Trap Analysis	Other biological particles - supplement	Direct Microscopic Exam (Qualitative)	Quatitative spore count direct exam	Dust Characterization	1-Media Surface Fungi (Genus ID + Asp. spp.)	Culturable Air Fungi (Genus ID + Asp. spp.)	Gram Stain and Counts (Culturable Air and Surface	*Legionella* culture	Total Coliform, *E.coli* (Presence/Absence)	QuantiTray-Sewage Screen	OTHER: (please specify test)	Asbestos in Air - PCM Airborne Fiber Count (NIOSH 7400)	Asbestos Bulk - PLM (EPA method 600/R-93-116)	Lead (Pb) / Paint Chip	PCR (please specify test)	Allergens (please specify test)
PLM 1-3	Gray Multi-Color Carpet Square and Mastic	B	STD																X			
PLM 4-6	Blue Cove Base and Mastic	B	STD																X			
PLM 7-9	Black Carpet Square and Mastic	B	STD																X			
PLM 10-12	New 2' X 2' Ceiling Tile	B	STD																X			
PLM 13-15	Old 2' X 2' Ceiling Tile	B	STD																X			
PLM 16-18	Orange Peel D.W. (paint,tex,tape,j.c.,d.w.)	B	STD																X			

SAMPLE TYPE CODES

BC - BioCassette™	**CP** - Contact Plate	**T** - Tape	**O** - Other:
A1S - Andersen	**ST** - Spore Trap	**SW** - Swab	
SAS - Surface Air Sampler	**B** - Bulk	**SO** - Soil	
NP - Non-potable Water	**P** - Potable Water	**D** - Dust	

RELINQUISHED BY	DATE & TIME	RECEIVED BY	DATE & TIME
Nick Marcos	6/23/2025	Peter Lugo	6/23/25 2:45pm

By submitting this Chain of Custody, you agree to be bound by the terms and conditions set forth at http://www.emlab.com/s/main/serviceterms.html

eurofins | Built Environment Testing

Report for:

Nick Marcos
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Eurofins Aerotech Built Environment Testing, LLC
Project: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 400 (E Pod)
EML ID: 4121023

Approved by:



Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 06-24-2025

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EB-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins Aerotech Built Environment Testing, LLC ("the Company"), a member of the Eurofins Built Environment Testing group of companies, shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 400 (E Pod)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Total Samples Submitted:	18
Total Samples Analyzed:	18
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM-1, Gray Mult-Color Carpet Square and Mastic

Lab ID-Version‡: 20574203-1

Sample Layers	Asbestos Content
Gray Carpet	ND
Tan Mastic	ND
Composite Non-Asbestos Content:	70% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-2, Gray Mult-Color Carpet Square and Mastic

Lab ID-Version‡: 20574204-1

Sample Layers	Asbestos Content
Gray Carpet	ND
Tan Mastic	ND
Composite Non-Asbestos Content:	70% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-3, Gray Mult-Color Carpet Square and Mastic

Lab ID-Version‡: 20574205-1

Sample Layers	Asbestos Content
Gray Carpet	ND
Tan Mastic	ND
Composite Non-Asbestos Content:	70% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-4, Blue Carpet and Mastic

Lab ID-Version‡: 20574206-1

Sample Layers	Asbestos Content
Blue Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	85% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 400 (E Pod)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-5, Blue Carpet and Mastic

Lab ID-Version‡: 20574207-1

Sample Layers	Asbestos Content
Blue Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	85% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-6, Blue Carpet and Mastic

Lab ID-Version‡: 20574208-1

Sample Layers	Asbestos Content
Blue Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	85% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-7, Blue Cove Base and Mastic

Lab ID-Version‡: 20574209-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Off-White Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-8, Blue Cove Base and Mastic

Lab ID-Version‡: 20574210-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Off-White Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 400 (E Pod)
Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-9, Blue Cove Base and Mastic Lab ID-Version‡: 20574211-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Off-White Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-10, New 2'x2' Ceiling Tile Lab ID-Version‡: 20574212-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-11, New 2'x2' Ceiling Tile Lab ID-Version‡: 20574213-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-12, New 2'x2' Ceiling Tile Lab ID-Version‡: 20574214-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 400 (E Pod)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-13, Old 2''x2'' Ceiling Tile Lab ID-Version‡: 20574215-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-14, Old 2''x2'' Ceiling Tile Lab ID-Version‡: 20574216-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-15, Old 2''x2'' Ceiling Tile Lab ID-Version‡: 20574217-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-16, Orange Peel D.W. (paint, tex, tape, j.c., dw) Lab ID-Version‡: 20574218-1

Sample Layers	Asbestos Content
Tan Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 400 (E Pod)
Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-17, Orange Peel D.W. (paint, tex, tape, j.c., dw) Lab ID-Version‡: 20574219-1

Sample Layers	Asbestos Content
Tan Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

Location: PLM-18, Orange Peel D.W. (paint, tex, tape, j.c., dw) Lab ID-Version‡: 20574220-1

Sample Layers	Asbestos Content
Tan Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 400 (E Pod)
Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

PROJECT ANALYST AND SIGNATORY REPORT

Project Analyst



Analyst: Jason Bosse

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY

www.eurofinsus.com/Built

eurofins | Built Environment Testing

East:(866) 871-1984
West/Central:(800) 651-4802

WEATHER		Fog	Rain	Snow	Wind	Clear
LEVEL	None					
	Light					
	Moderate					
	Heavy					

CONTACT INFORMATION

Company:	Dominion Environmental Consultants	Address:20045 N. 19th Ave., Phx, AZ 85027
Contact:	Nick Marcos	Special Instructions:
Phone:	623-516-1415	

PROJECT INFORMATION

Project ID:	AZ1418.59		
Project Description:	Kyrene Del Pueblo M.S. - Bldg. 400 (E Pod)		
Project Zip Code:		Sampling Date/Time:	6/20/2025
PO Number:	13749	Sampled By:	NM

TURN AROUND TIME CODES - (TAT)

STD - Standard (Default)
ND - Next Business Day
SD - Same Business Day
WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)
PLM 1-3	Gray Multi-Color Carpet Square and Mastic	B	STD		
PLM 4-6	Blue Carpet and Mastic	B	STD		
PLM 7-9	Blue Cove Base and Mastic	B	STD		
PLM 10-12	New 2' X 2' Ceiling Tile	B	STD		
PLM 13-15	Old 2" X 2' Ceiling Tile	B	STD		
PLM 16-18	Orange Peel D.W. (paint,tex,tape,j.c.,d.w.)	B	STD		

REQUESTED SERVICES

004121023

Non-Culturable					Culturable							Other Requests				
Spore Trap Analysis	Other biological particles - supplement	Direct Microscopic Exam (Qualitative)	Quantitative spore count direct exam	Dust Characterization	1-Media Surface Fungi (Genus ID + Asp. spp.)	Culturable Air Fungi (Genus ID + Asp. spp.)	Gram Stain and Counts (Culturable Air and Surfa	*Legionella* culture	Total Coliform, *E.coli* (Presence/Absence)	QuantiTray-Sewage Screen	OTHER: (please specify test)	Asbestos in Air - PCM Airborne Fiber Count (NIOSH 7400)	Asbestos Bulk - PLM (EPA method 600/R-93-116)	Lead (Pb) / Paint Chip	PCR (please specify test)	Allergens (please specify test)
													X			
													X			
													X			
													X			
													X			
													X			

SAMPLE TYPE CODES

BC - BioCassette™	**CP** - Contact Plate	**T** - Tape	**O** - Other:
A1S - Andersen	**ST** - Spore Trap	**SW** - Swab	
SAS - Surface Air Sampler	**B** - Bulk	**SO** - Soil	
NP - Non-potable Water	**P** - Potable Water	**D** - Dust	

RELINQUISHED BY	DATE & TIME	RECEIVED BY	DATE & TIME
Nick Marcos	6/23/2025	Perley Lugo	6/23/25 2:45pm

By submitting this Chain of Custody, you agree to be bound by the terms and conditions set forth at http://www.emlab.com/s/main/serviceterms.html

Aerobiology Laboratory Associates, Incorporated
Expertise Since 1997

Lab Use: 21001585 1/15/2021

Page 1 of 2

AZ, CA, CO, FL, GA, VA, NJ | AZ, CA, CO, VA | AZ, CA, CO, FL GA, NJ, VA

Aerobiology Client	c395 Dominion Environmental Consultants, Inc.		
Field Contact	Basilio Marcos	Collected By/Date: 1/15/21	Relinquished By/Date: 1/15/21
Reporting Address	20045 N. 19th Ave Building 7 Phoenix AZ 85027	Relinquished By/Date:	Received By/Date: 1:15:21
Billing Address	20045 N. 19th Ave Building 7 Phoenix AZ 85027	Sampler Type: Andersen___ SAS___	SampleAire___ AeroTrap___ Other___ BioCulture___
Phone/Fax	623-516-1414	PO#/Job#: Po # 263562 / A20959.2668	
Reporting Email (s)	bmarcos@dominion-env.com	Project Name: Kyrene De' Pueblo	
Routine [X]	24 Hour [ ] Same Day [ ] 4 Hour [ ] 2 Hour [ ]	Notes:	
SAMPLING LOCATION ZIP CODE		Lab Contacts: Simone Singh (408) 498-7901	Mandy Palm (858) 444-7138

	Sample No.	Test Code	Sample Location	Total Volume/Area
1	PIM 1	3002	Black Cove base + mastic	
2	2		↓	
3	3		↓	
4	4		Brown Cove base + mastic	
5	5		↓	
6	6		↓	
7	7		Blue Cove base + mastic	
8	8		↓	
9	9		↓	
10	10		Orange Peel Tex, DW, Tape, JC + Paint	
11	11		↓	
12	12		↓	
13	13		Multi-Colored Blue Carpet + mastic	
14	14		↓	
15	15	↓	↓	

1054	Direct, Non-viable Spore Trap	1015	Culture - WATER Legionella
1051	Direct, Qualitative- **Swab/Tape**	1017	Culture - SWAB Legionella
1050	Direct, Qualitative- **Bulk**	1010	WATER - Potable - E. coli/total coliforms
1005	AIR Culture - Bacterial Count w/ ID's	1012	SWAB - E. coli/total coliforms
1030	AIR Culture - Fungal Count w/ ID's	1028	SWAB - Sewage Screen (E. coli/Entero/fecal coliforms)
1006	SWAB Culture - Bacterial Count w/ ID's	2056	WATER - Heterotrophic Plate Count
1031	SWAB Culture - Fungal Count w/ ID's	3001	ASBESTOS - Point count
1008	BULK Culture - Bacterial Count w/ ID's	3002	ASBESTOS - PLM Analysis
1033	BULK Culture - Fungal Count w/ ID's	3003	ASBESTOS - Particle characterization
1007	WATER Culture - Bacterial Count w/ID's	3004	ASBESTOS - PCM Analysis

Washington, D.C. (877) 648-9150 | Atlanta, GA (770) 947-2828 | Denver, CO (303) 232-3746 | Phoenix, AZ (602) 441-3700 | Cherry Hill, NJ (856) 486-1177 | Los Angeles, CA (714) 895-8401 | Ft. Lauderdale, FL (954) 451-3725

ALL SAMPLES ACCEPTABLE
INIT/DATE KD 1.15.21

Aerobiology Laboratory Associates, Incorporated
Expertise Since 1997

Lab Use:
21001585
1/15/2021

AZ, CA, CO, FL, GA, VA, NJ

NVLAP
AZ, CA, CO, VA

AZ, CA, CO, FL GA, NJ, VA

Aerobiology Client	c395 Dominion Environmental Consultants, Inc.
Field Contact	Basilio Marcos
Reporting Address	20045 N. 19th Ave Building 7 Phoenix AZ 85027
Billing Address	20045 N. 19th Ave Building 7 Phoenix AZ 85027
Phone/Fax	623-516-1414
Reporting Email (s)	bmarcos@dominion-env.com
Routine ☑ / 24 Hour ☐ / Same Day ☐ / 4 Hour ☐ / 2 Hour ☐	
SAMPLING LOCATION ZIP CODE	

Collected By/Date: 1/15/21
Relinquished By/Date:
Received By/Date: 1/15/21
Sampler Type: Andersen ___ SAS ___ SampleAire ___ AeroTrap ___ Other ___ BioCulture ___
PO#/Job#: Pot# / A20959.2648
Project Name: Kyrene Del Pueblo
Notes:
Lab Contacts: Simone Singh (408) 498-7901 Mandy Palm (858) 444-7138

	Sample No.	Test Code	Sample Location	Total Volume/Area
1	PIM 16	3002	Brown Wallpaper + Mastic	
2	17		↓	
3	18		↓	
4	19		Orange Peel Tex, Greenboard, Tape, JC + Paint	
5	20		↓	
6	21		↓	
7	22		Smooth Tex, DW, Tape, JC + Paint	
8	23		↓	
9	24	↓	↓	
10				
11				
12				
13				
14				
15				

1054	Direct, Non-viable Spore Trap	1015	Culture - WATER Legionella
1051	Direct, Qualitative- **Swab/Tape**	1017	Culture - SWAB Legionella
1050	Direct, Qualitative- **Bulk**	1010	WATER - Potable - E. coli/total coliforms
1005	AIR Culture - Bacterial Count w/ ID's	1012	SWAB - E. coli/total coliforms
1030	AIR Culture - Fungal Count w/ ID's	1028	SWAB - Sewage Screen (E. coli/Entero/fecal coliforms)
1006	SWAB Culture - Bacterial Count w/ ID's	2056	WATER - Heterotrophic Plate Count
1031	SWAB Culture - Fungal Count w/ ID's	3001	ASBESTOS - Point count
1008	BULK Culture - Bacterial Count w/ ID's	3002	ASBESTOS - PLM Analysis
1033	BULK Culture - Fungal Count w/ ID's	3003	ASBESTOS - Particle characterization
1007	WATER Culture - Bacterial Count w/ID's	3004	ASBESTOS - PCM Analysis

NVLAP
TESTING NVLAP LAB CODE 500097-0

Aerobiology Laboratory Associates, Incorporated
A Pace Analytical® Laboratory

Aerobiology Laboratory Associates, Inc.
2228 W Northern Ave. Suite B-110
Phoenix, AZ 85021
(602) 441-3700
www.aerobiology.net

Certificate of Analysis

Client:
Dominion Environmental Consultants, Inc
20045 N. 19th Ave Building 7
Phoenix, AZ 85027
Attn: Ryan Kuhn

Project Name: 263562/AZ0959.2668 Kyrene Del Pueblo (BM)

Project ID: 21001585

Date Collected: 01/15/2021
Date Received: 01/15/2021
Date Analyzed: 01/15/2021
Date Reported: 01/15/2021

Test Requested: **Asbestos Bulk Analysis, Polarized Light Microscopy (PLM)**: EPA 600/R-93/116 Method for Asbestos in Bulk Building Materials, EPA-40 CFR Appendix E to Subpart E of Part 763, Interim Method for Asbestos in Bulk Insulation Samples

Total Samples Submitted: 24
Total Samples Analyzed: 24
Total Samples with Asbestos (≥1%): 0

Location: PLM-1 Black Cove Base & Mastic Lab ID: 21001585-001

Physical Description of Sample/Layer	Asbestos Detected
Black Cove Base	ND
Cream Mastic	ND

Location: PLM-2 Black Cove Base & Mastic Lab ID: 21001585-002

Physical Description of Sample/Layer	Asbestos Detected
Black Cove Base	ND
Cream Mastic	ND

Location: PLM-3 Black Cove Base & Mastic Lab ID: 21001585-003

Physical Description of Sample/Layer	Asbestos Detected
Black Cove Base	ND
Cream Mastic	ND

Location: PLM-4 Brown Cove Base & Mastic Lab ID: 21001585-004

Physical Description of Sample/Layer	Asbestos Detected
Brown Cove Base	ND
Yellow Mastic	ND

Location: PLM-5 Brown Cove Base & Mastic Lab ID: 21001585-005

Physical Description of Sample/Layer	Asbestos Detected
Brown Cove Base	ND
Yellow Mastic	ND

Location: PLM-6 Brown Cove Base & Mastic Lab ID: 21001585-006

Physical Description of Sample/Layer	Asbestos Detected
Brown Cove Base	ND
Yellow Mastic	ND

Location: PLM-7 Blue Cove Base & Mastic Lab ID: 21001585-007

Physical Description of Sample/Layer	Asbestos Detected
Blue Cove Base	ND
Cream Mastic	ND

Elle Teague
Analyst

Elle Teague
Manager-Asbestos

A Amosite
AC Actinolite
AN Anthophyllite
CHRY Chrysotile
CR Crocidolite
TR Tremolite
Trace Less Than 1%
ND None Detected

Non-Asbestos fiber percentage and matrix information available upon request

NVLAP
TESTING NVLAP LAB CODE 500097-0

Aerobiology Laboratory Associates, Incorporated
A Pace Analytical® Laboratory

Aerobiology Laboratory Associates, Inc.
2228 W Northern Ave. Suite B-110
Phoenix, AZ 85021
(602) 441-3700
www.aerobiology.net

Certificate of Analysis

Client:
Dominion Environmental Consultants, Inc
20045 N. 19th Ave Building 7
Phoenix, AZ 85027
Attn: Ryan Kuhn

Project Name: 263562/AZ0959.2668 Kyrene Del Pueblo (BM)

Project ID: 21001585

Date Collected: 01/15/2021
Date Received: 01/15/2021
Date Analyzed: 01/15/2021
Date Reported: 01/15/2021

Test Requested: **Asbestos Bulk Analysis, Polarized Light Microscopy (PLM)**: EPA 600/R-93/116 Method for Asbestos in Bulk Building Materials, EPA-40 CFR Appendix E to Subpart E of Part 763, Interim Method for Asbestos in Bulk Insulation Samples

Location: PLM-8 Blue Cove Base & Mastic Lab ID: 21001585-008

Physical Description of Sample/Layer	Asbestos Detected
Blue Cove Base	ND
Cream Mastic	ND

Location: PLM-9 Blue Cove Base & Mastic Lab ID: 21001585-009

Physical Description of Sample/Layer	Asbestos Detected
Blue Cove Base	ND
Cream Mastic	ND

Location: PLM-10 Orange Peel Tex, DW, Tape, JC & Paint Lab ID: 21001585-010

Physical Description of Sample/Layer	Asbestos Detected
Cream Paint	ND
White Texture	ND
White/Tan Drywall	ND

Location: PLM-11 Orange Peel Tex, DW, Tape, JC & Paint Lab ID: 21001585-011

Physical Description of Sample/Layer	Asbestos Detected
Cream Paint	ND
White Texture	ND
Pink Mesh	ND
White Joint Compound	ND
White/Tan Drywall	ND

Location: PLM-12 Orange Peel Tex, DW, Tape, JC & Paint Lab ID: 21001585-012

Physical Description of Sample/Layer	Asbestos Detected
Cream Paint	ND
White Texture	ND
Pink Mesh	ND
White Joint Compound	ND
White/Tan Drywall	ND

Elle Teague
Analyst

Elle Teague
Manager-Asbestos

A Amosite
AC Actinolite
AN Anthophyllite
CHRY Chrysotile
CR Crocidolite
TR Tremolite
Trace Less Than 1%
ND None Detected

Non-Asbestos fiber percentage and matrix information available upon request

NVLAP
TESTING NVLAP LAB CODE 500097-0

Aerobiology Laboratory Associates, Incorporated
A Pace Analytical® Laboratory

Aerobiology Laboratory Associates, Inc.
2228 W Northern Ave. Suite B-110
Phoenix, AZ 85021
(602) 441-3700
www.aerobiology.net

Certificate of Analysis

Client:
Dominion Environmental Consultants, Inc
20045 N. 19th Ave Building 7
Phoenix, AZ 85027
Attn: Ryan Kuhn

Project Name: 263562/AZ0959.2668 Kyrene Del Pueblo (BM)

Project ID: 21001585

Date Collected: 01/15/2021
Date Received: 01/15/2021
Date Analyzed: 01/15/2021
Date Reported: 01/15/2021

Test Requested: **Asbestos Bulk Analysis, Polarized Light Microscopy (PLM)**: EPA 600/R-93/116 Method for Asbestos in Bulk Building Materials, EPA-40 CFR Appendix E to Subpart E of Part 763, Interim Method for Asbestos in Bulk Insulation Samples

Location: PLM-13 Multicolored Blue Carpet & Mastic Lab ID: 21001585-013

Physical Description of Sample/Layer	Asbestos Detected
Multicolored Carpet	ND
Dark Yellow Mastic	ND

Location: PLM-14 Multicolored Blue Carpet & Mastic Lab ID: 21001585-014

Physical Description of Sample/Layer	Asbestos Detected
Multicolored Carpet	ND
Dark Yellow Mastic	ND

Location: PLM-15 Multicolored Blue Carpet & Mastic Lab ID: 21001585-015

Physical Description of Sample/Layer	Asbestos Detected
Multicolored Carpet	ND
Dark Yellow Mastic	ND

Location: PLM-16 Brown Wallpaper & Mastic Lab ID: 21001585-016

Physical Description of Sample/Layer	Asbestos Detected
Brown Wallcovering W/White Mesh	ND
Cream Mastic	ND

Location: PLM-17 Brown Wallpaper & Mastic Lab ID: 21001585-017

Physical Description of Sample/Layer	Asbestos Detected
Brown Wallcovering W/White Mesh	ND
Cream Mastic	ND

Location: PLM-18 Brown Wallpaper & Mastic Lab ID: 21001585-018

Physical Description of Sample/Layer	Asbestos Detected
Brown Wallcovering W/White Mesh	ND
Cream Mastic	ND

Elle Teague
Analyst

Elle Teague
Manager-Asbestos

A Amosite
AC Actinolite
AN Anthophyllite
CHRY Chrysotile
CR Crocidolite
TR Tremolite
Trace Less Than 1%
ND None Detected

Non-Asbestos fiber percentage and matrix information available upon request

NVLAP®
TESTING NVLAP LAB CODE 500097-0

Aerobiology Laboratory Associates, Incorporated
A Pace Analytical® Laboratory

Aerobiology Laboratory Associates, Inc.
2228 W Northern Ave. Suite B-110
Phoenix, AZ 85021
(602) 441-3700
www.aerobiology.net

Certificate of Analysis

Client:
Dominion Environmental Consultants, Inc
20045 N. 19th Ave Building 7
Phoenix, AZ 85027
Attn: Ryan Kuhn

Project Name: 263562/AZ0959.2668 Kyrene Del Pueblo (BM)

Project ID: 21001585

Date Collected: 01/15/2021
Date Received: 01/15/2021
Date Analyzed: 01/15/2021
Date Reported: 01/15/2021

Test Requested: **Asbestos Bulk Analysis, Polarized Light Microscopy (PLM)**: EPA 600/R-93/116 Method for Asbestos in Bulk Building Materials, EPA-40 CFR Appendix E to Subpart E of Part 763, Interim Method for Asbestos in Bulk Insulation Samples

Location: PLM-19 Orange Peel Tex, Green Board, Tape, JC & Paint Lab ID: 21001585-019

Physical Description of Sample/Layer	Asbestos Detected
Cream Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
Brown/Tan/Green Drywall	ND

Location: PLM-20 Orange Peel Tex, Green Board, Tape, JC & Paint Lab ID: 21001585-020

Physical Description of Sample/Layer	Asbestos Detected
Cream Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
Brown/Tan/Green Drywall	ND

Location: PLM-21 Orange Peel Tex, Green Board, Tape, JC & Paint Lab ID: 21001585-021

Physical Description of Sample/Layer	Asbestos Detected
Cream Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
Brown/Tan/Green Drywall	ND

Location: PLM-22 Smooth Tex, DW, Tape, JC & Paint Lab ID: 21001585-022

Physical Description of Sample/Layer	Asbestos Detected
Off White Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White/Tan Drywall	ND

Elle Teague
Analyst

Elle Teague
Manager-Asbestos

A Amosite
AC Actinolite
AN Anthophyllite
CHRY Chrysotile
CR Crocidolite
TR Tremolite
Trace Less Than 1%
ND None Detected

Non-Asbestos fiber percentage and matrix information available upon request

TESTING NVLAP LAB CODE 500097-0

Aerobiology Laboratory Associates, Inc.
2228 W Northern Ave. Suite B-110
Phoenix, AZ 85021
(602) 441-3700
www.aerobiology.net

Certificate of Analysis

Client:
Dominion Environmental Consultants, Inc
20045 N. 19th Ave Building 7
Phoenix, AZ 85027
Attn: Ryan Kuhn

Project Name: **263562/AZ0959.2668 Kyrene Del Pueblo (BM)**
Project ID: 21001585

Date Collected: 01/15/2021
Date Received: 01/15/2021
Date Analyzed: 01/15/2021
Date Reported: 01/15/2021

Test Requested: **Asbestos Bulk Analysis, Polarized Light Microscopy (PLM)**: EPA 600/R-93/116 Method for Asbestos in Bulk Building Materials, EPA-40 CFR Appendix E to Subpart E of Part 763, Interim Method for Asbestos in Bulk Insulation Samples

Location: PLM-23 Smooth Tex, DW, Tape, JC & Paint Lab ID: 21001585-023

Physical Description of Sample/Layer	Asbestos Detected
Off White Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White/Tan Drywall	ND

Location: PLM-24 Smooth Tex, DW, Tape, JC & Paint Lab ID: 21001585-024

Physical Description of Sample/Layer	Asbestos Detected
Off White/Cream Paint	ND
White/Cream Texture	ND
Cream Tape	ND
White Joint Compound	ND
White/Tan Drywall	ND

Elle Teague
Analyst

Elle Teague
Manager-Asbestos

A Amosite
AC Actinolite
AN Anthophyllite
CHRY Chrysotile
CR Crocidolite
TR Tremolite
Trace Less Than 1%
ND None Detected

Non-Asbestos fiber percentage and matrix information available upon request

Client:
Dominion Environmental Consultants, Inc
20045 N. 19th Ave Building 7
Phoenix, AZ 85027
Attn: Ryan Kuhn

Certificate of Analysis

Project Name: 263562/AZ0959.2668 Kyrene Del Pueblo (BM)

Project ID: 21001585

Date Collected: 01/15/2021
Date Received: 01/15/2021
Date Analyzed: 01/15/2021
Date Reported: 01/15/2021

General Notes

* **ND** indicates no asbestos was detected.

* The method detection limit is 1%.

* **Trace** or "<1" indicates asbestos was identified in the sample, but the concentration is less than 1%.

* All regulated asbestos minerals (i.e. chrysotile, amosite, crocidolite, anthophyllite, tremolite, and actinolite) were sought in every layer of each sample, but only those asbestos minerals detected are listed. Amosite is the common name for the asbestiform variety of the minerals cummingtonite and grunerite. Crocidolite is the common name used for the asbestiform variety of the mineral riebeckite.

* Tile, vinyl, foam, plastic, and fine powder samples may contain asbestos fibers of such small diameter (< 0.25 microns in diameter) that these fibers cannot be detected by PLM. For such samples, more sensitive analytical methods (e.g. TEM, SEM, and XRD) are recommended if greater certainty about asbestos content is required. Semi-quantitative bulk TEM floor tile analysis is accepted under NESHAP regulations.

* These results are submitted pursuant to Aerobiology Laboratory Associates, Inc.'s current terms and conditions of sale, including the company's standard warranty and limitation of liability provisions. No responsibility or liability is assumed for the manner in which the results are used or interpreted.

* Unless notified in writing to return the samples covered by this report, Aerobiology Laboratory Associates, Inc. will store the samples for a minimum period of thirty (30) days before discarding. A shipping and handling charge will be assessed for the return of any samples.

* Aerobiology does not guarantee the results of tape lifts, microvacs, wipe, and/or debris samples. Accurate analysis cannot be performed due to particle size, media used, and/or amount of material given. Analysis of these materials should be performed by a TEM. A result of ND does not indicate that the sample area does not contain asbestos. It means the analyst could not identify asbestos in the specific sample for the reasons listed above.

Notes Required by NVLAP

* Aerobiology Laboratory shall be responsible for all the information provided in the report, except when information is provided by the customer. Aerobiology Laboratory is not responsible for the sampling activity.

* This report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the Federal Government.

* This test report relates only to the items tested or calibrated.

* This report is not valid unless it bears the name of a NVLAP-approved signatory.

* Any reproduction of this document must include the entire document in order for the report to be valid.

Non-Asbestos fiber percentage and matrix information available upon request

eurofins | Built Environment Testing

Report for:

Nick Marcos
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Eurofins Aerotech Built Environment Testing, LLC
Project: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 500 (D Pod)
EML ID: 4121021

Approved by:



Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 06-25-2025

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EB-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins Aerotech Built Environment Testing, LLC ("the Company"), a member of the Eurofins Built Environment Testing group of companies, shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 500 (D Pod)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Total Samples Submitted:	18
Total Samples Analyzed:	18
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM-1, Gray Multi-Color Carpet Square and Mastic Lab ID-Version‡: 20574264-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	40% Synthetic Fibers < 1% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-2, Gray Multi-Color Carpet Square and Mastic Lab ID-Version‡: 20574265-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	40% Synthetic Fibers < 1% Glass Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-3, Gray Multi-Color Carpet Square and Mastic Lab ID-Version‡: 20574266-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	40% Synthetic Fibers < 1% Glass Fibers
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 500 (
D Pod)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-4, Blue Cove Base and Mastic

Lab ID-Version‡: 20574267-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 500 (D Pod)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-5, Blue Cove Base and Mastic Lab ID-Version‡: 20574268-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-6, Blue Cove Base and Mastic Lab ID-Version‡: 20574269-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-7, 2'x2' Ceiling Tile Lab ID-Version‡: 20574270-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 20% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-8, 2'x2' Ceiling Tile Lab ID-Version‡: 20574271-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 20% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 500 (D Pod)
Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-9, 2'x2' Ceiling Tile Lab ID-Version‡: 20574272-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 20% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-10, 2'x4' Ceiling Tile Lab ID-Version‡: 20574273-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-11, 2'x4' Ceiling Tile Lab ID-Version‡: 20574274-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-12, 2'x4' Ceiling Tile Lab ID-Version‡: 20574275-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 500 (D Pod)
Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-13, Orange Peel D.W. (paint, tex, tape, j.c., d.w.) Lab ID-Version‡: 20574276-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

Location: PLM-14, Orange Peel D.W. (paint, tex, tape, j.c., d.w.) Lab ID-Version‡: 20574277-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

Location: PLM-15, Orange Peel D.W. (paint, tex, tape, j.c., d.w.) Lab ID-Version‡: 20574278-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 500 (
D Pod)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-16, Lightly Textured 2'x2' Ceiling Tile

Lab ID-Version‡: 20574279-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 500 (D Pod)

Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-17, Lightly Textured 2'x2' Ceiling Tile Lab ID-Version‡: 20574280-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-18, Lightly Textured 2'x2' Ceiling Tile Lab ID-Version‡: 20574281-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".


Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 500 (D Pod)
Date of Sampling: 06-20-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

PROJECT ANALYST AND SIGNATORY REPORT

Project Analyst



Analyst: Renee Luna-Trepczynski

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY

www.eurofinsus.com/Built

eurofins | Built Environment Testing

East:(866) 871-1984
West/Central:(800) 651-4802

WEATHER		Fog	Rain	Snow	Wind	Clear
LEVEL	None					
	Light					
	Moderate					
	Heavy					

CONTACT INFORMATION

Company:	Dominion Environmental Consultants	Address:20045 N. 19th Ave., Phx, AZ 85027
Contact:	Nick Marcos	Special Instructions:
Phone:	623-516-1415	

PROJECT INFORMATION

Project ID:	AZ1418.59		
Project Description:	Kyrene Del Pueblo M.S. - Bldg. 500 (D Pod)		
Project Zip Code:		Sampling Date/Time:	6/20/2025
PO Number:	13748	Sampled By:	NM

TURN AROUND TIME CODES - (TAT)

STD - Standard (Default)
ND - Next Business Day
SD - Same Business Day
WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

REQUESTED SERVICES

Non-Culturable

Culturable

SAS, Soil,

004121021

Other Requests

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)	Spore Trap Analysis	Other biological particles - supplement	Direct Microscopic Exam (Qualitative)	Quantitative spore count direct exam	Dust Characterization	1-Media Surface Fungi (Genus ID + Asp. spp.)	Culturable Air Fungi (Genus ID + Asp. spp.)	Gram Stain and Counts (Culturable Air and Sur	*Legionella* culture	Total Coliform, *E.coli* (Presence/Absence)	QuantiTray-Sewage Screen	OTHER: (please specify test)	Asbestos in Air - PCM Airborne Fiber Count (NIOSH 7400)	Asbestos Bulk - PLM (EPA method 600/R-93-116)	Lead (Pb) / Paint Chip	PCR (please specify test)	Allergens (please specify test)
PLM 1-3	Gray Multi-Color Carpet Square and Mastic	B	STD																X			
PLM 4-6	Blue Cove Base and Mastic	B	STD																X			
PLM.7-9	2' X 2' Ceiling Tile	B	STD																X			
PLM 10-12	2' X 4' Ceiling Tile	B	STD																X			
PLM 13-15	Orange Peel D.W. (paint,tex,tape,j.c.,d.w.)	B	STD																X			
PLM 16-18	Lighly Textured 2' X 2' Ceiling Tile	B	STD																X			

SAMPLE TYPE CODES

BC - BioCassette™	**CP** - Contact Plate	**T** - Tape	**O** - Other:
A1S - Andersen	**ST** - Spore Trap	**SW** - Swab	
SAS - Surface Air Sampler	**B** - Bulk	**SO** - Soil	
NP - Non-potable Water	**P** - Potable Water	**D** - Dust	

RELINQUISHED BY	DATE & TIME	RECEIVED BY	DATE & TIME
Nick Marcos	6/23/2025	Patty Vega	6/23/25 2:45pm

By submitting this Chain of Custody, you agree to be bound by the terms and conditions set forth at http://www.emlab.com/s/main/serviceterms.html

eurofins | Built Environment Testing

Report for:

Tracey Carpenter
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Eurofins Aerotech Built Environment Testing, Inc.
Project: AZ1418.11; Pueblo-Bldg C
EML ID: 3573122

Approved by:

Renee Luna-Trepczynski

Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 03-18-2024

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EM-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins Aerotech Built Environment Testing, Inc. ("the Company"), a member of the Eurofins Built Environment Testing group of companies, shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins Aerotech Built Environment Testing, Inc.
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Tracey Carpenter
Re: AZ1418.11; Pueblo-Bldg C

Date of Sampling: 03-13-2024
Date of Receipt: 03-14-2024
Date of Report: 03-18-2024

ASBESTOS PLM REPORT

Total Samples Submitted:	6
Total Samples Analyzed:	6
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM1, Red 6"x6" Floor Tiles & Grout & Thinset Lab ID-Version‡: 17464524-1

Sample Layers	Asbestos Content
Red-Brown Grout	ND
White Paint	ND
White Compound	ND
Sample Composite Homogeneity:	Poor

Location: PLM2, Red 6"x6" Floor Tiles & Grout & Thinset Lab ID-Version‡: 17464525-1

Sample Layers	Asbestos Content
Red-Brown Ceramic Tile	ND
Red-Brown Grout	ND
Gray Thinset	ND
White Mastic	ND
Sample Composite Homogeneity:	Poor

Location: PLM3, Red 6"x6" Floor Tiles & Grout & Thinset Lab ID-Version‡: 17464526-1

Sample Layers	Asbestos Content
Red-Brown Ceramic Tile	ND
Red-Brown Grout	ND
Gray Thinset	ND
White Mastic	ND
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, Inc.
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Tracey Carpenter
Re: AZ1418.11; Pueblo-Bldg C

Date of Sampling: 03-13-2024
Date of Receipt: 03-14-2024
Date of Report: 03-18-2024

ASBESTOS PLM REPORT

Location: PLM4, Brown Cove Base & Mastic Lab ID-Version‡: 17464527-1

Sample Layers	Asbestos Content
Brown Baseboard	ND
Yellow Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM5, Brown Cove Base & Mastic Lab ID-Version‡: 17464528-1

Sample Layers	Asbestos Content
Brown Baseboard	ND
Yellow Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM6, Brown Cove Base & Mastic Lab ID-Version‡: 17464529-1

Sample Layers	Asbestos Content
Brown Baseboard	ND
Yellow Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY eurofins

www.EMLabPK.com

EMLab P&K

Marlton, NJ: 3000 Lincoln Dr E, Ste. A, Marlton, NJ 08053 * (866) 871-1984
Phoenix, AZ: 1501 West Knudsen Drive, Phoenix, AZ 85027 * (800) 651-4802
SSF, CA: 6000 Shoreline Ct, Ste. 205, S. San Francisco, CA 94080 * (866) 888-6653

WEATHER		Fog	Rain	Snow	Wind	Clear
LEVEL	None					
	Light					
	Moderate					
	Heavy					

003573122

CONTACT INFORMATION

Company:	Dominion Environmental Consultants	Address: 20045 N. 19th Ave, Bldg 7, Phoenix, AZ 85027
Contact:	Tracey Carpenter	Special Instructions: email results:
Phone:	(602) 989-9992	tcarpenter@dominion-env.com

PROJECT INFORMATION

Project ID:	AZ 1418.11		
Project Description:	Pueblo - Bldg C		
Project Zip Code:	85044	Sampling Date/Time:	3/13/24 @ 10 AM
PO Number:	316310	Sampled By:	TLC

TURN AROUND TIME CODES - (TAT)

- STD - Standard (Default)
- ND - Next Business Day
- SD - Same Business Day
- WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

REQUESTED ANALYSIS

Non-Culturable — Spore Trap: Spore Trap Analysis; Other biological particles - supplement. Tape, Swab, Bulk: Direct Microscopic Exam (Qualitative); Qualitative spore count direct exam; Dust Characterization.
BioC... Swa...: 1-Media Surface Fungi (Genus ID + Asp. spp.); Culturable Air Fungi (Genus ID + Asp. spp.); Gram Stain and Counts (Culturable Air and Surface Bacte...); *Legionella* culture; Total Coliform, *E.coli* (Presence/Absence); QuantiTray-Sewage Screen; OTHER: (please specify test).
Asbestos in Air - PCM Airborne Fiber Count (NIOSH 740...); Asbestos Bulk - PLM (EPA method 600/R-93-116); Lead (Pb); PCR (please specify test); Allergens (please specify test).

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)	Asbestos Bulk - PLM (EPA method 600/R-93-116)
PLM 1-3	Red 6" x 6" Floor Tiles + Grout + Thinset	B	STD			X
PLM 4-6	Brown Cove Base + Mastic	B	STD			X

SAMPLE TYPE CODES

BC - BioCassette™	CP - Contact Plate	T - Tape	O - Other:
A1S - Andersen	ST - Spore Trap	SW - Swab	
SAS - Surface Air Sampler	B - Bulk	SO - Soil	
NP - Non-potable Water	P - Potable Water	D - Dust	

RELINQUISHED BY	DATE & TIME	RECEIVED BY	DATE & TIME
Tracey Carp [signature]	3/14/24 @ 9:15 AM	[signature]	3-14-24 9:...

eurofins | Built Environment Testing

Report for:

Nick Marcos
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Eurofins Aerotech Built Environment Testing, LLC
Project: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 600 (C Pod)
EML ID: 4122887

Approved by:



Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 06-26-2025

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EB-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins Aerotech Built Environment Testing, LLC ("the Company"), a member of the Eurofins Built Environment Testing group of companies, shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 600 (C Pod)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Total Samples Submitted:	18
Total Samples Analyzed:	18
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM-1, Gray Multi-Color Carpet Square and Mastic Lab ID-Version‡: 20584051-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Tan Mastic	ND
Composite Non-Asbestos Content:	80% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-2, Gray Multi-Color Carpet Square and Mastic Lab ID-Version‡: 20584052-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Tan Mastic	ND
Composite Non-Asbestos Content:	80% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-3, Gray Multi-Color Carpet Square and Mastic Lab ID-Version‡: 20584053-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Tan Mastic	ND
Composite Non-Asbestos Content:	80% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-4, Blue Cove Base and Mastic Lab ID-Version‡: 20584054-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Off-White Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 600 (C Pod)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-5, Blue Cove Base and Mastic Lab ID-Version‡: 20584055-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Off-White Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-6, Blue Cove Base and Mastic Lab ID-Version‡: 20584056-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Off-White Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-7, New 2' x 2' Ceiling Tile Lab ID-Version‡: 20584057-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	65% Cellulose 10% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-8, New 2' x 2' Ceiling Tile Lab ID-Version‡: 20584058-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	65% Cellulose 10% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 600 (C Pod)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-9, New 2' x 2' Ceiling Tile Lab ID-Version‡: 20584059-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	65% Cellulose 10% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-10, Old 2 'x 2' Ceiling Tile Lab ID-Version‡: 20584060-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-11, Old 2 'x 2' Ceiling Tile Lab ID-Version‡: 20584061-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-12, Old 2 'x 2' Ceiling Tile Lab ID-Version‡: 20584062-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 600 (C Pod)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-13, 2' x 4' Ceiling Tile Lab ID-Version‡: 20584063-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-14, 2' x 4' Ceiling Tile Lab ID-Version‡: 20584064-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-15, 2' x 4' Ceiling Tile Lab ID-Version‡: 20584065-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-16, Orange Peel D.W. (paint,tex,tape,j.c.,d.w.) Lab ID-Version‡: 20584066-1

Sample Layers	Asbestos Content
Off-White Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 600 (C Pod)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

Location: PLM-17, Orange Peel D.W. (paint,tex,tape,j.c.,d.w.) Lab ID-Version‡: 20584067-1

Sample Layers	Asbestos Content
Off-White Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

Location: PLM-18, Orange Peel D.W. (paint,tex,tape,j.c.,d.w.) Lab ID-Version‡: 20584068-1

Sample Layers	Asbestos Content
Off-White Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg 600 (C Pod)

Date of Sampling: 06-24-2025
Date of Receipt: 06-24-2025
Date of Report: 06-26-2025

ASBESTOS PLM REPORT

PROJECT ANALYST AND SIGNATORY REPORT

Project Analyst



Analyst: Jason Bosse

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY

www.eurofinsus.com/Built

eurofins | Built Environment Testing

East:(866) 871-1984
West/Central:(800) 651-4802

WEATHER		Fog	Rain	Snow	Wind	Clear
LEVEL	None					
	Light					
	Moderate					
	Heavy					

CONTACT INFORMATION

Company:	Dominion Environmental Consultants	Address:20045 N. 19th Ave., Phx, AZ 85027
Contact:	Nick Marcos	Special Instructions:
Phone:	623-516-1415	

PROJECT INFORMATION

Project ID:	AZ1418.59		
Project Description:	Kyrene Del Pueblo M.S. - Bldg 600 (C Pod)		
Project Zip Code:		Sampling Date/Time:	6/24/2025
PO Number:	13752	Sampled By:	NM

TURN AROUND TIME CODES - (TAT)

STD - Standard (Default)
ND - Next Business Day
SD - Same Business Day
WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)
PLM 1-3	Gray Multi-Color Carpet Square and Mastic	B	STD		
PLM 4-6	Blue Cove Base and Mastic	B	STD		
PLM 7-9	New 2' X 2' Ceiling Tile	B	STD		
PLM 10-12	Old 2' X 2' Ceiling Tile	B	STD		
PLM 13-15	2' X 4' Ceiling Tile	B	STD		
PLM 16-18	Orange Peel D.W. (paint,tex,tape,j.c.,d.w.)	B	STD		

REQUESTED SERVICES

Non-Culturable

Spore Trap Analysis
Other biological particles - supplement
Direct Microscopic Exam (Qualitative)
Quantitative spore count direct exam
Dust Characterization

Culturable

1-Media Surface Fungi (Genus ID + *Asp.* spp.)
Culturable Air Fungi (Genus ID + *Asp.* spp.)
Gram Stain and Counts (Culturable Air and Surface)
Legionella culture
Total Coliform, *E.coli* (Presence/Absence)
QuantiTray-Sewage Screen
OTHER: (please specify test)

004122887

Other Requests

Asbestos in Air - PCM Airborne Fiber Count (NIOSH 7400)
Asbestos Bulk - PLM (EPA method 600/R-93-116)

SAMPLE ID	Asbestos Bulk - PLM (EPA method 600/R-93-116)
PLM 1-3	X
PLM 4-6	X
PLM 7-9	X
PLM 10-12	X
PLM 13-15	X
PLM 16-18	X

Lead (Pb) / Paint Chip
PCR (please specify test)
Allergens (please specify test)

SAMPLE TYPE CODES

BC - BioCassette™	**CP** - Contact Plate	**T** - Tape	**O** - Other:
A1S - Andersen	**ST** - Spore Trap	**SW** - Swab	
SAS - Surface Air Sampler	**B** - Bulk	**SO** - Soil	
NP - Non-potable Water	**P** - Potable Water	**D** - Dust	

RELINQUISHED BY	DATE & TIME
Nick Marcos	6/24/2025

RECEIVED BY	DATE & TIME
Lydia Cotero	4:10PM 6/24/25

By submitting this Chain of Custody, you agree to be bound by the terms and conditions set forth at http://www.emlab.com/s/main/serviceterms.html

eurofins | Built Environment Testing

Report for:

Nick Marcos
Dominion Environmental Consultants, Inc.
20045 N. 19th Ave, Bldg 7
Phoenix, AZ 85027

Regarding: Eurofins Aerotech Built Environment Testing, LLC
Project: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 700 (Pod I/J)
EML ID: 4121017

Approved by:



Approved Signatory
Renee Luna-Trepczynski

Dates of Analysis:
Asbestos PLM: 06-25-2025

Service SOPs: Asbestos PLM (EPA 40CFR App E to Sub E of Part 763 & EPA METHOD 600/R-93-116, SOP EB-AS-S-1267)
NVLAP Lab Code 500031-0

All samples were received in acceptable condition unless noted in the Report Comments portion in the body of the report. The results relate only to the samples as received and tested. The results include an inherent uncertainty of measurement associated with estimating percentages by polarized light microscopy. Measurement uncertainty data for sample results with >1% asbestos concentration can be provided when requested.

Eurofins Aerotech Built Environment Testing, LLC ("the Company"), a member of the Eurofins Built Environment Testing group of companies, shall have no liability to the client or the client's customer with respect to decisions or recommendations made, actions taken or courses of conduct implemented by either the client or the client's customer as a result of or based upon the Test Results. In no event shall the Company be liable to the client with respect to the Test Results except for the Company's own willful misconduct or gross negligence nor shall the Company be liable for incidental or consequential damages or lost profits or revenues to the fullest extent such liability may be disclaimed by law, even if the Company has been advised of the possibility of such damages, lost profits or lost revenues. In no event shall the Company's liability with respect to the Test Results exceed the amount paid to the Company by the client therefor.

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 700 (Pod I/J)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Total Samples Submitted:	18
Total Samples Analyzed:	18
Total Samples with Layer Asbestos Content > 1%:	0

Location: PLM-1, Gray Mulit-Color Carpet Square and Mastic Lab ID-Version‡: 20574350-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	40% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-2, Gray Mulit-Color Carpet Square and Mastic Lab ID-Version‡: 20574351-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	40% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-3, Gray Mulit-Color Carpet Square and Mastic Lab ID-Version‡: 20574352-1

Sample Layers	Asbestos Content
Multicolored Carpet	ND
Yellow Mastic	ND
Composite Non-Asbestos Content:	40% Synthetic Fibers
Sample Composite Homogeneity:	Moderate

Location: PLM-4, Blue Cove Base and Mastic Lab ID-Version‡: 20574353-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 700 (Pod I/J)
Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-5, Blue Cove Base and Mastic Lab ID-Version‡: 20574354-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-6, Blue Cove Base and Mastic Lab ID-Version‡: 20574355-1

Sample Layers	Asbestos Content
Blue Cove Base	ND
Cream Mastic	ND
Sample Composite Homogeneity:	Moderate

Location: PLM-7, Orange Peel D.W. (paint, tex, tape, j.c., d.w.) Lab ID-Version‡: 20574356-1

Sample Layers	Asbestos Content
White Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 700 (Pod I/J)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-8, Orange Peel D.W. (paint, tex, tape, j.c., d.w.)

Lab ID-Version‡: 20574357-1

Sample Layers	Asbestos Content
Tan Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 700 (Pod I/J)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-9, Orange Peel D.W. (paint, tex, tape, j.c., d.w.) Lab ID-Version‡: 20574358-1

Sample Layers	Asbestos Content
Beige Paint	ND
White Texture	ND
Cream Tape	ND
White Joint Compound	ND
White Drywall with Brown Paper	ND
Composite Non-Asbestos Content:	15% Cellulose
Sample Composite Homogeneity:	Poor

Location: PLM-10, New 2'x2' Ceiling Tile Lab ID-Version‡: 20574359-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-11, New 2'x2' Ceiling Tile Lab ID-Version‡: 20574360-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-12, New 2'x2' Ceiling Tile Lab ID-Version‡: 20574361-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 700 (Pod I/J)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-13, Old 2'x2' Ceiling Tile Lab ID-Version‡: 20574362-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-14, Old 2'x2' Ceiling Tile Lab ID-Version‡: 20574363-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-15, Old 2'x2' Ceiling Tile Lab ID-Version‡: 20574364-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-16, Textured 2'x2' Ceiling Tile Lab ID-Version‡: 20574365-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 700 (Pod I/J)

Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

Location: PLM-17, Textured 2'x2' Ceiling Tile

Lab ID-Version‡: 20574366-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

Location: PLM-18, Textured 2'x2' Ceiling Tile

Lab ID-Version‡: 20574367-1

Sample Layers	Asbestos Content
Gray Ceiling Tile with White Surface	ND
Composite Non-Asbestos Content:	40% Cellulose 40% Glass Fibers
Sample Composite Homogeneity:	Good

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

All components not quantified as asbestos content and non-asbestos content are considered to be non-fibrous matrix components. Matrix components may include, but are not limited to, gypsum, paint, silicate minerals, vinyl, binder, calcium carbonate, tar, and foam.

Inhomogeneous samples are separated into homogeneous subsamples and analyzed individually. ND means no fibers were detected. When detected, the minimum detection and reporting limit is less than 1% unless point counting is performed. Floor tile samples may contain large amounts of interference material and it is recommended that the sample be analyzed by gravimetric point count analysis to lower the detection limit and to aid in asbestos identification.
‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".


Eurofins Aerotech Built Environment Testing, LLC
1501 West Knudsen Drive, Phoenix, AZ 85027
(800) 651-4802 www.eurofinsus.com/Built

Client: Dominion Environmental Consultants, Inc.
C/O: Nick Marcos
Re: AZ1418.59; Kyrene Del Pueblo M.S. - Bldg. 700 (Pod I/J)
Date of Sampling: 06-23-2025
Date of Receipt: 06-23-2025
Date of Report: 06-25-2025

ASBESTOS PLM REPORT

PROJECT ANALYST AND SIGNATORY REPORT

Project Analyst



Analyst: Renee Luna-Trepczynski

The test report shall not be reproduced except in full, without written approval of the laboratory. The report must not be used by the client to claim product certification, approval, or endorsement by NVLAP, NIST, or any agency of the federal government. The Company reserves the right to dispose of all samples after a period of thirty (30) days, according to all state and federal guidelines, unless otherwise specified.

‡ A "Version" indicated by -"x" after the Lab ID# with a value greater than 1 indicates a sample with amended data. The revision number is reflected by the value of "x".

CHAIN OF CUSTODY

www.eurofinsus.com/Built

eurofins | Built Environment Testing

East:(866) 871-1984
West/Central:(800) 651-4802

WEATHER		Fog	Rain	Snow	Wind	Clear
LEVEL	None					
	Light					
	Moderate					
	Heavy					

CONTACT INFORMATION

Company:	Dominion Environmental Consultants	Address:20045 N. 19th Ave., Phx, AZ 85027
Contact:	Nick Marcos	Special Instructions:
Phone:	623-516-1415	

PROJECT INFORMATION

Project ID:	AZ1418.59		
Project Description:	Kyrene Del Pueblo M.S. - Bldg. 700 (Pod I/J)		
Project Zip Code:		Sampling Date/Time:	6/23/2025
PO Number:	13751	Sampled By:	NM

TURN AROUND TIME CODES - (TAT)

STD - Standard (Default)
ND - Next Business Day
SD - Same Business Day
WH - Weekend/Holiday/ASAP

Rushes received after 2pm or on weekends, will be considered received the next business day. Please alert us in advance of weekend analysis needs.

REQUESTED SERVICES

Non-Culturable | Culturable

004121017

SAMPLE ID	DESCRIPTION	Sample Type (Below)	TAT (Above)	Total Volume/Area (as applicable)	NOTES (Time of day, Temp, RH, etc.)	Spore Trap Analysis	Other biological particles - supplement	Direct Microscopic Exam (Qualitative)	Quantitative spore count direct exam	Dust Characterization	1-Media Surface Fungi (Genus ID + Asp. spp.	Culturable Air Fungi (Genus ID + Asp. spp.)	Gram Stain and Counts (Culturable Air and Su	*Legionella* culture	Total Coliform, *E.coli* (Presence/Absence)	Quant/Tray-Sewage Screen	OTHER: (please specify test)	Other Requests: Asbestos in Air - PCM Airborne Fiber Count (NIOSH 7400)	Asbestos Bulk - PLM (EPA method 600/R-93-116)	Lead (Pb) / Paint Chip	PCR (please specify test)	Allergens (please specify test)
PLM 1-3	Gray Multi-Color Carpet Square and Mastic	B	STD																X			
PLM 4-6	Blue Cove Base and Mastic	B	STD																X			
PLM.7-9	Orange Peel D.W. (paint,tex,tape,j.c.,d.w.)	B	STD																X			
PLM 10-12	New 2' X 2' Ceiling Tile	B	STD																X			
PLM 13-15	Old 2' X 2' Ceiling Tile	B	STD																X			
PLM 16-18	Textured 2' X 2' Ceiling Tile	B	STD																X			

SAMPLE TYPE CODES

BC - BioCassette™	**CP** - Contact Plate	**T** - Tape	**O** - Other:
A1S - Andersen	**ST** - Spore Trap	**SW** - Swab	
SAS - Surface Air Sampler	**B** - Bulk	**SO** - Soil	
NP - Non-potable Water	**P** - Potable Water	**D** - Dust	


RELINQUISHED BY	DATE & TIME	RECEIVED BY	DATE & TIME
Nick Marcos	6/23/2025	Patty Lugo	6/23/25 2:45pm

By submitting this Chain of Custody, you agree to be bound by the terms and conditions set forth at http://www.emlab.com/s/main/serviceterms.html

SECTION 10

♦

ASSUMED ACBM LOCATION MAPS

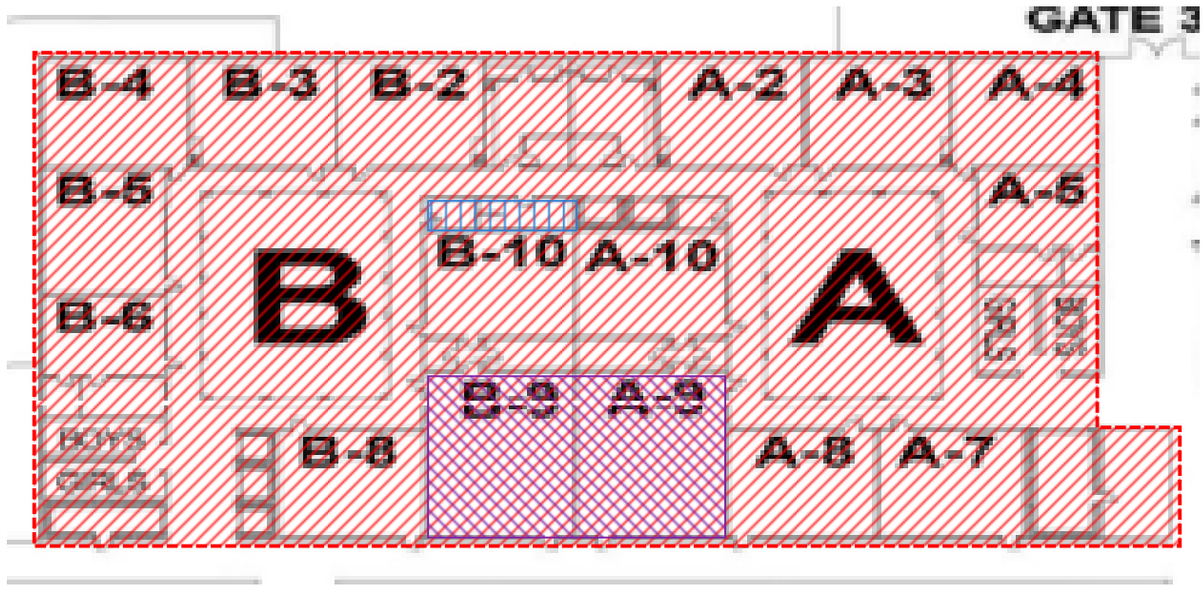

Assumed Asbestos-Containing

Interior Caulking, Tacboard, Black Sink Coating, & Brick & Mortar

Assumed Asbestos-Containing

Black Countertops & Fume Hood Panel

Assumed Asbestos-Containing

Gray 5" x 5" Ceramic Floor Tile, Grout & Mastic, & Gray 5" x 5" Ceramic Wall Tile, Grout, & Mastic

Assumed Asbestos-Containing


Exterior Caulking & Exterior Plaster Overhang

Assumed Asbestos-Containing Material Location Map (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 100 - Pod A/B

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

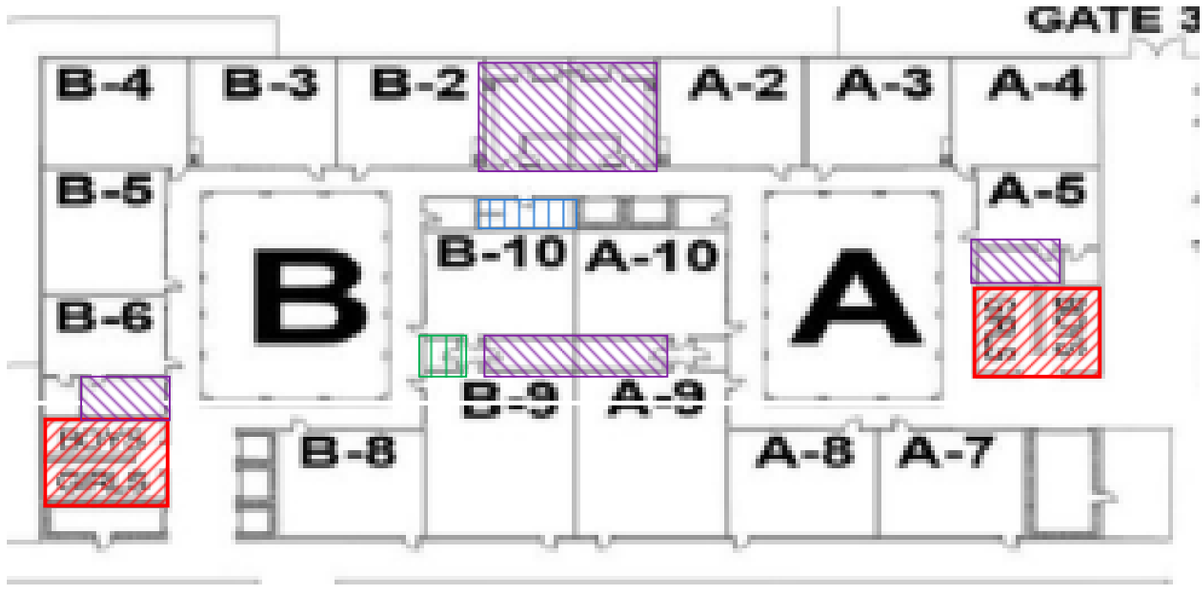

Assumed Asbestos-Containing

Tan 4" x 6" Ceramic Wall Tile, Brown 4" x 6" Ceramic Wall Tile, Grout & Mastic for Ceramic Wall Tiles, & Fixture Caulking

Assumed Asbestos-Containing

Tan 12" x 12" Vinyl Floor Tile & Mastic & Brown Cove Base & Mastic

Assumed Asbestos-Containing

Smooth Drywall System

Assumed Asbestos-Containing


Fiberglass Reinforced Plastic & Mastic

Assumed Asbestos-Containing Material Location Map (2)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 100 - Pod A/B

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

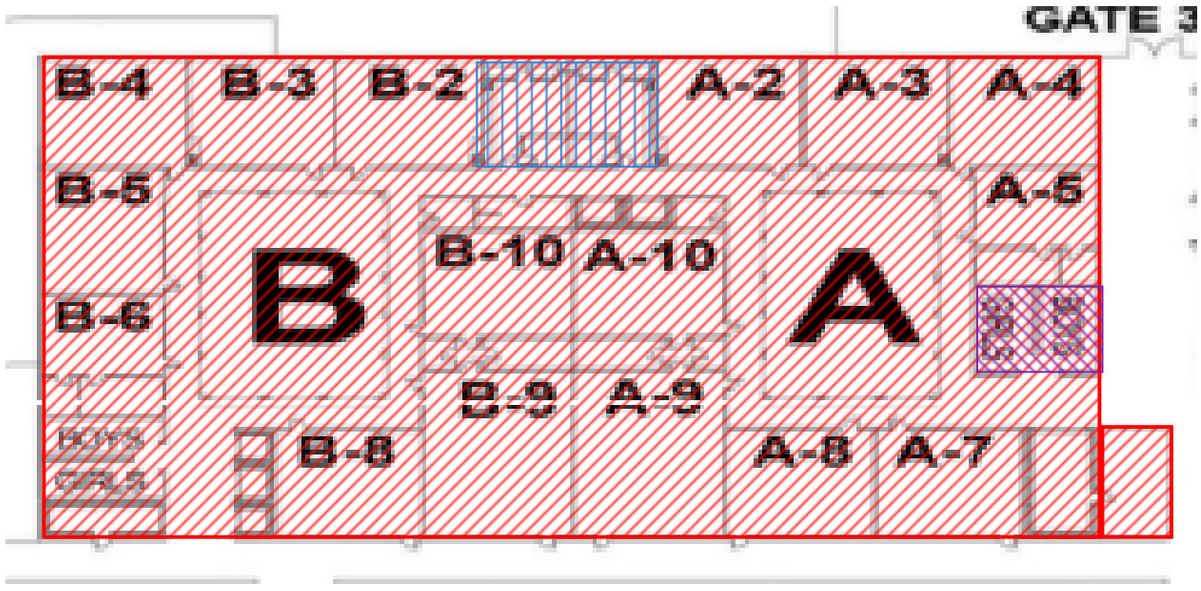

Assumed Asbestos-Containing

White Duct Tape & Mastic,
Unfinished Drywall System,
& Gray Flex Duct Wrap

*** Above Plenum**

Assumed Asbestos-Containing

Dark Brown 4" x 4"
Replacement Ceramic Wall Tile

Assumed Asbestos-Containing


Divider Wall

Assumed Asbestos-Containing Material Location Map (3)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 100 - Pod A/B

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

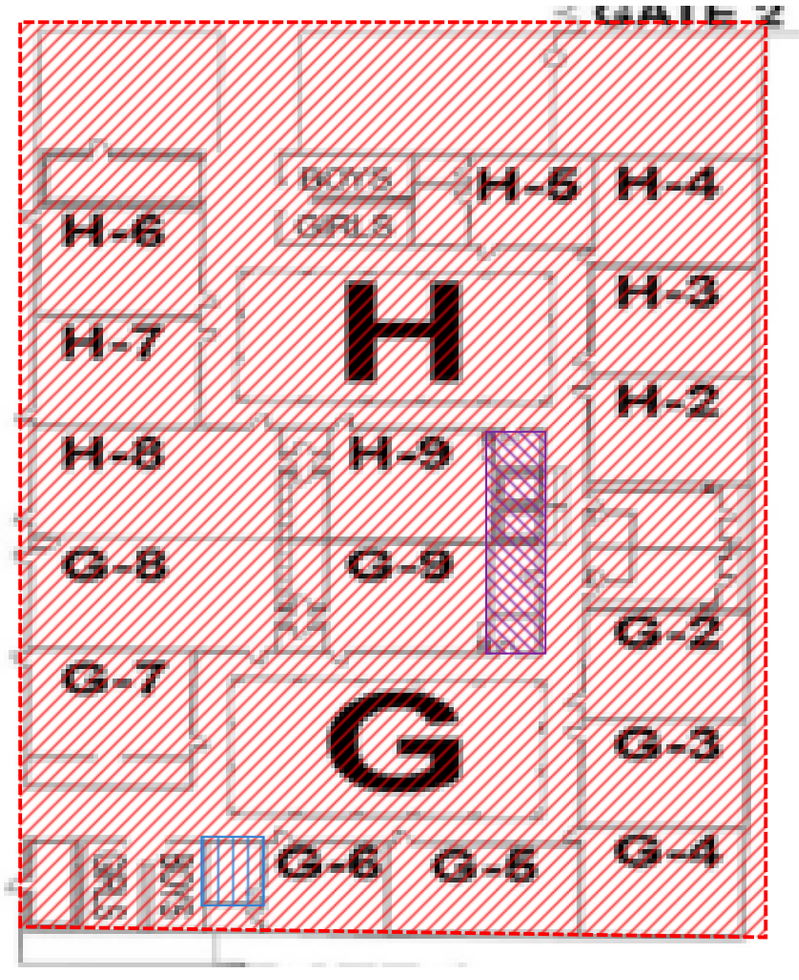

N

Assumed Asbestos-Containing

Interior Caulking, Tacboard, Black Sink Coating, & Brick & Mortar

Assumed Asbestos-Containing

Gray 6" x 6" Ceramic Floor Tile, Grout & Thinset, & Gray 4" x 6" Ceramic Wall Tile, Grout, & Mastic

Assumed Asbestos-Containing

Blue 12" x 12" Vinyl Floor Tile & Mastic

Assumed Asbestos-Containing


Exterior Caulking & Exterior Plaster Overhang


Assumed Asbestos-Containing Material Location Map (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226


Project No. AZ1418.59

Building 200 - Pod G/H

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

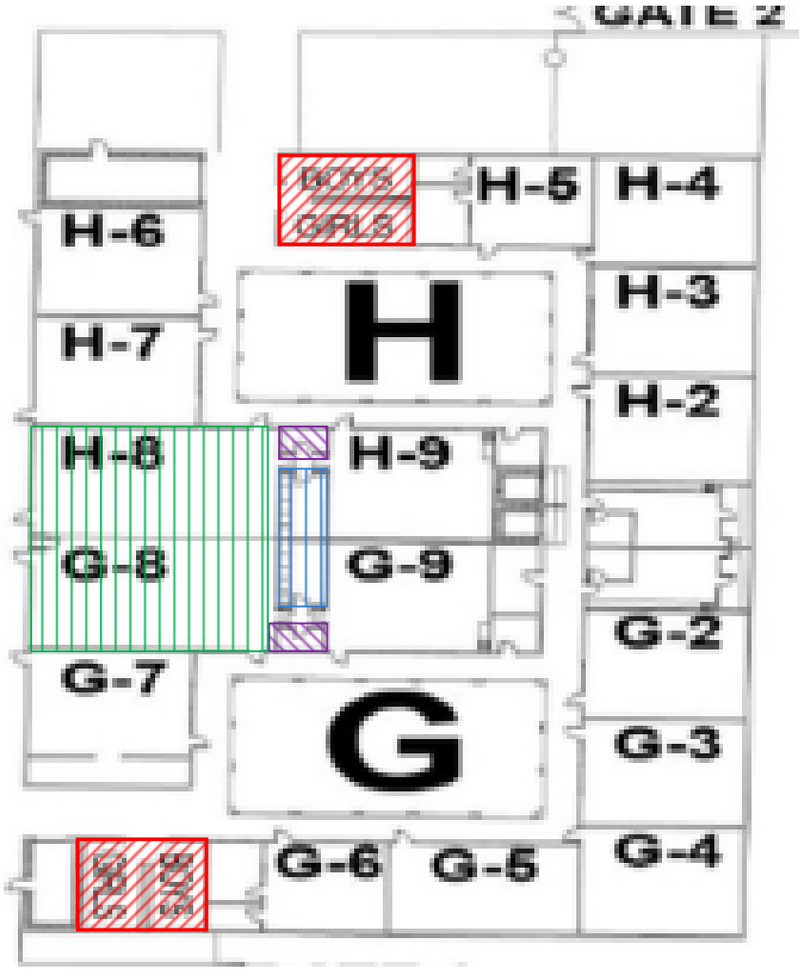





Assumed Asbestos-Containing

Tan 4" x 6" Ceramic Wall Tile, Grout & Mastic & Fixture Caulking




Assumed Asbestos-Containing

Fiberglass Reinforced Plastic & Mastic & Old Black Cove Base & Masitc



Assumed Asbestos-Containing

Tan 12" x 12" Vinyl Floor Tile & Mastic & Brown Cove Base & Mastic



Assumed Asbestos-Containing


Black Countertops & Fume Hood Panel

Assumed Asbestos-Containing Material Location Map (2)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 200 - Pod G/H

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

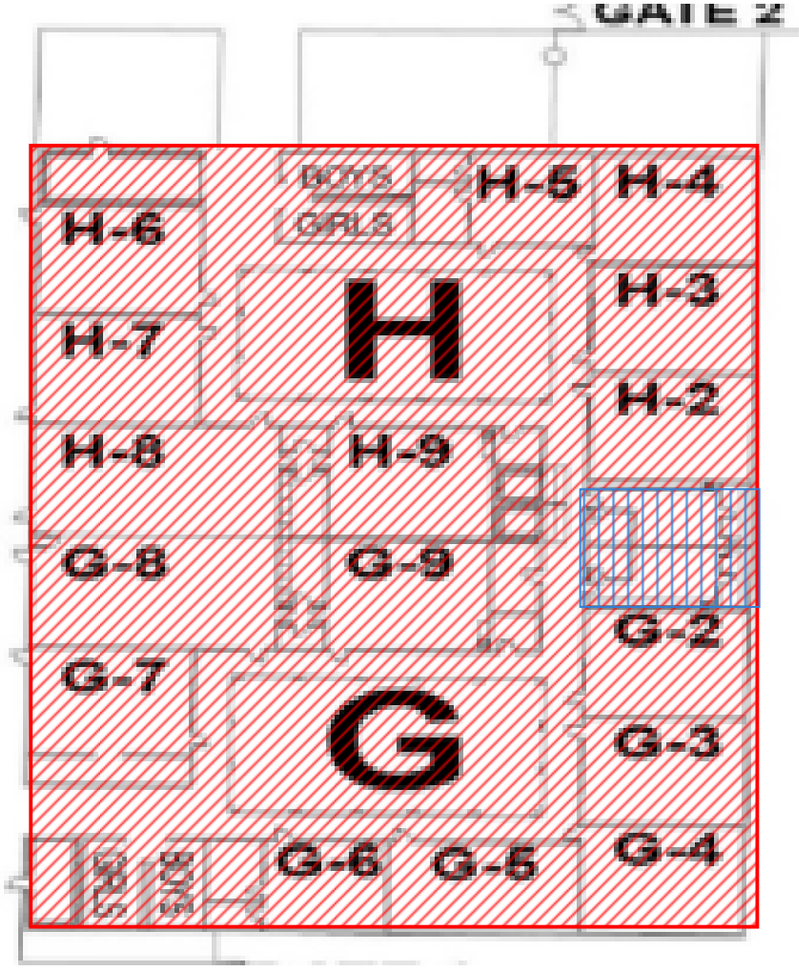

Assumed Asbestos-Containing

White Duct Tape & Mastic,
White Pipe Wrap & Mastic,
& Unfinished Drywall System

*** Above the Plenum**

Assumed Asbestos-Containing


Divider Wall

Assumed Asbestos-Containing Material Location Map (3)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 200 - Pod G/H

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

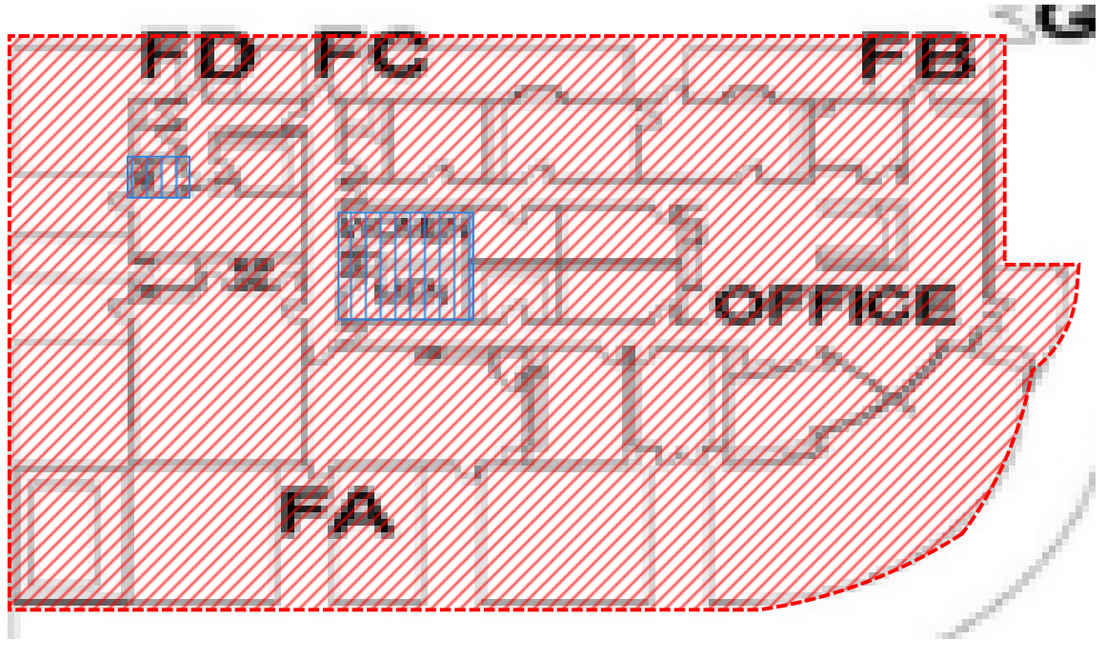

Assumed Asbestos-Containing

Interior Caulking, Tacboard, Black Sink Coating, Glass Block Mortar, & Brick & Mortar

Assumed Asbestos-Containing

Fixture Caulking


Assumed Asbestos-Containing

Exterior Caulking

Assumed Asbestos-Containing Material Location Map (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59
Building 300 - Administration Office

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

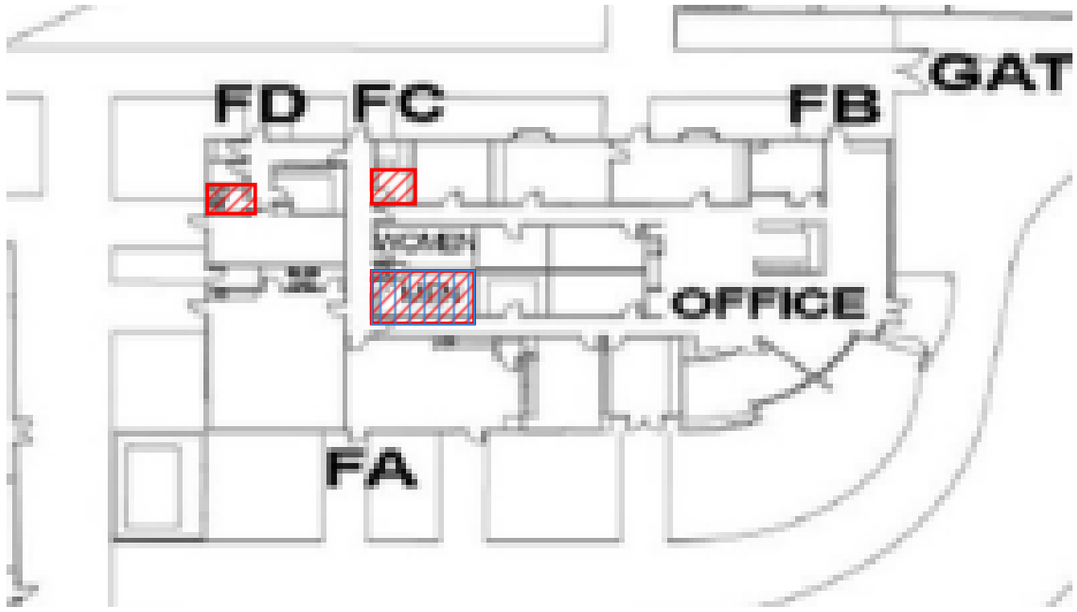

Assumed Asbestos-Containing

Tan 12" x 12" Vinyl Floor Tile & Mastic

Assumed Asbestos-Containing


Brown Cove Base & Mastic

Assumed Asbestos-Containing Material Location Map (2) — Project No. AZ1418.59

Kyrene Del Pueblo Middle School

360 South Twelve Oaks Boulevard, Chandler, Arizona 85226 — Building 300 - Administration Office

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

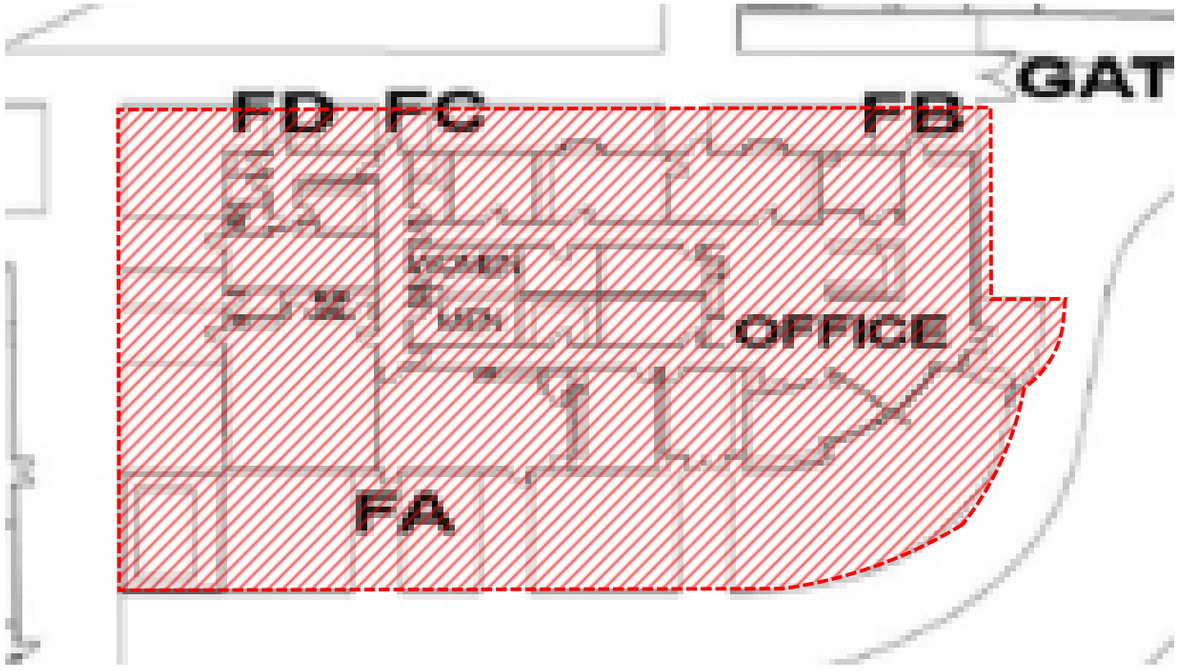

Assumed Asbestos-Containing


White Duct Tape & Mastic, Gray Duct Mastic, Silver Flex Duct Wrap, Gray Flex Duct Wrap, Silver Duct Tape, Silver Duct Wrap, & Unfinished Drywall System

*** Above the Plenum**

Assumed Asbestos-Containing Material Location Map (3)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59
Building 300 - Administration Office

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

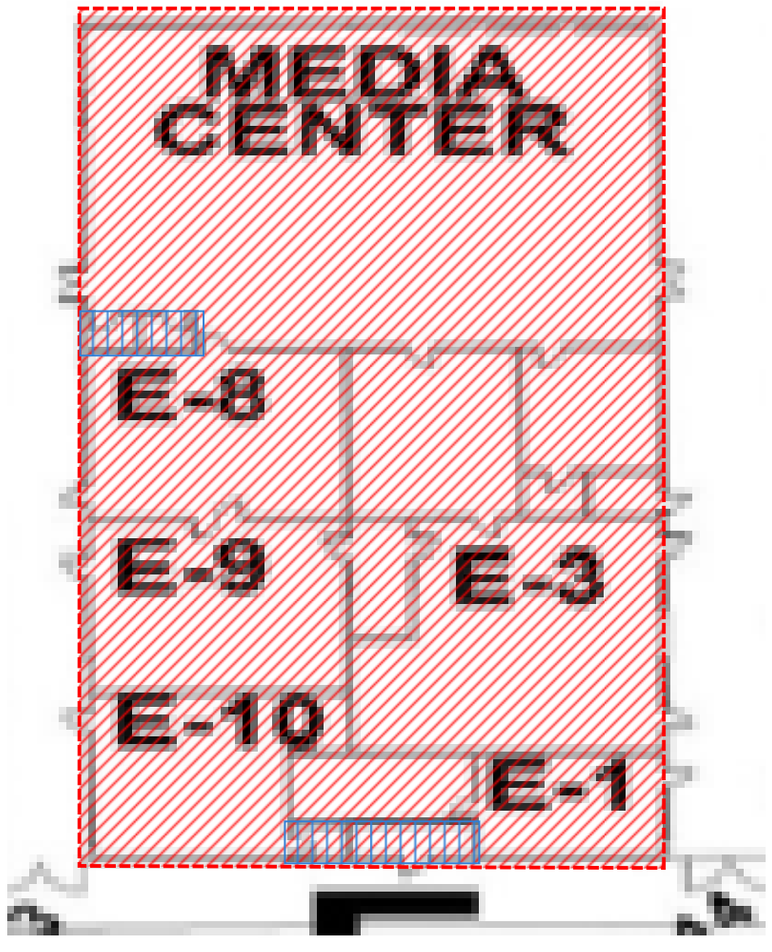

Assumed Asbestos-Containing

Interior Caulking, Tacboard, Black Sink Coating, Tan 12" x 12" Vinyl Floor Tile & Mastic, Wallpaper, & Brick & Mortar

Assumed Asbestos-Containing

Fixture Caulking

Assumed Asbestos-Containing


Exterior Caulking

Assumed Asbestos-Containing Material Location Map (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 400 - Pod E

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

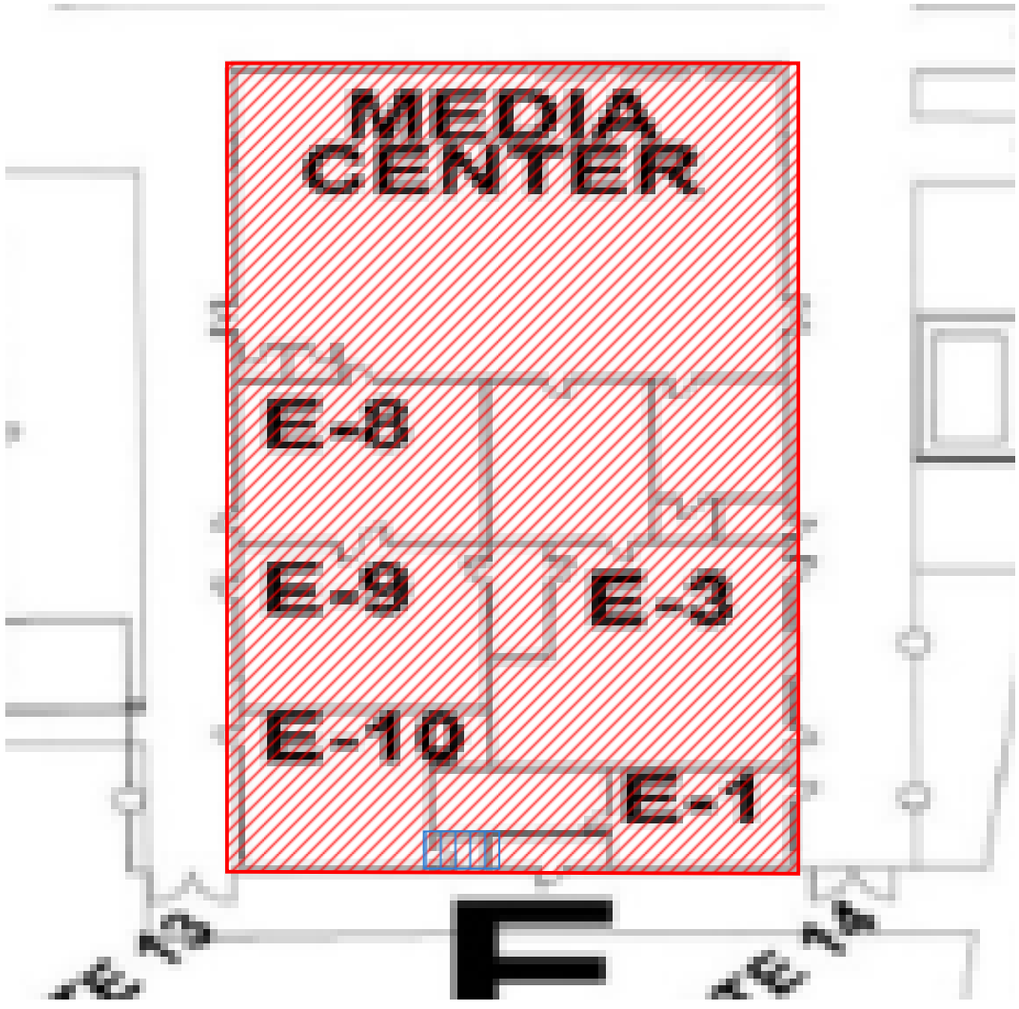

Assumed Asbestos-Containing

White Duct Seam Tape & Mastic,
Silver Flex Duct Wrap,
Gray Flex Duct Wrap,
White Pipe Wrap & Mastic,
Unfinished Drywall System,
& Skylight Insulation Panel

*** Above the Plenum**

Assumed Asbestos-Containing


Gray Cove Base & Mastic

Assumed Asbestos-Containing Material Location Map (2)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 400 - Pod E

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

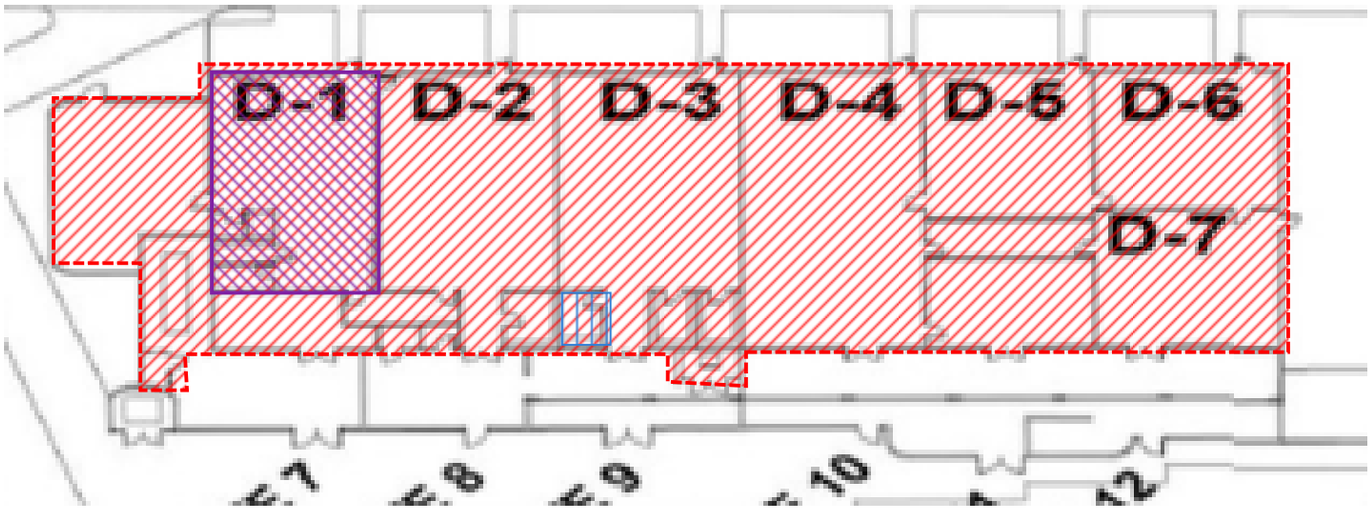

Assumed Asbestos-Containing

Interior Caulking, Tacboard, Black Sink Coating, & Brick & Mortar

Assumed Asbestos-Containing

Rubber Flooring & Fiberglass Reinforced Plastic & Mastic

Assumed Asbestos-Containing

Brown Carpet & Mastic

Assumed Asbestos-Containing


Exterior Caulking

Assumed Asbestos-Containing Material Location Map (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 500 - Pod D

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

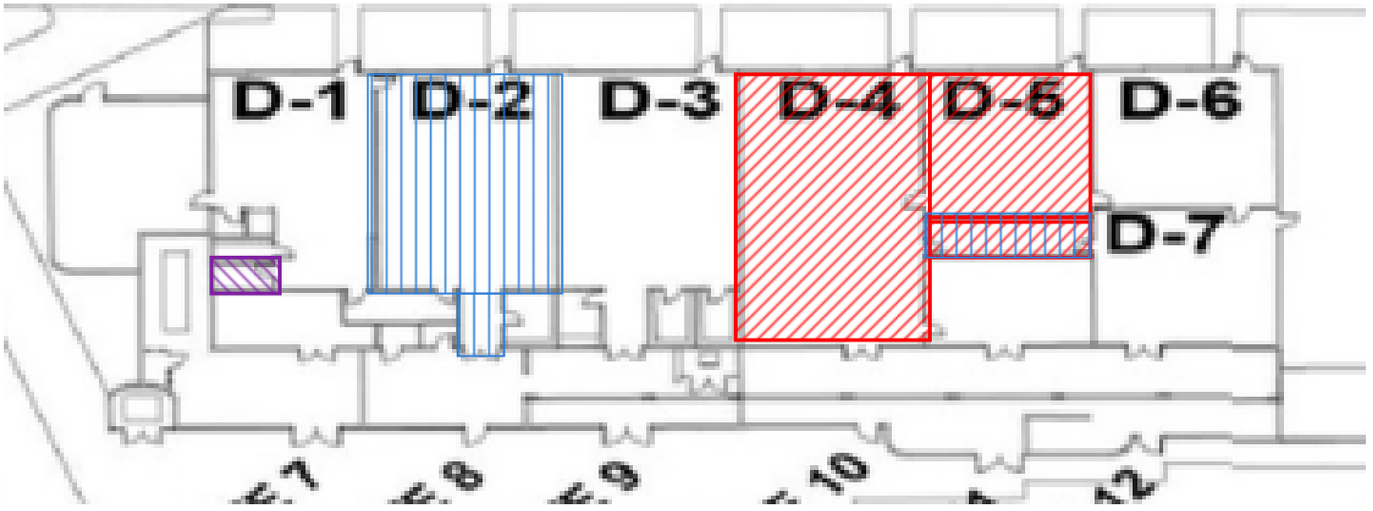

Assumed Asbestos-Containing

Black 12" x 12" Vinyl Floor Tile & Mastic, Divider Wall, & Gray Sink Coating

Assumed Asbestos-Containing

Tan 12" x 12" Vinyl Floor Tile & Mastic

Assumed Asbestos-Containing


Polished Concrete

Assumed Asbestos-Containing Material Location Map (2)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 500 - Pod D

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

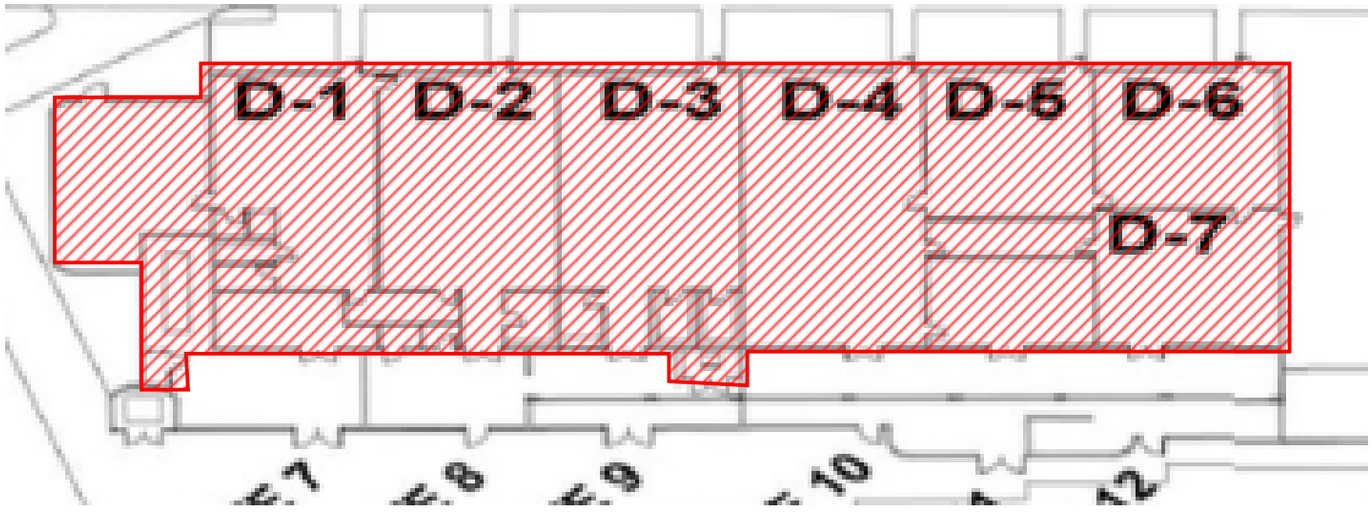


Assumed Asbestos-Containing

Silver Duct Wrap, Silver Flex Duct Wrap,
White Duct Seam Tape & Mastic,
Silver Duct Tape, Gray Duct Mastic,
Skylight Insulation Panel, &
Unfinished Drywall System

*** Above the Plenum**

Assumed Asbestos-Containing Material Location Map (3) — Project No. AZ1418.59
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226 — Building 500 - Pod D

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

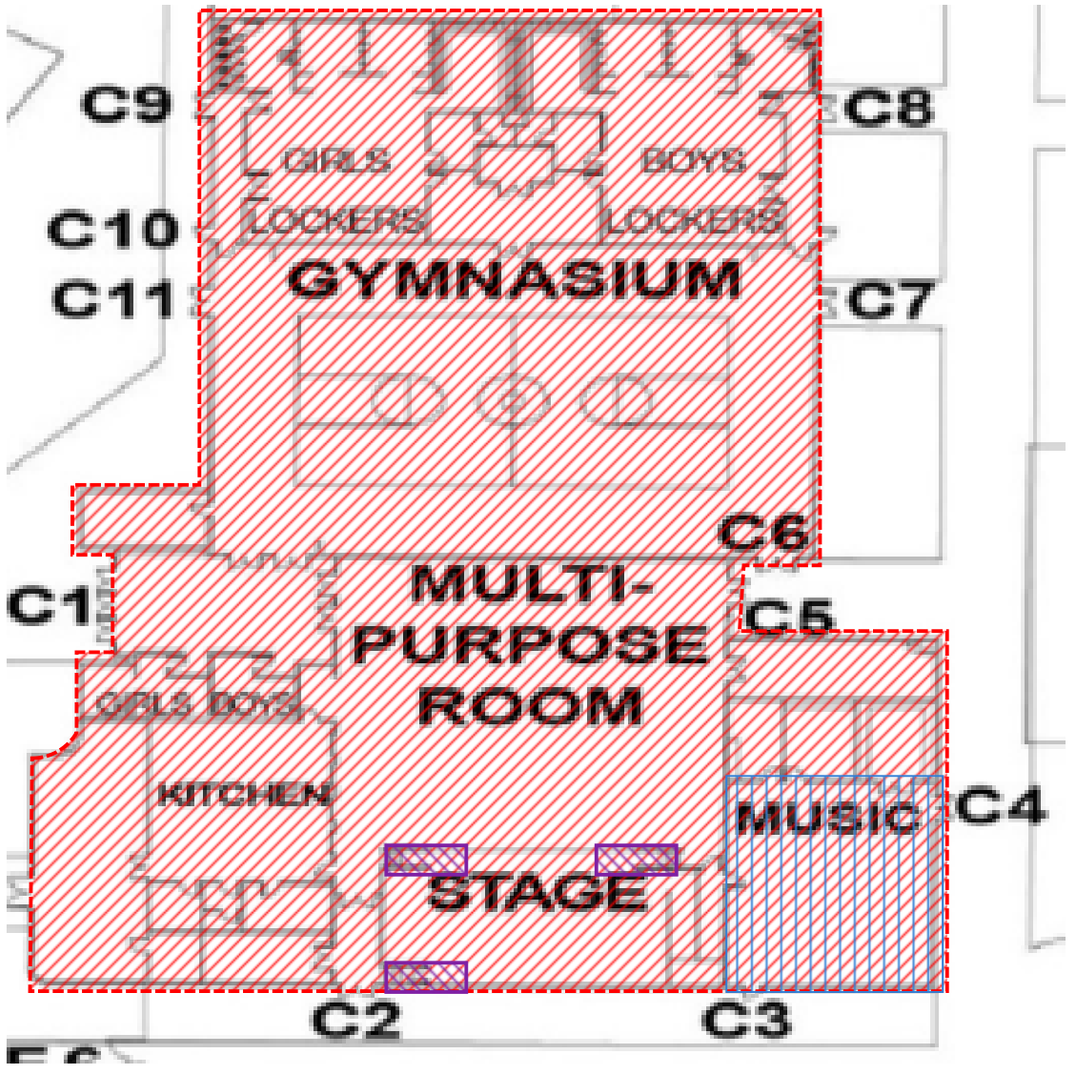

N

Assumed Asbestos-Containing

Interior Caulking &
Brick & Mortar

Assumed Asbestos-Containing

Black Stair Tread & Mastic
& Red Ramp Tread & Mastic

Assumed Asbestos-Containing

Black Sink Coating

Assumed Asbestos-Containing


Exterior Caulking &
Exterior Plaster Overhang


Assumed Asbestos-Containing Material Location Map (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226


Project No. AZ1418.59

Building 600 - Pod C

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

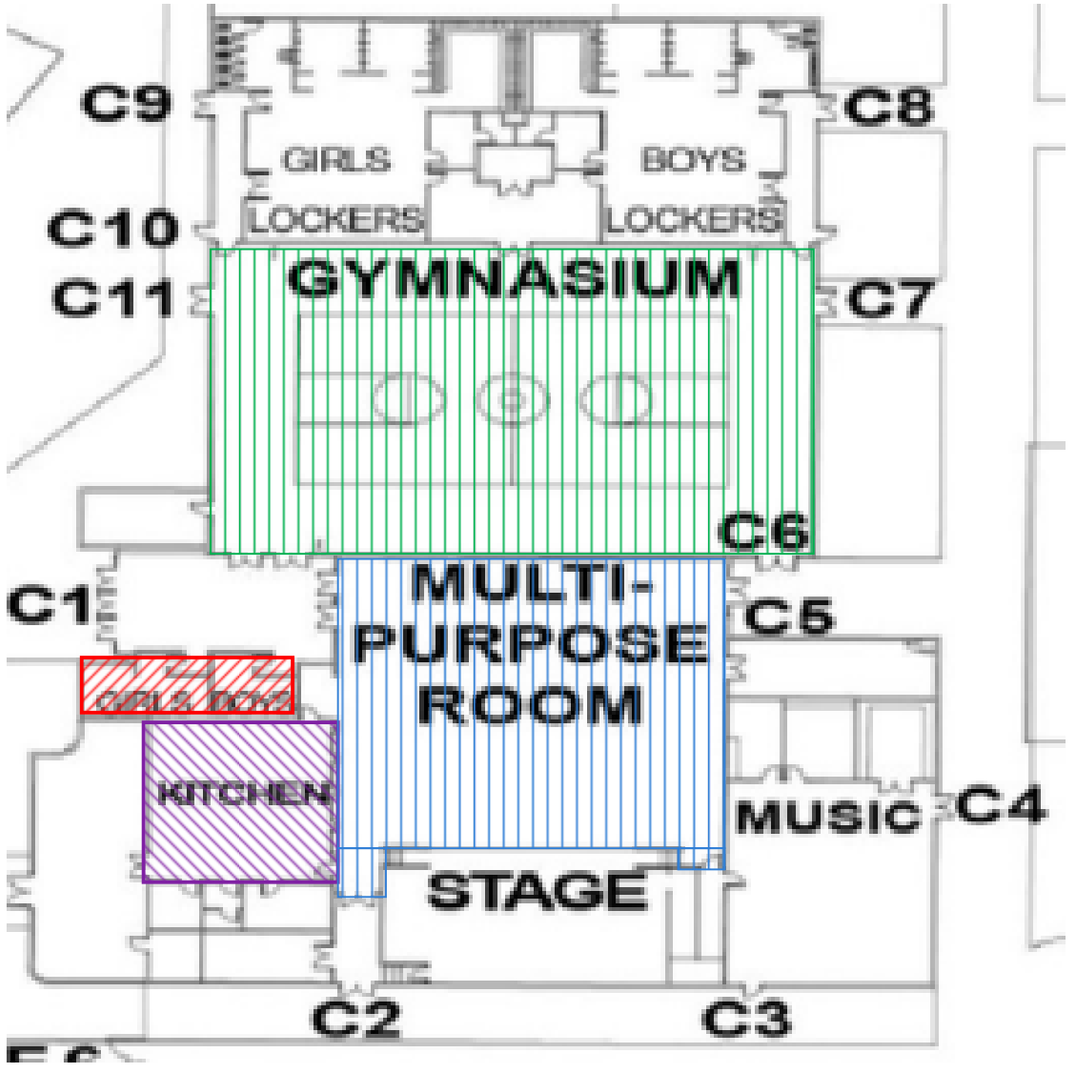





Assumed Asbestos-Containing

White 4" x 4" Ceramic Wall Tile, Beige 4" x 4" Ceramic Wall Tile, Maroon 4" x 4" Ceramic Wall Tile, Grout & Mastic for Ceramic Wall Tiles, Fixture Caulking, & Gray Floor Coating




Assumed Asbestos-Containing

Red 6" x 6" Ceramic Wall Tile, Grout & Mortar, 2' x 4' Drywall Ceiling Tile, Fiberglass Reinforced Plastic & Mastic, & Silver Kitchen Caulking



Assumed Asbestos-Containing

Polished Concrete & Floor Expansion Joint



Assumed Asbestos-Containing


Black L-Shaped Cove Base & Mastic


Assumed Asbestos-Containing Material Location Map (2)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226


Project No. AZ1418.59

Building 600 - Pod C

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

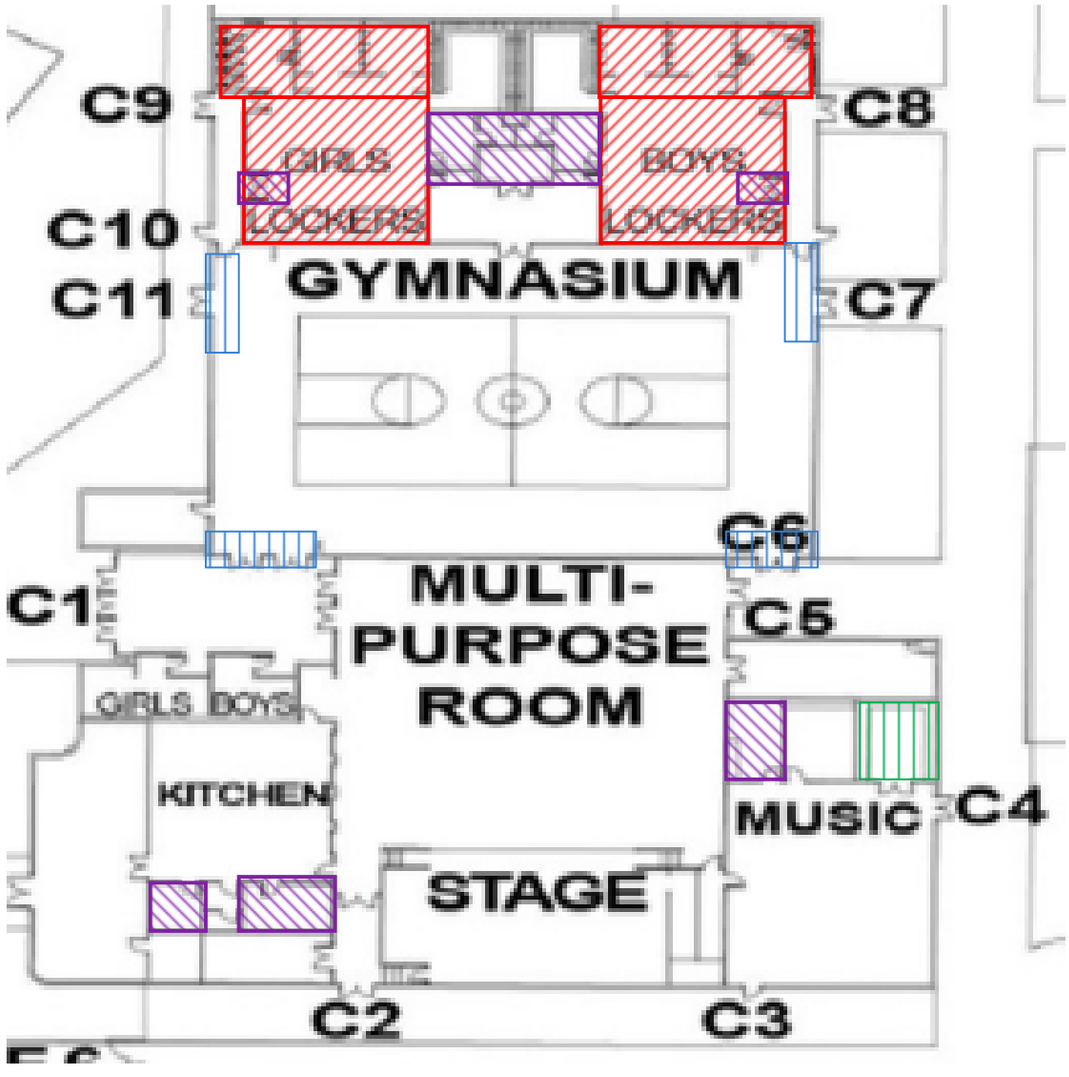





Assumed Asbestos-Containing

Tan 2" x 2" Ceramic Floor Tile, Grout & Thinset, Beige 4" x 6" Ceramic Wall Tile, Brown 4" x 6" Ceramic Wall Tile, & Grout & Mastic for Ceramic Wall Tiles




Assumed Asbestos-Containing

Tan 12" x 12" Vinyl Floor Tile & Mastic



Assumed Asbestos-Containing

Black Carpet Squares & Mastic



Assumed Asbestos-Containing


Wallpaper


Assumed Asbestos-Containing Material Location Map (3)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 600 - Pod C

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

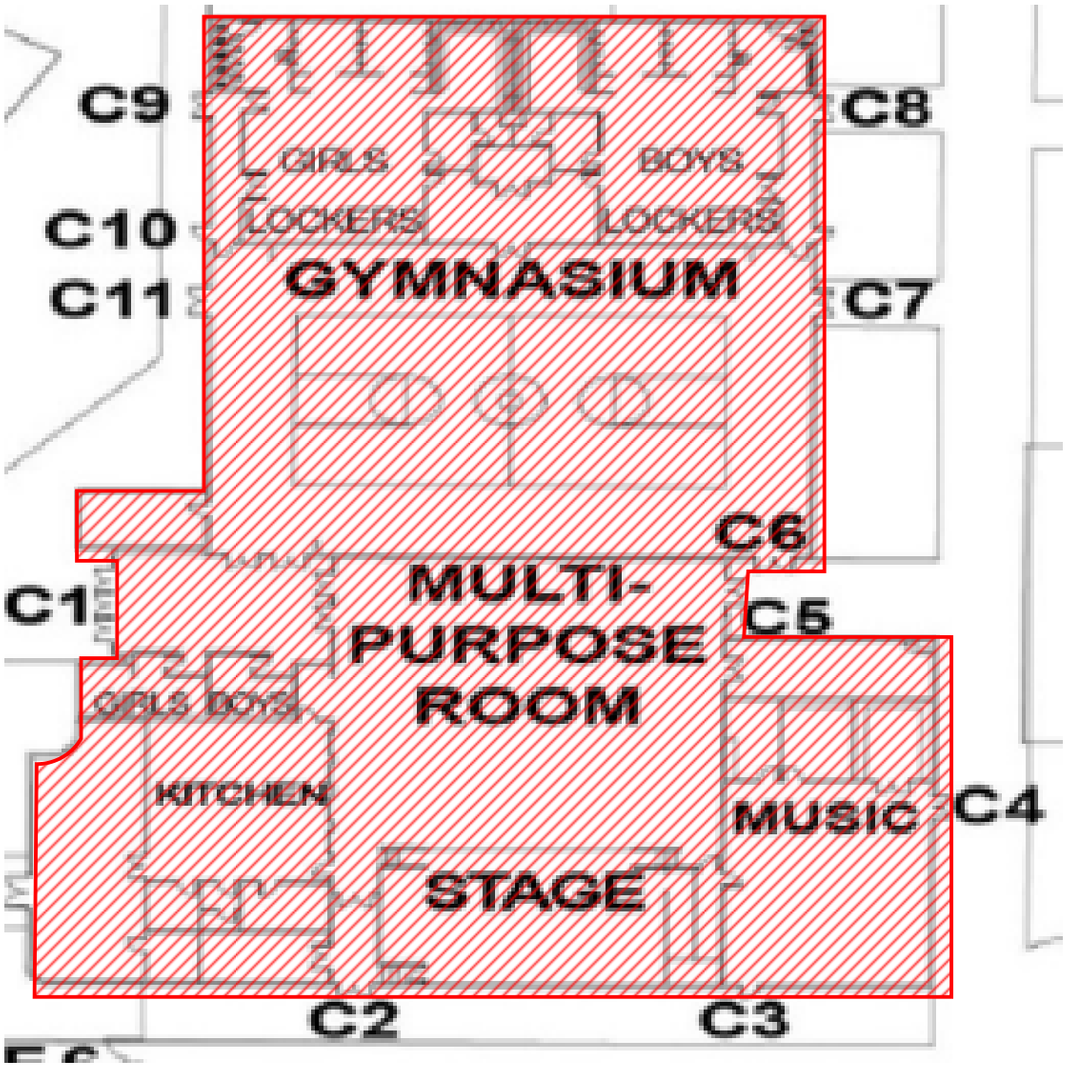



Assumed Asbestos-Containing

Unfinished Drywall System,
White Duct Seam Tape & Mastic,
Silver Flex Duct Wrap, &
Gray Silver Duct Wrap


*** Above the Plenum**

Assumed Asbestos-Containing Material Location Map (4)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 600 - Pod C

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

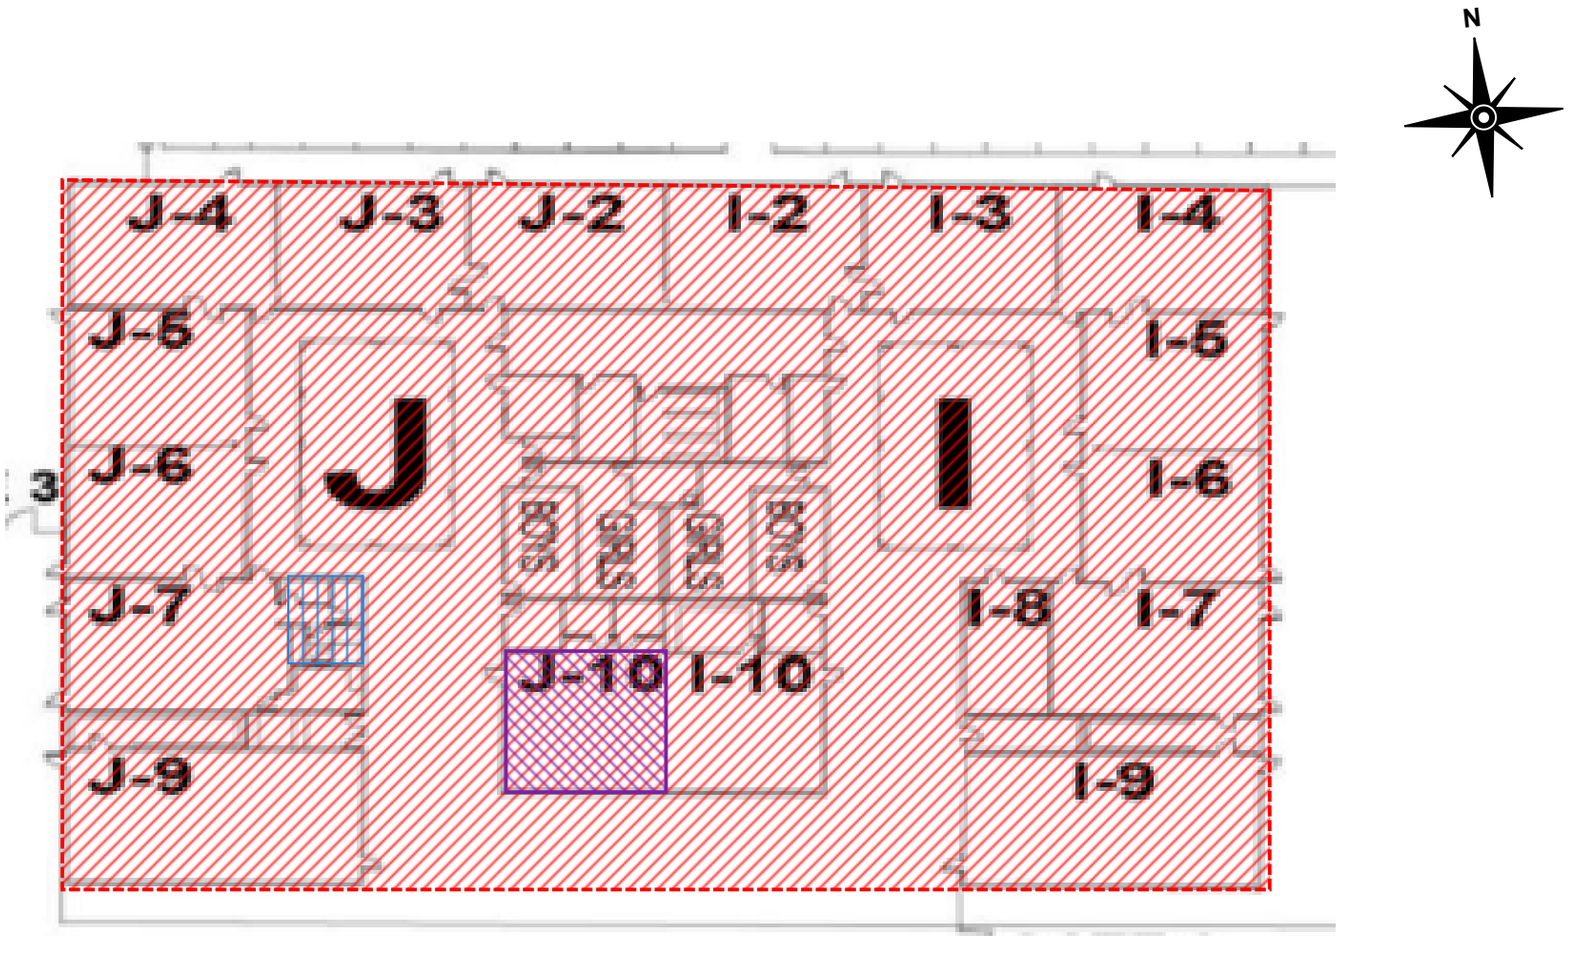

Assumed Asbestos-Containing

Interior Caulking, Tacboard, Fiberglass Reinforced Plastic & Mastic, & Brick & Mortar

Assumed Asbestos-Containing

Soundboard Wrap & Mastic

Assumed Asbestos-Containing

Tan 12" x 12" Vinyl Floor Tile & Mastic

Assumed Asbestos-Containing


Exterior Caulking & Exterior Plaster Overhang

Assumed Asbestos-Containing Material Location Map (1)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 700 - Pod I/J

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

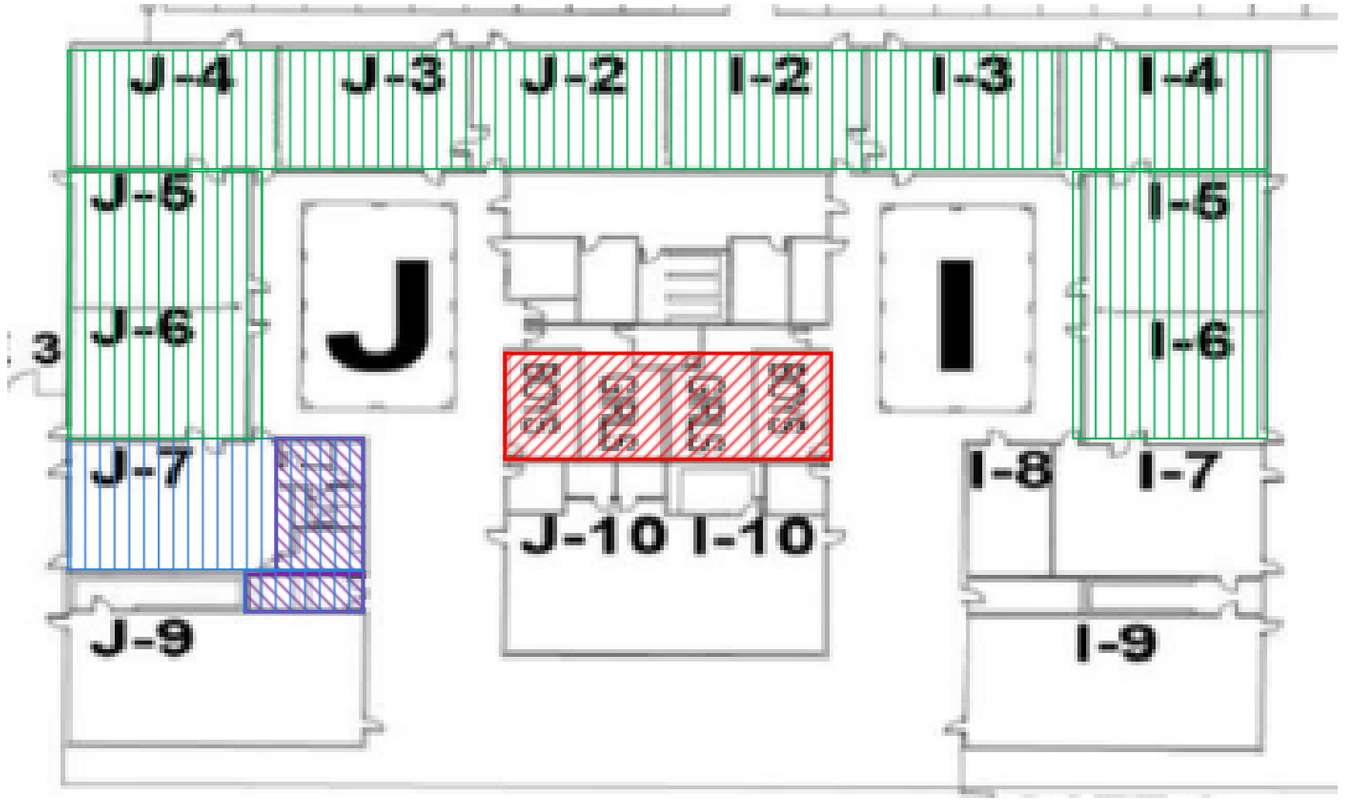

Assumed Asbestos-Containing

White 2" x 2" Ceramic Floor Tile, Grout, & Thinset, White 4" x 4" Ceramic Wall Tile, Black 2" x 2" Ceramic Wall Tile, Grout & Mastic for Ceramic Wall Tiles, Fixture Caulking, & Black Sink Coating

Assumed Asbestos-Containing

Gray Cove Base & Mastic

Assumed Asbestos-Containing

Beige Streak 12" x 12" Vinyl Floor Tile & Mastic

Assumed Asbestos-Containing


Divider Wall

Assumed Asbestos-Containing Material Location Map (2)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 700 - Pod I/J

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

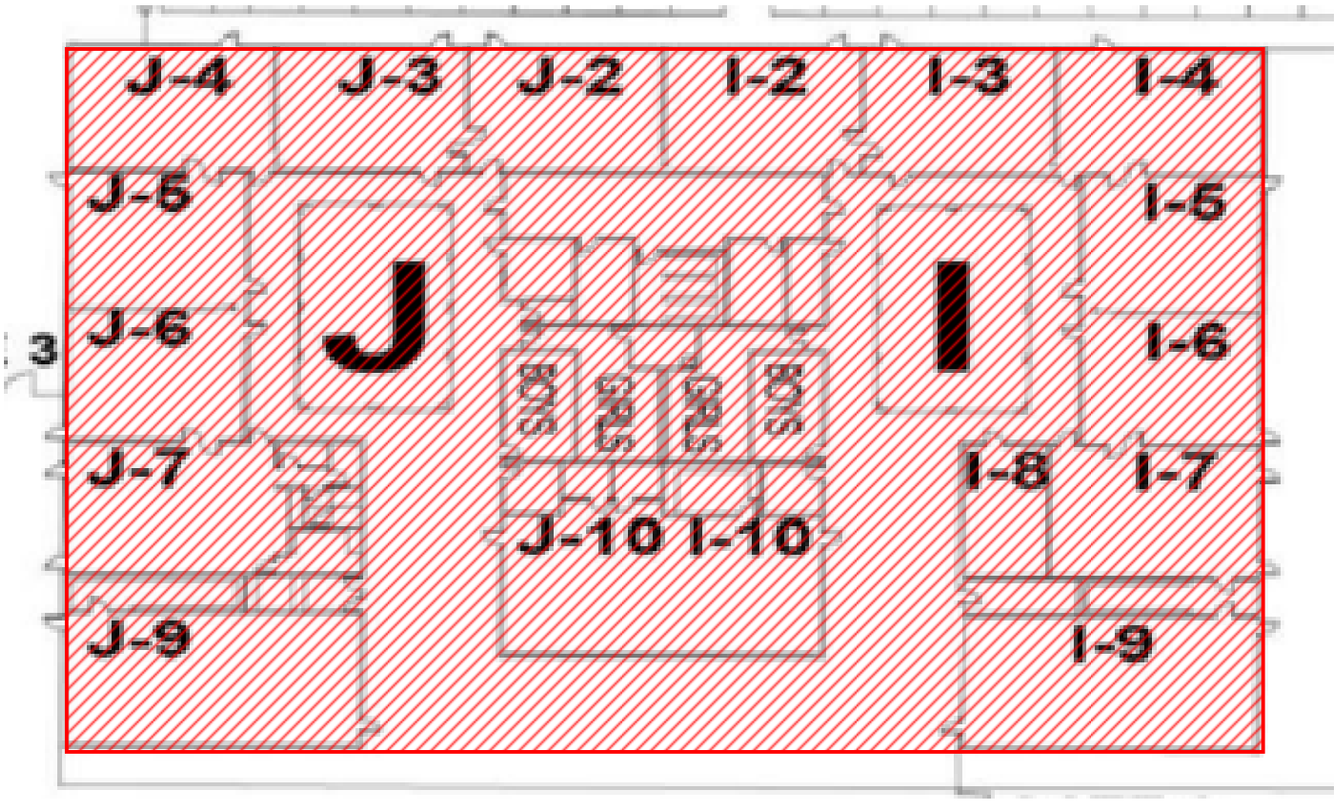

Assumed Asbestos-Containing

Unfinished Drywall System, White Duct Tape & Mastic, White Pipe Wrap & Mastic, Gray Duct Mastic, Silver Duct Wrap, Silver Flex Duct Wrap, & Black Foam Pipe Insulation

Assumed Asbestos-Containing Material Location Map (3)
Kyrene Del Pueblo Middle School
360 South Twelve Oaks Boulevard, Chandler, Arizona 85226

Project No. AZ1418.59

Building 700 - Pod I/J

Dominion Environmental Consultants, Inc.
20045 North 19th Avenue - Building 7 - Phoenix, Arizona 85027 - (623) 516-1415

SECTION 11

♦

INSPECTOR ACCREDITATIONS

THE ASBESTOS INSTITUTE

Certifies that

Basilio Marcos

has attended and received instruction in the EPA approved course

AHERA Building Inspector Refresher

on

June 01, 2021

and successfully completed and passed the competency exam.

Certificate:
ON-4644-1419-060121

Date of Examination:
1-Jun-2021
Date of Expiration:
01-Jun-2022

William T. Cavness
Director

Approved Instructor

THE ASBESTOS INSTITUTE
20033 N. 19th Ave, Building 6, Phoenix, AZ 85027
602-864-6564 – www.theasbestosinstitute.com

This training meets all requirements for asbestos certification under Toxic Substance Control Act Title II.

THE ASBESTOS INSTITUTE

Certifies that

Nicholas Marcos

has attended and received instruction in the EPA approved course

AHERA Building Inspector Refresher

on

March 29, 2021

and successfully completed and passed the competency exam.

Certificate:
ON-4644-8873-032921

Date of Examination:
29-Mar-2021
Date of Expiration:
29-Mar-2022

William T. Cavness
Director

Approved Instructor

THE ASBESTOS INSTITUTE
20033 N. 19th Ave, Building 6, Phoenix, AZ 85027
602-864-6564 – www.theasbestosinstitute.com

This training meets all requirements for asbestos certification under Toxic Substance Control Act Title II.

THE ASBESTOS INSTITUTE

Certifies that

Tracey Carpenter

has attended and received instruction in the EPA approved course

AHERA Building Inspector Refresher

on

September 05, 2023

and successfully completed and passed the competency exam.

Certificate:
ON-4644-14588-090523

Date of Examination:
5-Sep-2023

Date of Expiration:
05-Sep-2024

William T. Cavness
Director

Approved Instructor

THE ASBESTOS INSTITUTE
20033 N. 19th Ave, Building 6, Phoenix, AZ 85027
602-864-6564 – www.theasbestosinstitute.com

The person receiving this certificate has completed the requisite training for asbestos accreditation under TSCA Title II.

THE ASBESTOS INSTITUTE

Certifies that

Nicholas Marcos

has attended and received instruction in the EPA approved course

AHERA Building Inspector Refresher

on

March 13, 2025

and successfully completed and passed the competency exam.

Certificate:
ON-188748-8873-031325

Date of Examination:
13-Mar-2025
Date of Expiration:
13-Mar-2026

A. Zwanenburg
Director

Approved Instructor

THE ASBESTOS INSTITUTE
20033 N. 19th Ave, Building 6, Phoenix, AZ 85027
602-864-6564 – www.theasbestosinstitute.com

FL Course # CRS228

The person receiving this certificate has completed the requisite training for asbestos accreditation under TSCA Title II.

SECTION 12

♦

LABORATORY ACCREDITATIONS

United States Department of Commerce
National Institute of Standards and Technology

Certificate of Accreditation to ISO/IEC 17025:2017

NVLAP LAB CODE: 500031-0

Eurofins EMLab P&K

Phoenix, AZ

is accredited by the National Voluntary Laboratory Accreditation Program for specific services, listed on the Scope of Accreditation, for:

Asbestos Fiber Analysis

This laboratory is accredited in accordance with the recognized International Standard ISO/IEC 17025:2017. This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (refer to joint ISO-ILAC-IAF Communique dated January 2009).

2021-01-01 through 2021-12-31

Effective Dates

For the National Voluntary Laboratory Accreditation Program

National Voluntary Laboratory Accreditation Program

SCOPE OF ACCREDITATION TO ISO/IEC 17025:2017

Eurofins EMLab P&K
1501 W. Knudsen Dr.
Phoenix, AZ 85027-1307
Mr. Dan Shelby
Phone: 623-298-1015
Email: dshelby@emlabpk.com
http://www.emlab.com

ASBESTOS FIBER ANALYSIS — NVLAP LAB CODE 500031-0

Bulk Asbestos Analysis

Code	*Description*
18/A01	EPA -- 40 CFR Appendix E to Subpart E of Part 763, Interim Method of the Determination of Asbestos in Bulk Insulation Samples
18/A03	EPA 600/R-93/116: Method for the Determination of Asbestos in Bulk Building Materials

For the National Voluntary Laboratory Accreditation Program

United States Department of Commerce
National Institute of Standards and Technology

Certificate of Accreditation to ISO/IEC 17025:2017

NVLAP LAB CODE: 500031-0

Eurofins EMLab P&K

Phoenix, AZ

is accredited by the National Voluntary Laboratory Accreditation Program for specific services, listed on the Scope of Accreditation, for:

Asbestos Fiber Analysis

This laboratory is accredited in accordance with the recognized International Standard ISO/IEC 17025:2017. This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (refer to joint ISO-ILAC-IAF Communique dated January 2009).

2022-01-01 through 2022-12-31

Effective Dates

For the National Voluntary Laboratory Accreditation Program

SCOPE OF ACCREDITATION TO ISO/IEC 17025:2017

Eurofins EMLab P&K
1501 W. Knudsen Dr.
Phoenix, AZ 85027-1307
Mr. Dan Shelby
Phone: 623-298-1015
Email: dan.shelby@eurofinset.com
http://www.emlab.com

ASBESTOS FIBER ANALYSIS — NVLAP LAB CODE 500031-0

Bulk Asbestos Analysis

Code	*Description*
18/A01	EPA -- 40 CFR Appendix E to Subpart E of Part 763, Interim Method of the Determination of Asbestos in Bulk Insulation Samples
18/A03	EPA 600/R-93/116: Method for the Determination of Asbestos in Bulk Building Materials

For the National Voluntary Laboratory Accreditation Program

United States Department of Commerce
National Institute of Standards and Technology

Certificate of Accreditation to ISO/IEC 17025:2017

NVLAP LAB CODE: 500031-0

Eurofins EMLab P&K

Phoenix, AZ

is accredited by the National Voluntary Laboratory Accreditation Program for specific services, listed on the Scope of Accreditation, for:

Asbestos Fiber Analysis

This laboratory is accredited in accordance with the recognized International Standard ISO/IEC 17025:2017. This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (refer to joint ISO-ILAC-IAF Communique dated January 2009).

2024-01-01 through 2024-12-31

Effective Dates

For the National Voluntary Laboratory Accreditation Program

National Voluntary Laboratory Accreditation Program

SCOPE OF ACCREDITATION TO ISO/IEC 17025:2017

Eurofins EMLab P&K
1501 W. Knudsen Dr.
Phoenix, AZ 85027-1307
Claudia Palermo
Phone: 856-334-1001
Email: claudia.palermo@et.eurofinsus.com
https://www.eurofinsus.com/environment-testing/built-environment/

ASBESTOS FIBER ANALYSIS — NVLAP LAB CODE 500031-0

Bulk Asbestos Analysis

Code	*Description*
18/A01	EPA -- 40 CFR Appendix E to Subpart E of Part 763, Interim Method of the Determination of Asbestos in Bulk Insulation Samples
18/A03	EPA 600/R-93/116: Method for the Determination of Asbestos in Bulk Building Materials

For the National Voluntary Laboratory Accreditation Program

United States Department of Commerce
National Institute of Standards and Technology

Certificate of Accreditation to ISO/IEC 17025:2017

NVLAP LAB CODE: 500031-0

Eurofins EMLab P&K

Phoenix, AZ

is accredited by the National Voluntary Laboratory Accreditation Program for specific services, listed on the Scope of Accreditation, for:

Asbestos Fiber Analysis

This laboratory is accredited in accordance with the recognized International Standard ISO/IEC 17025:2017. This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (refer to joint ISO-ILAC-IAF Communique on ISO/IEC 17025).

2025-01-01 through 2025-12-31

Effective Dates

For the National Voluntary Laboratory Accreditation Program

National Voluntary Laboratory Accreditation Program

SCOPE OF ACCREDITATION TO ISO/IEC 17025:2017

Eurofins EMLab P&K
1501 W. Knudsen Dr.
Phoenix, AZ 85027-1307
Joshua Snyder
Phone: 800-651-4802
Email: joshua.snyder@et.eurofinsus.com
https://www.eurofinsus.com/environment-testing/built-environment/

ASBESTOS FIBER ANALYSIS — NVLAP LAB CODE 500031-0

Bulk Asbestos Analysis

Code	*Description*
18/A01	EPA -- 40 CFR Appendix E to Subpart E of Part 763, Interim Method of the Determination of Asbestos in Bulk Insulation Samples
18/A03	EPA 600/R-93/116: Method for the Determination of Asbestos in Bulk Building Materials

For the National Voluntary Laboratory Accreditation Program
