ORANGEBURG COUNTY SCHOOL DISTRICT

BOARD MEETING





ORANGEBURG
COUNTY SCHOOL DISTRICT
We Are **One**


OPERATIONS UPDATE





EAST LAKE ELEMENTARY



EAST LAKE ELEMENTARY

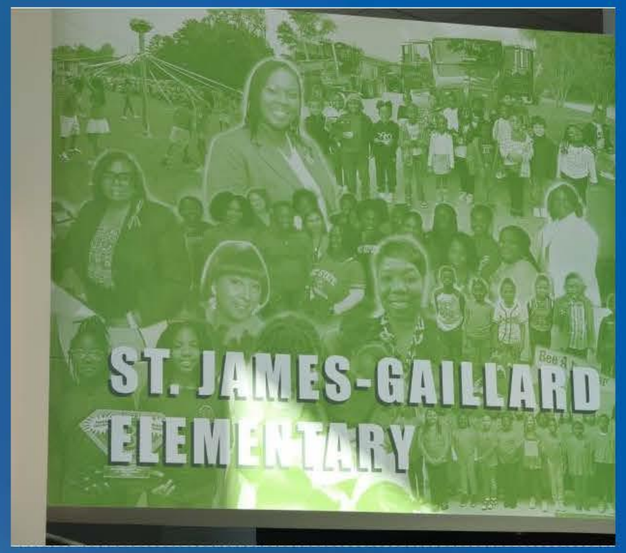

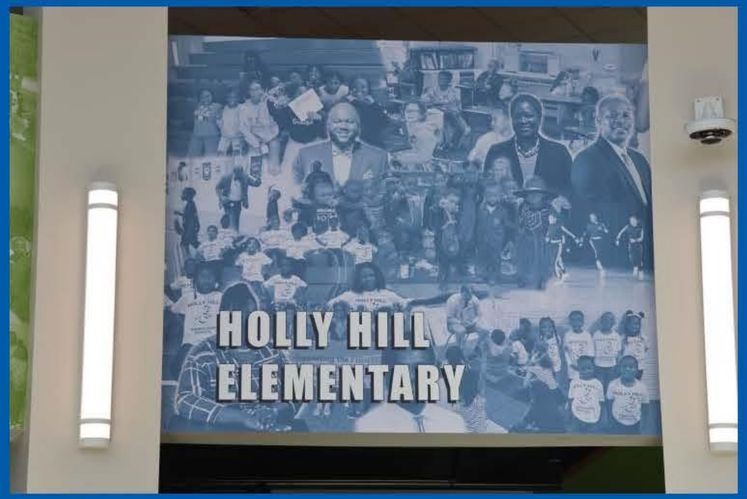

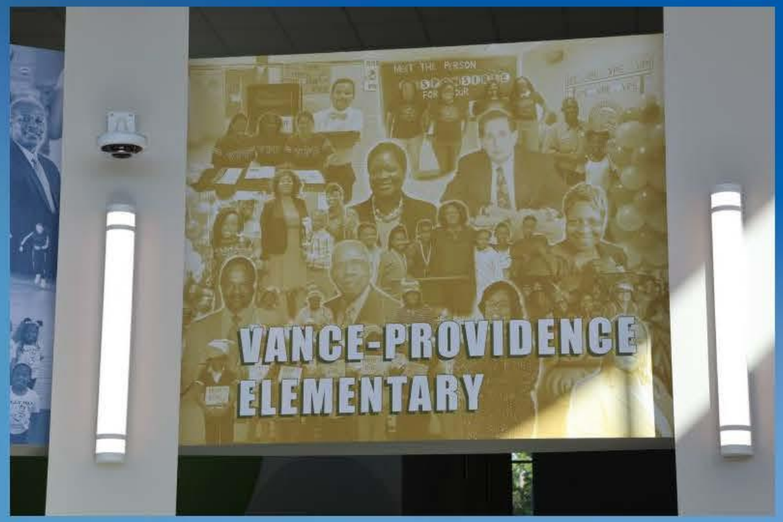

ORANGEBURG-WILKINSON HIGH SCHOOL

SAFETY	
Incidents to Date	1
First Aids to Date	0

WEATHER	
Working Days	323
Weather Days	49
Activities Delayed	2

MANPOWER	
Number of Trades	12
Average Workers *(per day)*	167

SCHEDULE MILESTONES	
Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continued.
- Roofing in area C and F2 was installed.
- Brick in areas D, and F1 continued.
- The press box retaining wall continued.
- Exterior insulation continues around the gym, media center and field house.
- Windows at the BB/SB building were installed. Brick is complete.
- Storm drain lines in the courtyard between D and B was begun.
- Steel in area A2 continued, with erection beginning in the auditorium.
- Parapet framing at the field house began.
- Gas lines to the site began.

Upcoming Activities

- Exterior insulation will begin around the academic wings.
- DOT work at 601 will begin.







ORANGEBURG-WILKINSON HIGH SCHOOL

SAFETY	
Incidents to Date	1
First Aids to Date	0
WEATHER	
Working Days	328
Weather Days	49
Activities Delayed	2
MANPOWER	
Number of Trades	14
Average Workers *(per day)*	186
SCHEDULE MILESTONES	
Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continued.
- Roofing at area A1 began.
- Brick in areas D, and F1 continued.
- The press box retaining wall continued.
- Exterior insulation continues around the gym, media center and field house.
- Windows in the cafeteria were installed.
- Storm drain lines in the courtyards continued.
- Steel in area A2 and the auditorium continued.
- Parapet framing at the field house continued. .
- DPU began preparations for power lines.

Upcoming Activities

- Exterior insulation will begin around the academic wings.
- DOT work at 601 will begin.







ORANGEBURG-WILKINSON HIGH SCHOOL

SAFETY	
Incidents to Date	1
First Aids to Date	0
WEATHER	
Working Days	313
Weather Days	46
Activities Delayed	2
MANPOWER	
Number of Trades	11
Average Workers *(per day)*	151
SCHEDULE MILESTONES	
Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continued.
- Roofing at the gym began.
- CMU nears completion in classroom wings A1 & A2.
- The press box retaining wall has begun.
- Exterior insulation continued at F1 & was completed at the BB/SB building.
- Brick continued in area E2 & D.
- Paving continued at the football parking lot.
- Roof joists in A1 began.

Upcoming Activities

- Press box retaining wall will begin.
- Brick at the gym will begin.
- Brick at the SB/BB will begin







ROBERT E. HOWARD ELEMENTARY SCHOOL

SAFETY	
Incidents to Date	0
First Aids to Date	0
WEATHER	
Working Days	79
Weather Days	4
Activities Delayed	0
MANPOWER	
Number of Trades	4
Average Workers *(per day)*	20
SCHEDULE MILESTONES	
Job Start	5/27/2025
Contract Completion	12/14/2026

Top Activities This Week

- Continued demolition and slab removal in area 2 and hauling off debris
- Continued prepping for in wall and underground.
- Continued storm water system installation along Chesnut Rd.
- Building pad preparation in progress
- Aggregate piers installation at rotunda area
- Continued excavation of the pond and backfilling for the parking lot and road

Upcoming Activities

- Demolition of area 3
- Storm Drainage continuing
- Concrete mobilizing 9/2/25
- Temporary power







ROBERT E. HOWARD ELEMENTARY SCHOOL

SAFETY	
Incidents to Date	0
First Aids to Date	0
WEATHER	
Working Days	73
Weather Days	4
Activities Delayed	0
MANPOWER	
Number of Trades	4
Average Workers *(per day)*	20
SCHEDULE MILESTONES	
Job Start	5/27/2025
Contract Completion	12/14/2026

Top Activities This Week

- Demolition of area 3 at the far end and hauling off debris in progress
- Graded building A pad for proof roll
- Continued storm water system installation along Chesnut Rd.
- Building pad preparation in progress
- Aggregate piers installation at rotunda area

Upcoming Activities

- Demolition of area 3
- Storm Drainage continuing
- Concrete mobilizing 9/2/25
- Temporary power





