
ORANGEBURG COUNTY SCHOOL DISTRICT

BOARD MEETING



ORANGEBURG
COUNTY SCHOOL DISTRICT
We Are **One**

OPERATIONS UPDATE

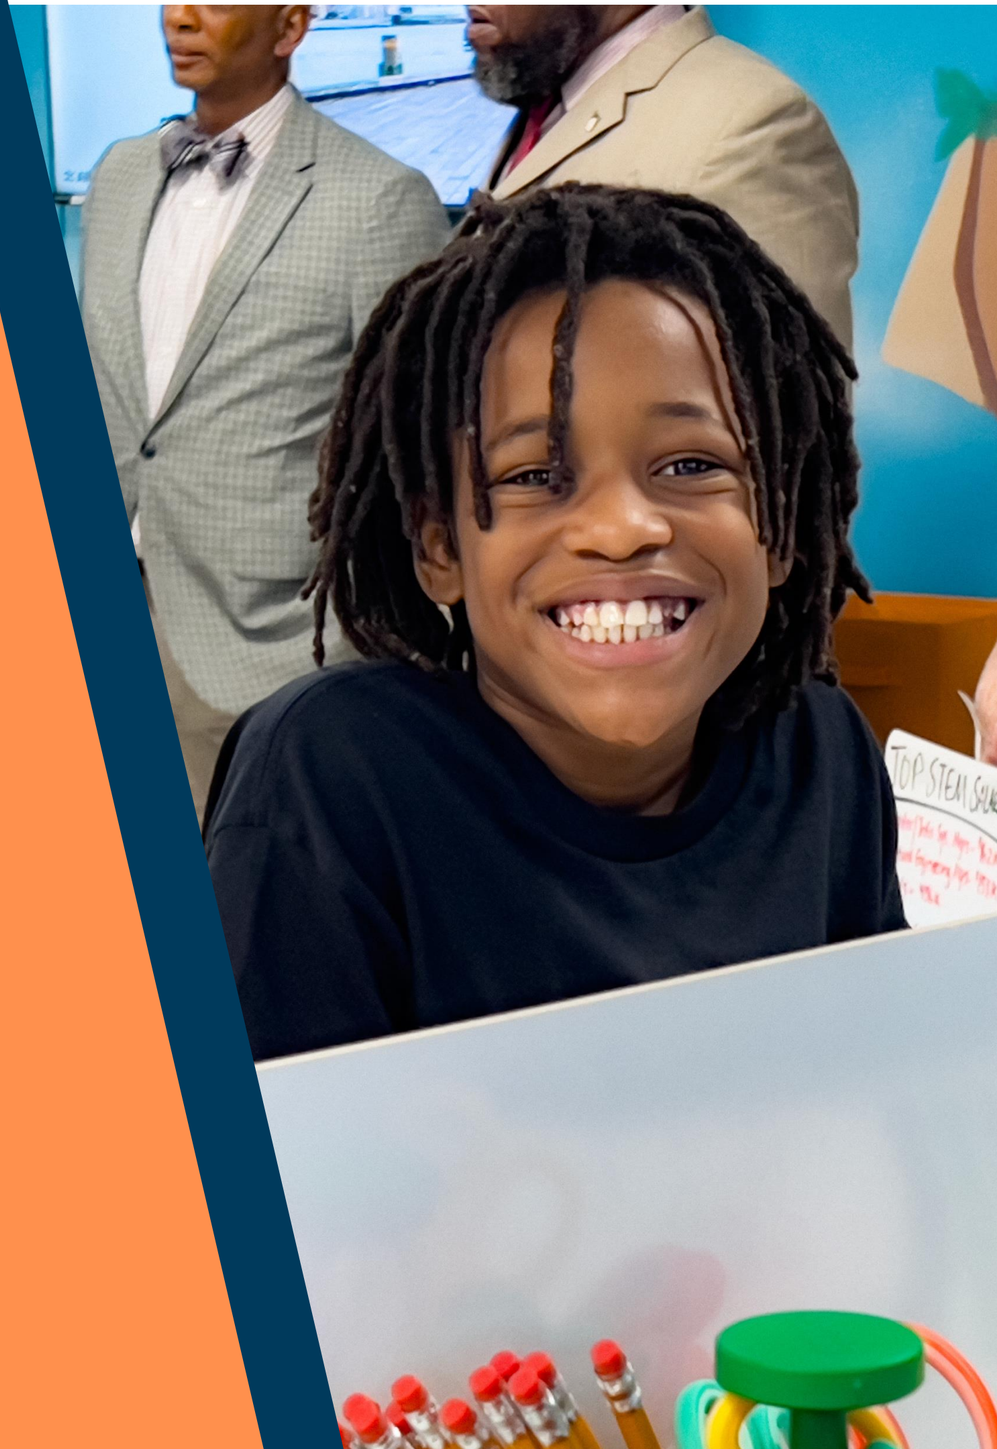

ORANGEBURG-WILKINSON HIGH SCHOOL

ORANGEBURG WILKINSON HIGH SCHOOL

SAFETY

Incidents to Date	1
First Aids to Date	0

WEATHER

Working Days	347
Weather Days	49
Activities Delaved	2

MANPOWER

Number of Trades	11
Average Workers *(per day)*	163

SCHEDULE MILESTONES

Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continued.
- MEP OH rough-in at the field house continues.
- Brick continued in areas B, A1 & A2.
- The press box retaining wall continues.
- Exterior insulation continued in area A1.
- BB.SB backstop walls were poured.
- Steel in area A2 and the auditorium continued.
- DPU continued with gas lines and power poles.
- Windows are being installed in area B and F1.
- Painting continued in area A1 and A2.

Upcoming Activities

- DOT work at Belleville will begin.
- Metal wall panels will begin.
- Installation of the kitchen walk in will start.







Week of **September 22, 2025**

ORANGEBURG-WILKINSON HIGH SCHOOL

ORANGEBURG WILKINSON HIGH SCHOOL

SAFETY	
Incidents to Date	1
First Aids to Date	0
WEATHER	
Working Days	352
Weather Days	49
Activities Delayed	2
MANPOWER	
Number of Trades	11
Average Workers *(per day)*	167
SCHEDULE MILESTONES	
Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continued.
- Plumbing rough-in at the field house is complete.
- Brick continued in areas A1 & A2.
- The press box retaining wall continues.
- Exterior insulation continued in area A1.
- Steel in area A2 and the auditorium is nearly complete.
- DPU continued with gas lines and power poles.
- Windows are being installed in area B 2nd floor.
- Painting continued in area A1 and A2.
- Wall framing in the admin. area began.
- Drywall topping out continues.

Upcoming Activities

- DOT work at Belleville will begin.
- Metal wall panels will begin.
- Ceiling grid will begin.







Week of **September 29, 2025**

ROBERT E. HOWARD ELEMENTARY SCHOOL

ROBERT E. HOWARD ELEMENTARY SCHOOL

SAFETY	
Incidents to Date	0
First Aids to Date	0
WEATHER	
Working Days	100
Weather Days	5
Activities Delayed	0
MANPOWER	
Number of Trades	5
Average Workers *(per day)*	45
SCHEDULE MILESTONES	
Job Start	5/27/2025
Contract Completion	12/14/2026

Top Activities This Week

- Completed demolition and hauling off debris of remaining structures
- Continued digging and installing rebar for footings
- Masonry began stem wall CMU install on building C
- Continued installation of sewer pipe and underground structures
- Continued demo of existing parking lot and loop
- Cutting in the road around Building C
- Continued cleaning out the detention pond and installing the dams
- Continued underground electrical on the main & emergency electrical rooms.
- Continued raceway to Building B & A and started the duct bank for the transformer

Upcoming Activities

- Continue concrete footings in Building C and move east towards Building B
- Continue stem wall install







Week of **September 26th, 2025**

ROBERT E. HOWARD ELEMENTARY SCHOOL

ROBERT E. HOWARD ELEMENTARY SCHOOL

SAFETY	
Incidents to Date	0
First Aids to Date	0
WEATHER	
Working Days	105
Weather Days	5
Activities Delayed	0
MANPOWER	
Number of Trades	5
Average Workers *(per day)*	50
SCHEDULE MILESTONES	
Job Start	5/27/2025
Contract Completion	12/14/2026

Top Activities This Week

- Continued storm water system
- Continued site grading and pond work
- Continued stem wall CMU in Building C
- Continued underground electrical
- Installed underground waste water line
- Continued onsite road work and bus loop
- Continued Building B footings and rebar installation

Upcoming Activities

- Continue footings, rebar install and CMU stem wall in Building B
- Continue preparing onsite road work and bus loop cut in
- Concrete slab pour in Building C







Week of **September 29th, 2025**
