MAJOR CONSTRUCTION PROJECTS UPDATE

OCTOBER 17, 2025

ASCENSION PUBLIC SCHOOLS

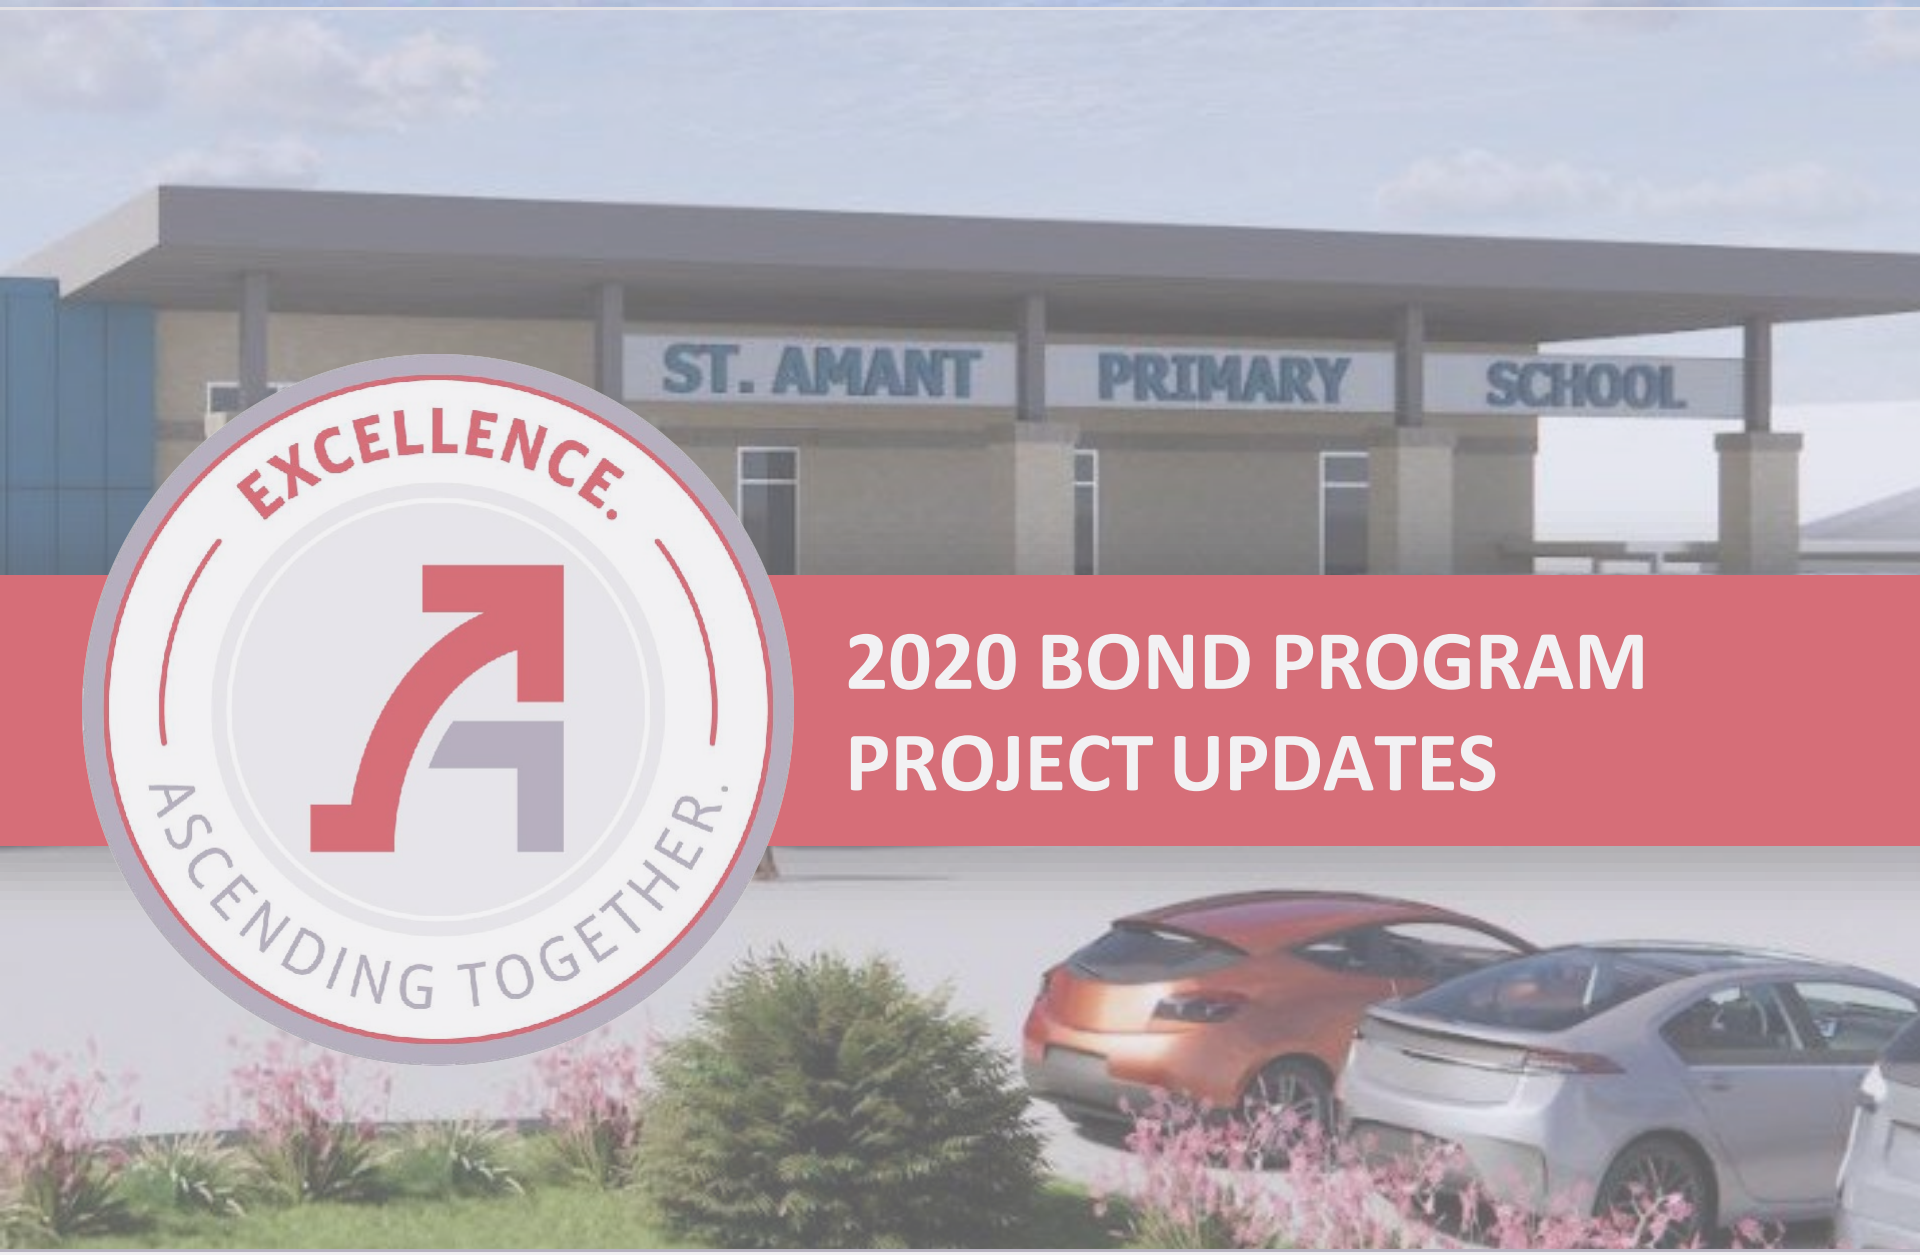

EXCELLENCE.
ASCENDING TOGETHER.

2020 BOND PROGRAM PROJECT UPDATES

OCTOBER 17, 2025

ASCENSION PUBLIC SCHOOLS

ST. AMANT PRIMARY RENOVATIONS & ADDITIONS

CONCEPTUAL RENDERING

CONCEPTUAL RENDERING

SCHOOL

St. Amant Primary School

TOTAL INSTALLED COSTS

$10,164,000

PROJECT DETAILS

New Construction / Renovations

PROFESSIONAL OF RECORD

Gossen-Holloway-Cortez, APAC

GENERAL CONTRACTOR

Stuart & Co General Contractors

ANTICIPATED COMPLETION

Phase III – Fall 2026

PROJECT STATUS

- Phase III – Early Package is complete.
- Contractor has begun to mobilize onsite for Phase III, which includes construction of new building.

**Total Installed Costs also include SAMS Renovations*

DUTCHTOWN HIGH SCHOOL REAR ACCESS

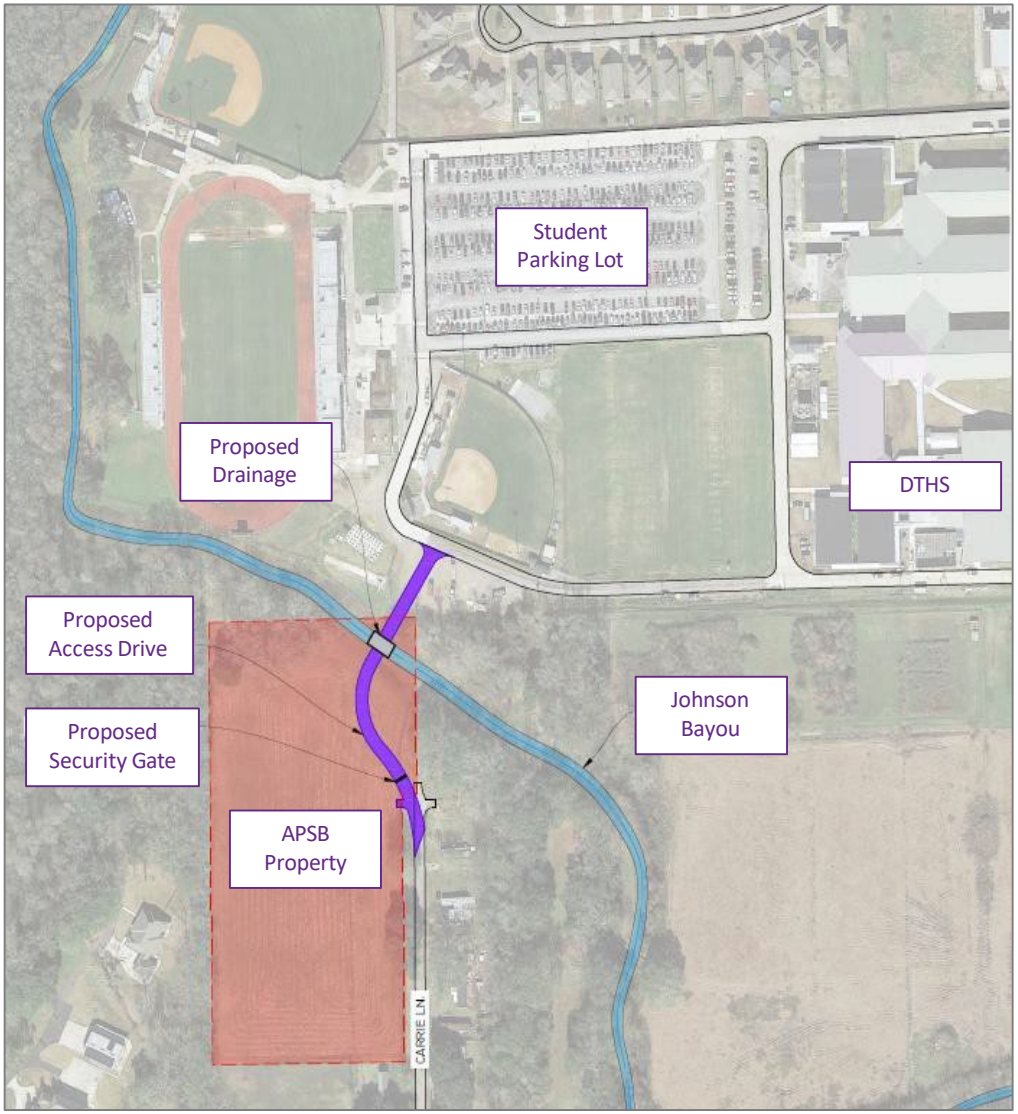

SCHOOL
Dutchtown High School

TOTAL INSTALLED COSTS
$1,500,000

PROJECT DETAILS
Road Improvements to Carrie Lane

PROFESSIONAL OF RECORD
McKim & Creed Inc.

GENERAL CONTRACTOR
M & J Civil Construction, LLC

ANTICIPATED COMPLETION
Spring 2026

PROJECT STATUS

- Project in partnership with Move Ascension.
- Preconstruction Meeting held on 10-02-25.
- Contractor has mobilized onsite and clearing/grubbing to begin shortly.

PRAIRIEVILLE HIGH SCHOOL ROAD IMPROVEMENTS

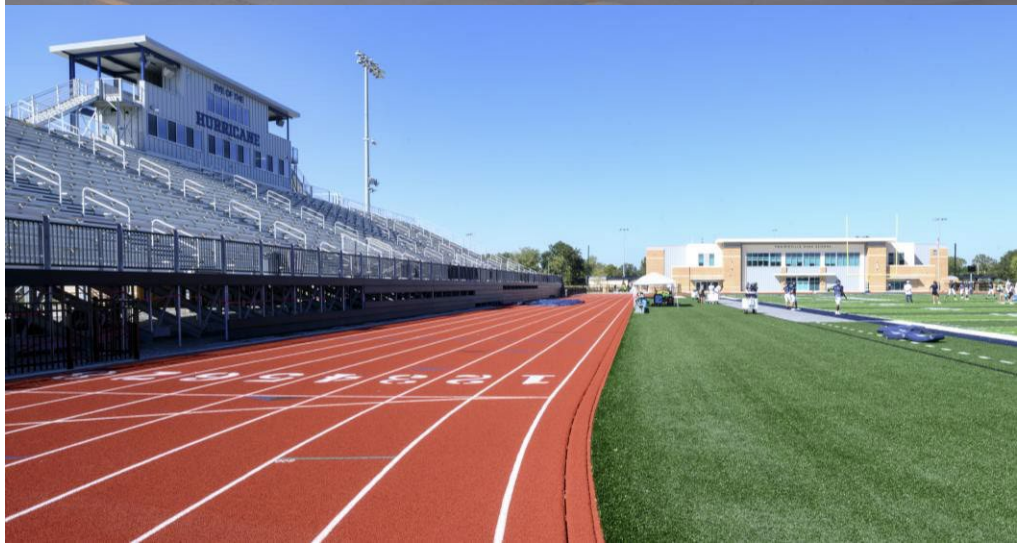

SCHOOL

Prairieville High School

TOTAL INSTALLED COSTS

n/a

PROJECT DETAILS

Road Improvements to Parker/929

PROFESSIONAL OF RECORD

McKim & Creed Inc.

GENERAL CONTRACTOR

TBD

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Project in partnership with Move Ascension.
- Working with Project Team on status of utility relocation, acquisitions, budget and schedule.

2024 BOND PROGRAM PROJECT UPDATES

OCTOBER 17, 2025

ASCENSION PUBLIC SCHOOLS

LAKE ELEMENTARY RENOVATION AND ADDITIONS

CONCEPTUAL RENDERING

CONCEPTUAL RENDERING

SCHOOL

Lake Elementary School

TOTAL INSTALLED COSTS

$50,000,000

PROJECT DETAILS

New Construction / Renovations

PROFESSIONAL OF RECORD

Grace Design Studio

GENERAL CONTRACTOR

TBD

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Coordinating Wetland Mitigation proposal with Wetlands Vendor.
- Design Notice to Proceed (NTP) scheduled for upcoming weeks.
- Advertainments for CMAR Contractor to begin early next year.

DUTCHTOWN HIGH RENOVATIONS AND ADDITIONS

CONCEPTUAL RENDERING

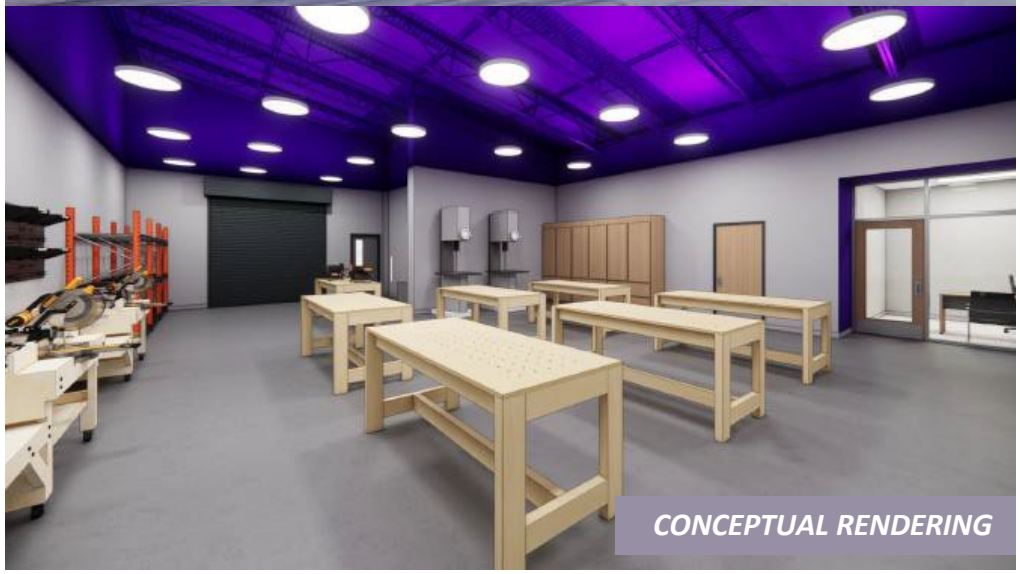

CONCEPTUAL RENDERING

SCHOOL

Dutchtown High School

TOTAL INSTALLED COSTS

$17,000,000

PROJECT DETAILS

New Construction / Renovations

PROFESSIONAL OF RECORD

Domain Architecture

GENERAL CONTRACTOR

Stuart & Co General Contractors

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Design: 60% Complete
- Design Team finalizing Design Development Submittal.
- Once finalized, Preconstruction Manager will provide pricing based on Design Development.

GONZALES MIDDLE RENOVATIONS AND UPGRADES

CONCEPTUAL RENDERING

SCHOOL

Gonzales Middle School

TOTAL INSTALLED COSTS

$13,000,000

PROJECT DETAILS

New Construction / Renovations

PROFESSIONAL OF RECORD

Gossen-Holloway-Cortez, APAC

GENERAL CONTRACTOR

Woodward Design+Build

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Design: 45% Complete
- Design Team working on Design Development Submittal.
- Once finalized, Preconstruction Manager will provide pricing based on Design Development.

MIDDLE SCHOOL GYMNASIUMS AT CENTRAL MIDDLE AND ST. AMANT MIDDLE

CONCEPTUAL RENDERING

CONCEPTUAL RENDERING

SCHOOL

Central Middle / St. Amant Middle

TOTAL INSTALLED COSTS

$10,000,000

PROJECT DETAILS

New Construction

PROFESSIONAL OF RECORD

Mougeot Architecture, LLC

GENERAL CONTRACTOR

TBD

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Design: 80% Complete
- Design Team working on Construction Documents.
- First advertisement for construction scheduled for early Spring 2026.

LEBLANC SPECIAL EDUCATION CENTER REMODEL

SITE

Leblanc Special Education Center

TOTAL INSTALLED COSTS

$6,000,000

PROJECT DETAILS

Demo / Renovations / HVAC Upgrades

PROFESSIONAL OF RECORD

RHH Architects, APAC

GENERAL CONTRACTOR

Cangelosi Ward Contractors

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Design: 30% Complete
- Initial pricing received by CMAR Contractor based on Schematic Design.

EAST ASCENSION HIGH GYMNASIUM RENOVATION

CONCEPTUAL RENDERING

SCHOOL

East Ascension High School

TOTAL INSTALLED COSTS

$3,000,000

PROJECT DETAILS

Demo / Renovations

PROFESSIONAL OF RECORD

Fusion Architects, APC

GENERAL CONTRACTOR

TBD

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Design Team working on Construction Documents.
- Abatement/Demolition portion anticipated to be completed by end of year.
- First advertisement for construction scheduled for early Spring 2026.

ROOFING REPLACEMENTS AT LOWERY ELEMENTARY AND ST. AMANT HIGH

SCHOOL

Lowery Elementary / St. Amant High

TOTAL INSTALLED COSTS

$3,000,000

PROJECT DETAILS

Roof Replacements

PROFESSIONAL OF RECORD

Gasaway Gasaway Bankston

GENERAL CONTRACTOR

TBD

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Design: 100% Complete
- Project includes roofing replacements to Main Building, Math and Science Buildings, Ag Building and Band Building.
- First advertisement scheduled for mid-October 2025 and anticipated bid opening scheduled for November 2025.

GALVEZ PRIMARY SCHOOL RENOVATIONS

SCHOOL

Galvez Primary School

TOTAL INSTALLED COSTS

$2,500,000

PROJECT DETAILS

Canopy and Drainage Upgrades

PROFESSIONAL OF RECORD

Kern Architects

GENERAL CONTRACTOR

TBD

ANTICIPATED COMPLETION

Fall 2026

PROJECT STATUS

- Design: 100% Complete
- First advertisement for construction scheduled for mid-October 2025.
- Anticipated bid opening scheduled for November 2025.

GONZALES PRIMARY SCHOOL & DONALDSONVILLE HIGH SCHOOL KITCHEN/SERVING LINE UPGRADES

SCHOOL

Gonzales Primary / DHS

TOTAL INSTALLED COSTS

$1,500,000

PROJECT DETAILS

Demo / Renovations

PROFESSIONAL OF RECORD

Tipton Associates APAC

GENERAL CONTRACTOR

TBD

ANTICIPATED COMPLETION

Fall 2026

PROJECT STATUS

- Design: 60% Complete
- Design Team has submitted Design Development drawings for Owner review.
- First advertisement for construction scheduled for Spring 2026.

SCHOOL BOARD FUNDED PROJECTS UPDATE

OCTOBER 17, 2025

ASCENSION PUBLIC SCHOOLS

ITTC RENOVATIONS

SITE

Central Middle School

TOTAL INSTALLED COSTS

$600,000

PROJECT DETAILS

Demo / Renovations

PROFESSIONAL OF RECORD

Meyer Engineers, Ltd

GENERAL CONTRACTOR

TASK Industries, L.L.C.

ANTICIPATED SUBSTANTIAL COMPLETION

October 31, 2025

PROJECT STATUS

- Construction: 90%
- Construction nearing completion.
- Furniture and AV installation is ongoing.

ROOFING PROGRAM

SCHOOL
St. Amant High School

TOTAL INSTALLED COSTS
$3,000,000

PROJECT DETAILS
Roof/Building Envelope Upgrades

PROFESSIONAL OF RECORD
Gasaway Gasaway Bankston

GENERAL CONTRACTOR
TBD

ANTICIPATED COMPLETION
TBD

PROJECT STATUS
Project to include coating of Gold Dome and upgrades to roof/building envelope.

DONALDSONVILLE HIGH SCHOOL FIELDHOUSE RENOVATIONS AND ADDITIONS

CONCEPTUAL RENDERING

CONCEPTUAL RENDERING

SCHOOL

Donaldsonville High School

TOTAL INSTALLED COSTS

$6,200,000

PROJECT DETAILS

New Construction / Renovations

PROFESSIONAL OF RECORD

Domain Architecture

GENERAL CONTRACTOR

TBD

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Design: 25% Complete
- Pre-Qualification Meeting for CMAR Contractor held on 09-26-25.
- CMAR Contractor responses received on 10-13-25.
- CMAR Selection to follow shortly after responses received.

NEW SCHOOL BOARD OFFICE

CONCEPTUAL RENDERING

CONCEPTUAL RENDERING

SITE

School Board Office

TOTAL INSTALLED COSTS

$5,700,000

PROJECT DETAILS

New Construction

PROFESSIONAL OF RECORD

Mougeot Architecture, LLC

GENERAL CONTRACTOR

TBD

ANTICIPATED COMPLETION

TBD

PROJECT STATUS

- Design: 15% Complete
- Pre-Qualification Meeting for CMAR Contractor held on 09-26-25.
- CMAR Contractor responses received on 10-13-25.
- CMAR selection to follow shortly after responses received.
