Capital Projects Update
November 2025







White Plains Public Schools
WP
REAL LIFE LEARNING

Presenter – Triton Construction Company

Chris Pearson
Senior Vice President

Presenter – H2M architects + engineers

Joseph C. Ciserano, AIA, NCARB
Senior Associate | Studio Director

Joseph M. Mottola
Executive VP | Chief Operating Officer

Capital Projects Update

HVAC and Filtration Upgrades

- White Plains High School
- Highland Middle School
- Eastview Middle School
- Church Street Elementary School
- George Washington Elementary School

Complete

- Ridgeway Elementary School
- Mamaroneck Elementary School

Construction Projects

(Underway)

- High School Innovation Wing
- Rochambeau Alterations & HVAC
- Four elementary schools (George Washington, Church Street, Ridgeway & Mamaroneck) – All (4) In Closeout

SED Approved / Bidding

- Ed. House Electric Service Upgrade
- Mamaroneck Restroom Renovations

In Design / Future Work

- HS Phase-II Interior Alterations and accessibility improvements
- Additional A/C Projects
- Serving Lines at the High School

HVAC & Filtration Upgrades

Ridgeway

- Completed. Project is in construction close-out phase with contractors.

MAS

- Transformer was delivered. New electric service connected to transformer and building.
- Upgrade to street service line in progress
- Con-Ed in progress with off-site electrical work to bring new power to site.

Construction Projects

High School Innovation Wing

- Construction underway
- Foundations Complete, Steel Erection in progress, Site Utility Improvements continuing

Rochambeau HS Renovations

- Phasing has been developed to allow for normal operation throughout school year
- Phase I work nearing completion and occupancy
- Phase II work to commence once Phase I is occupied
- Items that will be completed at later date(s):
  - Air Conditioning Condensers
  - Window Replacement
  - Casework
  - New Electric Service

H2M architects + engineers
practical approach. creative results.

TRITON CONSTRUCTION

Innovation Wing Progress

White Plains Public Schools WP REAL LIFE LEARNING









H 2 M architects + engineers
practical approach. creative results.


TRITON CONSTRUCTION

Rochambeau Progress

White Plains Public Schools WP REAL LIFE LEARNING





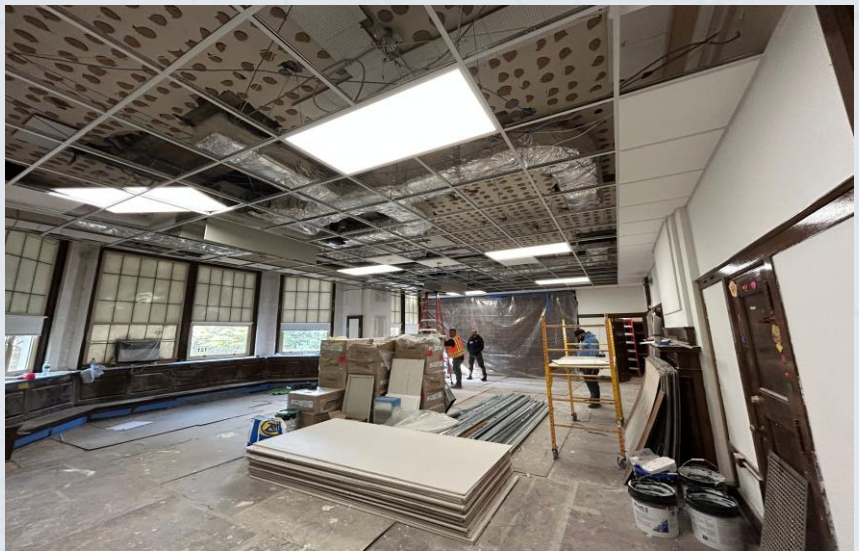



Construction Projects


Church Street ES

George Washington ES

Mamaroneck Avenue ES

Ridgeway ES

- Projects are substantially complete and are in the close-out phase with all (9) prime contractors

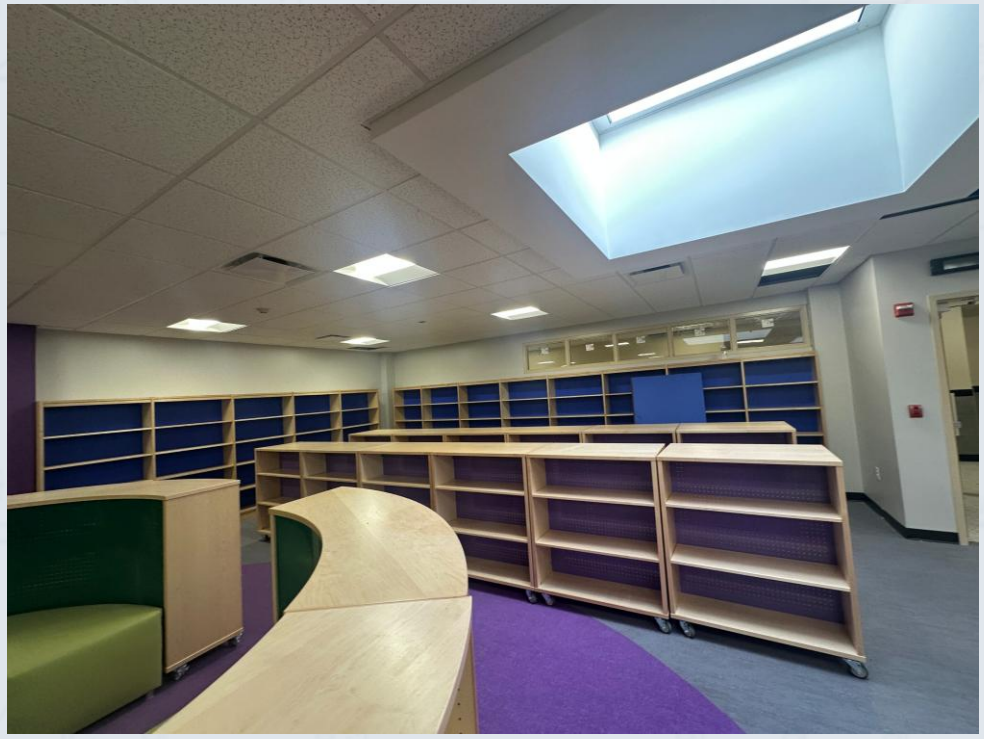



H2M architects + engineers
practical approach. creative results.

TRITON CONSTRUCTION

Elementary School Projects

White Plains Public Schools WP REAL LIFE LEARNING







SED Approval/Bidding

Education House Electric Service & MAS Bathroom Renovations:

- SED approvals received/complete on both projects
- Bid schedule to be determined for both project in coming weeks
- Targeting Summer 2026 Construction

In Design / Future Work

HS Phase-II Interior Alts – In Design

- Accessibility and Security Improvements, Corridor Widening @ 90%. Construction documents to be finalized and submitted to SED for technical review by end of November 2025.

Additional A/C - Future

- Due to savings on the current HVAC projects (all full-size classrooms), additional spaces will be air conditioned; including all Gymnasiums, Resources Rooms and Offices that were not covered under the original classroom scope.

Serving Lines at High School - Future

- Due to savings on the current capital projects, the Team is pursuing the design of new serving lines for both of the High School serveries.

Thank you! Any questions?

