Waller Independent School District

BOND CONSTRUCTION UPDATE

January 2026


#ThankYouVoters

WALLER ISD BOND 22

2022-$363M BOND SUMMARY

- Lowe Elementary (#6) $48 million - COMPLETE 2024
- McReavy Elementary (#7) $49.1 million - COMPLETE 2024
- Cure Elementary (#8) $55.4 million- Open 2025
- Smith Andrews Ag Science Complex: $13.2 million - Open 2025
- Education Service Center and Transportation Center: $62.7 million - Open 2025
- Priority 1 District Facility and HVAC Upgrades: $75.1 million
  In progress and punch list corrections started.
- Land, Buses, Technology, Safety & Security, Bond Management: $60 Million
  Ongoing

CURE ELEMENTARY

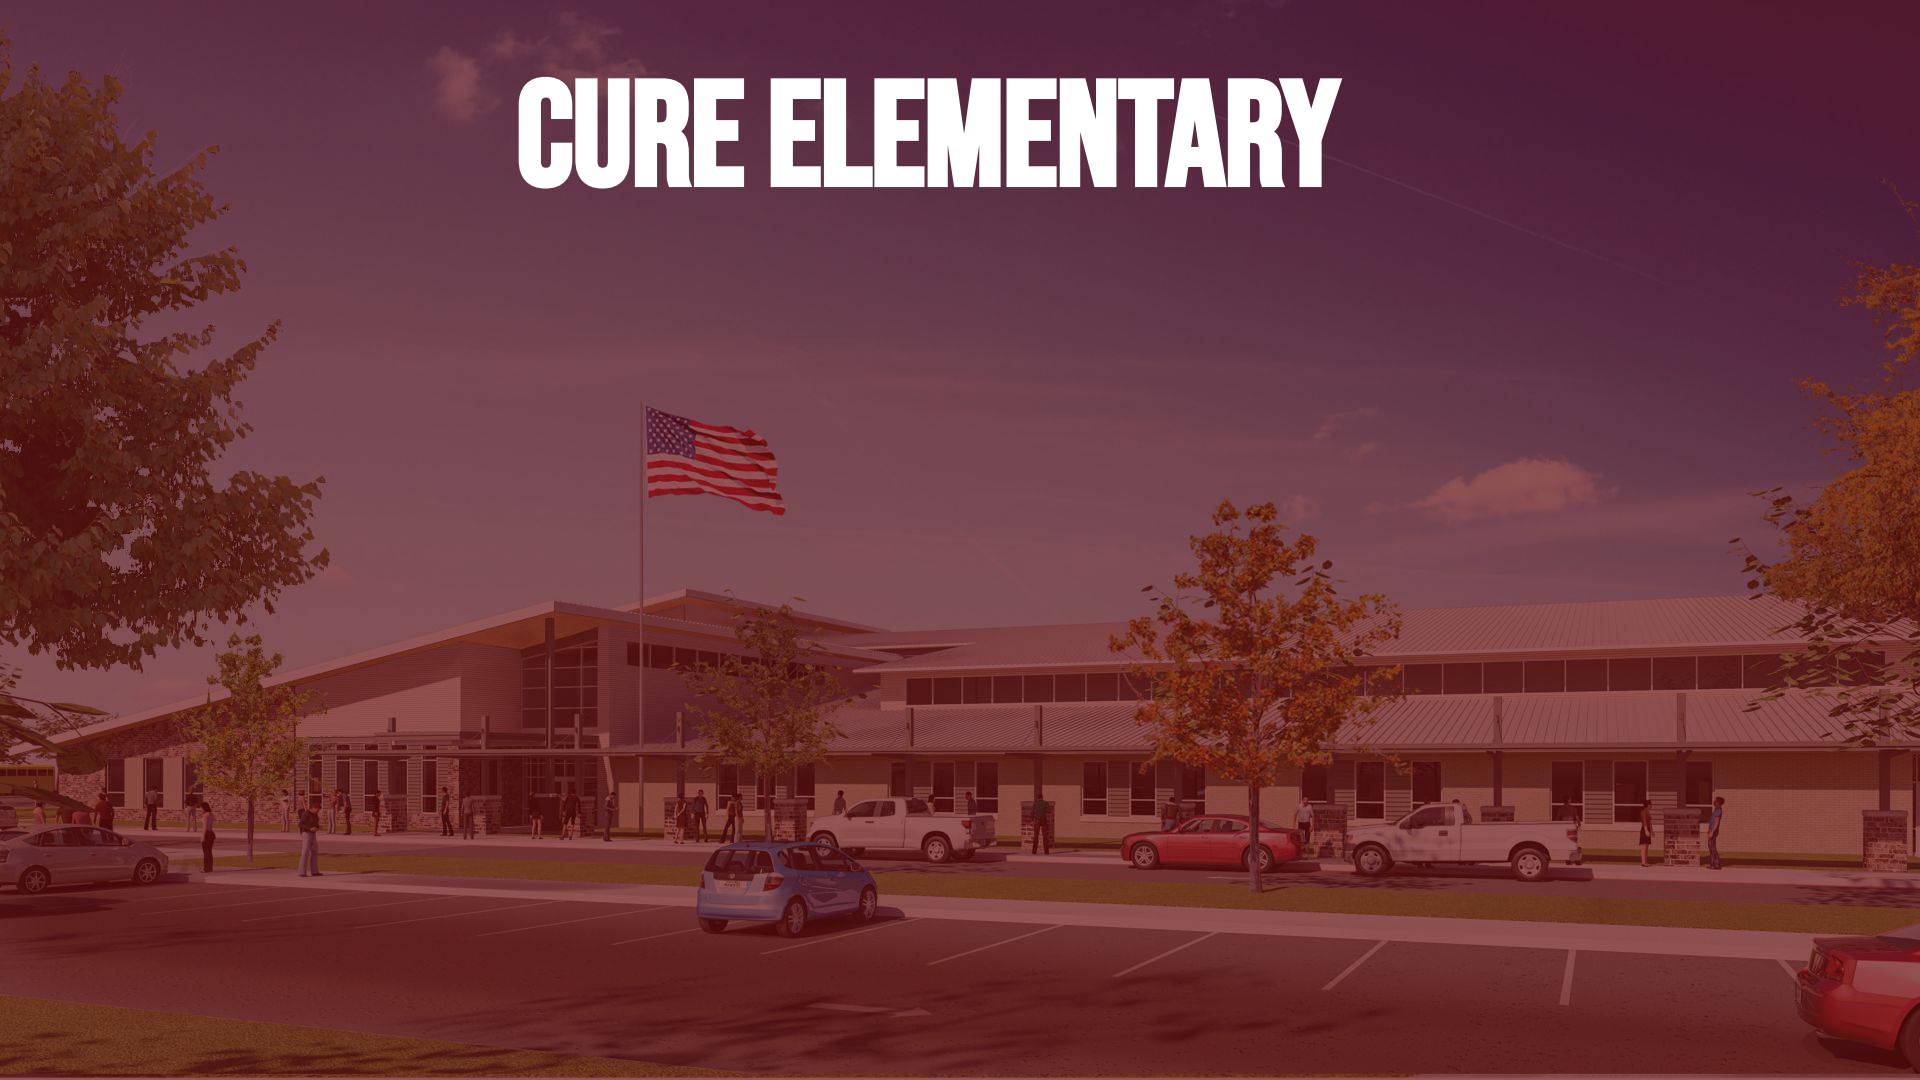

CURE ELEMENTARY (#8)

- Campus is open and 1-year warranty period is ongoing.
- 11-month warranty walk is scheduled for May 2026.
- Testing and Balancing and the Commissioning are nearing completion.

WALLER ISD BOND 22

Cure Elementary



Front Elevation

WALLER ISD CONSTRUCTION

EDUCATION SERVICE CENTER



EDUCATION SERVICE CENTER

- Building is open and the 1-year warranty period is ongoing.
- Architectural punch list is nearly complete.
- 11-month warranty walk is scheduled for June 2026.
- Testing and Balancing and the Commissioning are nearing completion.

WALLER ISD BOND 22

EDUCATION SERVICE CENTER



Front Elevation

WALLER ISD CONSTRUCTION

2022 BOND - PRIORITY 1 PROJECTS



WALLER ISD BOND 22

Priority 1 Improvement

District Wide Improvements

- Fire Alarm Upgrades
  - FSE, TES, RRE are ongoing.
- Intrusion/Access Control Upgrades in progress at all campuses.
- Graphics design packages have been approved and installation has started.
- LED lighting upgrades are approx 85% complete throughout.
- Stage curtains at all elementaries and SJH have been installed.
- Punch list items have begun - identifying and corrections are ongoing.

WALLER ISD BOND 22

Priority 1 Improvement

Roberts Road ES

- New flooring throughout the campus installed.
- P-lam panels at library & cafeteria are 90% complete.
- Doors & hardware scheduled in January.
- Graphic installation has begun.

Turlington ES

- Front waiting area is 95% complete.
- Doors & hardware scheduled in January.
- Library portal is 95% complete.
- Paint and vinyl walls are complete.
- Library HVLV fans are installed.

Fields Store ES

- HVAC is complete, clean up and punch list ongoing.
- LVT & epoxy flooring is 90% complete.
- Canopies are complete.
- P-lam panels have been reordered after installation of coiling door.
- Doors & hardware scheduled in January.
- Room signage is complete.
- New light poles are installed.

WALLER ISD BOND 22

Priority 1 Improvement

Schultz JH

- HVAC is complete with clean up and punch ongoing.
- Auditorium sound system has been installed.
- Auditorium house lighting has been installed.
- Parking lot light poles have been installed.

Holleman ES

- Additional LED lighting installed.
- Doors & hardware scheduled in January.
- Room signage has been installed.
- Graphics painting has begun.

Waller JH Stadium

- Epoxy & weight room flooring complete.
- Grandstands complete.
- Restroom building complete.
- Track Synthetic surface installed and striping scheduled in January.
- Parking lot resurfacing and pipe fencing is scheduled for completion in December.

Jones ES

- Glass frosting is complete.
- Sliding marker boards are complete.

WALLER ISD BOND 22

Priority 1 Improvement



Roberts Road Elem Cafeteria Graphic

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvement



Roberts Road Elem Gym Graphic

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvement



Field Store Elem Site Lighting

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvement







Turlington Elem Lighting & HVLV Fans

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvement

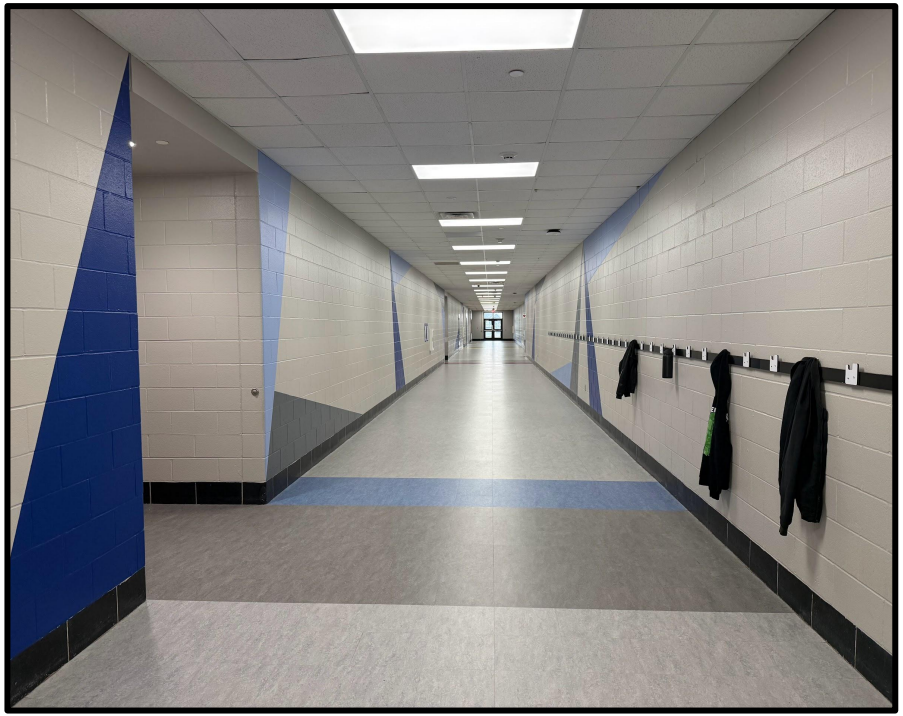

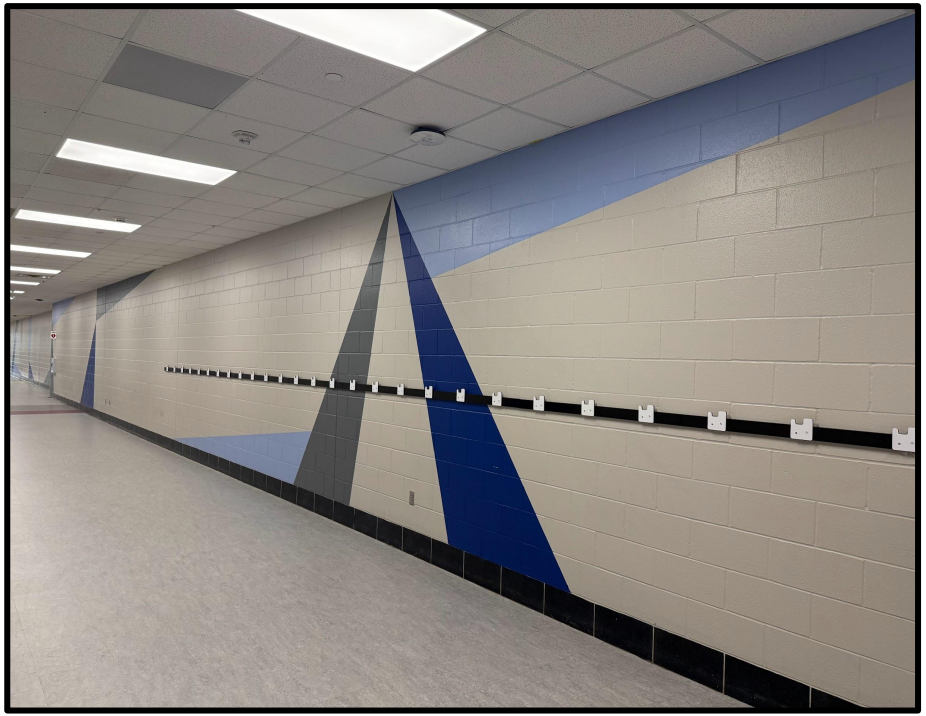

HES Fine Arts Hallway Painting

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvement



Fields Store Entry Corridor

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvement





HES Main Corridor & Library Painting

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvement





WJH Track Surface and Fencing

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvement





WJH Parking Resurfacing and Striping

WALLER ISD CONSTRUCTION


2024 - $702 M BOND

WALLER ISD BOND 22

WARREN RANCH HIGH SCHOOL

- Site clearing and dirt work commenced November 14, 2025.
- Main Building pad is 80% complete.
- Groundbreaking ceremony is planned.
- Underground storm and sanitary lines are in progress.
- Drilled piers have started.
- Grade Beams and slab are scheduled to start in February.
- Structural Steel deliveries scheduled to start in May.
- Opening scheduled in Summer 2028.

WALLER ISD BOND 22

Warren Ranch HS



Site Overview

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Warren Ranch HS





Drilled piers

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Warren Ranch HS





Storm and Sanitary piping

WALLER ISD CONSTRUCTION

ELEMENTARY #9

- GMP contract Amendment approved in December.
- Construction starting in January.
- Groundbreaking ceremony is being planned.
- Opening scheduled in August 2027.

WALLER ISD BOND 24

ELEMENTARY #9



WALLER ISD CONSTRUCTION


#ThankYouVoters
Waller
Independent School District
