ORANGEBURG COUNTY SCHOOL DISTRICT


BOARD MEETING



ORANGEBURG
COUNTY SCHOOL DISTRICT
We Are **One**

OPERATIONS UPDATE

FEBRUARY 10, 2026

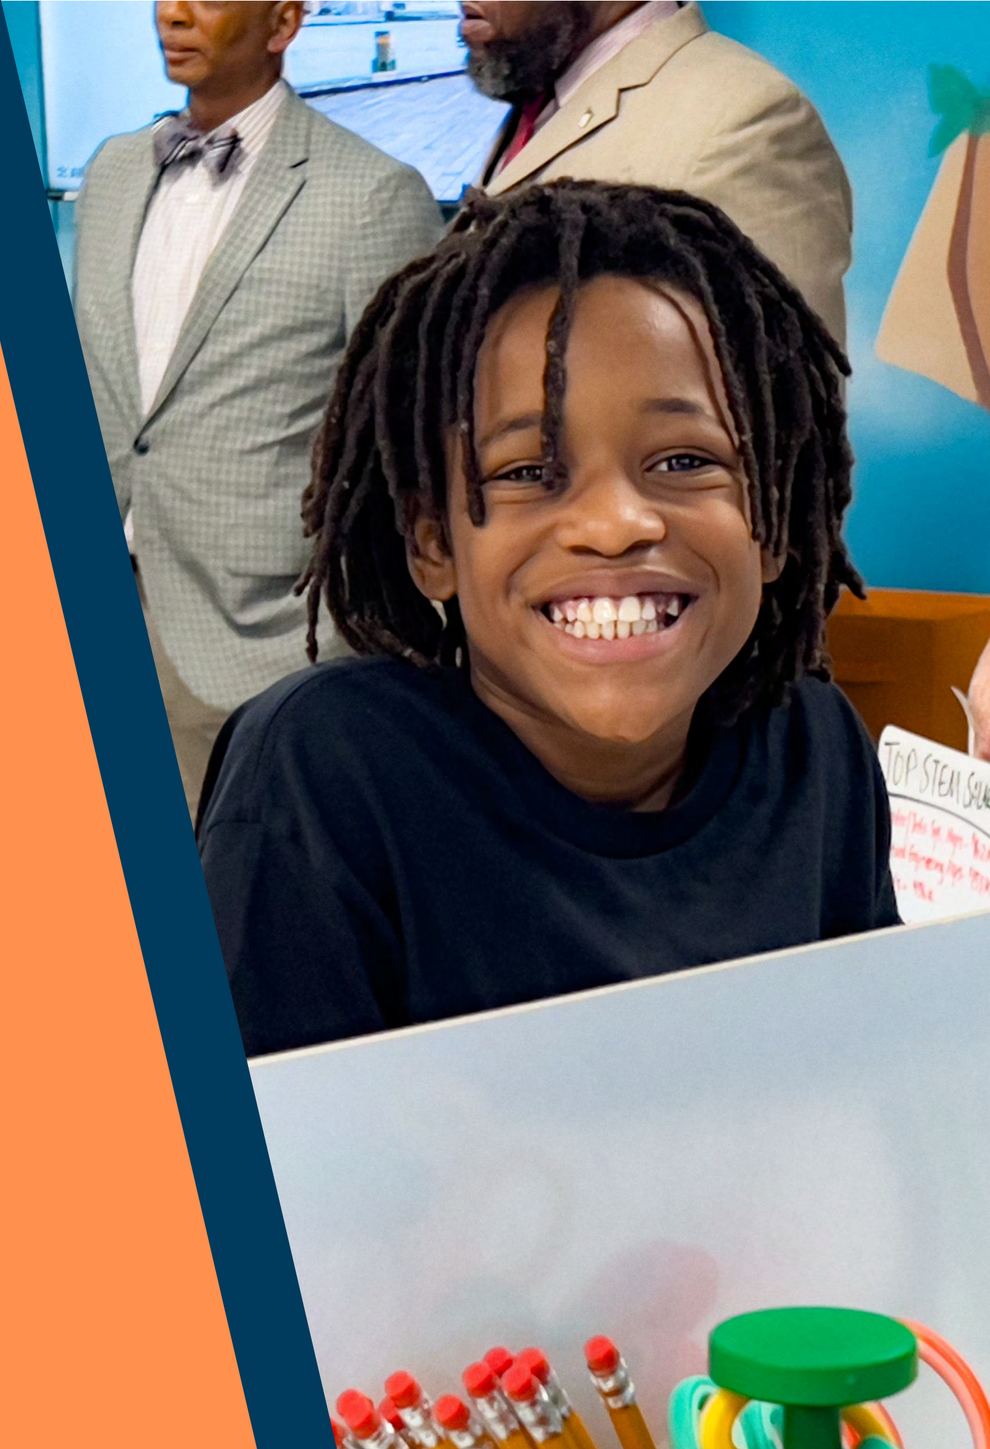

ORANGEBURG-WILKINSON HIGH SCHOOL

ORANGEBURG WILKINSON HIGH SCHOOL

KAHN | LLE CONSTRUCTION GROUP

SAFETY

Incidents to Date	1
First Aids to Date	0

WEATHER

Working Days	419
Weather Days	53
Activities Delayed	2

MANPOWER

Number of Trades	15
Average Workers *(per day)*	167

SCHEDULE MILESTONES

Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- Athletic lighting installation continued.
- Scoreboard installation began.
- Front entrance curtain wall began.
- Ceiling framing continues in E, F, B & C.
- HVAC startup work continues.
- Work at Belleville & Cook Rd. continued.
- Communications infrastructure continued.
- The gas meter to the main building was installed.
- Press box masonry continued.
- Foundations for the football bleachers continued.
- Turf installation on the SB field began.
- Curb/gutter installation at the rear parking lot began.

Upcoming Activities

- Permanent power at the SB building will be ready.
- Sidewalks around the BB.SB building will be installed.







Week of **January 12, 2026**

ORANGEBURG-WILKINSON HIGH SCHOOL

ORANGEBURG WILKINSON HIGH SCHOOL

SAFETY	
Incidents to Date	1
First Aids to Date	0
WEATHER	
Working Days	429
Weather Days	54
Activities Delayed	2
MANPOWER	
Number of Trades	11
Average Workers *(per day)*	103
SCHEDULE MILESTONES	
Job Start	5/6/2024
Contract Completion	11/5/2026







Top Activities This Week

- Athletic lighting installation continued.
- Scoreboard installation is nearly complete.
- Front curtain wall glazing continued.
- Ceiling framing continues in E, B & C.
- MEP overhead rough-in in the auditorium continues.
- Metal panels at area D were installed.
- Foundations for the football bleachers are complete.
- Prep work for turf and fencing at the BB & SB fields continued.
- Curb/gutter installation at the rear parking lot continued. Sidewalks were poured at the rear of the school.

Upcoming Activities

- Air conditioning in E2 and F will start.
- Resinous flooring to begin in the kitchen.
- Paving at the main entrance to begin.

Week of **January 26, 2026**

ROBERT E. HOWARD ELEMENTARY SCHOOL

ROBERT E. HOWARD ELEMENTARY SCHOOL

SAFETY	
Incidents to Date	0
First Aids to Date	0
WEATHER	
Working Days	186
Weather Days	14
Activities Delayed	0
MANPOWER	
Number of Trades	8
Average Workers *(per day)*	75
SCHEDULE MILESTONES	
Job Start	5/27/2025
Contract Completion	12/14/2026

Top Activities This Week

- Continued Rotunda steel welding
- Continued installing decking over kitchen area in Building B
- Continued water main install adjacent to Russell Street and spreading topsoil in the green areas in Area 2
- Continued setting block in Building A and Rotunda and grouted several areas for bond beams
- Continued filling block outs in Building C for 2nd floor slab on deck placement
- Continued in-wall in Building A and lighting home runs in Building C
- Began installing cable tray in Building C
- Continued to install control home runs and pull wire
- Completed wire mesh placement and layout for the loading dock

Upcoming Activities

- Continue CMU install in Building B and moving into Building A
- Continue lighting home runs in Building C
- Continue water line install & top soil placement
- Building C slab on deck pour tentatively scheduled for February 6th







Week of **January 30th, 2025**

ROBERT E. HOWARD ELEMENTARY SCHOOL



ROBERT E. HOWARD ELEMENTARY SCHOOL



ROBERT E. HOWARD ELEMENTARY SCHOOL



ROBERT E. HOWARD ELEMENTARY SCHOOL

