

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors | Resource Names |
|---|---|---|---|---|---|---|---|
| 1 | | **Bidding** | **60 days** | **Fri 2/6/26** | **Thu 4/30/26** | | |
| 2 | | TMP to issues CD's | 0 days | Fri 2/6/26 | Fri 2/6/26 | | |
| 3 | | Submit to State for Plan Review/Permitting | 3 mons | Fri 2/6/26 | Thu 4/30/26 | 2 | |
| 4 | | Sub-contractor Bidding | 3 wks | Mon 2/9/26 | Fri 2/27/26 | 2FS+1 day | |
| 5 | | Interviews & Awards | 1 wk | Mon 3/2/26 | Fri 3/6/26 | 4 | |
| 6 | | Submit Recommendation for Board Approval | 0 days | Mon 3/23/26 | Mon 3/23/26 | 5FS+11 days | |
| 7 | | **Construction** | **293 days** | **Mon 6/15/26** | **Wed 7/28/27** | | |
| 8 | | **Site Works** | **130 days** | **Mon 6/15/26** | **Fri 12/11/26** | | |
| 9 | | Site Demo | 10 days | Mon 6/15/26 | Fri 6/26/26 | | |
| 10 | | New Underground Utilities | 15 days | Mon 6/29/26 | Fri 7/17/26 | 9 | |
| 11 | | Pour Building Foundations | 20 days | Mon 7/20/26 | Fri 8/14/26 | 10 | |
| 12 | | Masonry Below Grade | 10 days | Mon 8/17/26 | Fri 8/28/26 | 11 | |
| 13 | | MEP Underground | 20 days | Mon 8/17/26 | Fri 9/11/26 | 11 | |
| 14 | | Slab on Grade | 10 days | Mon 9/14/26 | Fri 9/25/26 | 13 | |
| 15 | | Masonry | 25 days | Mon 9/28/26 | Fri 10/30/26 | 14 | |
| 16 | | Lintels Delivery | 1 day | Mon 9/28/26 | Mon 9/28/26 | 15SS | |
| 17 | | Store-Front Door/Window System | 5 days | Mon 11/2/26 | Fri 11/6/26 | 15 | |
| 18 | | Install Glazing Complete | 5 days | Mon 11/9/26 | Fri 11/13/26 | 17 | |
| 19 | | Structural Steel Install | 15 days | Mon 11/2/26 | Fri 11/20/26 | 15 | |
| 20 | | Roofing System Complete | 15 days | Mon 11/23/26 | Fri 12/11/26 | 19 | |
| 21 | | **Interiors** | **140 days** | **Mon 12/21/26** | **Fri 7/2/27** | | |
| 22 | | Drywall Framing | 5 days | Mon 12/21/26 | Fri 12/25/26 | 20FS+5 days | |
| 23 | | MEP Rough In | 30 days | Mon 12/21/26 | Fri 1/29/27 | 20FS+5 days | |
| 24 | | Drywall/Ceilings | 25 days | Mon 2/1/27 | Fri 3/5/27 | 23 | |
| 25 | | MEP Finishes | 30 days | Mon 3/8/27 | Fri 4/16/27 | 24 | |
| 26 | | Painting Prime/First Coat | 20 days | Mon 3/8/27 | Fri 4/2/27 | 24 | |
| 27 | | Tile Bathroom Walls & Floors | 20 days | Mon 3/8/27 | Fri 4/2/27 | 24 | |
| 28 | | Door and Hardware | 10 days | Mon 4/5/27 | Fri 4/16/27 | 27 | |
| 29 | | Casework/Millwork Install | 10 days | Mon 4/19/27 | Fri 4/30/27 | 28 | |
| 30 | | Metal Locker Install | 10 days | Mon 4/5/27 | Fri 4/16/27 | 26 | |
| 31 | | Classroom Tout and Cubby System | 15 days | Mon 5/3/27 | Fri 5/21/27 | 29 | |
| 32 | | Finish Floor & Base Install | 10 days | Mon 5/24/27 | Fri 6/4/27 | 31 | |
| 33 | | Wall Partition Install | 5 days | Mon 6/7/27 | Fri 6/11/27 | 32 | |
| 34 | | Final Paint | 15 days | Mon 6/14/27 | Fri 7/2/27 | 33 | |
| 35 | | **Exterior Finnishes** | **85 days** | **Thu 4/1/27** | **Wed 7/28/27** | | |
| 36 | | Cast-in-place Concrete Walls & Lids | 10 days | Thu 4/1/27 | Wed 4/14/27 | | |
| 37 | | Finish Grading | 10 days | Thu 4/15/27 | Wed 4/28/27 | 36 | |
| 38 | | Concrete Pavement install | 15 days | Thu 4/29/27 | Wed 5/19/27 | 37 | |

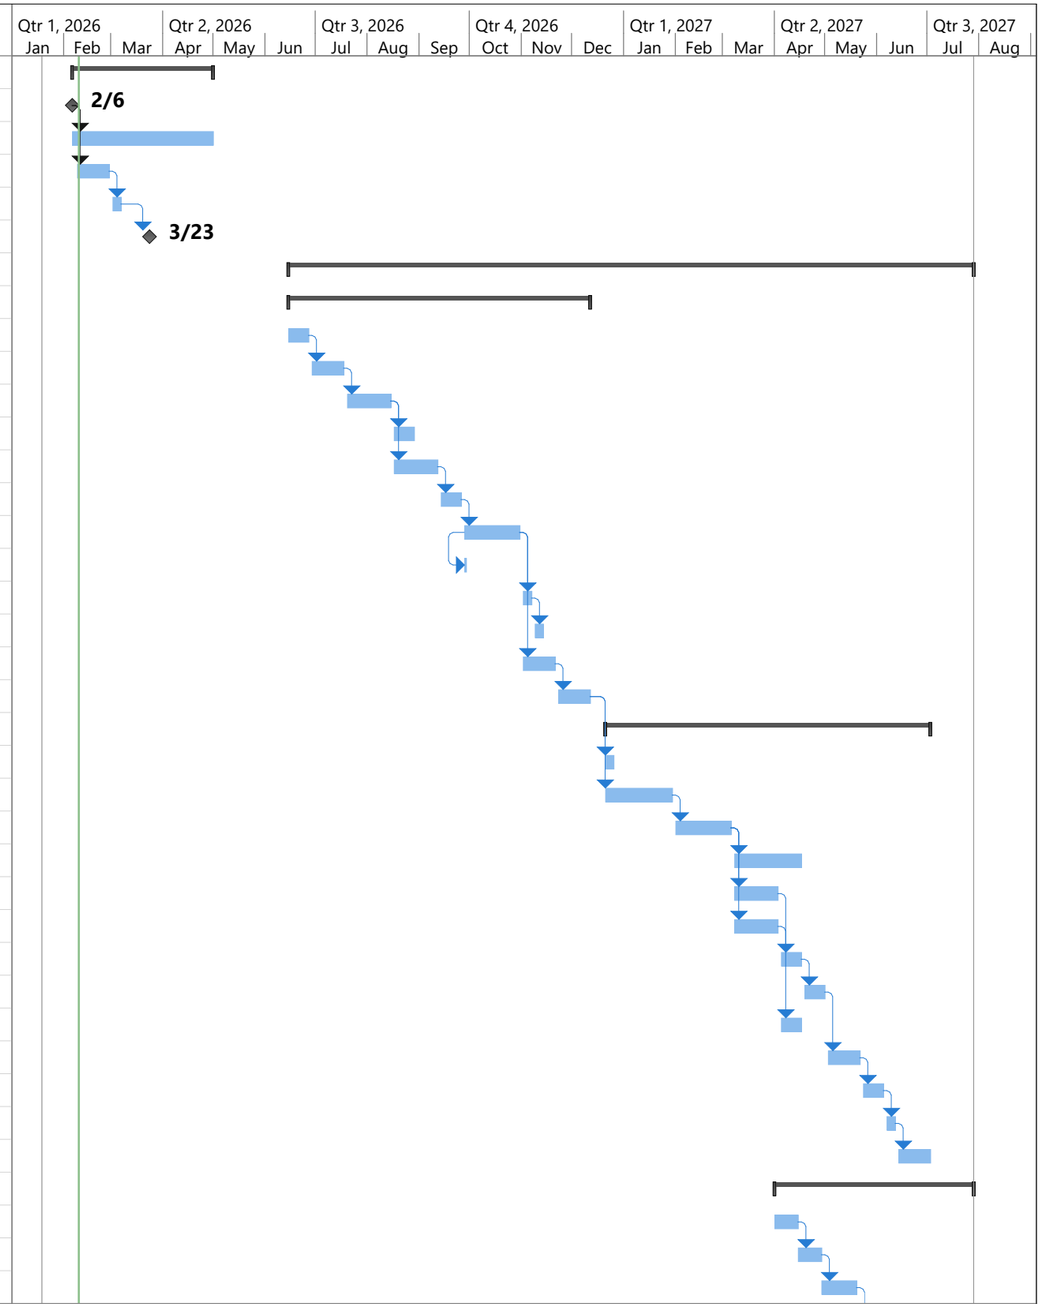


Project: Wylie Bidding Schedule
Date: Tue 2/10/26

| | | | | | |
|---|---|---|---|---|---|
| Task | Project Summary | Manual Task | Start-only | Deadline | |
| Split | Inactive Task | Duration-only | Finish-only | Progress | |
| Milestone | Inactive Milestone | Manual Summary Rollup | External Tasks | Manual Progress | |
| Summary | Inactive Summary | Manual Summary | External Milestone | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors | Resource Names |
|---|---|---|---|---|---|---|---|
| 39 | | Exterior Concrete Walks & Stoops | 20 days | Thu 5/20/27 | Wed 6/16/27 | 38 | |
| 40 | | Baseball Field Fencing & Surface | 15 days | Thu 6/17/27 | Wed 7/7/27 | 39 | |
| 41 | | Landscaping | 15 days | Thu 7/8/27 | Wed 7/28/27 | 40 | |




Project: Wylie Bidding Schedule
Date: Tue 2/10/26

| | | | | | | | |
|---|---|---|---|---|---|---|---|
| Task | Project Summary | Manual Task | Start-only | Deadline |
| Split | Inactive Task | Duration-only | Finish-only | Progress |
| Milestone | Inactive Milestone | Manual Summary Rollup | External Tasks | Manual Progress |
| Summary | Inactive Summary | Manual Summary | External Milestone | |
