
ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**Bidding**	**64 days**	**Tue 3/3/26**	**Fri 5/29/26**	
7		**Construction**	**63 days**	**Mon 6/1/26**	**Wed 8/26/26**	
8		**Site Works**	**63 days**	**Mon 6/1/26**	**Wed 8/26/26**	
9		Last day of School Sports Prectice	0 days	Mon 6/1/26	Mon 6/1/26	
10		Mobilize/Soil Erosion Works	5 days	Mon 6/1/26	Fri 6/5/26	9
11		Site Demolition	10 days	Mon 6/8/26	Fri 6/19/26	10
12		Under Ground Utilities & Site Lighting	10 days	Mon 6/22/26	Fri 7/3/26	11
13		**Track Storage Building**	**20 days**	**Mon 6/22/26**	**Fri 7/17/26**	
14		Abatment & Selective Demo	10 days	Mon 6/22/26	Fri 7/3/26	11
15		Install New Roof	5 days	Mon 7/6/26	Fri 7/10/26	14
16		Interior Rework	5 days	Mon 7/13/26	Fri 7/17/26	15
17		Decerative fencing	5 days	Mon 6/29/26	Fri 7/3/26	12SS+5 days
18		New Chain-link Fencing	5 days	Mon 7/6/26	Fri 7/10/26	17
19		Fine Grade Walkways	3 days	Mon 7/13/26	Wed 7/15/26	18
20		Hardscape Around Track	7 days	Thu 7/16/26	Fri 7/24/26	19
21		Paint Existing Fence	15 days	Mon 7/27/26	Fri 8/14/26	20
22		Entryway - Footings and Stairs	7 days	Mon 7/27/26	Tue 8/4/26	20
23		Steel Columns & Arch	3 days	Mon 8/3/26	Wed 8/5/26	22SS+5 days
24		Masonry Columns	3 days	Thu 8/6/26	Mon 8/10/26	23
25		Concrete Stairs & Sidewalk	7 days	Tue 8/11/26	Wed 8/19/26	24
26		Fine Grading & Landscaping	5 days	Thu 8/20/26	Wed 8/26/26	25
27		Complete	0 days	Wed 8/26/26	Wed 8/26/26	26

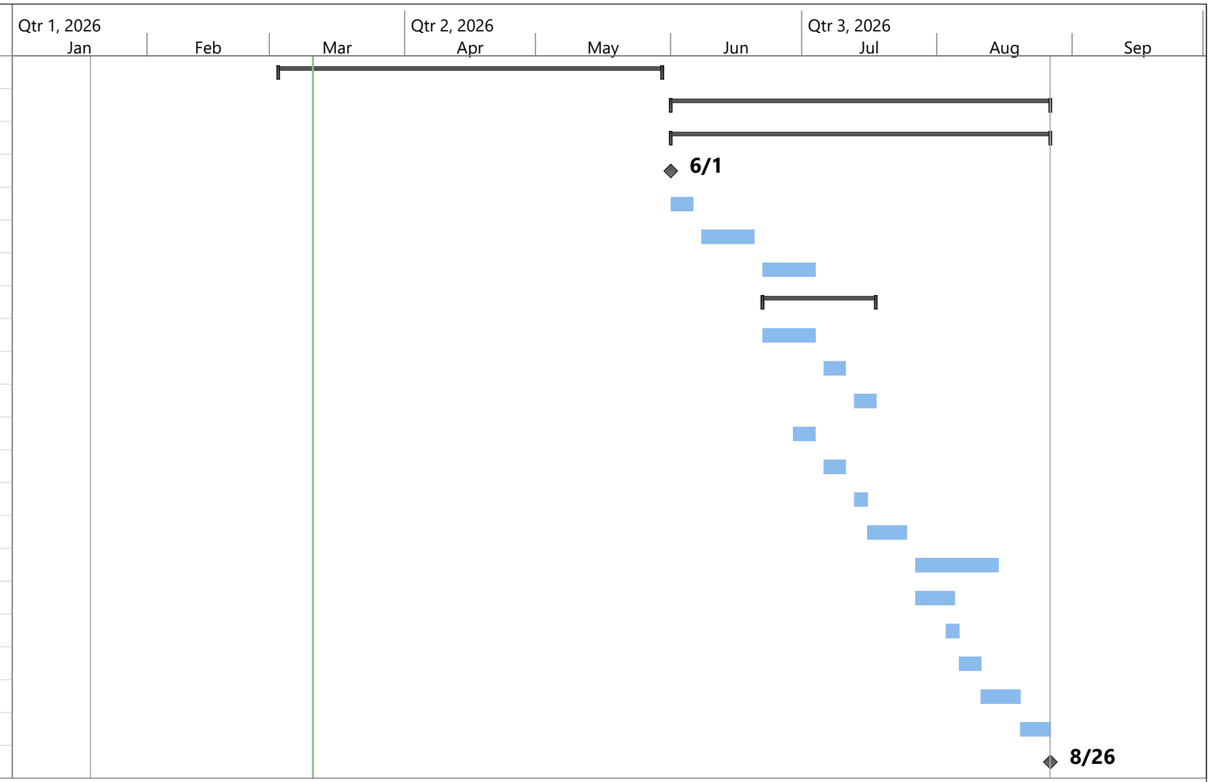

Project: Wylie Bidding Schedule
Date: Wed 3/11/26

Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		
