Empowering Today to Excel Tomorrow

#WeAreHEBISD

HEB ISD BOND 2023
Update
March 30, 2026

District Priorities:

- Student Success
- Employee Success
- Safety and Wellbeing
- Effectiveness and Efficiency
- Family and Community Partnerships

HEBISD

Project Updates

- Faye Beaulieu Family Support Center
- Debbie Williams Activity Center - Completed
- L.D. Bell High School
- Trinity High School

- Hurst Junior High Administration Addition – Completed

- Bell Manor Elementary
- Hurst Hills Elementary
- Midway Park Elementary
- Wilshire Elementary

Empowering Today to Excel Tomorrow

#WeAreHEBISD

Faye Beaulieu Family Support Center



SDB Huckabee

EXTERIOR PERSPECTIVE - MAIN ENTRY - SOUTH VIEW

06

HEB ISD





Faye Beaulieu Family Support Center

☑ Status: Bid

☑ Construction began March 2025

□ Building estimated opening April 2026

HEB ISD



HEBISD





HEBISD



HEB ISD





HEB ISD



HEB ISD



Empowering Today to Excel Tomorrow

#WeAreHEBISD

Hurst Hills Elementary Project



HEBISD

HEB ISD





Hurst Hills Elementary

☑ Status: Bid

☑ Construction began April 2025

□ Phase #1 estimated completion July 2026

□ Site estimated completion November 2026

HEB ISD



HEB ISD



HEB ISD



HEB ISD





COLOR LEGEND

- Pavement/Roads
- Sidewalks
- Grass
- Playgrounds
- Trees
- Hardcourt
- Building
- Parent Drop-Off Lane
- Bus Drop-Off Lane

PARKING COUNT

160 PARKING SPACES

Huckabee

Hurst Hills & Wilshire Elementary School Replacements

NOT FOR REGULATORY APPROVAL, PERMITTING, OR CONSTRUCTION

AUBREY MOSES, AIA 23077

0 100

SITE PLAN - HURST HILLS

Empowering Today to Excel Tomorrow

#WeAreHEBISD

Midway Park Elememementary Project



HEBISD

HEBISD





Midway Park Elementary

- ☑ Status: Bid
- ☑ Construction begins July 2025
- □ Phase #1 estimated completion October 2026
- □ Site estimated completion June 2027

HEB ISD



HEB ISD



HEB ISD




HEB ISD



HEB ISD



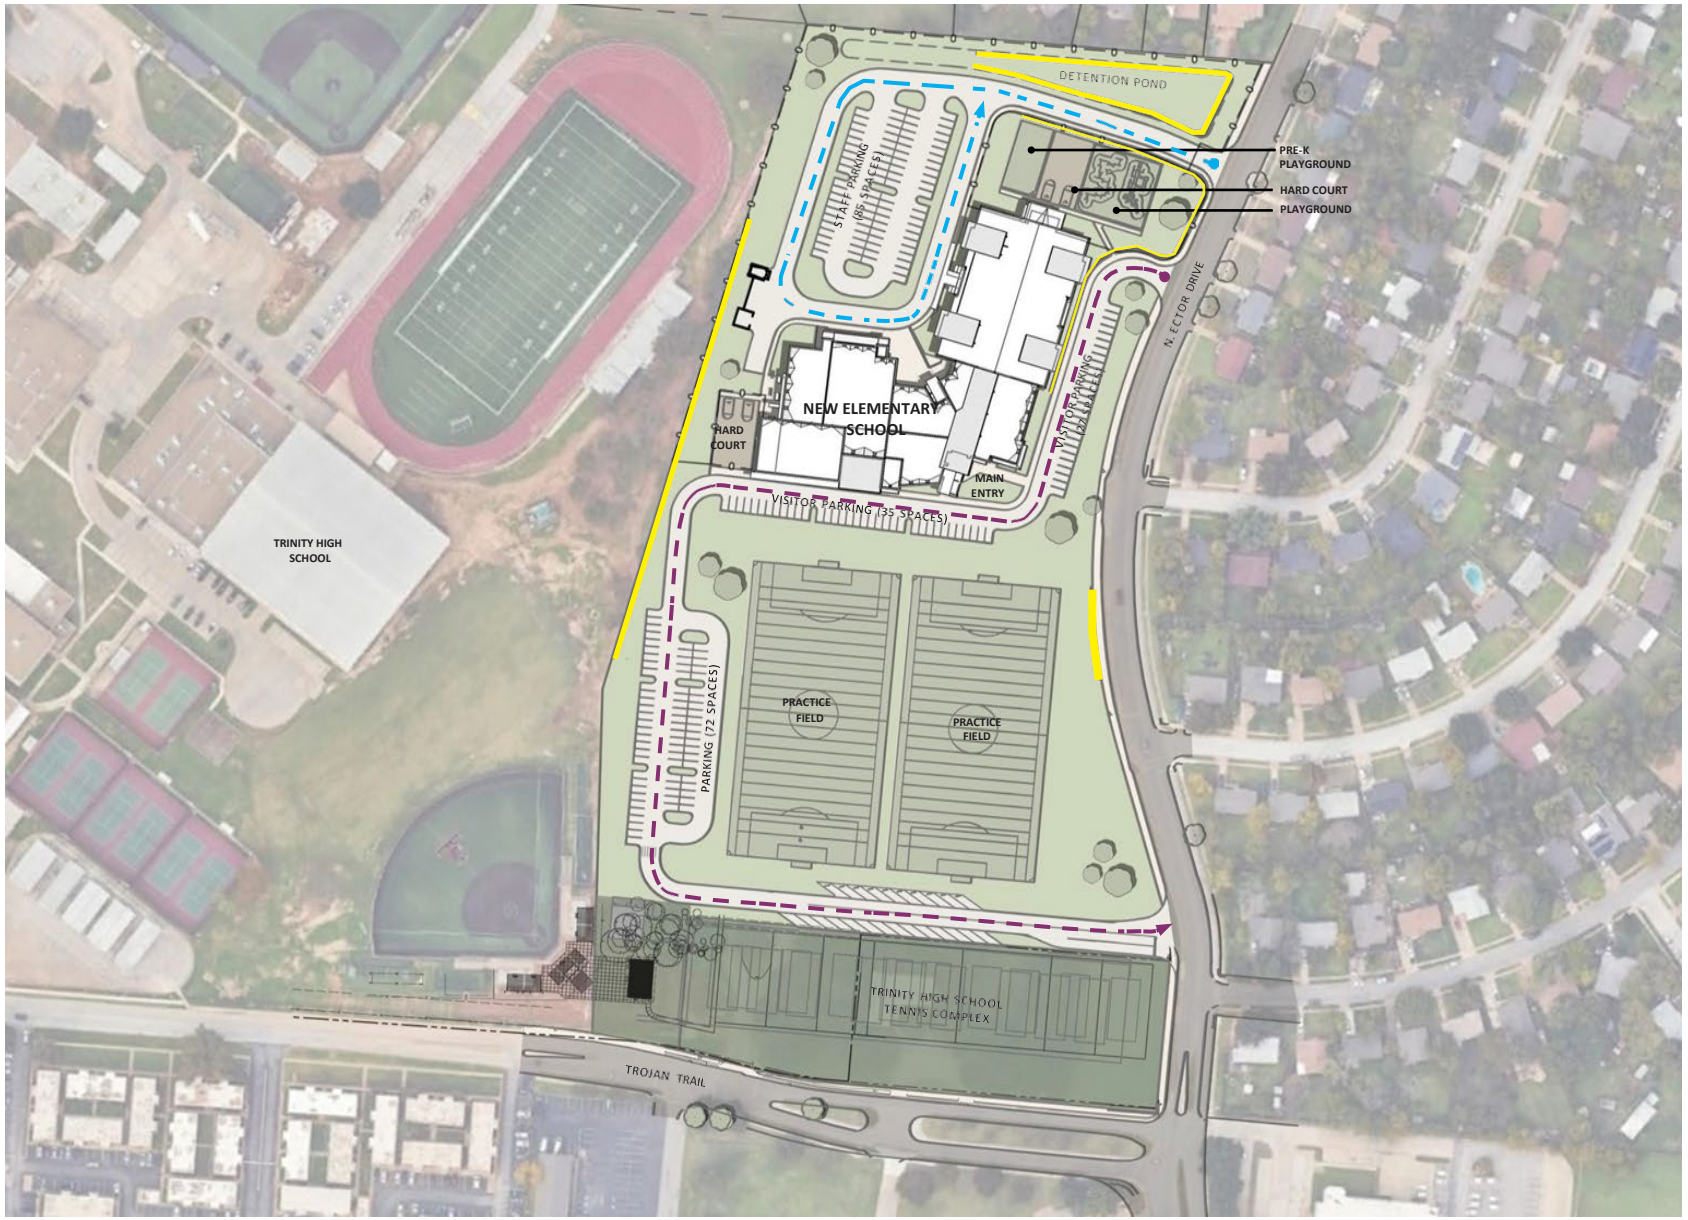

COLOR LEGEND

- Pavement/Roads
- Sidewalks
- Grass
- Playgrounds
- Trees
- Hardcourt
- HS Tennis Courts
- Building
- Parent Drop-Off Lane
- Bus Drop-Off Lane
- Retaining wall

PARKING COUNT

147 PARKING SPACES

72 OVERFLOW PARKING SPACES

Huckabee

BELL MANOR & MIDWAY PARK ELEMENTARY REPLACEMENTS

NOT FOR REGULATORY APPROVAL, PERMITTING OR CONSTRUCTION. AUBREY MOSES, AIA 23077

0 160

SITE PLAN - MIDWAY PARK

Empowering Today to Excel Tomorrow

#WeAreHEBISD

Wilshire Elementary Project



HEBISD

HEB ISD





Wilshire Elementary

- ☑ Status: Bid
- ☑ Construction begins estimated October 2025
- □ Phase #1 estimated completion December 2026
- □ Site estimated completion May 2027


HEB ISD



HEB ISD



HEB ISD

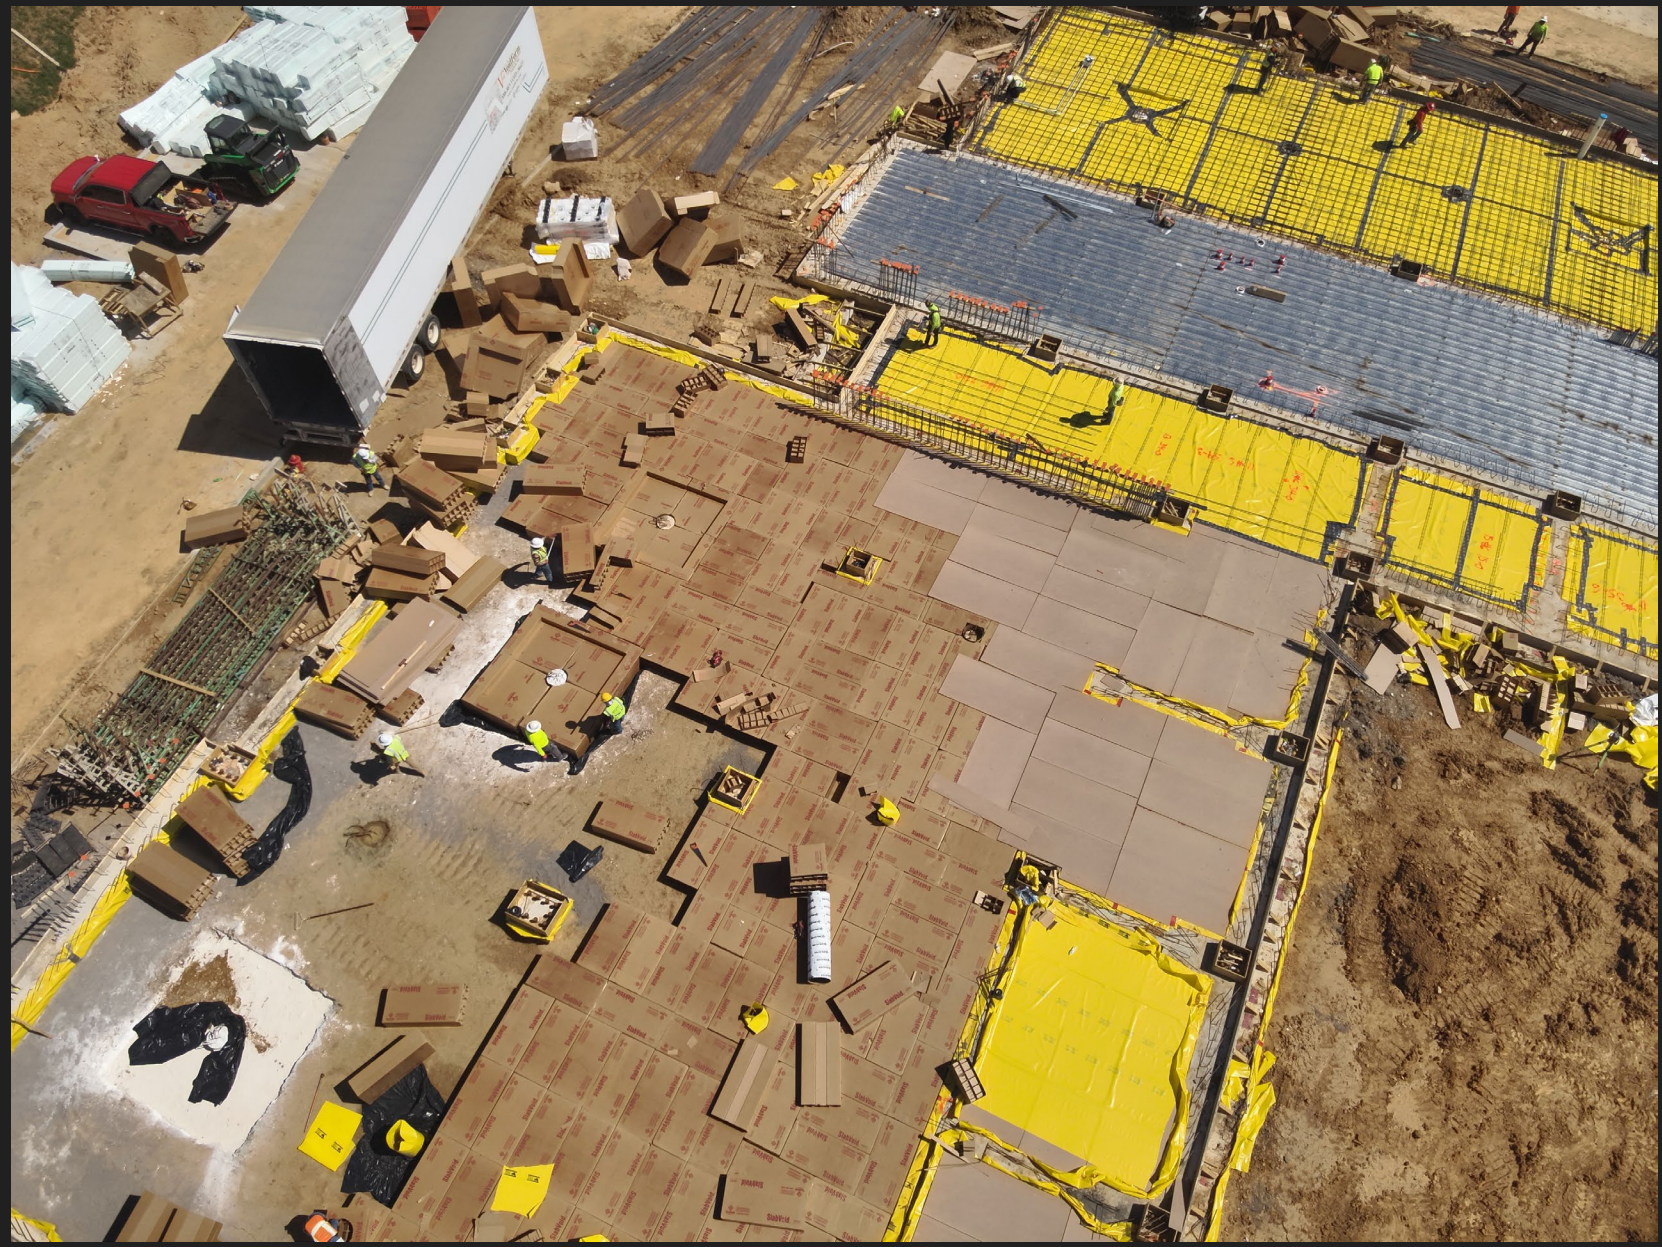

HEBISD





COLOR LEGEND

- Pavement/Roads
- Sidewalk
- Grass
- Playing Fields
- Trees
- Building

PARKING COUNT

154 PARKING SPACES

Huckabee

Hurst Hills & Wilshire Elementary School Replacements

NOT FOR REGULATORY APPROVAL, PERMITTING, OR CONSTRUCTION

AUBREY MOSES, AIA 23077

0 100

SITE PLAN WILSHIRE

Empowering Today to Excel Tomorrow

#WeAreHEBISD


Bell Manor Elementary Project



HEBISD

HEB ISD



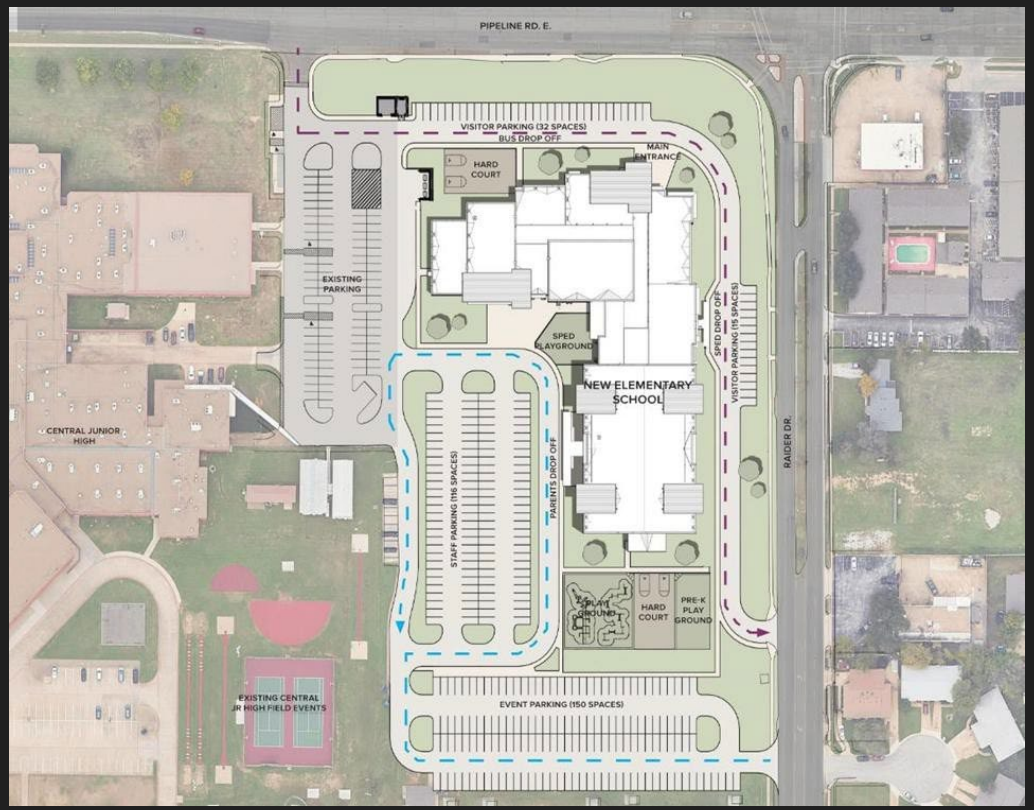


Bell Manor Elementary

☑ Status: Construction Documents

□ Construction begins estimated April 2026
(Pending completion of Faye Beaulieu Family Support Center)

□ Building opening estimated Summer 2027

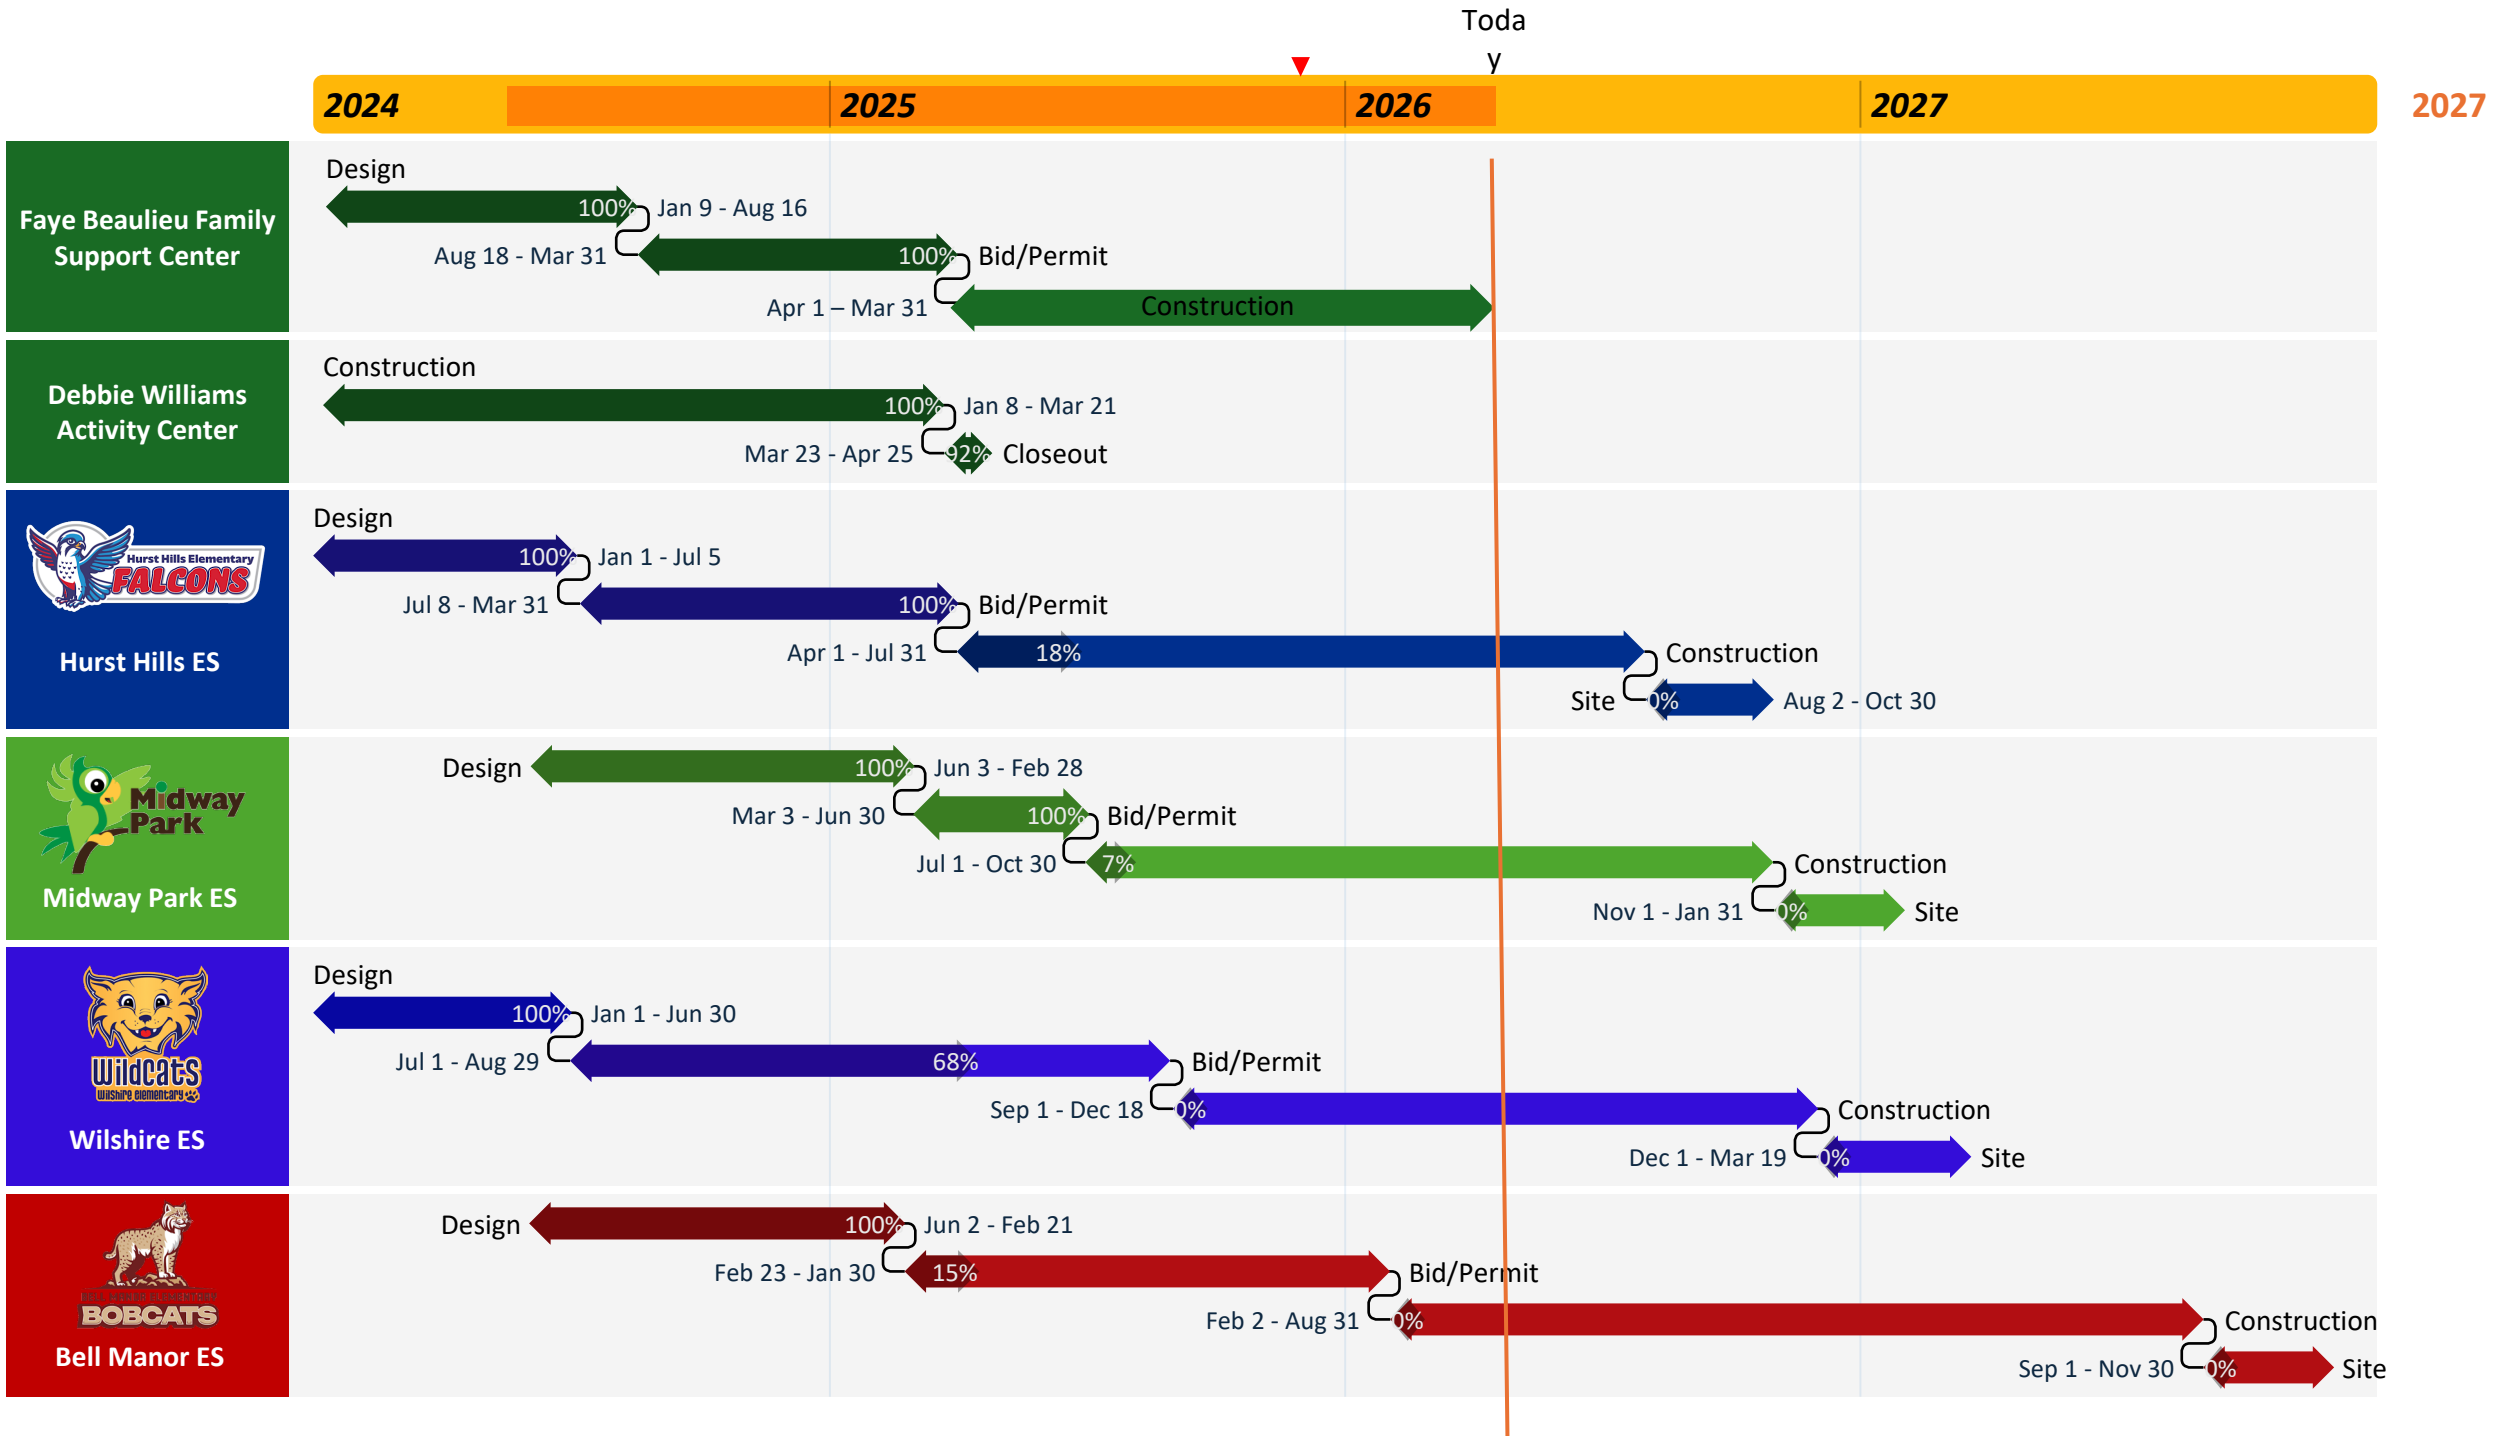
Today
2024
2025
2026
2027
2027
Faye Beaulieu Family Support Center
Design
100%
Jan 9 - Aug 16
Aug 18 - Mar 31
100%
Bid/Permit
Apr 1 – Mar 31
Construction
Debbie Williams Activity Center
Construction
100%
Jan 8 - Mar 21
Mar 23 - Apr 25
92%
Closeout
Hurst Hills ES
Design
100%
Jan 1 - Jul 5
Jul 8 - Mar 31
100%
Bid/Permit
Apr 1 - Jul 31
18%
Construction
Site
0%
Aug 2 - Oct 30
Midway Park ES
Design
100%
Jun 3 - Feb 28
Mar 3 - Jun 30
100%
Bid/Permit
Jul 1 - Oct 30
7%
Construction
Nov 1 - Jan 31
0%
Site
Wilshire ES
Design
100%
Jan 1 - Jun 30
Jul 1 - Aug 29
68%
Bid/Permit
Sep 1 - Dec 18
0%
Construction
Dec 1 - Mar 19
0%
Site
Bell Manor ES
Design
100%
Jun 2 - Feb 21
Feb 23 - Jan 30
15%
Bid/Permit
Feb 2 - Aug 31
0%
Construction
Sep 1 - Nov 30
0%
Site

Empowering Today to Excel Tomorrow

#WeAreHEBISD

L.D. BELL HIGH SCHOOL REPLACEMENT

JOERIS CORGAN





HEB
HURST - EULESS - BEDFORD
Independent School District

LD BELL HIGH SCHOOL - SITE PLAN

01/10/2024

CORGAN

HEB ISD



HEB ISD





HEB ISD



HEB ISD




L.D. Bell High School – PHASING PLAN


JOERIS General Contractors

1 **MARCH 2025 – MAY 2028**
(38 MONTHS)

2A **2B** **AUG 2028 – AUG 2029**
(12 MONTHS)

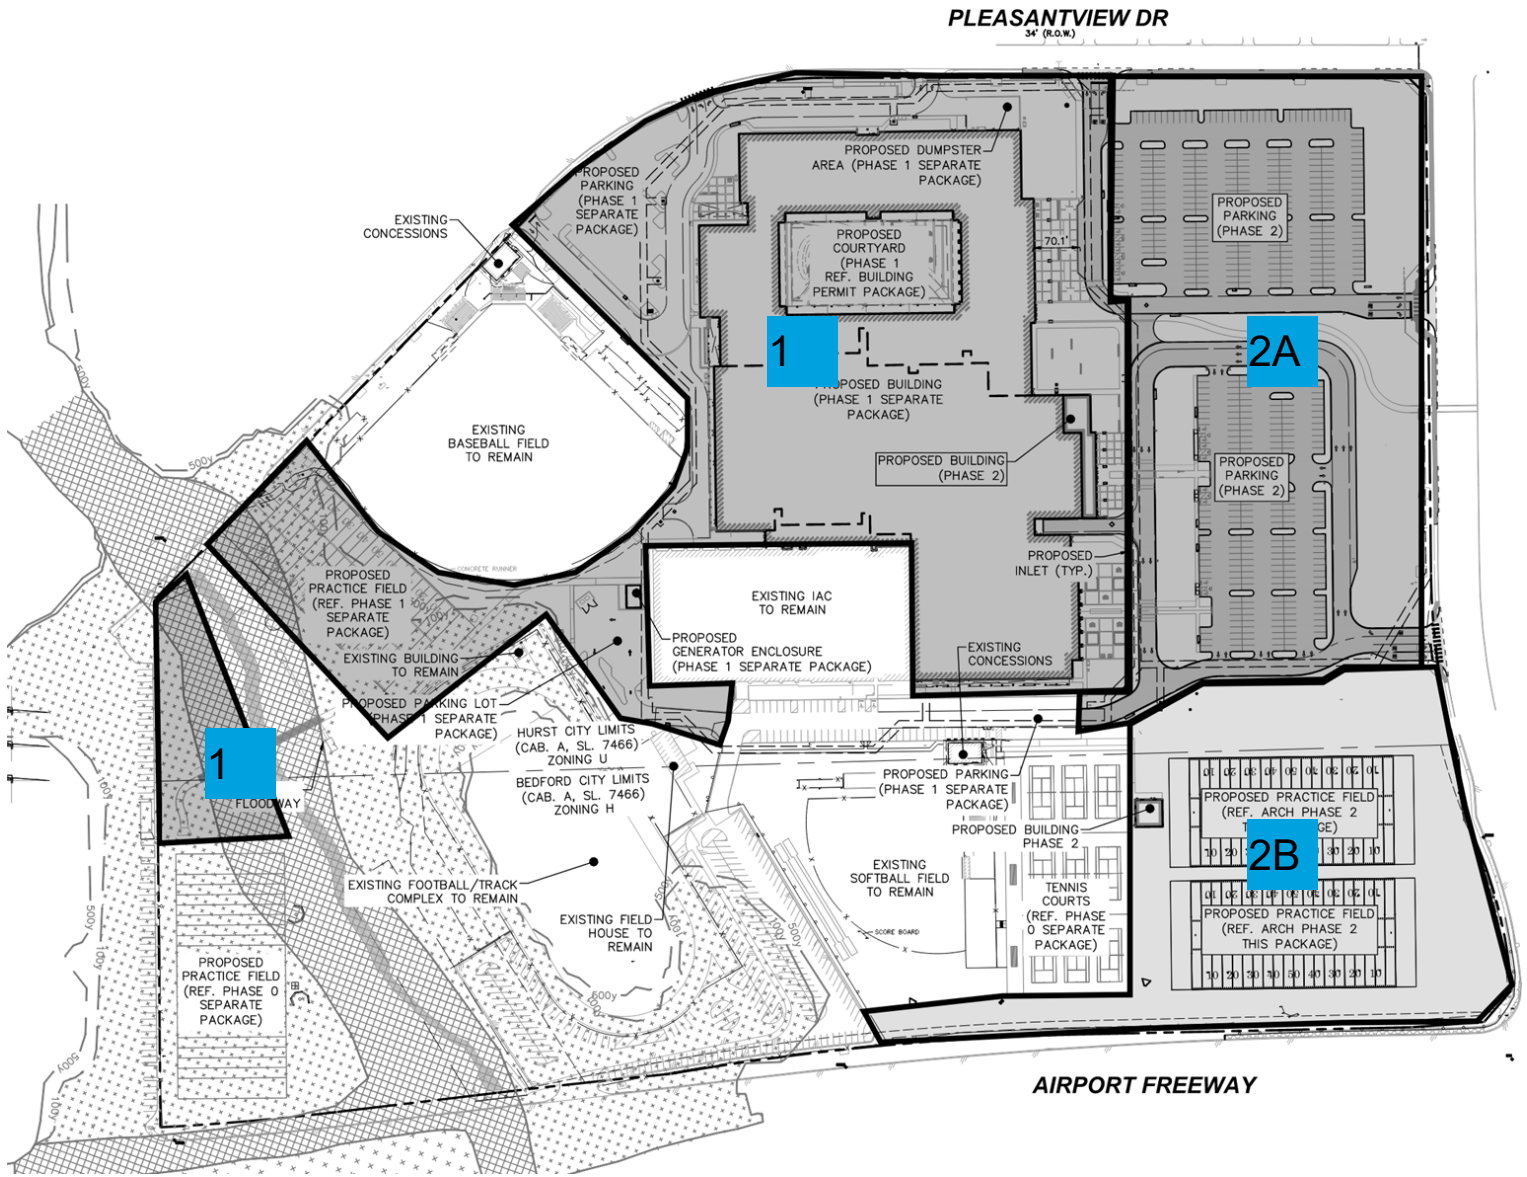

L.D. BELL HIGH SCHOOL SCHEDULE

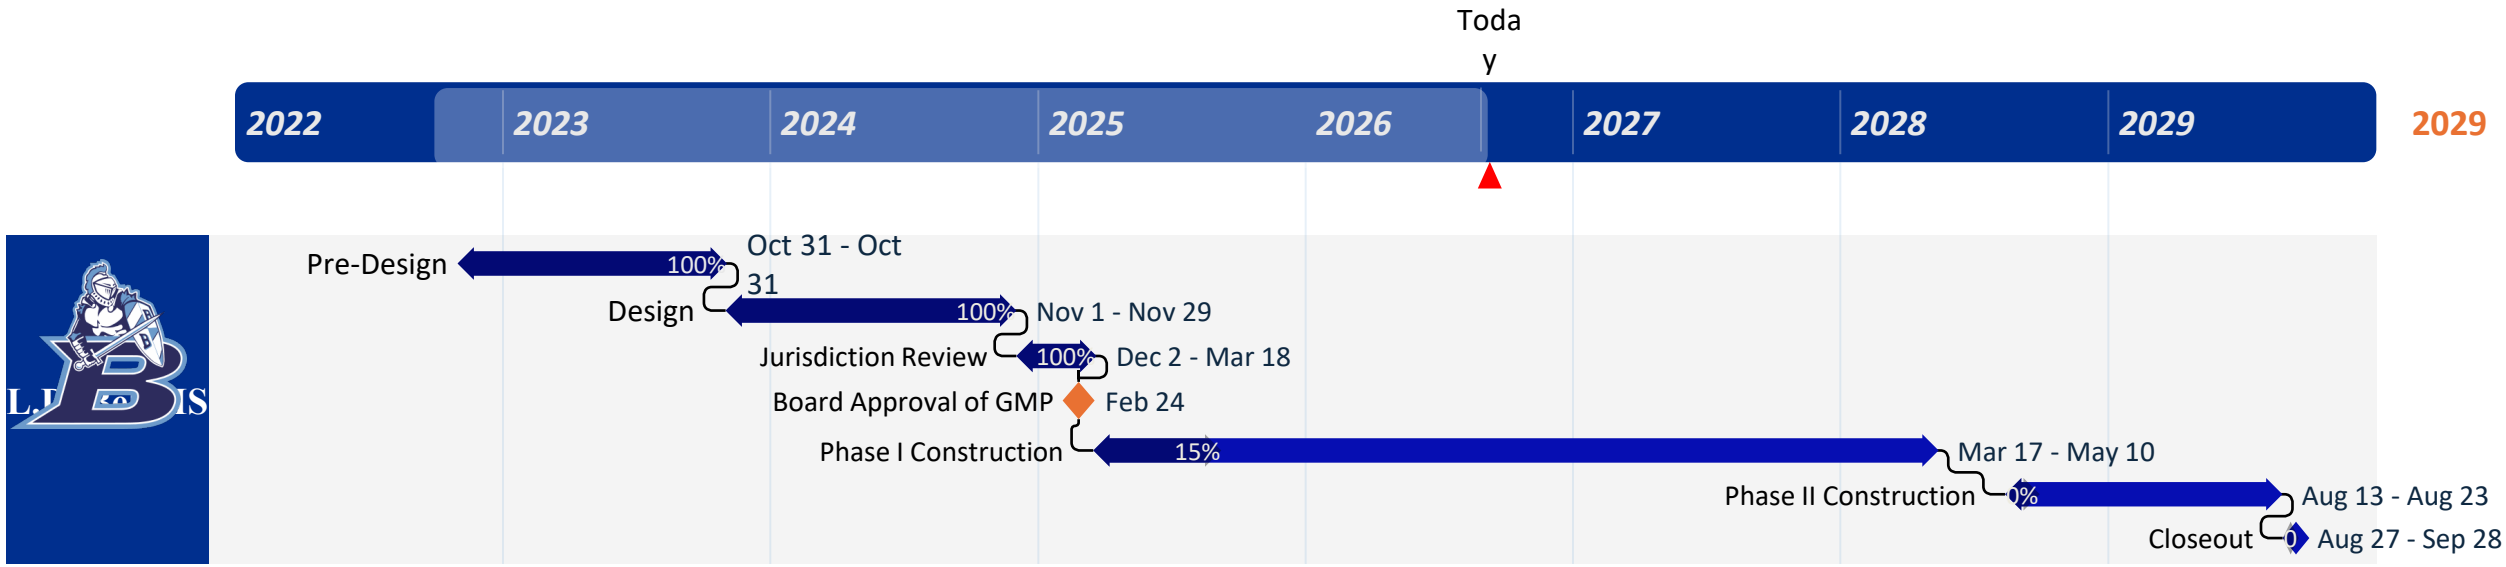



Empowering Today to Excel Tomorrow


#WeAreHEBISD

TRINITY HIGH SCHOOL REPLACEMENT

JOERIS CORGAN

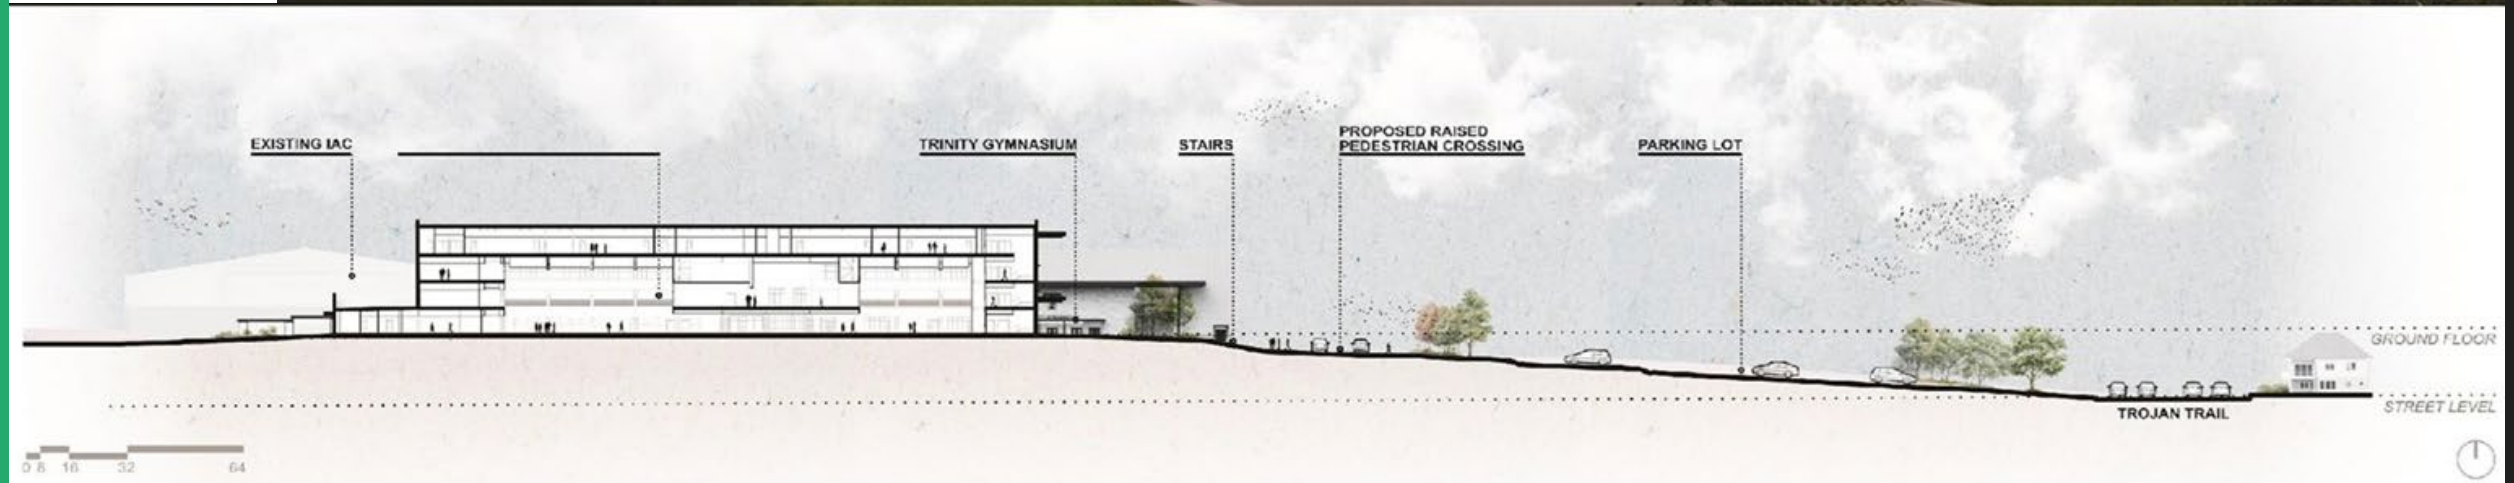

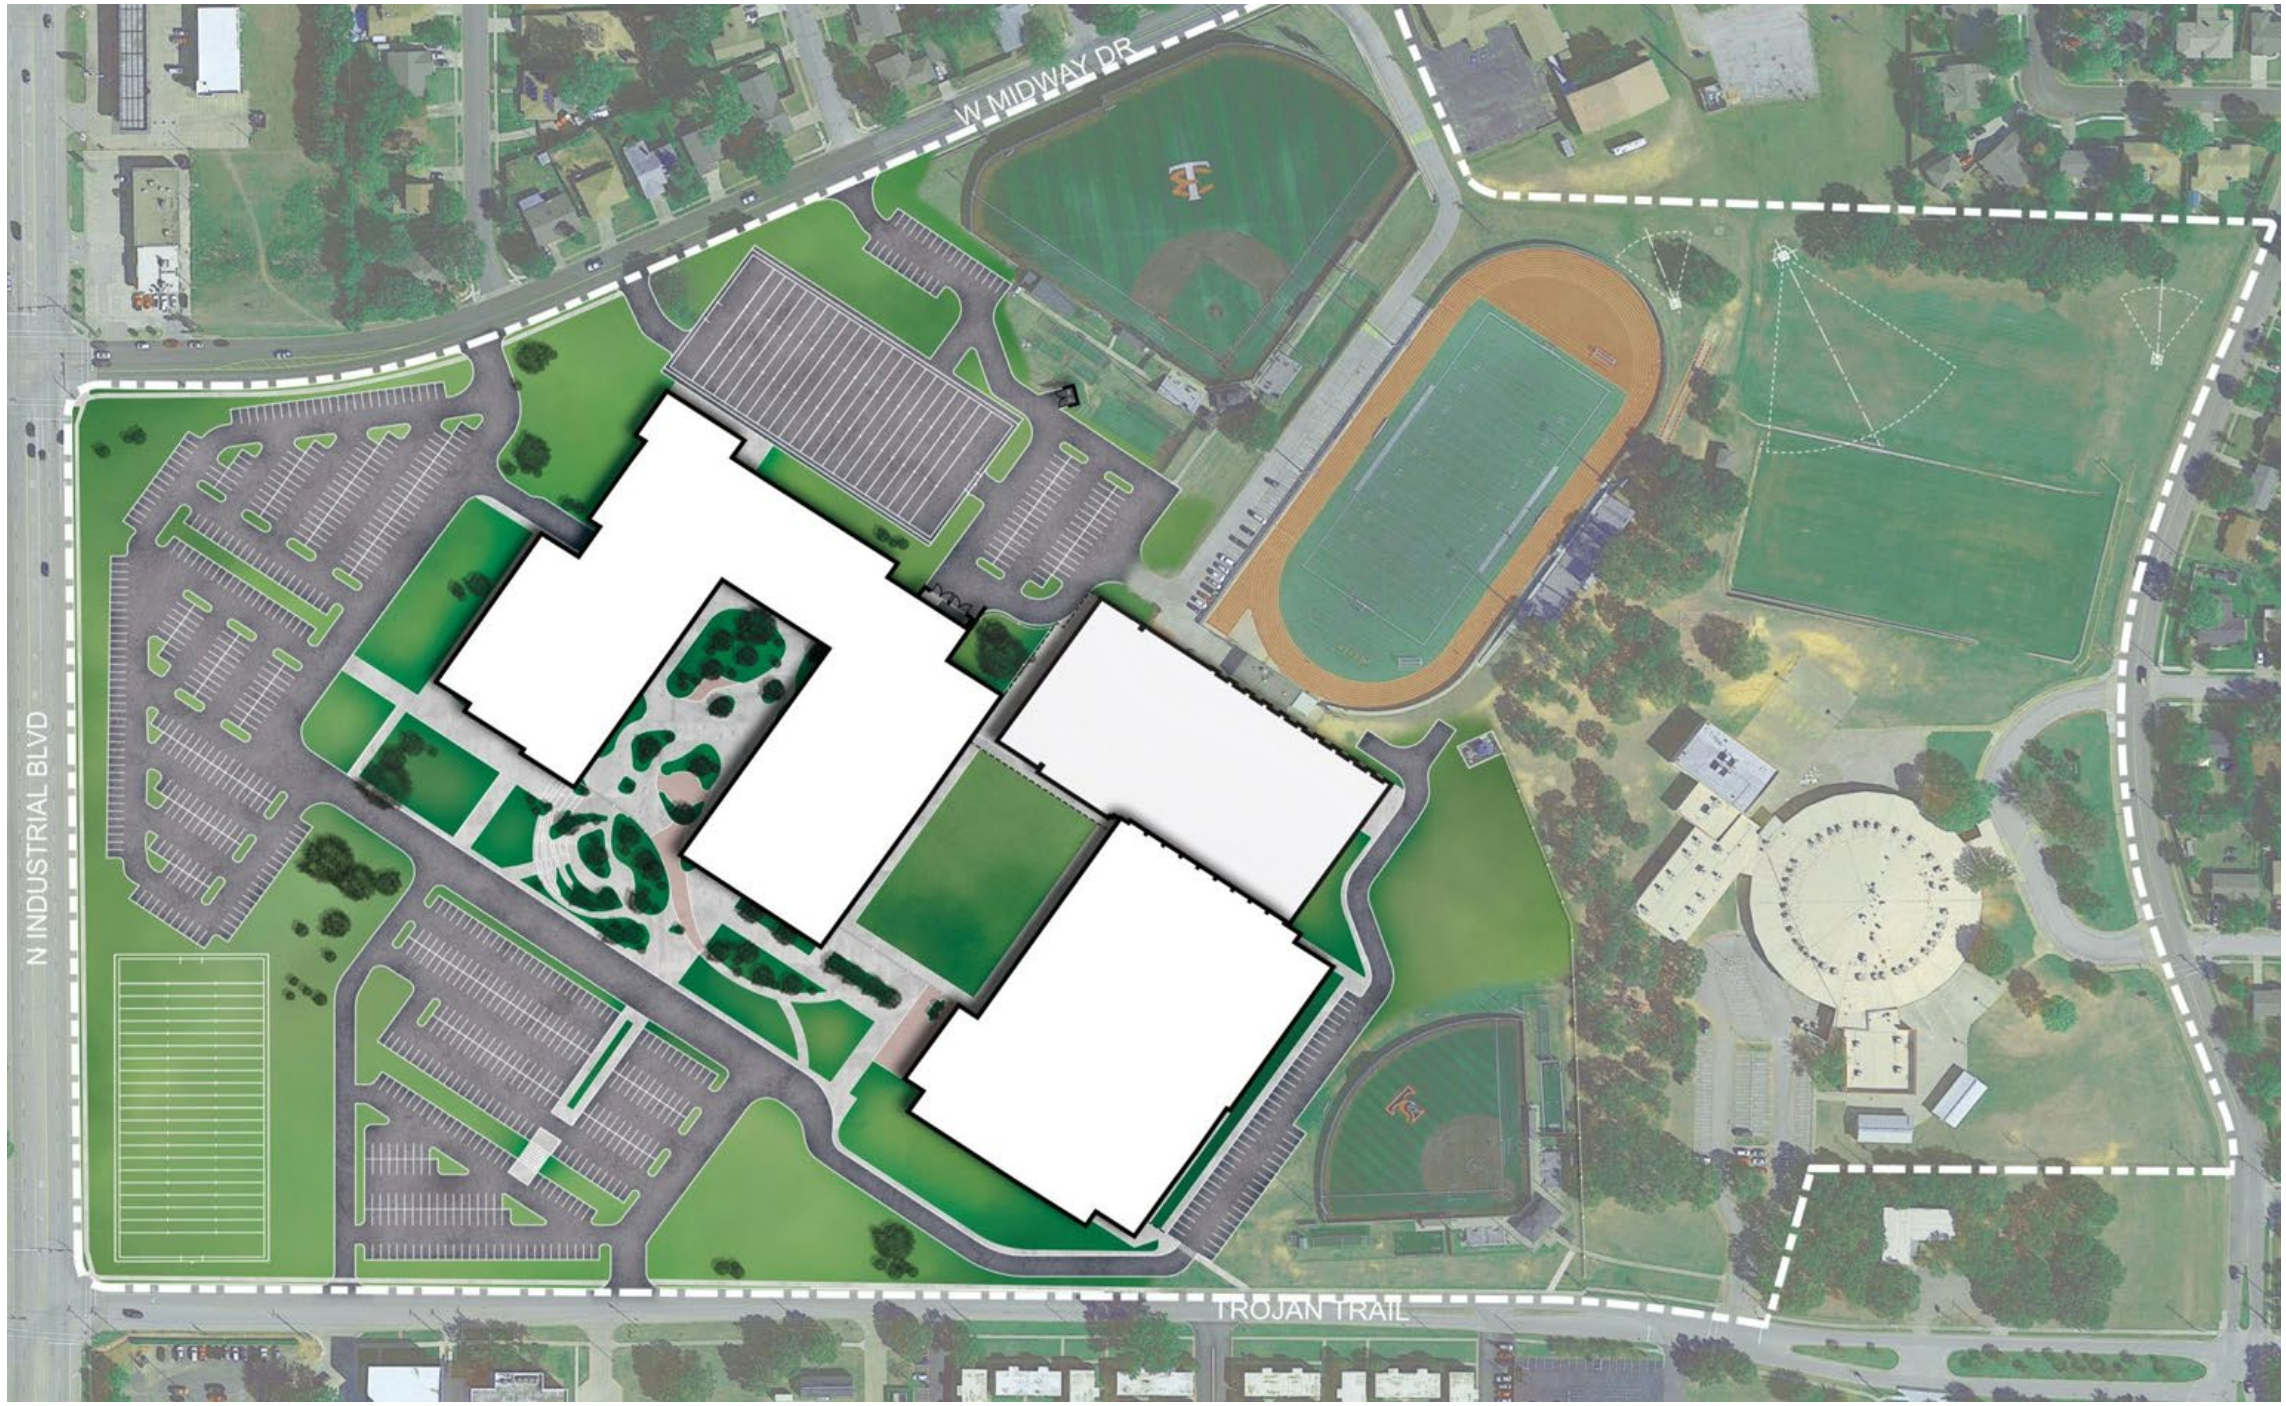
W MIDWAY DR
N INDUSTRIAL BLVD
TROJAN TRAIL

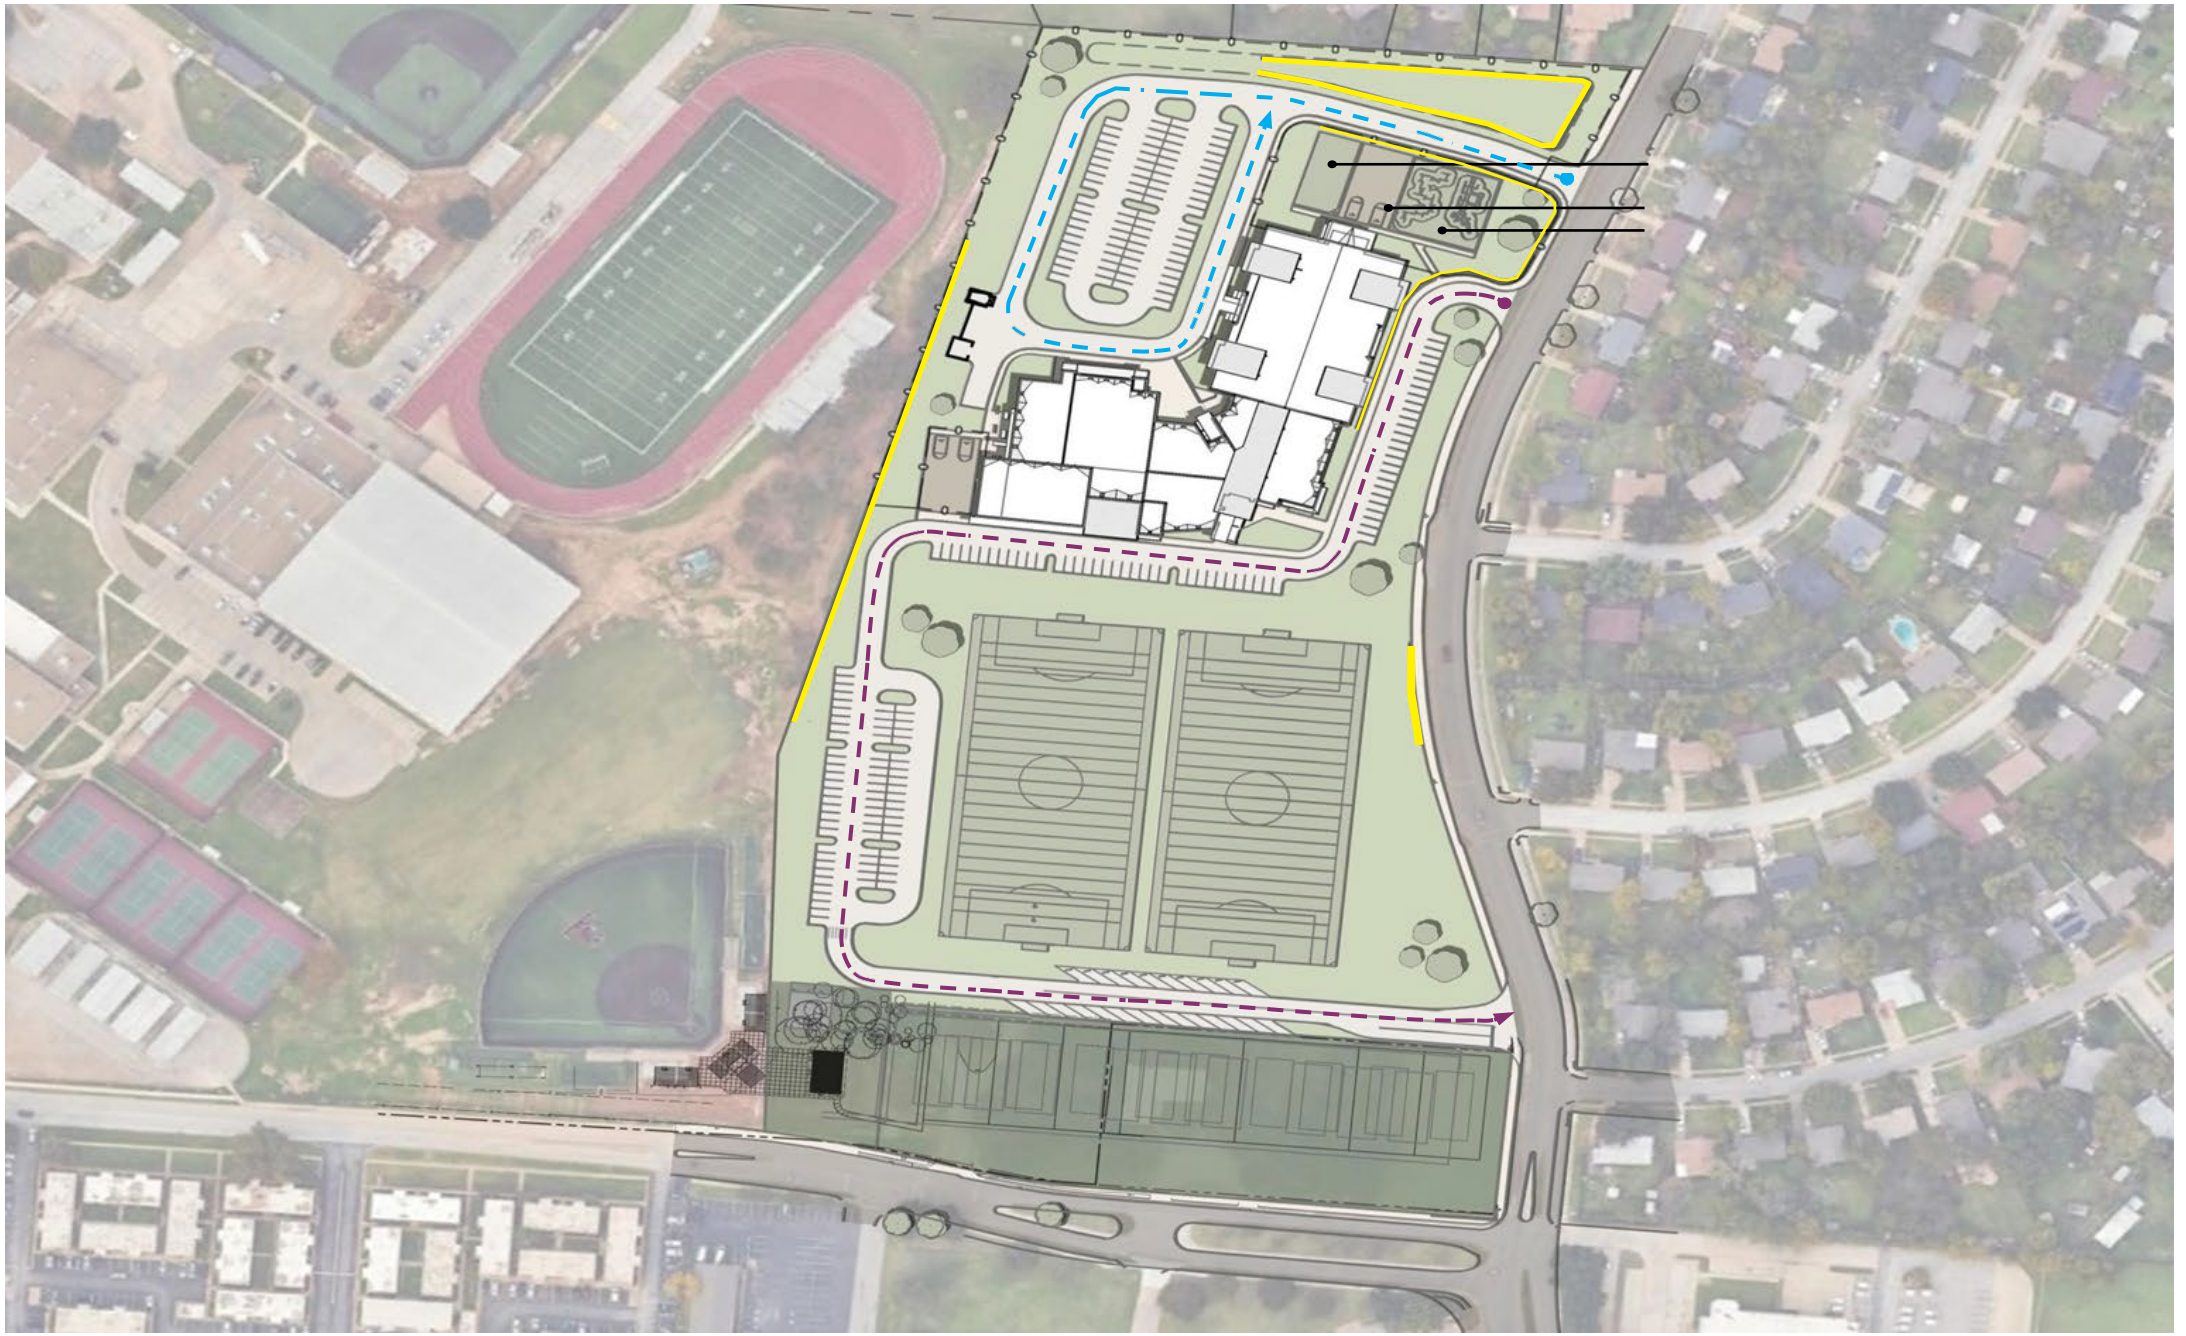


HEB ISD



HEB ISD



HEB ISD

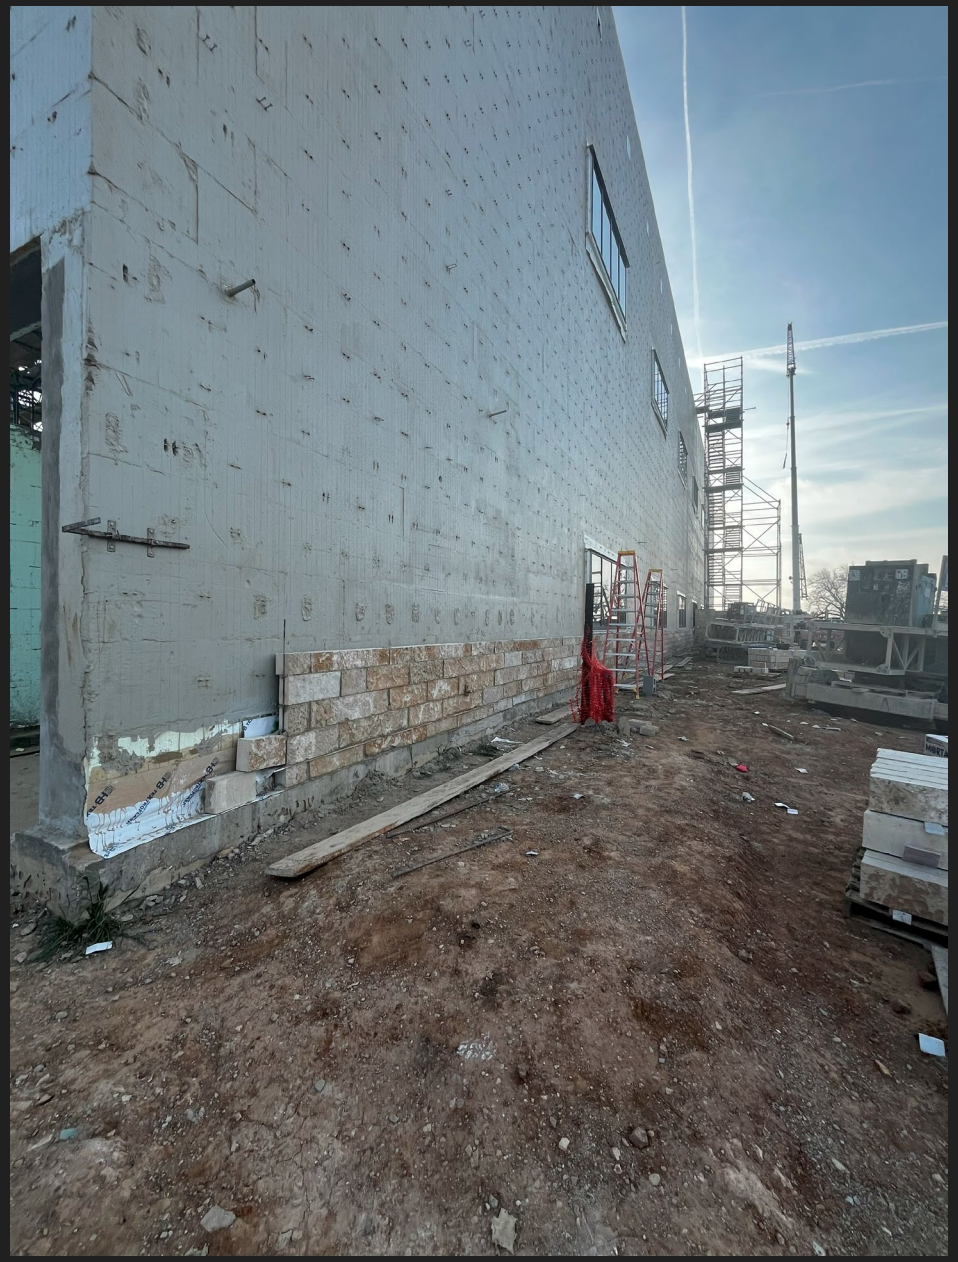

HEB ISD






HEBISD



Trinity High School – PHASING PLAN

JOERIS General Contractors

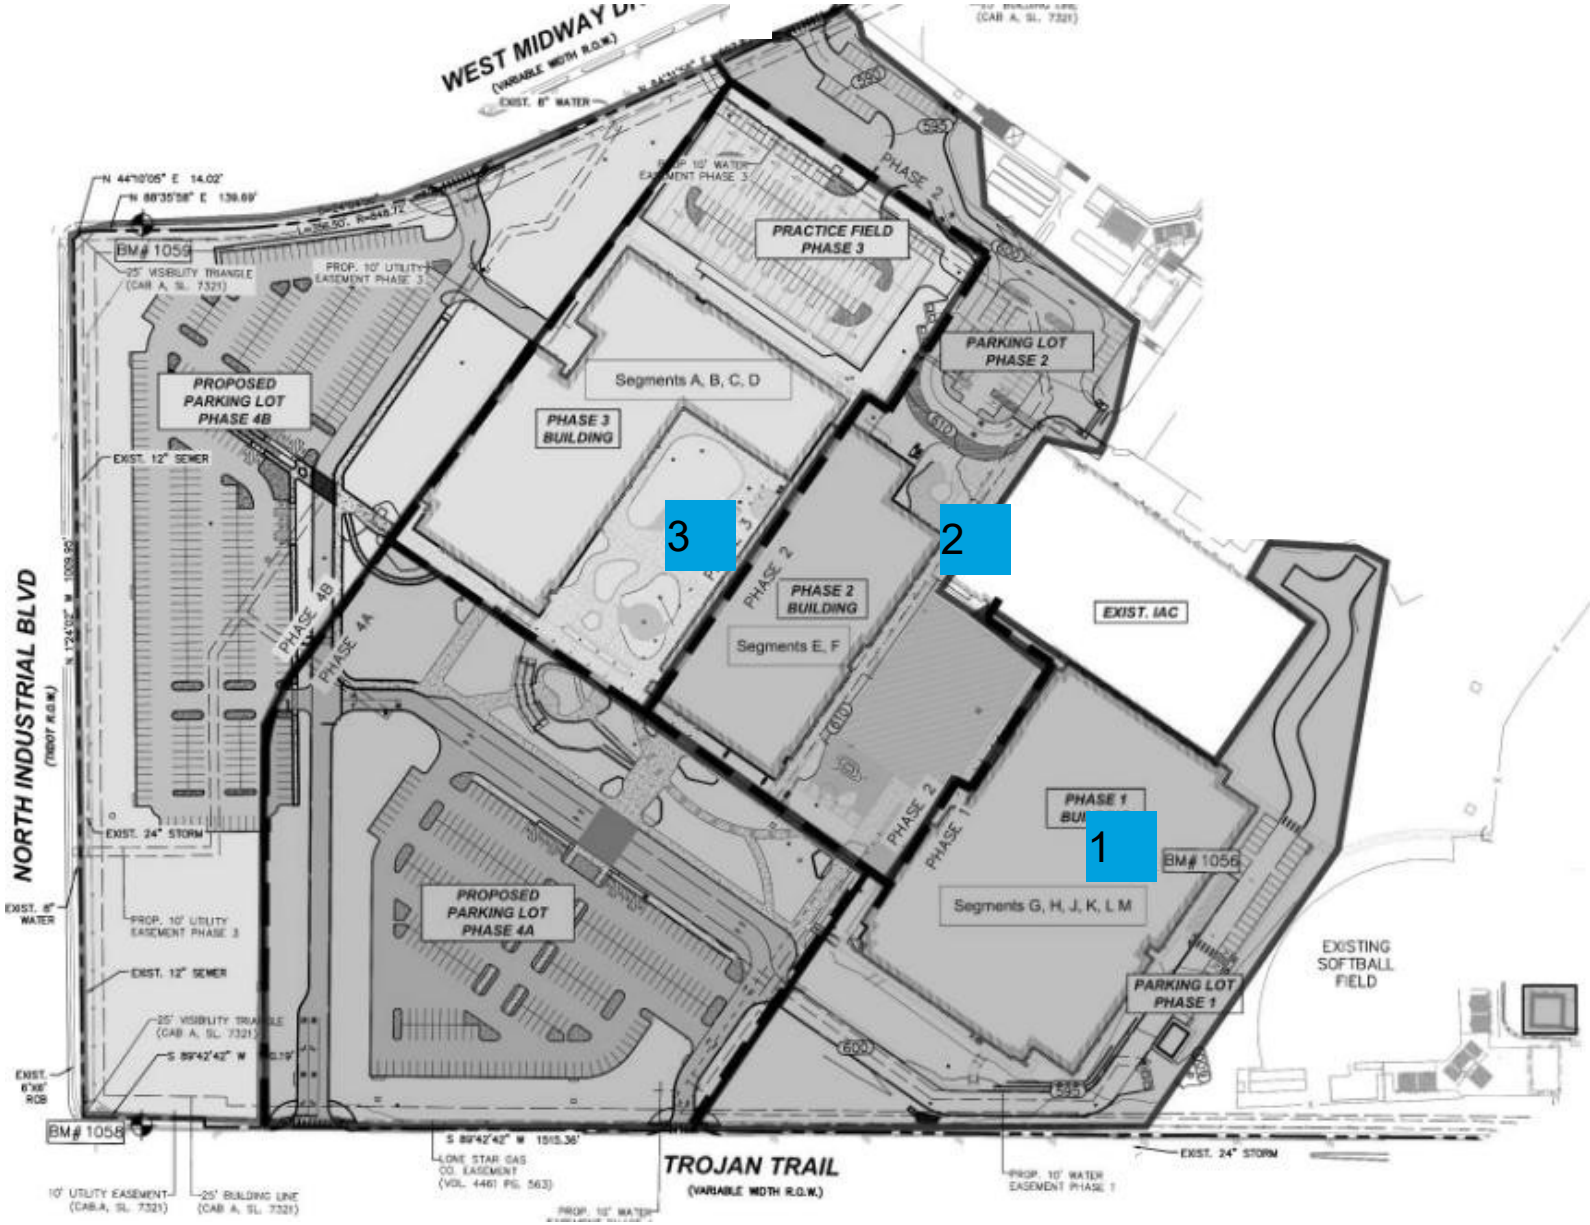

1 **APRIL 2025 – JUNE 2026**
(15 MONTHS)


2 **AUG 2026 – MAY 2028**
(22 MONTHS)

3 **SEP 2028 – FEB 2030**
(18 MONTHS)

1

TRINITY HIGH SCHOOL SCHEDULE

Trinity HS

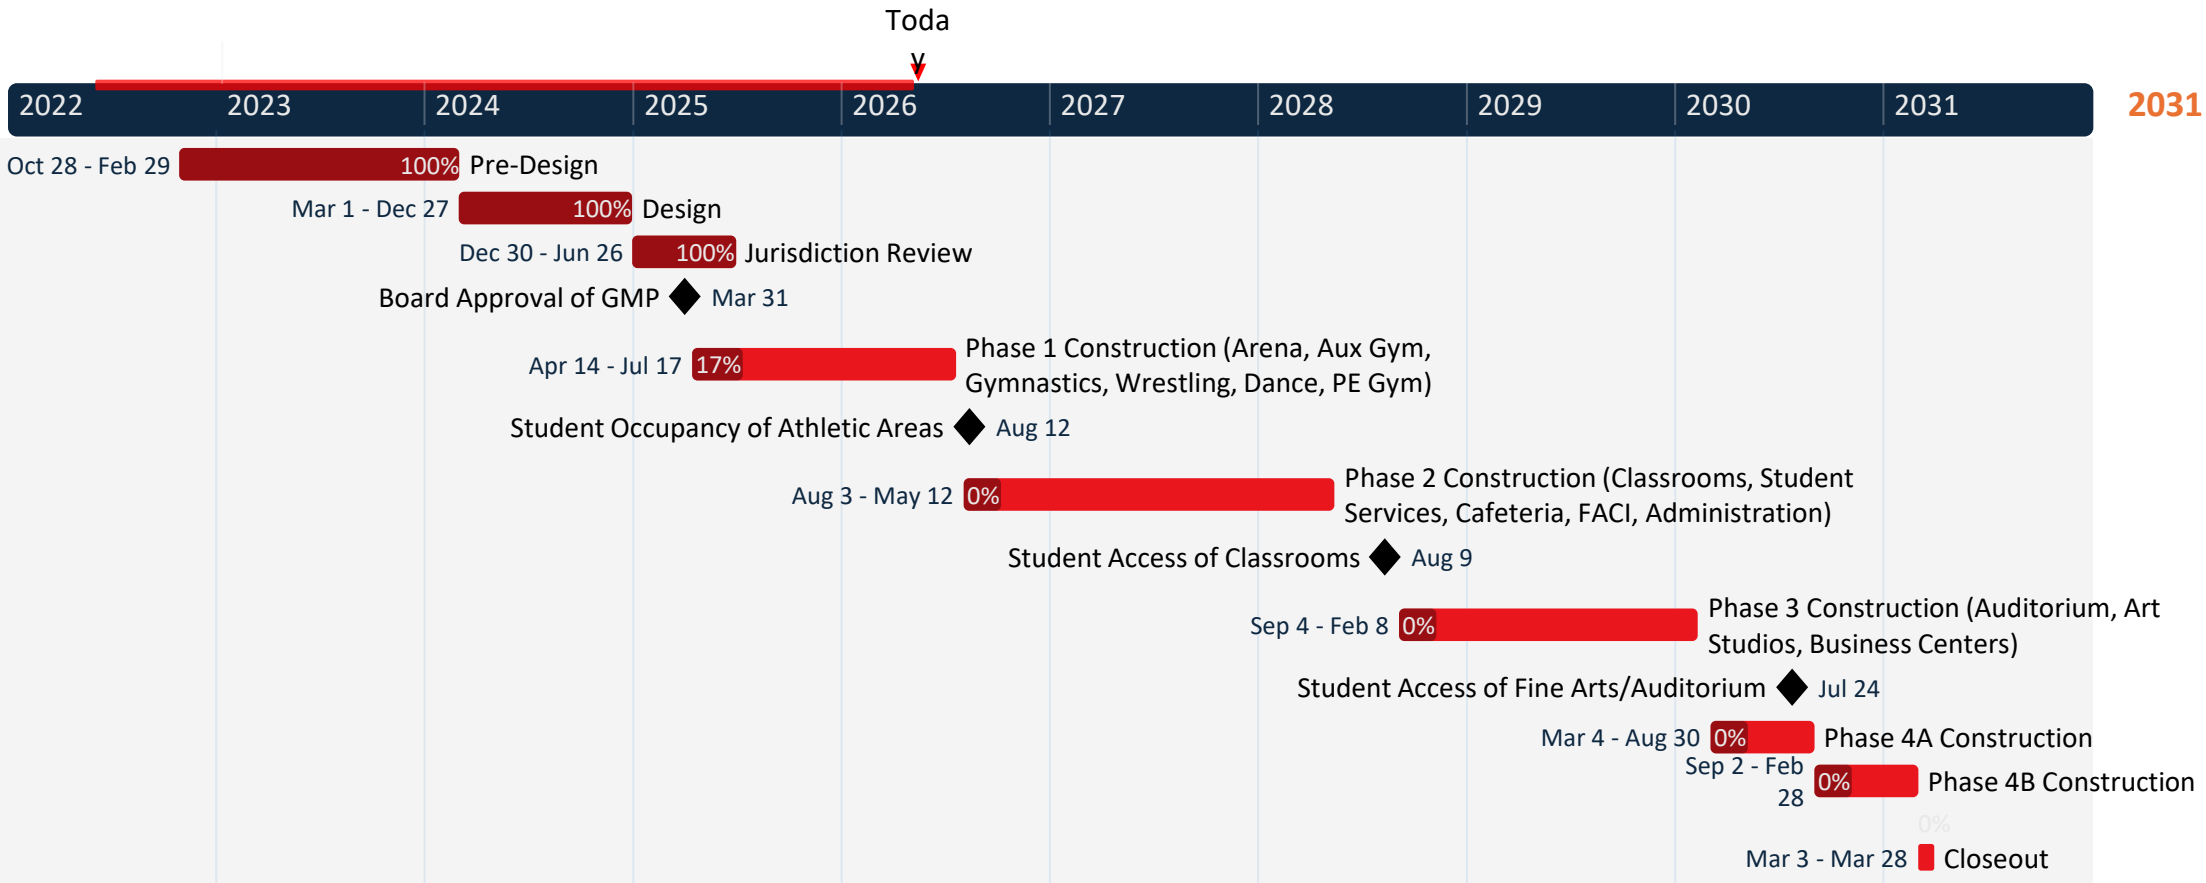

HEBISD

Empowering Today to Excel Tomorrow

#WeAreHEBISD
