
Waller Independent School District

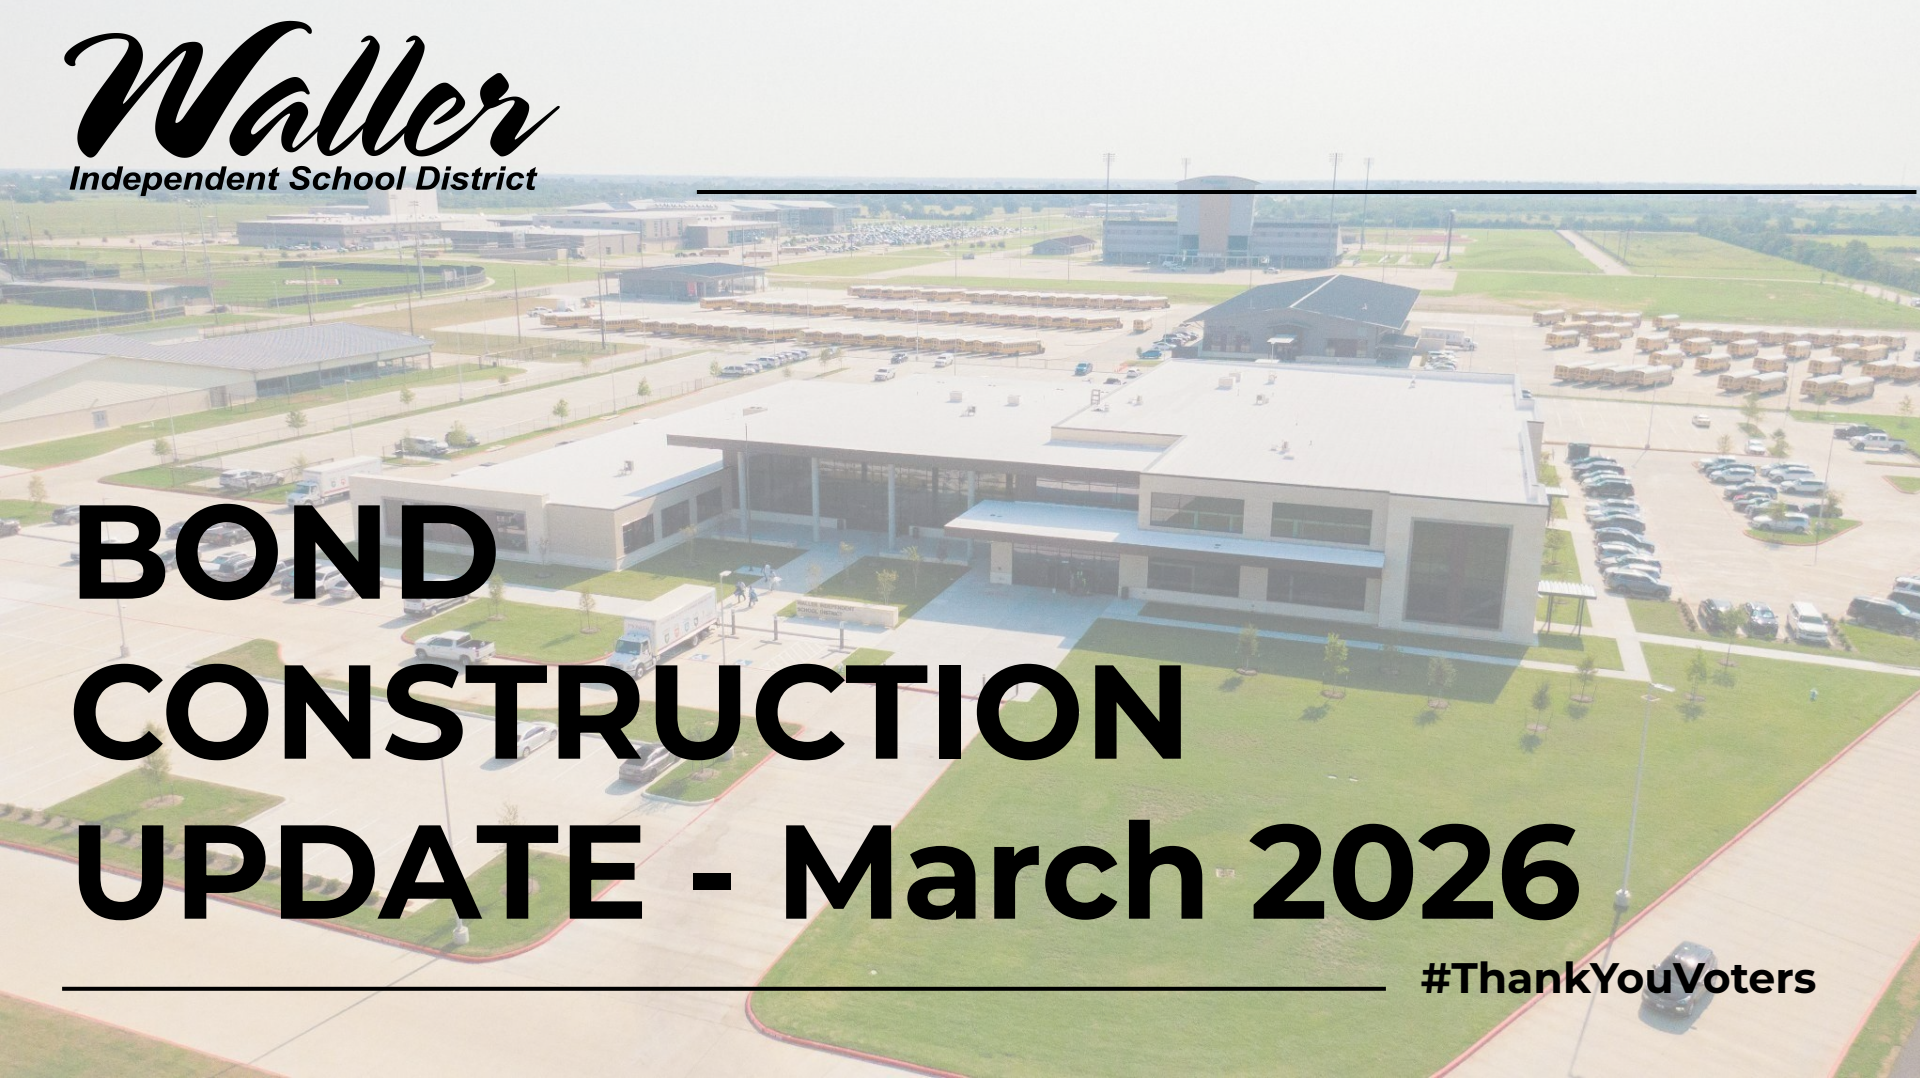

BOND CONSTRUCTION UPDATE - March 2026

#ThankYouVoters

WALLER ISD BOND 22

2022-$363M BOND SUMMARY

- **Lowe Elementary (#6)** $48 million - COMPLETE 2024
- **McReavy Elementary (#7)** $49.1 million - COMPLETE 2024
- **Cure Elementary (#8)** $55.4 million - Open 2025
- **Smith Andrews Ag Science Complex** $13.2 million - Open 2025
- **Education Service Center & Transportation Center** $62.7 million - Open 2025
- **Priority 1 District Facility & HVAC Upgrades**: $75.1 million - in progress; punch list started
- **Land, Buses, Technology, Safety & Security, Bond Management:** $60 million - Ongoing

WALLER ISD CONSTRUCTION

2022 BOND - PRIORITY 1 PROJECTS



WALLER ISD BOND 22

Priority 1 Improvements

Districtwide Improvements

- **Fire Alarm Upgrades**
  - FSE, TES, RRE, & SJH - substantially complete
- **Intrusion/Access Control Upgrades** in progress at all campuses
- **Graphics Design Packages**
  - HES & TES - complete
  - RRE, FSE, & JES - ongoing
- **LED Lighting Upgrades** - approx 90% complete throughout
- **Stage Curtains** - Installed at all elementaries & SJH
- **Punch Lists -** identification and corrections are ongoing

WALLER ISD BOND 22

Priority 1 Improvements

Roberts Road ES

- New flooring throughout the campus installed
- P-lam panels at library & cafeteria are 90% complete
- Doors & hardware are substantially complete
- Graphic installation has begun
- Monument has been installed

Turlington ES

- Front waiting area is complete
- Doors & hardware are substantially complete
- Library portal is 95% complete
- Paint and vinyl walls are complete
- Library HVLV fans are installed

Fields Store ES

- HVAC is complete, clean up and punch list ongoing
- LVT & epoxy flooring is 90% complete
- Canopies are complete
- P-lam panels have been reordered after installation of coiling door
- Doors & hardware are substantially complete
- Room signage is complete
- New light poles are installed
- Monument and site signage installed
- Power washing has been completed on the roof areas near the entry

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvements

Schultz JH

- HVAC is complete with clean up and punch ongoing
- Auditorium sound system has been installed
- Auditorium house lighting has been installed
- Parking lot light poles have been installed

Holleman ES

- Additional LED lighting installed
- Doors & hardware have begun with more being replaced during spring break
- Room signage has been installed

Waller JH Stadium

- Epoxy & weight room flooring complete
- Grandstands complete
- Restroom building complete
- Track Synthetic surface installed and striping is complete
- Parking lot resurfacing and pipe fencing have been completed

Jones ES

- Glass frosting is complete
- Sliding marker boards are complete
- Coiling door has been installed

WALLER ISD BOND 22

Priority 1 Improvements



RRE Cafeteria Graphic

WALLER ISD CONSTRUCTION

Priority 1 Improvements



RRE Gym Graphic

WALLER ISD BOND 22

Priority 1 Improvements





RRE/FSE Monuments

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvements





HES Reception & Hallway Graphic

WALLER ISD CONSTRUCTION

WALLER ISD
BOND 22

Priority 1 Improvements





HES Main Corridor & Cafeteria Graphic

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvements





TES Front Office & Gym Graphic

WALLER ISD CONSTRUCTION

Priority 1 Improvements



TES Main Corridor Graphic

WALLER ISD BOND 22

Priority 1 Improvements





TES Hallway Graphics

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvements






FSE Entry & Gym Graphic

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvements

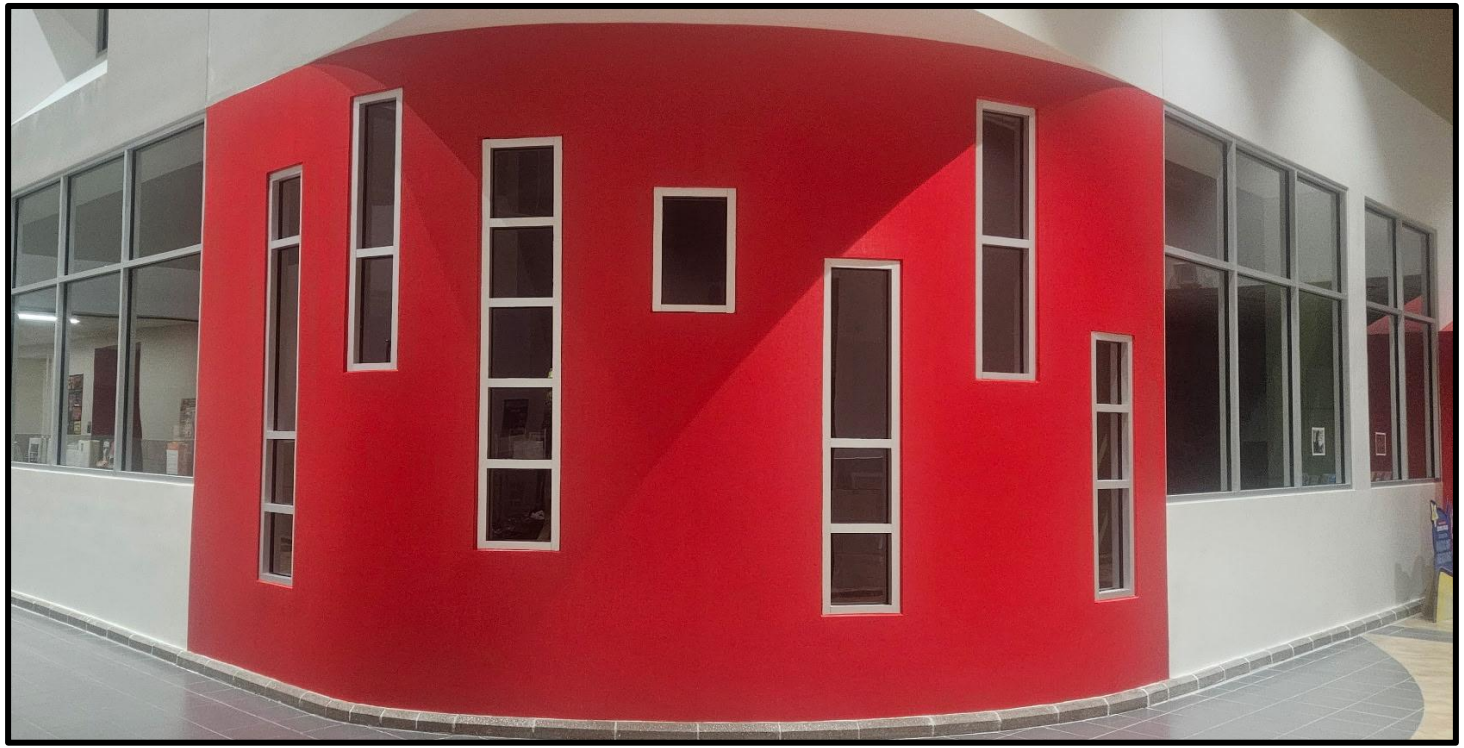

JES Curved Wall Vinyl Covering

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvements



JES Cafeteria Graphic

WALLER ISD CONSTRUCTION

WALLER ISD BOND 22

Priority 1 Improvements



JES Computer Lab Graphic

WALLER ISD CONSTRUCTION


2024 - $702 M BOND

WALLER ISD BOND 24

2024-$363M BOND SUMMARY

- **Warren Ranch High School** - construction started and opening in 2028
- **Johnson Junior High** - construction start and opening TBD
- **Elementary #9** - construction started and opening in 2027
- **Elementary #10** - construction start and opening TBD
- **Land & Buses** - ongoing; 15 buses ordered, 2 buses have been delivered

WALLER ISD BOND 24

WARREN RANCH HIGH SCHOOL

- Main Building pad is 100% complete
- Underground storm and sanitary lines are in progress
- Drilled piers are 99% complete this week on the high school building
- Central Plant construction has started
- Driveways and parking lot paving have started
- Underground plumbing and electrical are in progress
- Grade Beams and slab have started
- Structural Steel deliveries scheduled to start in May
- Opening scheduled in summer 2028

WALLER ISD CONSTRUCTION

WALLER ISD BOND 24

WARREN RANCH HIGH SCHOOL



Site Overview

WALLER ISD CONSTRUCTION

WALLER ISD BOND 24

WARREN RANCH HIGH SCHOOL





Drilled Piers

WALLER ISD CONSTRUCTION

WALLER ISD BOND 24

WARREN RANCH HIGH SCHOOL







Storm & Sanitary Piping

WALLER ISD CONSTRUCTION

WALLER ISD BOND 24

WARREN RANCH HIGH SCHOOL





Underground Plumbing & Electrical

WALLER ISD CONSTRUCTION

ELEMENTARY #9

- GMP contract amendment approved in December
- Campus is in the Cypress Green development east of Hopfe Road
- Contractor has mobilized and construction started
- Opening scheduled in August 2027

WALLER ISD BOND 24

ELEMENTARY #9



Rendering

WALLER ISD CONSTRUCTION

WALLER ISD BOND 24

ELEMENTARY #9





Dirt Work

WALLER ISD CONSTRUCTION


#ThankYouVoters
Waller
Independent School District
