ORANGEBURG COUNTY SCHOOL DISTRICT


BOARD MEETING



ORANGEBURG
COUNTY SCHOOL DISTRICT
We Are **One**

OPERATIONS UPDATE

MAY 12, 2026

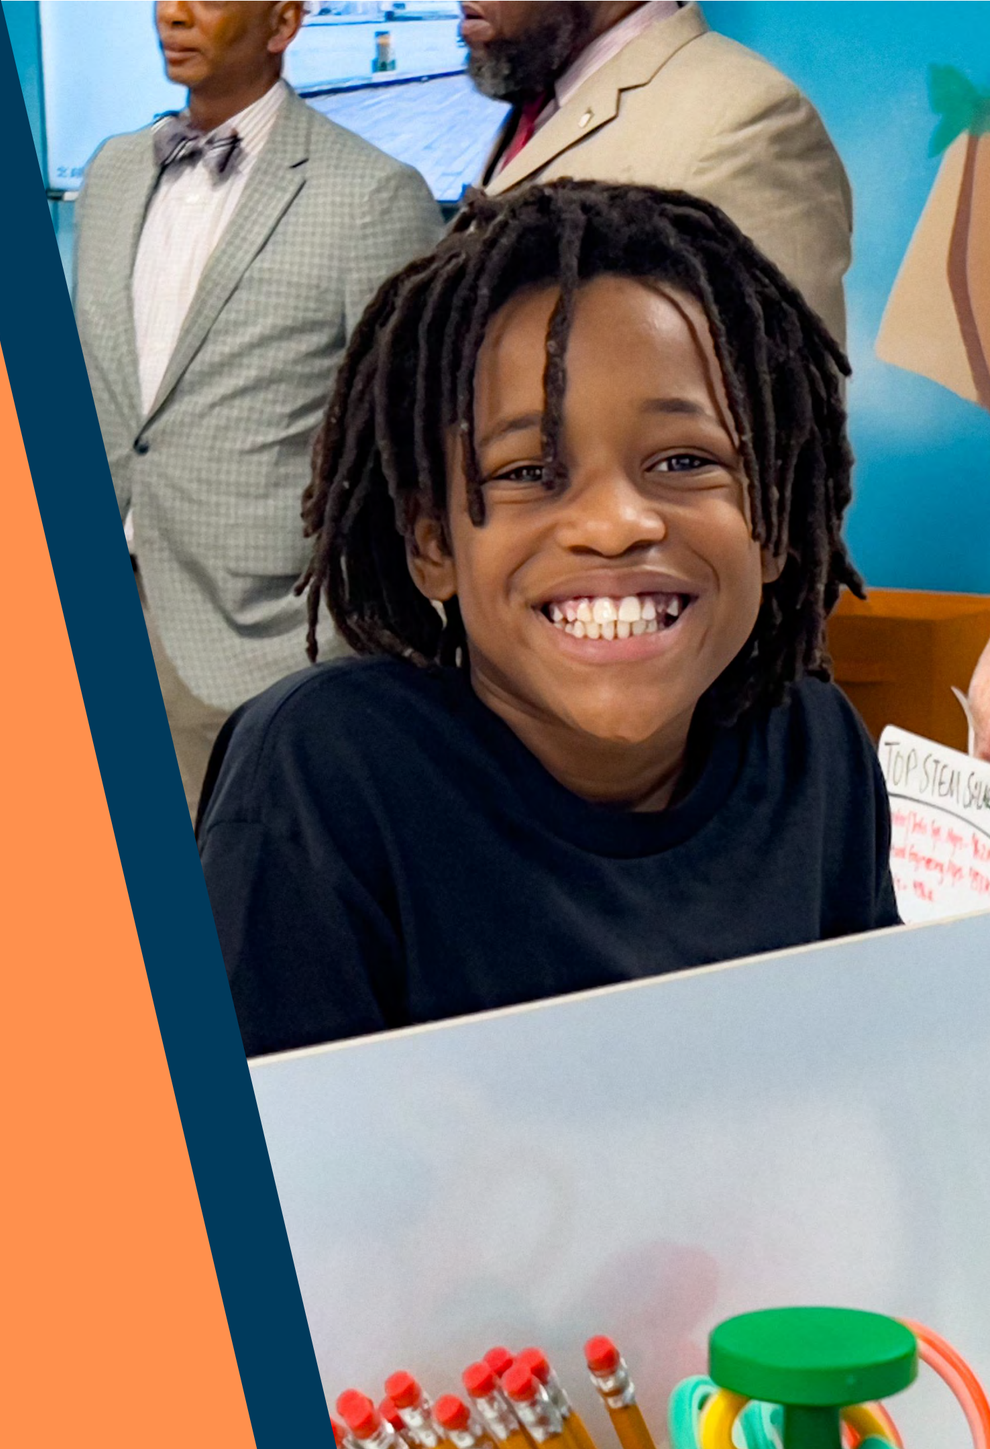

ORANGEBURG-WILKINSON HIGH SCHOOL

ORANGEBURG WILKINSON HIGH SCHOOL

SAFETY	
Incidents to Date	1
First Aids to Date	0
WEATHER	
Working Days	489
Weather Days	56
Activities Delayed	2
MANPOWER	
Number of Trades	13
Average Workers *(per day)*	169
SCHEDULE MILESTONES	
Job Start	5/6/2024
Anticipated Completion	Summer 2026

Top Activities This Week

- Drywall in the auditorium and lobby is nearly complete.
- Plumbing fixtures in area C continue.
- Football field turf began.
- Flooring continues in bathrooms and classrooms.
- Science and regular casework continues.
- Bath partition install continues.
- Ceilings continue in A1/A2.
- Theater rigging continues.
- Elevator installation continues.
- Fencing around the football field and SB/BB area continues.
- Outdoor athletic equipment continued.
- The sound system in the gyms began.

Upcoming Activities

- Tennis courts to begin.
- Cook Rd. work to resume.
- Gym flooring to start.
- Markerboard install to begin.







Week of **April 20, 2026**

ORANGEBURG-WILKINSON HIGH SCHOOL

ORANGEBURG WILKINSON HIGH SCHOOL

SAFETY	
Incidents to Date	1
First Aids to Date	0
WEATHER	
Working Days	494
Weather Days	56
Activities Delayed	2
MANPOWER	
Number of Trades	17
Average Workers *(per day)*	177
SCHEDULE MILESTONES	
Job Start	5/6/2024
Anticipated Completion	Summer 2026







Top Activities This Week

- Gym flooring vapor barrier started and subfloor materials were received.
- Marker board installation is approximately 75% complete.
- Toilet partitions have been installed in the first floor of B & C and began in E2.
- Metal façade panels started at the admin area.
- Areas in A1,A2,E1, and E2 passed overhead inspections. This puts overheads at 85% complete.
- The temporary access at the gym is being closed.
- The artificial turf is in progress at the football field.

Upcoming Activities

- Tennis courts to begin next week.
- Acoustical wall panels deliver 5/1/26.
- Entrance & bus entrance signs will begin.
- Sidewalks will begin at the stadium entrance.

Week of **April 27, 2026**

ROBERT E. HOWARD ELEMENTARY SCHOOL

ROBERT E. HOWARD ELEMENTARY SCHOOL

SAFETY	
Incidents to Date	0
First Aids to Date	0
WEATHER	
Working Days	245
Weather Days	16
Activities Delayed	0
MANPOWER	
Number of Trades	8
Average Workers *(per day)*	97
SCHEDULE MILESTONES	
Job Start	5/27/2025
Contract Completion	12/14/2026







Top Activities This Week

- Continue brick veneer on Building B and began Building A
- Building A hangers, carrier brackets and overhead piping continues
- Began framing gym walls in Building B
- Bar joists/Decking in Building C 2nd floor in progress
- HVAC controls in progress in Building A & B
- Supply and Exhaust ductwork in progress in Buildings A, B, C
- Continue CMU on Building C 2nd floor
- Building A roofing in progress
- Conduit being ran and wire pulled in Building A & B
- Building C 2nd floor outlet boxes in progress
- Transformer power being pulled

Upcoming Activities

- CMU to continue on Building C 2nd floor
- Brick veneer to continue in Buildings A & B
- MEP overhead work to continue on Building C 2nd floor and Building A
- Building A roofing to continue
- Entrances & Windows upcoming

Week of **April 20th, 2026**

ROBERT E. HOWARD ELEMENTARY SCHOOL

ROBERT E. HOWARD ELEMENTARY SCHOOL

SAFETY	
Incidents to Date	0
First Aids to Date	0
WEATHER	
Working Days	250
Weather Days	16
Activities Delayed	0
MANPOWER	
Number of Trades	7
Average Workers *(per day)*	88
SCHEDULE MILESTONES	
Job Start	5/27/2025
Contract Completion	12/14/2026

Top Activities This Week

- Continue brick veneer on Building A & B
- Building A overhead piping continues
- Exterior wall framing in Building B gym area and Rotunda walls in progress
- Decking continuing in Building C 2nd floor
- Started setting the main stairwell in the Rotunda
- HVAC controls in progress in Building A & B
- Supply and Exhaust ductwork in progress in Building A
- Continuing CMU on Building C 2nd floor
- Building A roof completed
- Conduit being ran and wire pulled in Buildings A, B, and C

Upcoming Activities

- CMU to continue on Building C 2nd floor
- Brick veneer to continue on Buildings A & B
- Wall framing in Rotunda & Gym to continue
- Building C roof to begin
- Entrances & Windows upcoming







Week of **April 27th, 2026**
