
ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**Construction**	**307 days**	**6/15/26**	**8/17/27**	
2		**Existing Building - Interior**	**61 days**	**6/15/26**	**9/8/26**	
3		Selective Demolition	10 days	6/15/26	6/26/26	
4		MEP Rough in	25 days	6/29/26	7/31/26	3
5		Set CMU Walls and Tooth Openings	15 days	7/6/26	7/24/26	4SS+5 days
6		Install Scene Shop Mezzanine	15 days	6/29/26	7/17/26	3
7		Life Safety and Make Ready for Occupancy	25 days	7/27/26	8/28/26	5,6
8		Start of School	0 days	9/8/26	9/8/26	7,4
9		**Site Work - Front Addition Entrance Weight Room**	**152 days**	**6/15/26**	**1/12/27**	
10		Mobalize / Site Set up / Make Safe	5 days	6/15/26	6/19/26	
11		Selective Site Demo	10 days	6/22/26	7/3/26	10
12		Excavate/Grade Building Foundations	20 days	7/6/26	7/31/26	11
13		Grade and Place New Parking Lot for School 2026	15 days	8/3/26	8/21/26	12
14		Building Foundations	25 days	7/6/26	8/7/26	12SS
15		Structural Steel Install	20 days	8/10/26	9/4/26	14
16		Roof Decking	15 days	8/24/26	9/11/26	15SS+10 days
17		Masonry Below Grade	10 days	9/7/26	9/18/26	16SS+10 days
18		Backfill/Grade for SOG	10 days	9/16/26	9/29/26	17SS+7 days
19		SOG	10 days	9/30/26	10/13/26	18
20		Exterior Masonry	35 days	10/7/26	11/24/26	19SS+5 days
21		Roofing System Complete	30 days	11/25/26	1/5/27	20
22		Store-Front Door/Window System	20 days	11/25/26	12/22/26	20
23		Install Glazing Complete	15 days	12/23/26	1/12/27	22
24		**Interiors - Front Addition Entrance Weight Room**	**215 days**	**10/7/26**	**8/3/27**	
25		MEP Over Head	35 days	10/7/26	11/24/26	19SS+5 days
26		Interior Masonry	25 days	1/6/27	2/9/27	25SS+5 days,21
27		MEP In Wall	25 days	1/6/27	2/9/27	26SS
28		Painting Prime/First Coat	15 days	2/10/27	3/2/27	25,26
29		Drywall/Ceilings	25 days	3/3/27	4/6/27	28
30		MEP Finishes	30 days	3/3/27	4/13/27	28
31		Tile Bathroom Walls & Floors	20 days	4/7/27	5/4/27	29
32		Finish Floor & Base Install	25 days	4/14/27	5/18/27	29,30
33		Casework/Millwork Install	10 days	5/19/27	6/1/27	32,30
34		Doors and Hardware	10 days	5/5/27	5/18/27	31,23
35		Paint Finish Coat	10 days	6/2/27	6/15/27	33
36		Commissioning	20 days	6/16/27	7/13/27	35,34
37		Punchlist	15 days	7/14/27	8/3/27	36
38		**Exterior Finishes**	**65 days**	**5/3/27**	**7/30/27**	
39		Site Utilities	10 days	5/3/27	5/14/27	23
40		Grading	20 days	5/17/27	6/11/27	39
41		Parking lot/Concrete Walk Demo	10 days	6/14/27	6/25/27	39
42		Site Lighting	10 days	5/24/27	6/4/27	40SS+5 days
43		Exterior Concrete Walks & Stoops	15 days	6/14/27	7/2/27	40,42
44		Concrete /Asphalt install	15 days	6/28/27	7/16/27	43SS+10 days
45		Landscaping	10 days	7/19/27	7/30/27	44
46		**Site Work - CTE Addition**	**123 days**	**6/15/26**	**12/2/26**	
47		Selective Site Demo	5 days	6/15/26	6/19/26	3SS
48		Excavate/Grade Building Foundations	15 days	7/13/26	7/31/26	12SS+5 days
49		Site Utilities	10 days	8/3/26	8/14/26	48
50		Building Foundations	10 days	8/10/26	8/21/26	48SS,14
51		Structural Steel Install	15 days	8/17/26	9/4/26	50SS+5 days
52		Roofing Decking	20 days	8/24/26	9/18/26	51SS+5 days
53		Below Grade Masonry	10 days	8/27/26	9/9/26	52SS+3 days
54		Backfill/Grade for SOG	10 days	9/10/26	9/23/26	53
55		SOG	10 days	9/24/26	10/7/26	54
56		Exterior Masonry	20 days	10/1/26	10/28/26	55SS+5 days
57		Roofing System Complete	25 days	10/29/26	12/2/26	56
58		Store-Front Door/Window System	15 days	10/29/26	11/18/26	56
59		OH Door System	10 days	11/19/26	12/2/26	58
60		**Interiors - CTE Addition**	**229 days**	**10/1/26**	**8/17/27**	
61		MEP Over Head	30 days	10/29/26	12/9/26	56
62		Interior Masonry	25 days	12/3/26	1/6/27	61SS+5 days,57
63		Mezzanine Steel	10 days	1/7/27	1/20/27	62
64		MEP In Wall	25 days	10/1/26	11/4/26	56SS
65		Painting Prime/First Coat	10 days	1/21/27	2/3/27	61,62,63
66		Drywall/Ceilings	15 days	4/7/27	4/27/27	65,29
67		MEP Finishes	15 days	4/14/27	5/4/27	65,30
68		Finish Floor & Base Install	20 days	5/5/27	6/1/27	67
69		Casework/Millwork Install	10 days	6/2/27	6/15/27	67,68
70		Doors and Hardware	10 days	12/3/26	12/16/26	59
71		Paint Finish Coat	10 days	6/16/27	6/29/27	69
72		Commissioning	20 days	6/30/27	7/27/27	71
73		Punchlist	15 days	7/28/27	8/17/27	72

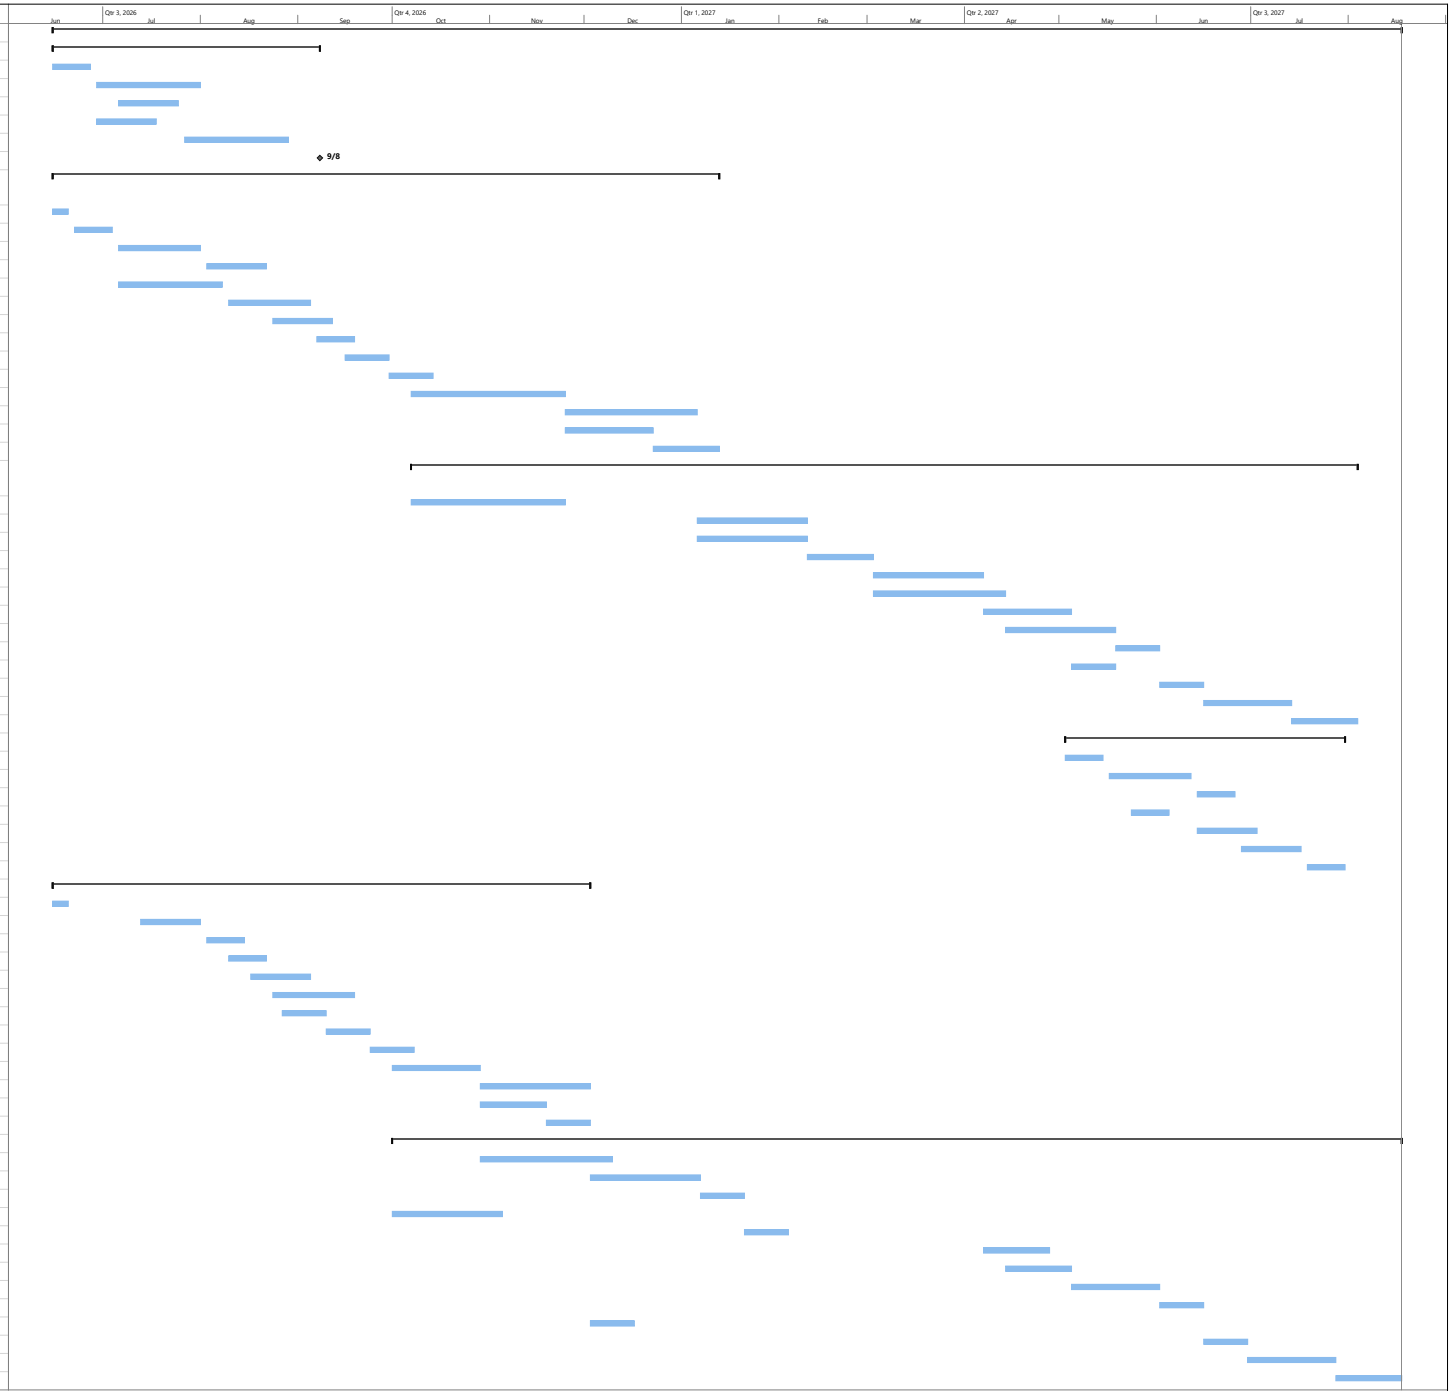

Project: Wylie Bidding Schedule
Date: 5/13/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
