
ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors
1		**Construction**	**310 days**	**8/24/26**	**10/29/27**		
2		**Site Works and Structure**	**185 days**	**8/24/26**	**5/7/27**		
3		Mobilize/ Site Set up	5 days	8/24/26	8/28/26		4
4		Site Prep/Excavation/Grading	25 days	8/31/26	10/2/26	3	6SS+15 days,5SS+5 d
5		Site Utilities	20 days	9/7/26	10/2/26	4SS+5 days	7
6		Foundations	35 days	9/21/26	11/6/26	4SS+15 days	7SS+10 days,8SS+20
7		Backfill	15 days	10/5/26	10/23/26	6SS+10 days,5	9
8		MEP Underground	20 days	10/19/26	11/13/26	6SS+20 days	9
9		Slab on Grade	20 days	11/16/26	12/11/26	8,7	10SS+10 days
10		PEMB Erection	40 days	11/30/26	1/22/27	9SS+10 days	11SS+15 days,18SS+3
11		Masonry Shell + Brick Veneer	60 days	12/21/26	3/12/27	10SS+15 days	12SS+15 days
12		Exterior metal Panels	30 days	1/11/27	2/19/27	11SS+15 days	14,13SS+25 days
13		Roofing System	30 days	2/15/27	3/26/27	12SS+25 days	19
14		Kelwall Install	20 days	2/22/27	3/19/27	12	15
15		Backfill Exterior	20 days	3/22/27	4/16/27	14	16,35
16		Store-Front Door/Window System	15 days	4/19/27	5/7/27	15	
17		**Interiors**	**210 days**	**1/11/27**	**10/29/27**		
18		Slab on Metal Deck	15 days	1/11/27	1/29/27	10SS+30 days	
19		MEP Over Head Rough In	40 days	3/29/27	5/21/27	13	20SS+15 days,21SS+3
20		Masonry Non Bearing	25 days	4/19/27	5/21/27	19SS+15 days	23
21		Painting Prime/First Coat	20 days	5/10/27	6/4/27	19SS+30 days	24,27,23,22SS+5 days
22		Drywall/Ceilings	15 days	5/17/27	6/4/27	21SS+5 days	23
23		Tile Walls & Floors	20 days	6/7/27	7/2/27	21,20,22	27
24		MEP Finishes	30 days	6/7/27	7/16/27	21	25
25		Paint Ceiling Deck	15 days	7/19/27	8/6/27	24	26
26		Sports Netting Install	20 days	8/9/27	9/3/27	25	30
27		Casework/Millwork Install	10 days	7/5/27	7/16/27	21,23	28
28		Other Floor Finish & Base Install	20 days	7/19/27	8/13/27	27	29
29		Doors and Hardware	15 days	8/16/27	9/3/27	28	31
30		Turf Field and Track	25 days	9/6/27	10/8/27	26	33
31		Paint Finish Coat	20 days	9/6/27	10/1/27	29	32
32		Comissioning	10 days	10/4/27	10/15/27	31	33
33		Punch List	10 days	10/18/27	10/29/27	32,30	
34		**Exterior Finishes**	**95 days**	**4/19/27**	**8/27/27**		
35		Grade Hardscape	20 days	4/19/27	5/14/27	15	37,36SS+10 days
36		Landscape Retaining Walls	15 days	5/3/27	5/21/27	35SS+10 days	41
37		Site Concrete	25 days	5/17/27	6/18/27	35	38
38		Pave Parking Lot (Base)	10 days	6/21/27	7/2/27	37	39
39		Site Lighting	15 days	7/5/27	7/23/27	38	40
40		Parkinglot Top Coat and Striping	10 days	7/26/27	8/6/27	39	41
41		Landscaping	15 days	8/9/27	8/27/27	40,36	

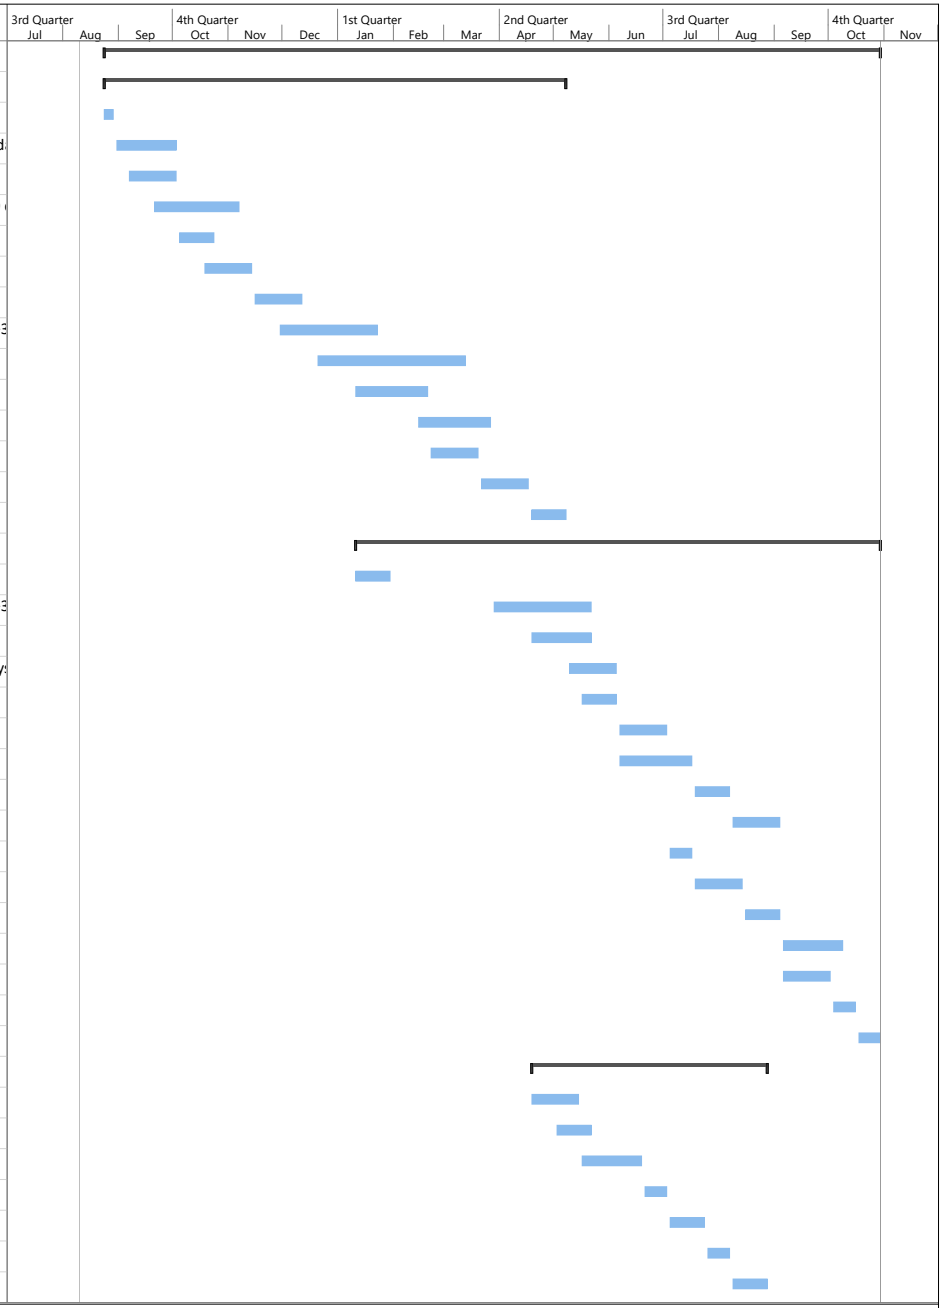

Project: Wylie Bidding Schedule
Date: 5/22/26

Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		
