

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**Bidding**	**96 days**	**Fri 2/6/26**	**Mon 6/22/26**	
8		**Construction**	**227 days**	**Mon 6/15/26**	**Tue 4/27/27**	
9		**Mobalize/Site Setup**	**15 days**	**Mon 6/15/26**	**Fri 7/3/26**	
10		Soil Erosion & Site Demo - Hardscape & Topsoil	5 days	Mon 6/15/26	Fri 6/19/26	
11		Civil Works North of School (C103.2)	10 days	Mon 6/22/26	Fri 7/3/26	10
12		Relocate Existing Electrical Service	5 days	Mon 6/22/26	Fri 6/26/26	10
13		**Existing Building Prep Works**	**22 days**	**Mon 6/29/26**	**Tue 7/28/26**	
14		Selective Demolition	5 days	Mon 6/29/26	Fri 7/3/26	12
15		Plumbing Underground - Area E	2 days	Mon 7/6/26	Tue 7/7/26	14
16		Floor Slab Infills Area E	1 day	Wed 7/8/26	Wed 7/8/26	15
17		Masonry at Portal Frame	4 days	Thu 7/9/26	Tue 7/14/26	16
18		Structural Steel Beams & Decking	3 days	Wed 7/15/26	Fri 7/17/26	17
19		Drywall above Portal Frame & Temp Fire Wall	3 days	Mon 7/20/26	Wed 7/22/26	18
20		Roofing Area E	4 days	Thu 7/23/26	Tue 7/28/26	19
21		**New Structure**	**86 days**	**Thu 7/23/26**	**Thu 11/19/26**	
22		Site Utilities	6 days	Thu 7/23/26	Thu 7/30/26	19,11
23		Excavate Footings	5 days	Fri 7/31/26	Thu 8/6/26	22
24		Pour Footings	10 days	Fri 8/7/26	Thu 8/20/26	23
25		CMU Foundation Walls	7 days	Fri 8/21/26	Mon 8/31/26	24
26		Backfill Foundations	3 days	Tue 9/1/26	Thu 9/3/26	25
27		MEP Underground	4 days	Fri 9/4/26	Wed 9/9/26	26
28		Slab on Grade	5 days	Thu 9/10/26	Wed 9/16/26	27
29		CMU Walls	25 days	Thu 9/17/26	Wed 10/21/26	28
30		Brick Veneer	20 days	Thu 10/8/26	Wed 11/4/26	29FS-10 days
31		Structural Steel	8 days	Thu 10/22/26	Mon 11/2/26	29
32		Glazing	5 days	Thu 11/5/26	Wed 11/11/26	30
33		Roof Covering	13 days	Tue 11/3/26	Thu 11/19/26	31
34		**New Build Interiors**	**113 days**	**Fri 11/20/26**	**Tue 4/27/27**	
35		MEP Rough In	25 days	Fri 11/20/26	Thu 12/24/26	33,32
36		Drywall	20 days	Fri 12/4/26	Thu 12/31/26	35SS+10 days
37		Painting Prime/First Coat	11 days	Mon 12/14/26	Mon 12/28/26	36SS+6 days
38		Ceiling Grid	10 days	Tue 12/29/26	Mon 1/11/27	37
39		MEP Finishes	15 days	Tue 1/12/27	Mon 2/1/27	38,37
40		Casework/Millwork Install	10 days	Tue 1/12/27	Mon 1/25/27	38
41		Tile Bathroom Walls & Floors	12 days	Tue 1/12/27	Wed 1/27/27	38,35
42		Floor Finishes	15 days	Thu 1/28/27	Wed 2/17/27	41
43		Classroom Tout and Cubby System	8 days	Thu 2/18/27	Mon 3/1/27	42
44		Wall Partition Install	8 days	Tue 3/2/27	Thu 3/11/27	43

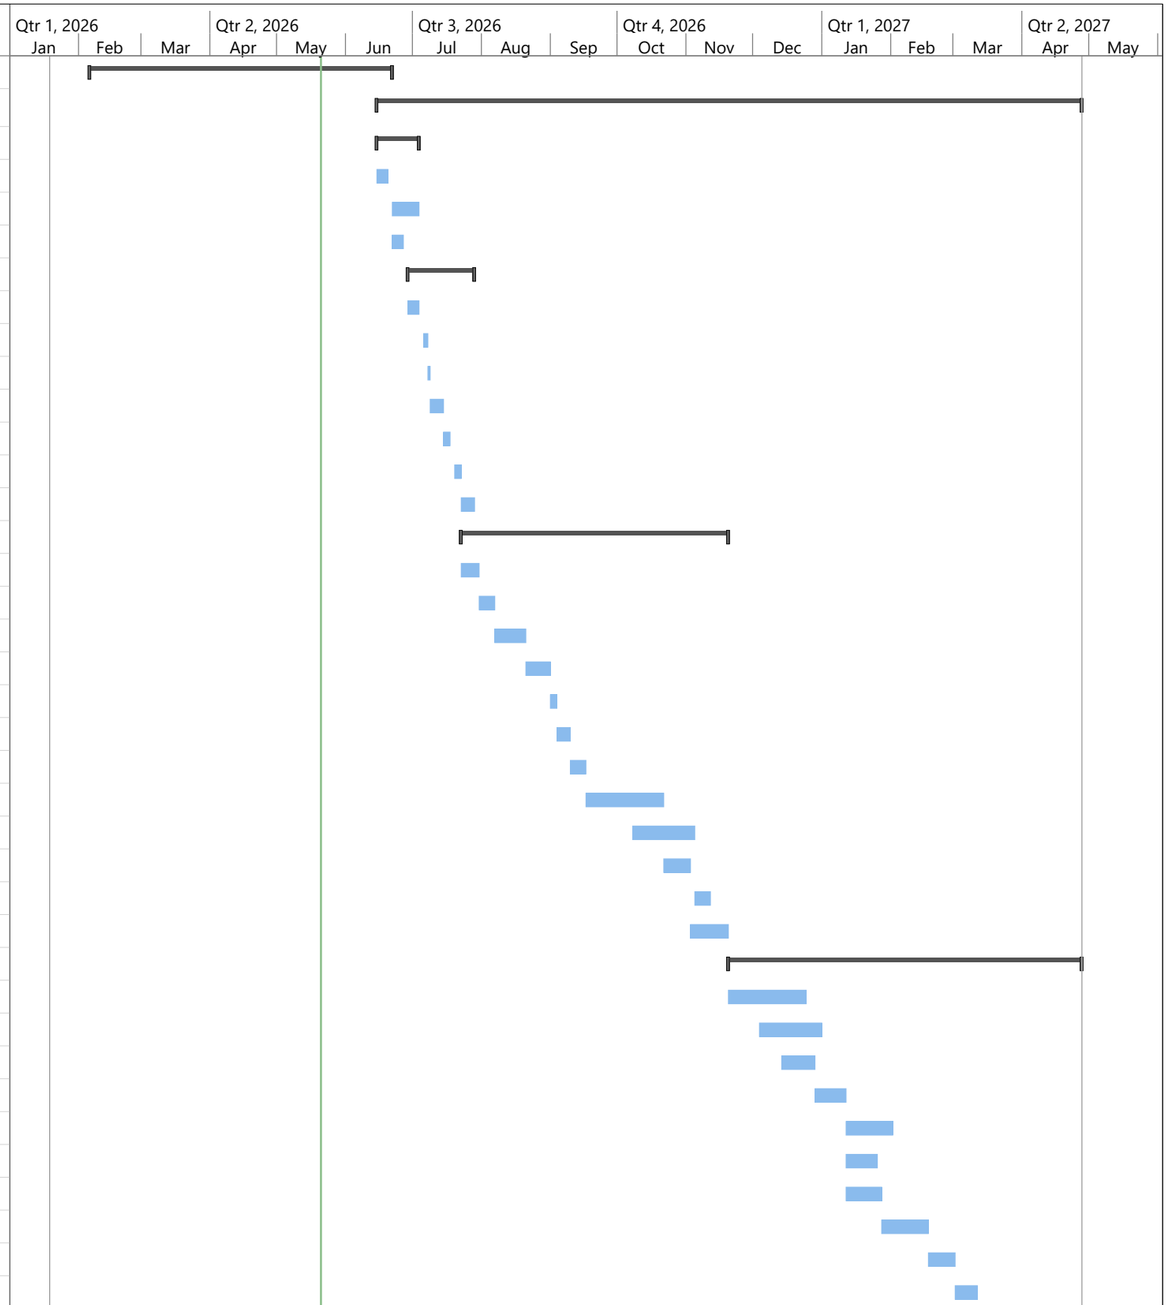

Project: Wylie Bidding Schedule
Date: Thu 5/21/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
45		Metal Locker Install	10 days	Fri 3/12/27	Thu 3/25/27	44
46		Door and Hardware	8 days	Fri 3/26/27	Tue 4/6/27	45
47		Final Paint	10 days	Wed 4/7/27	Tue 4/20/27	46
48		Final Cleaning	5 days	Wed 4/21/27	Tue 4/27/27	47
49		**Exterior Finnishes**	**32 days**	**Mon 3/15/27**	**Tue 4/27/27**	
50		Softball Field Fencing	5 days	Mon 3/15/27	Fri 3/19/27	
51		Softball Field Play Surface	5 days	Mon 3/22/27	Fri 3/26/27	50
52		Fine Grading	3 days	Mon 3/29/27	Wed 3/31/27	51
53		Site Concrete	5 days	Thu 4/1/27	Wed 4/7/27	52
54		Landscaping	5 days	Thu 4/8/27	Wed 4/14/27	53
55		Complete	0 days	Tue 4/27/27	Tue 4/27/27	54,48

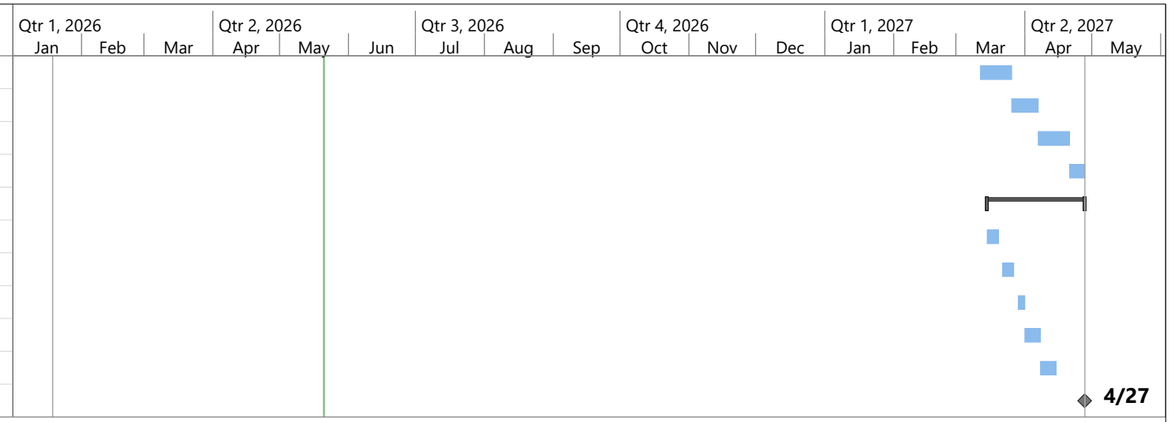

Project: Wylie Bidding Schedule
Date: Thu 5/21/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
