Bond Projects Program Update
Board of Trustees Meeting
June 11, 2026


Measure BB-2018

New Laurelwood Elementary School at the Former Patrick Henry Site

- Turf field under construction.
- Parking lots and drives ready for asphalt.
- PG&E electrical service projected on June 5 (1,122 days from first application for service.).
- New sidewalks on Teal Drive are complete.
- The school is on track to open in August 2026.



View above Teal Drive on June 2, 2026. The office is on the right, classroom wings in the middle, and the multipurpose building on the left. Street curbs and walks are nearly complete.

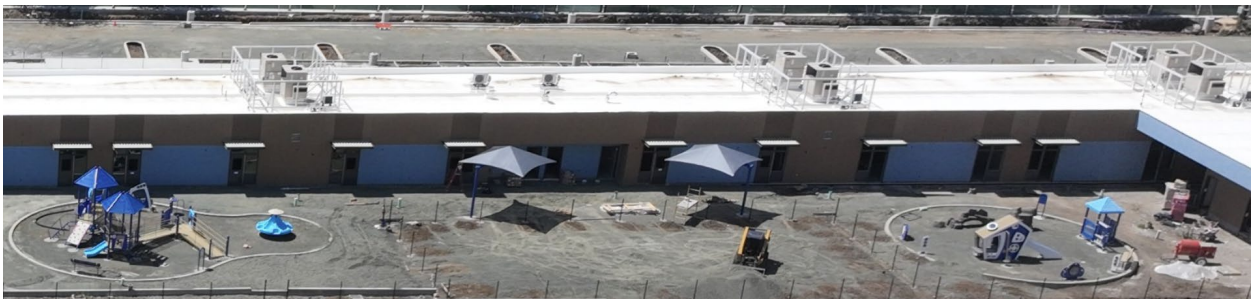

Kindergarten and preschool play areas ready for surfacing and turf.


Campus Modernization Program: Bracher, Briarwood and Westwood Elementary Schools.

Bracher Elementary School.

- The multipurpose building and classroom building steel is erected.
- Attempts to secure clean soil have been successful. The next round of soil export and import will take place this summer.
- The building occupancy is expected in December. Final parking lot construction will be completed in summer 2027.



Aerial view looking northwest on May 20, 2026.

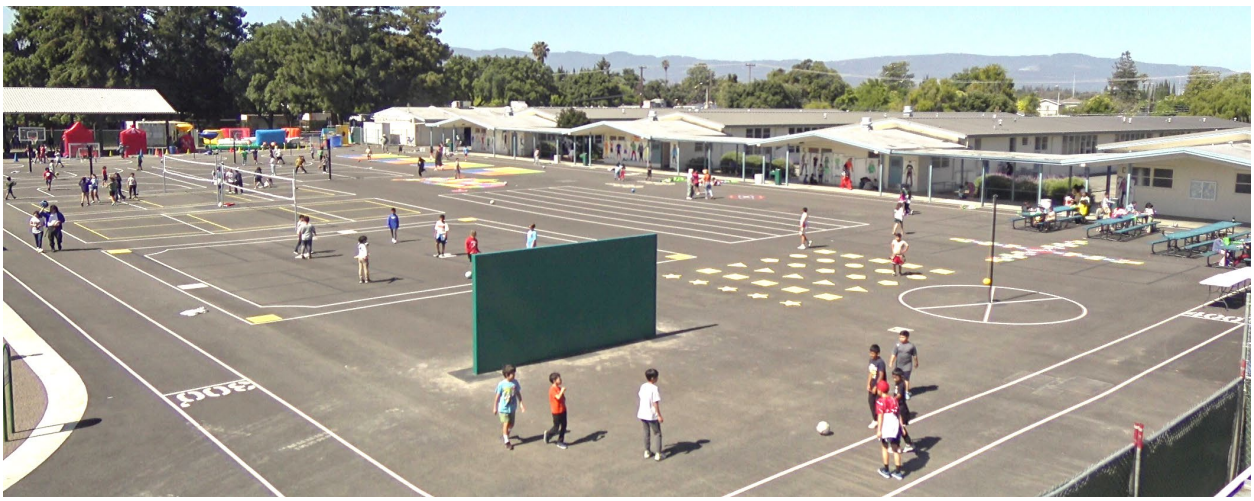

New playground.

Briarwood Elementary School

- Roofing is complete. Solar panel supports in place.
- Interior drywall is underway
- The Verkada security and access systems are being incorporated into the project.
- Work is commencing on the new lots, drives and Townsend Avenue street improvements.



Aerial View looking northeast on May 20, 2026.



View on June 3, 2026. Exterior plaster is underway.

Westwood Elementary School

- Standing seam metal roofing on the office, library, and kindergarten wing will be completed this summer.
- The building occupancy is expected in December.
- The Verkada security and access systems are being integrated into the project.
- Building demolition and parking lot construction will take place in Summer 2027.




Aerial view on May 20, 2026. The kitchen is in the foreground, the covered lunch court is in the middle and the multipurpose room with exterior stage is in the rear.



Covered lunch court looking toward the library. Kitchen is on the right.

New Valley High School Campus / Laurelwood Campus Reconfiguration

- Schematic design is nearly complete
- The space program has been finalized.
- Focus group meetings are continuing with interim and new staff members.
- Structural and mechanical systems have been selected. The structural system will incorporate mass timber components in the roof and floor systems.
- Geotechnical survey work is underway.
- DTSC directed soils sampling results have been obtained. Additional sampling is underway. A preliminary evaluation meeting is being scheduled with DTSC.
- Work to relocate the Wilson High School post-secondary special education program classes from portables to permanent classrooms with take place this summer.

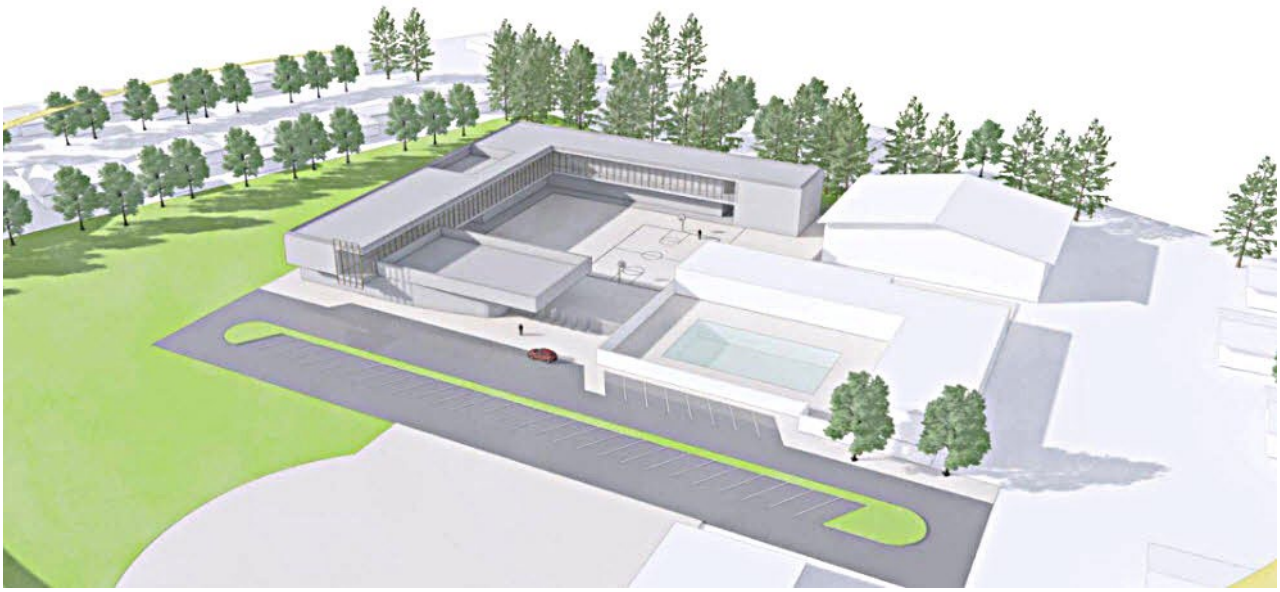

Peterson Middle School Fields

- A new pool of Architects and Engineers has been approved by the Board. The project scope is being determined from the Peterson Campus Master Plan. A request for proposals (RFP) for the project will then be issued.

Santa Clara High School Swimming Pool Modernization


- Ceramic tile is underway.
- Underground obstructions are hampering installation of light poles and shade structures.
- Project completion will extend into the summer.



View towards Main Gymnasium.

Wilcox High School Swimming Pool Modernization

- Work will begin after graduation.
- Demolition will take place over the summer, mitigating disruption from noise and dust
- The work area is bounded by buildings on all sides.
- Because of limited access, the pool modernization work must be substantially completed before the restroom building can commence.

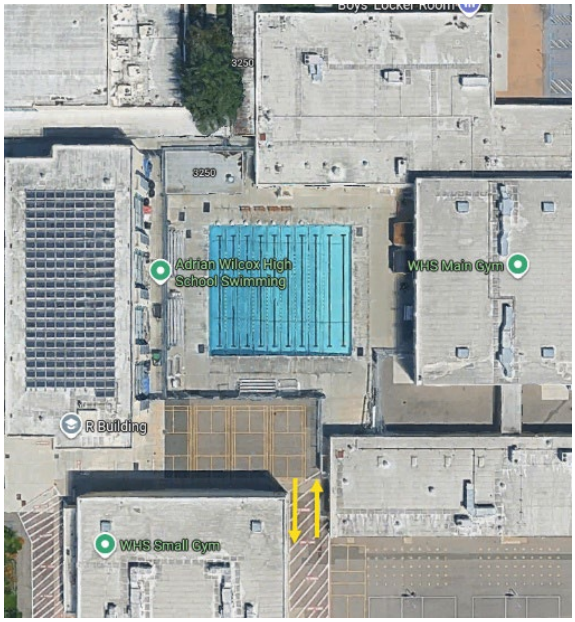

Wilcox Pedestrian Bridge over Calabazas Creek



- Legal counsel has been retained to assist with negotiations with the Water District on the agreements for the new and existing bridges. The draft agreement requires an annual fee of $27,900.00 per year, increasing 4% each year, for school use of the existing and new bridges.
- The Santa Clara Valley Water District response has been slow, fragmented, and inconsistent. Efforts to obtain a permit for a replacement bridge are entering a third year.
- The DSA bridge permit will expire next year. A new permit submittal will be required under a new building code edition.

[End]
