Foster School Construction Update

May 2026



EVANSTON/SKOKIE
SCHOOL DISTRICT 65

Every Child, Every Day, Whatever it Takes

Foster School Construction Update

Completed	Current	Next Up
• Gym bleachers • Ceramic floor & wall wainscot tile installation • LVT tile flooring and stair treads • Drains for playground & planter beds • Final cleaning for the 2nd floor • Kitchen equipment install	• Form work for curbs and sidewalks • Playfield and running track • Playground • Basketball court • Plantings and seeding • Parking Lot • Audio Visual Installation • Security Cameras	• Gym floor Lines • Fencing • Asphalt for Parking Lot • EV Station • Classroom Furniture • Commissioning • Certificate of Occupancy • Ribbon Cutting

Foster School Construction Update



Simpson Front Entrance

Sidewalk and front entry concrete are completed and the grass, trees and shrubs have been planted.



Ashland Entrance

Concrete steps and ramp have been poured with the drop-off lane still awaiting asphalt.

May 2026

Foster School Construction Update





Playground and Playfield on South Side of Building

Playground installation ongoing.

May 2026

Foster School Construction Update





Parking Lot

Curbs and lighting have been installed and asphalt and parking striping are next.

The Corner of Simpson and Dewey


The new school sign matches other D65 schools.

Foster School Construction Update



Gym

Bleachers and baskets are installed and new flooring awaits the striping for basketball and volleyball.

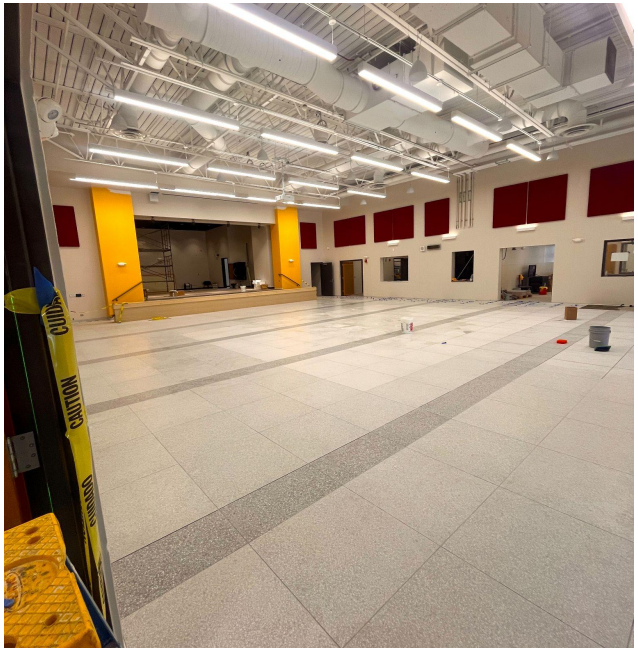

Cafetorium

Ceramic tile flooring is finished and the stage awaits the curtain installation.

May 2026

Financial Update

Remaining Construction Work: $3,508,935 (9.6%)

• General Trades	9%	• Kitchen Equipment	22%
• Paint	31%	• Playground	100%
• Plumbing	8%	• Sidewalks/Curbs	66%
• Electrical	1%	• Landscaping	100%
• Flooring	7%	• Fencing	100%
• Fire Prevention Systems	11%	• Site Work	46%
• HVAC/Mechanical	10%	• Mixed Metals	100%
• Roofing	7%	• FF&E Install/Moving	100%
• Windows	8%	• Safe Walk Routes	100%

100% Completed Work: Site Clearing, Ground Improvements, Precast Walls, Building Concrete, Steel

Foster School Monthly Budget Update -- May 2026

