
Paul Laurence Dunbar High School – Roof Replacement


- **Completed/Work in Progress:**
  - Area A Mod-Bit work in progress – crew of 9 workers plus Tremco rep on site.
  - Crew is working on 19 sq. section of tear-off. Edges are sealed off for weather protection during progress.
    - Crew completed approximately 18 sq. up to base sheet installation the day prior.
  - Demolished materials are being hauled off site.
  - Tremco representative has been on site working with installation team.
  - Substantial amounts of material are placed on roof and ready for installation.
  - Field condition of existing deck and slope is good in area uncovered thus far.

- **Upcoming Look Ahead:**
  - Continue work in Area A.
  - Shop Drawing coordination with GC and skylight installer.
  - Temporary detail coordination with prefinished metal roofing representative and GC.
  - Active construction is expected to continue as weather permits.

Paul Laurence Dunbar High School – Roof Replacement

Installation progress – Area ‘A’

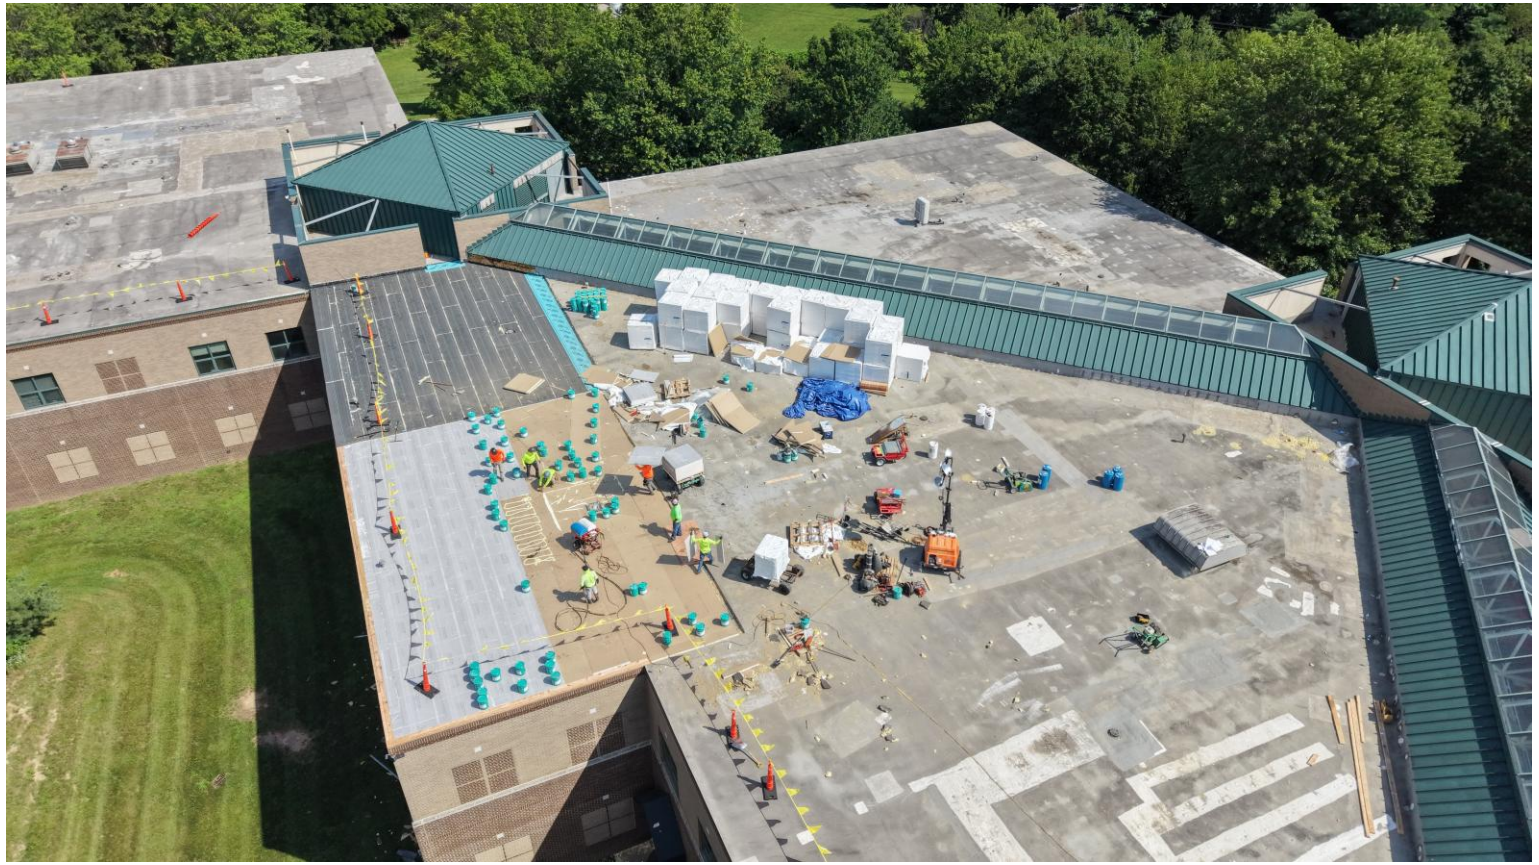


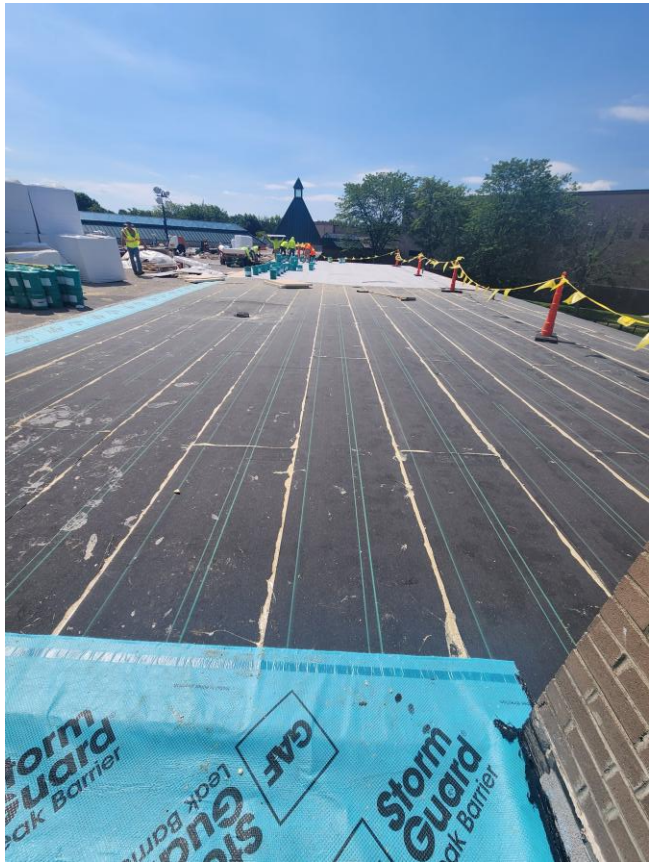

Paul Laurence Dunbar High School – Roof Replacement

New insulation ready to be installed and old insulation ready for disposal.



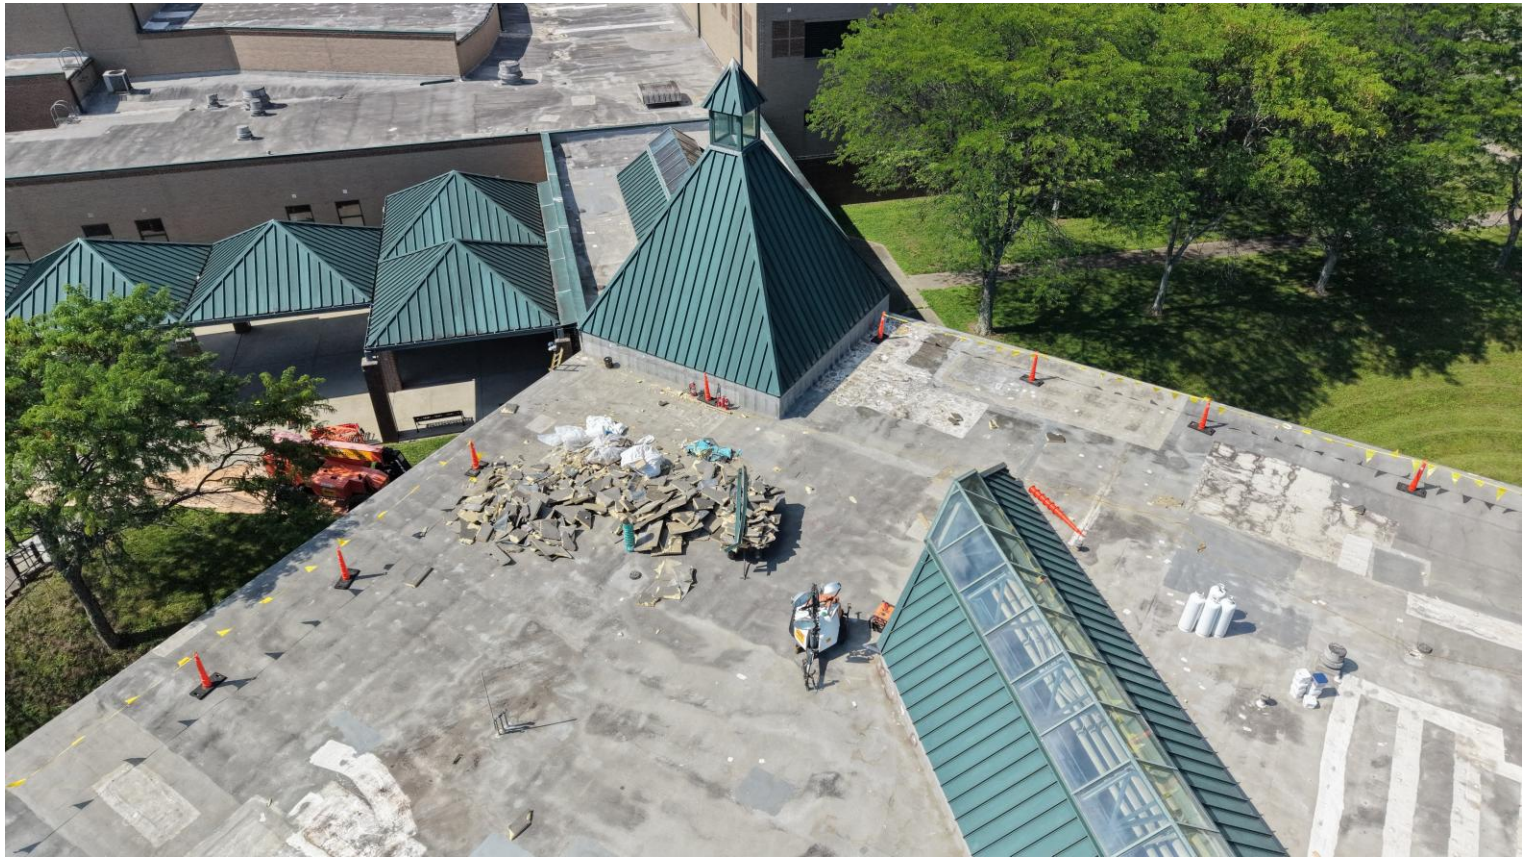

Paul Laurence Dunbar High School – Roof Replacement

Overall work area, detail of cover board installation.





Paul Laurence Dunbar High School – Turf & Track Replacement

- **Completed/Work in Progress:**
  - Demolition work in progress.
  - Progress has been slow due to recent weather.

- **Upcoming Look Ahead:**
  - Demo should be complete of all items.
  - Materials will continue to arrive to the site.
  - New fencing to begin installation in lawn areas.
  - Milling of the asphalt track to begin.
  - Grade work for new walks to begin.

Paul Laurence Dunbar High School – Turf & Track Replacement

Drone Shot



Paul Laurence Dunbar High School – Turf & Track Replacement

Drone Shot

