
Northwest
INDEPENDENT SCHOOL DISTRICT

FACILITIES, PLANNING & CONSTRUCTION UPDATE


June 22, 2026




The 2026-2027 Delivery Roadmap

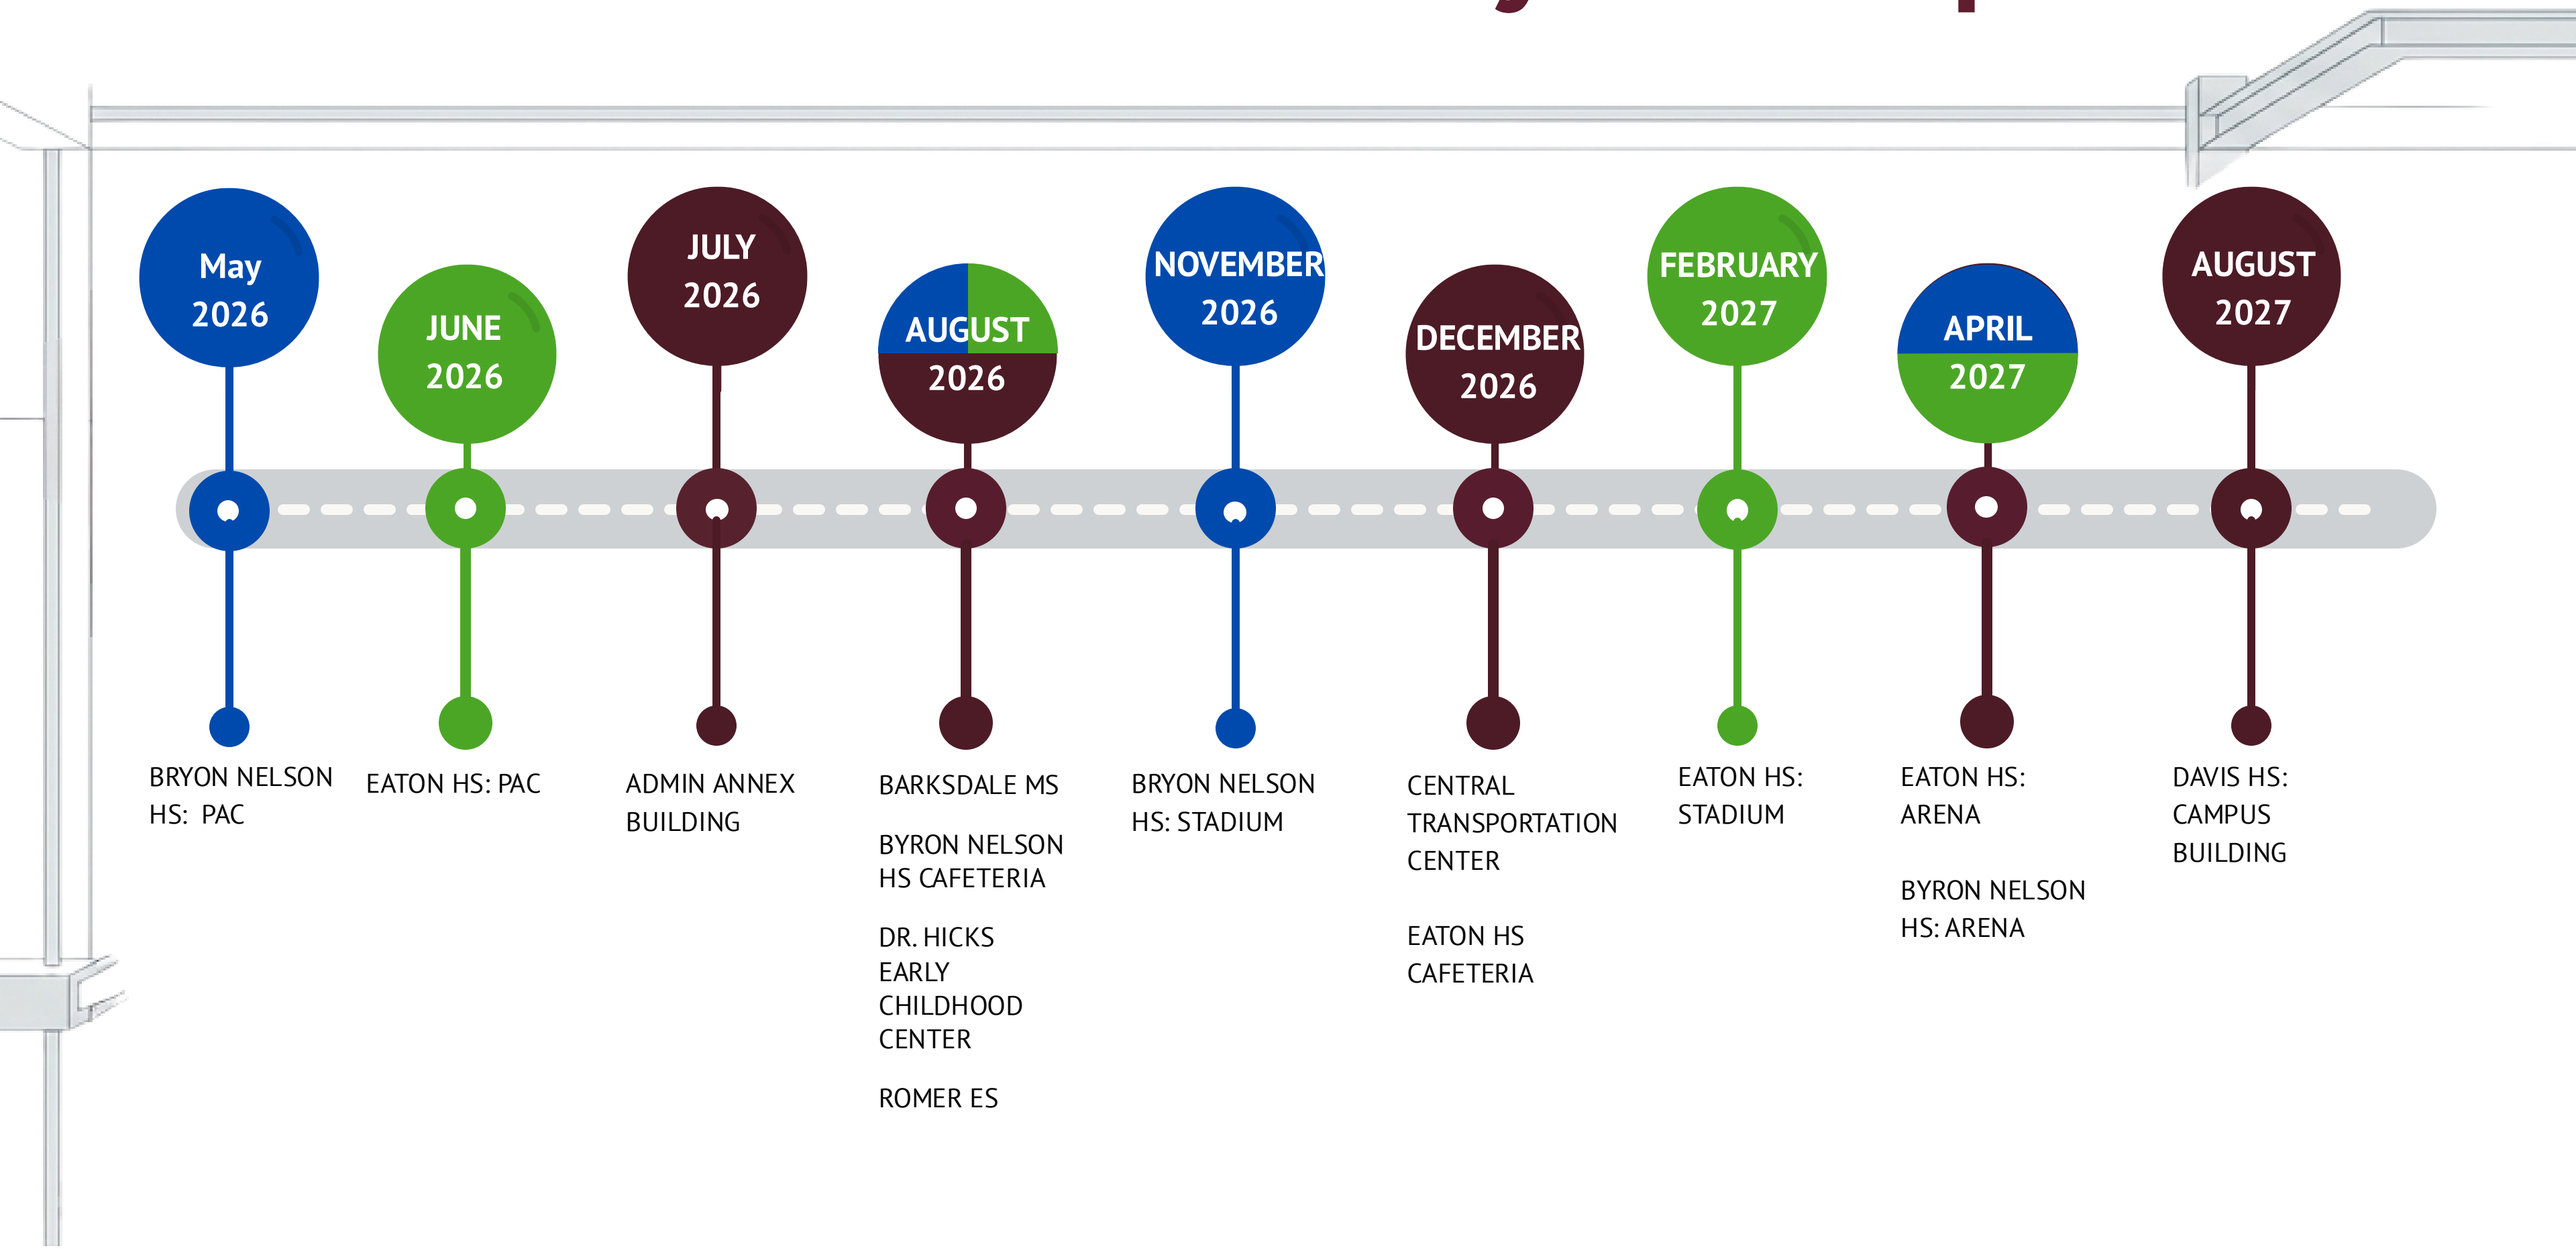


District Portfolio Status Dashboard

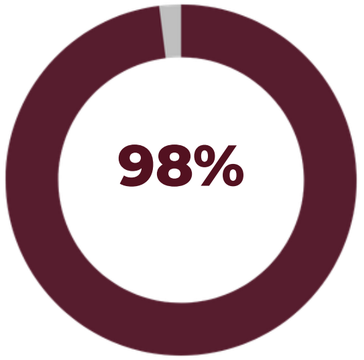


Barksdale Middle School

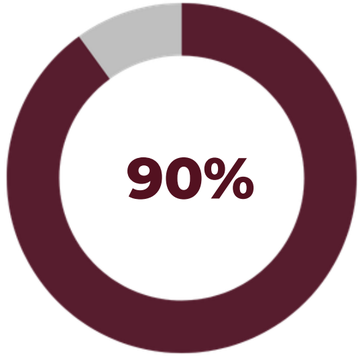


Dr. Romer Elementary School

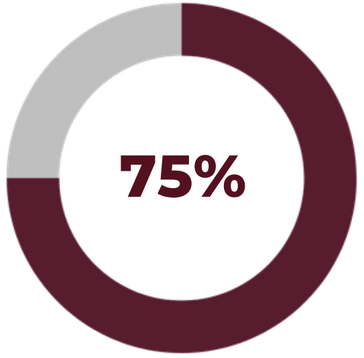


Dr. Hicks Early Childhood Center

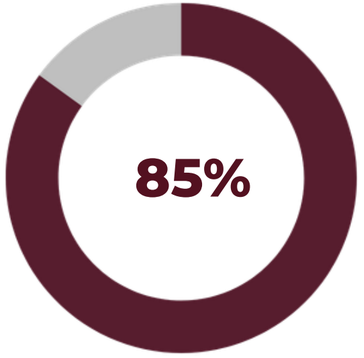


NISD Facilities




Central Transportation Relocation




Davis High School

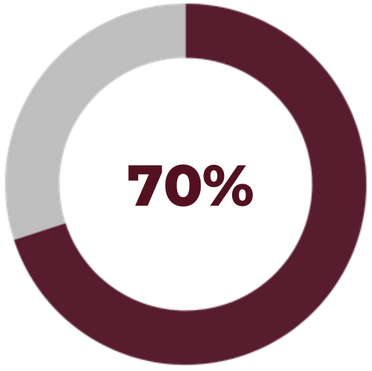


Byron Nelson HS Stadium




Byron Nelson HS Cafeteria

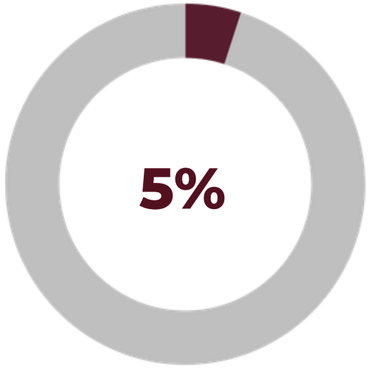


Byron Nelson HS Arena/Welding

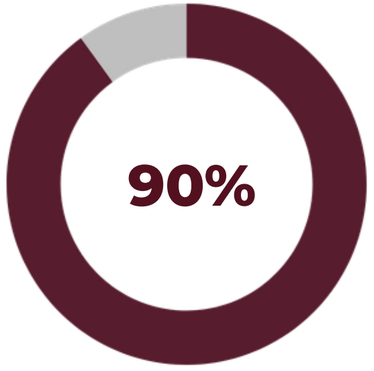

Eaton HS PAC

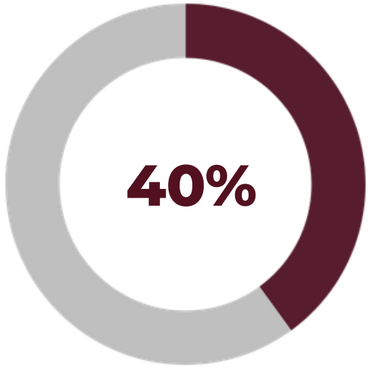

Eaton HS Stadium



Eaton HS Cafeteria/Arena/ Welding

Barksdale Middle School

98% Complete | Opening: August 2026



Barksdale Middle School

98% Complete | Opening: August 2026





Barksdale Middle School

98% Complete | Opening: August 2026






Barksdale Middle School

98% Complete | Opening: August 2026



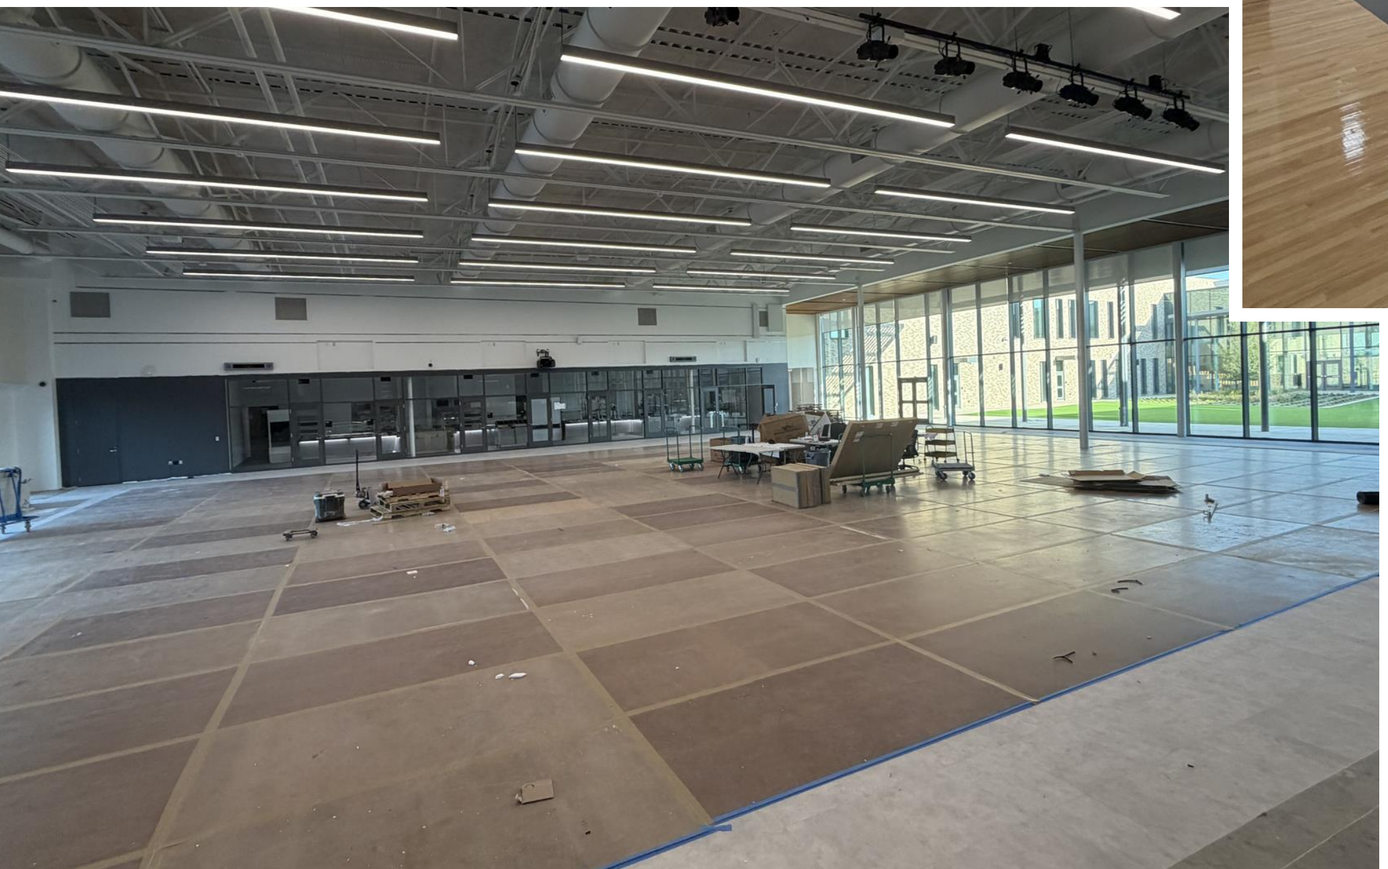

Barksdale Middle School

98% Complete | Opening: August 2026





Dr. Romer Elementary School

90% Complete | Opening: August 2026



Dr. Romer Elementary School

90% Complete | Opening: August 2026







Dr. Romer Elementary School

90% Complete
Opening: August 2026




Dr. Romer Elementary School

90% Complete | Opening: August 2026





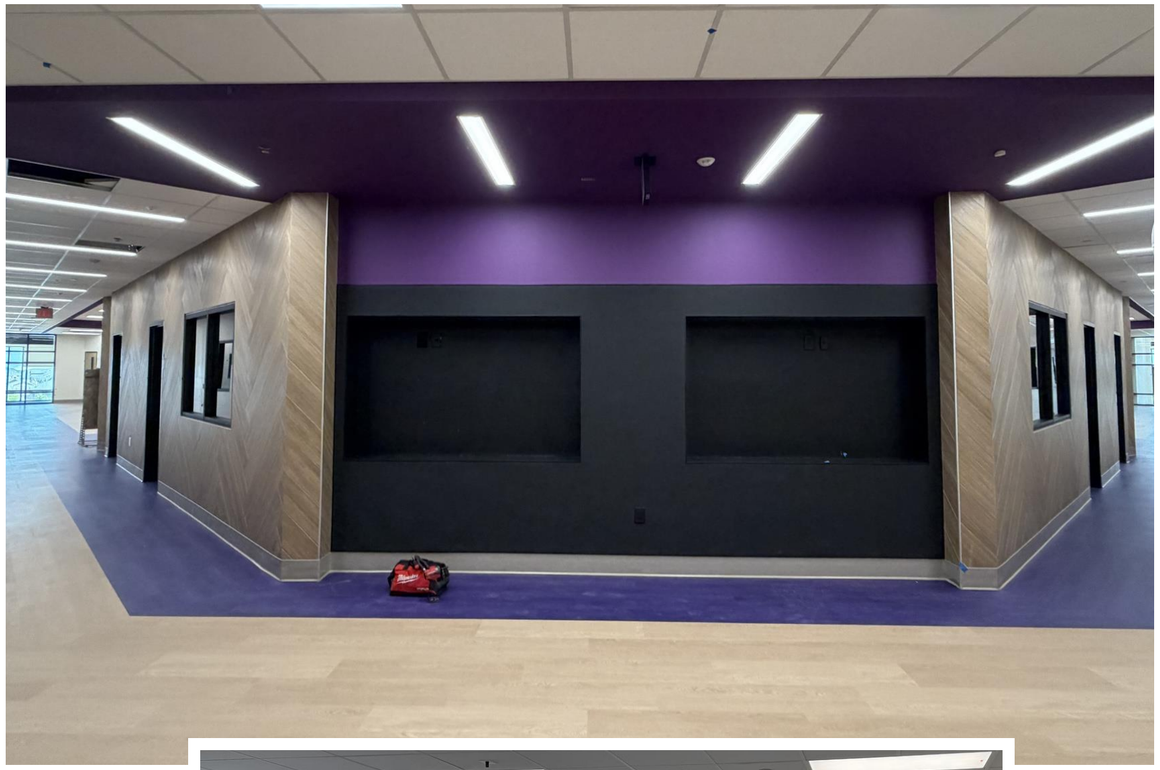



Dr. Romer Elementary School

90% Complete | Opening: August 2026





Dr. Hicks Early Childhood Center

75% Complete | Opening: August 2026



Dr. Hicks Early Childhood Center

75% Complete | Opening: August 2026





Dr. Hicks Early Childhood Center

75% Complete | Opening: August 2026







Dr. Hicks Early Childhood Center

75% Complete | Opening: August 2026





NISD Facilities Building


85% Complete | Opening: August 2026





NISD Facilities Building


85% Complete | Opening: August 2026

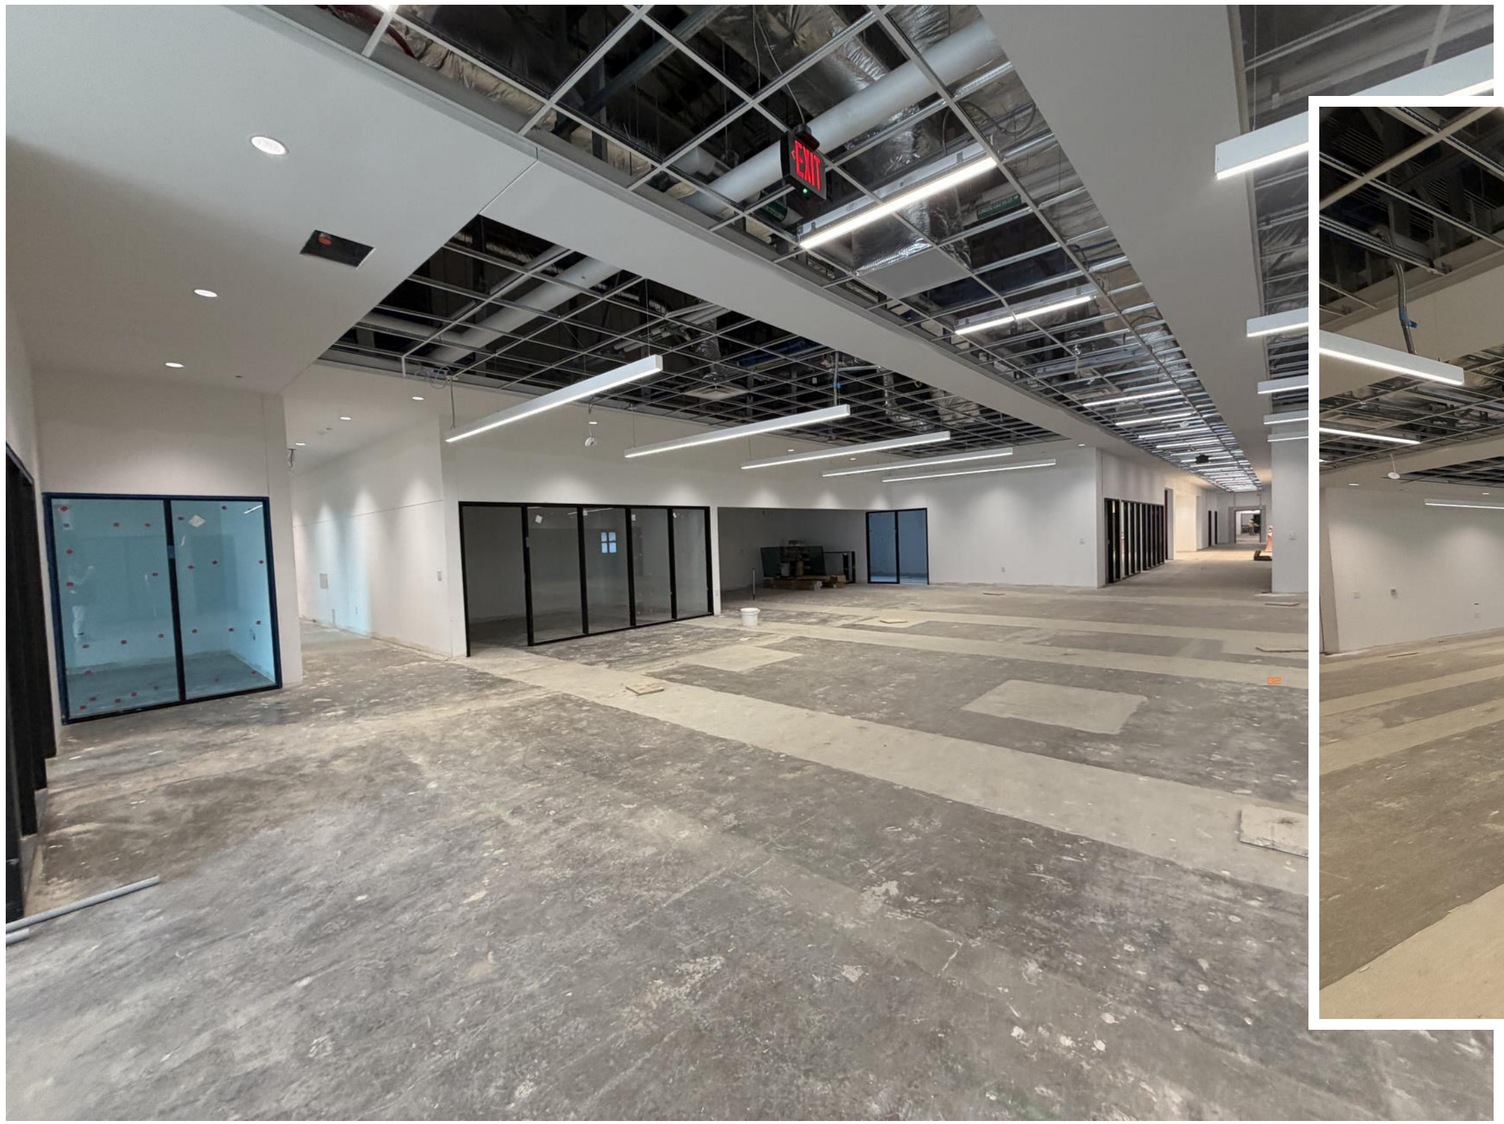



NISD Facilities Building

85% Complete | Opening: August 2026

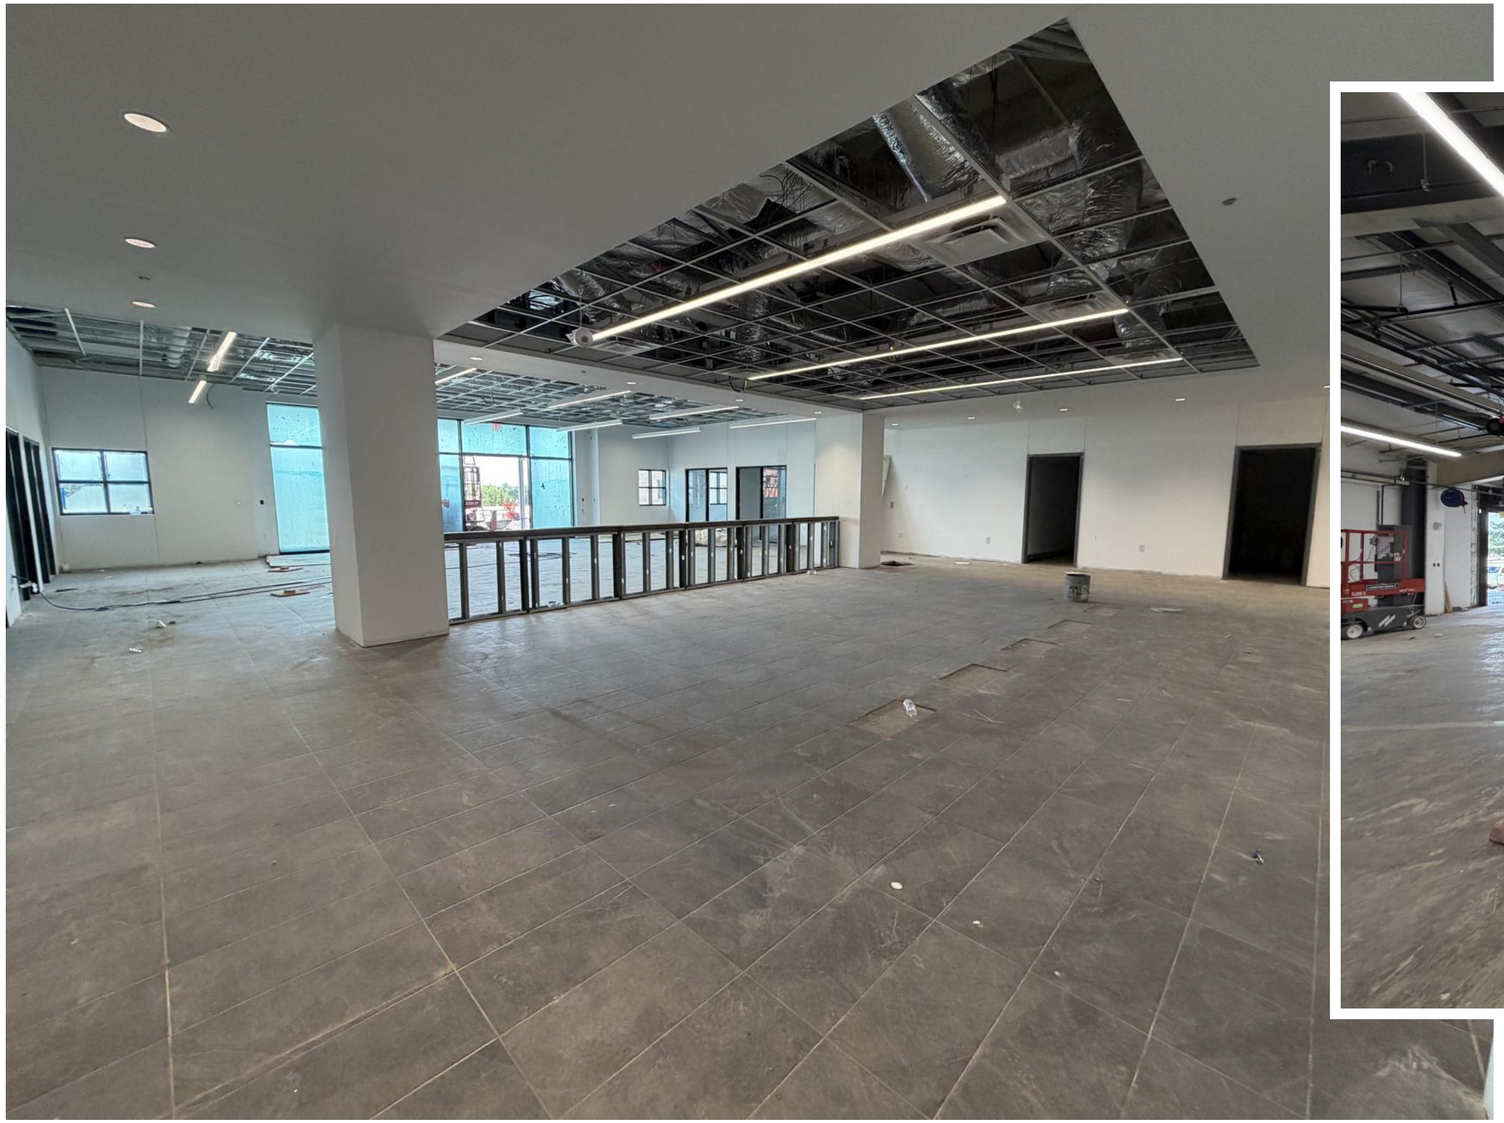



Byron Nelson High School - Aerial View



Byron Nelson HS: Stadium

70% Complete | Target Delivery: November 2026





Byron Nelson HS: Stadium

70% Complete | Target Delivery: November 2026






Byron Nelson HS: Cafeteria

65% Complete | Target Delivery: August 2026



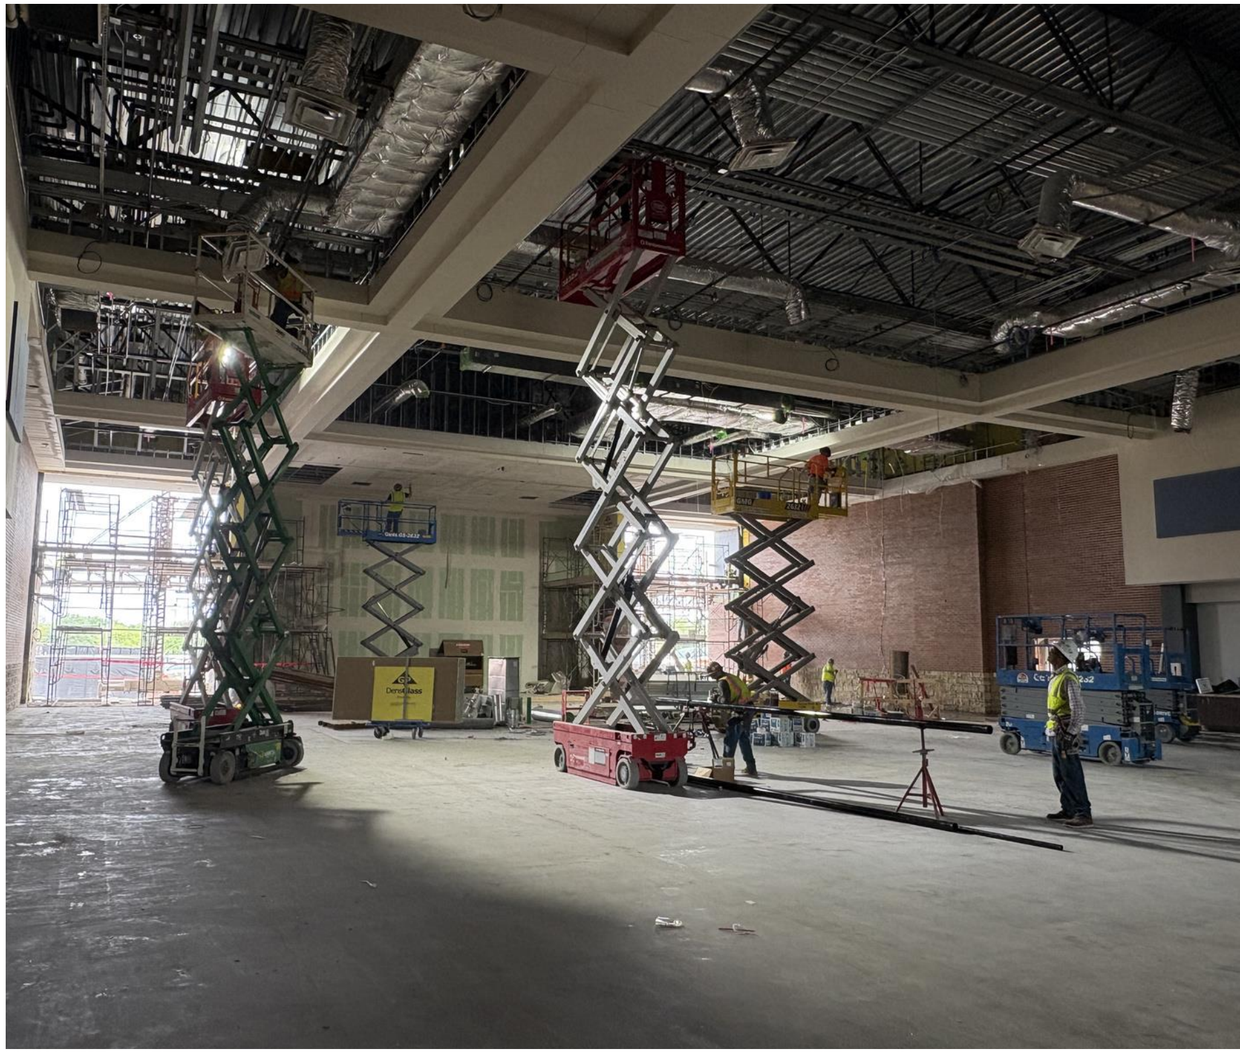

Byron Nelson High School - Arena

5% Complete | Opened: April 2027



V.R. Eaton High School: Performing Arts Center

90% Complete | Target Delivery: June 2026





V.R. Eaton High School: Stadium

40% Complete | Target Delivery: February 2027



V.R. Eaton High School: Arena

5% Complete | Target Delivery: April 2027





V.R. Eaton High School: Cafeteria/Welding

5% Complete | Target Delivery: August 2026



Central Transportation

25% Complete | Opening: December 2026





Davis High School:

50% Complete | Target Delivery: August 2027





Davis High School:

50% Complete | Target Delivery: August 2027





Davis High School:


50% Complete | Target Delivery: August 2027






Davis High School:

50% Complete | Target Delivery:
August 2027

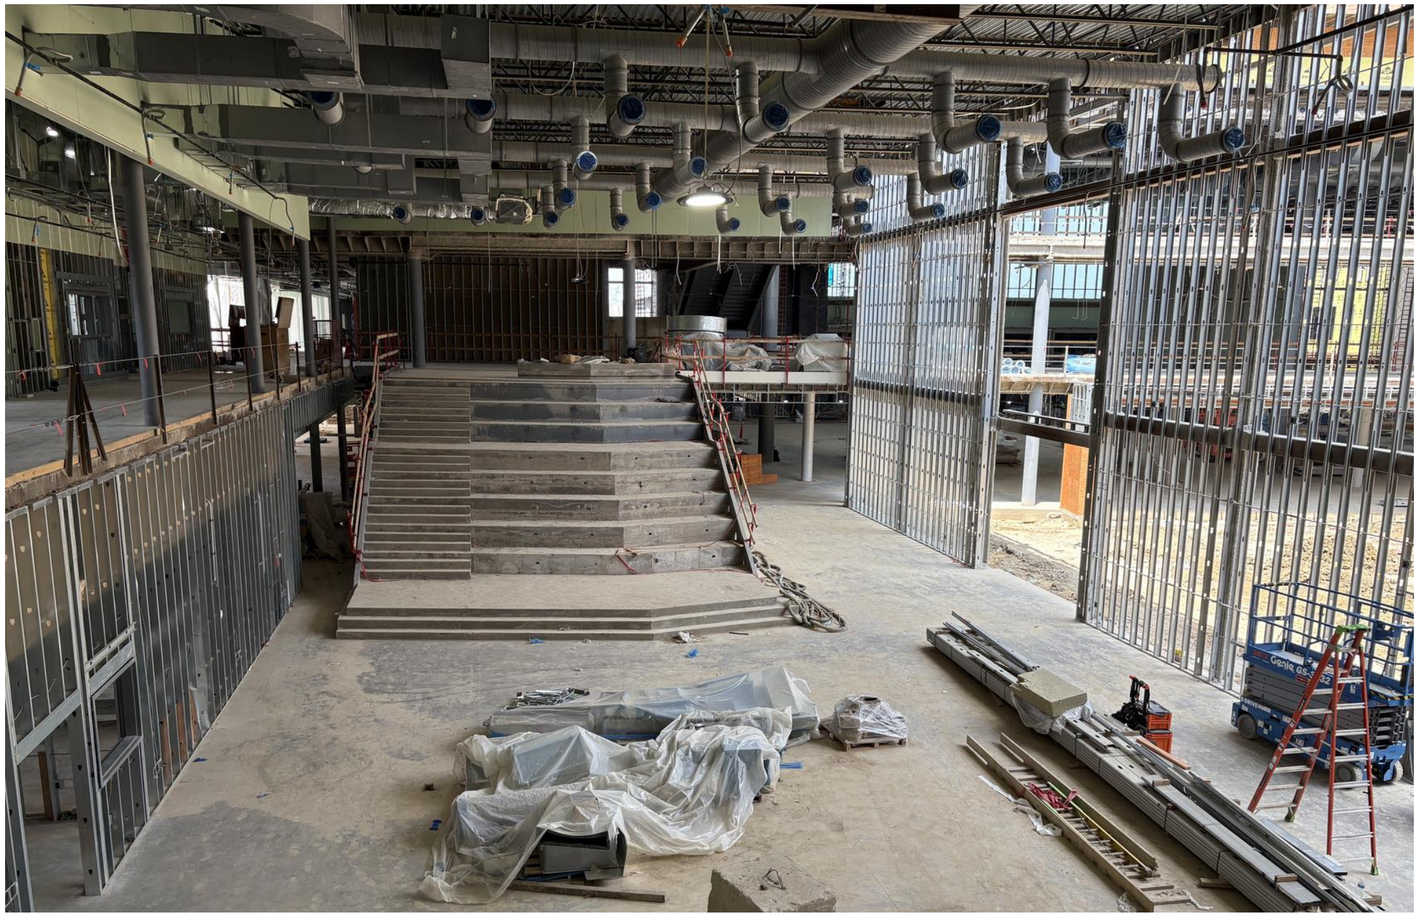



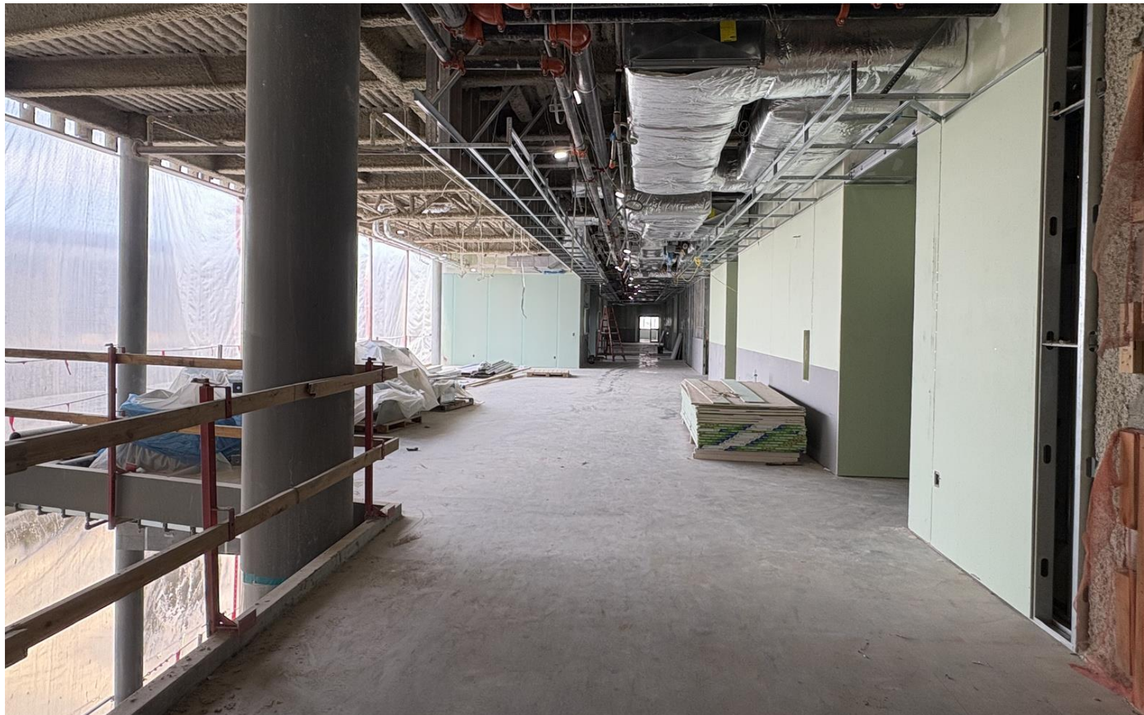

Davis High School: Indoor Activity Center/JROTC

50% Complete | Target Delivery: August 2027





TRACK OUR PROGRESS

www.nisdtxconstruction.org

Northwest Independent School District
Facilities, Planning and Construction

