Paul Laurence Dunbar High School – Roof Replacement

- **Completed/Work in Progress:**
  - Science wing is 99% ready for cap sheet, besides thru wall flashing and penthouse areas.
  - Drainage on the new roof is looking effective and saddles are in place.
  - Several exhaust fans have been raised up to accommodate additional insulation thickness.

- **Upcoming Look Ahead:**
  - Cap sheet installation to begin within next several days.
  - After that, opposite sides of areas ‘A’ and ‘B’ to receive base sheet.
  - Masonry work and penthouse work to begin shortly.
  - Begin sheet metal installation in next couple weeks.

Paul Laurence Dunbar High School – Roof Replacement

Science wing getting ‘Based – In’



Paul Laurence Dunbar High School – Roof Replacement


Progress in areas ‘A’ and ‘B’ ready for cap sheet installation




Paul Laurence Dunbar High School – Roof Replacement

Vent Flashing, Drain Pans and High Wall Flashing



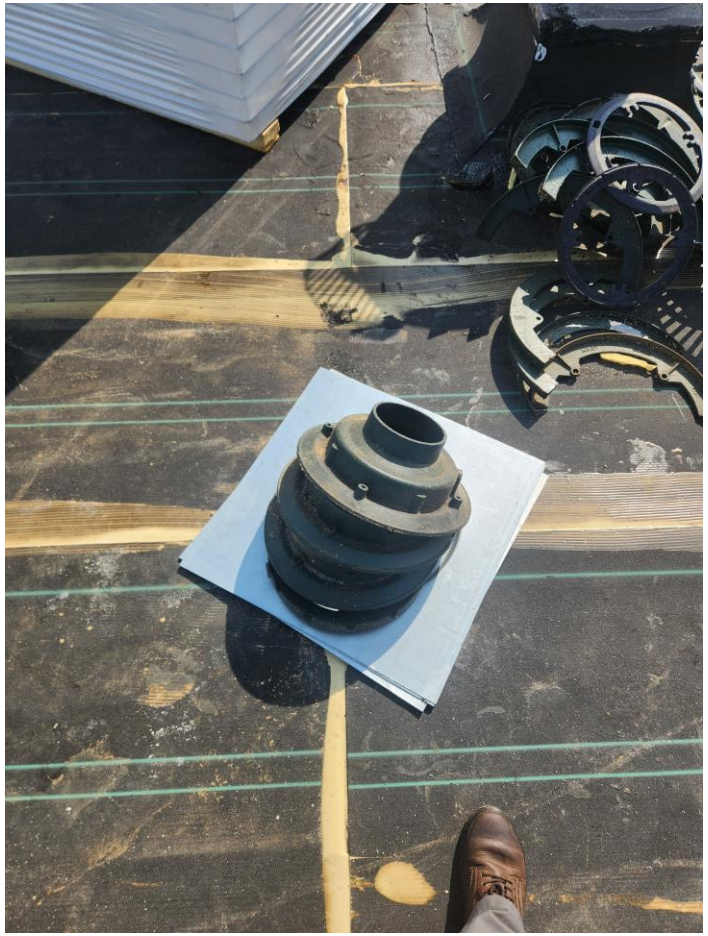

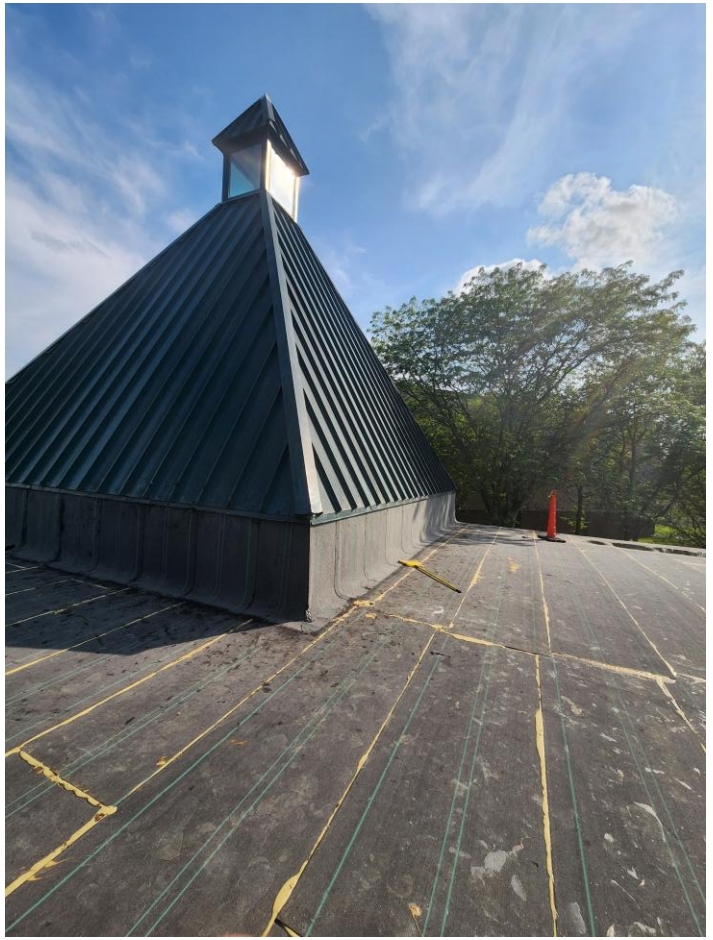

Paul Laurence Dunbar High School – Turf & Track Replacement

- **Completed/Work in Progress:**
  - Site concrete is nearly complete.
  - Shotput is complete.
  - Interior track edge is being prepared for surface coating.
  - Asphalt drive and band staging area asphalt have been paved.
  - Storm structure surface elevations are being brought up to grade.

- **Upcoming Look Ahead:**
  - Site grading to continue.
  - Entry drive apron to be installed.
  - Track surface coating to be installed soon.
  - Fencing to be installed.

Paul Laurence Dunbar High School – Turf & Track Replacement

Turf Installation and Track Surfacing prep




Paul Laurence Dunbar High School – Turf & Track Replacement

Driveway and Shotput pad



Paul Laurence Dunbar High School – Turf & Track Replacement

Long Jump

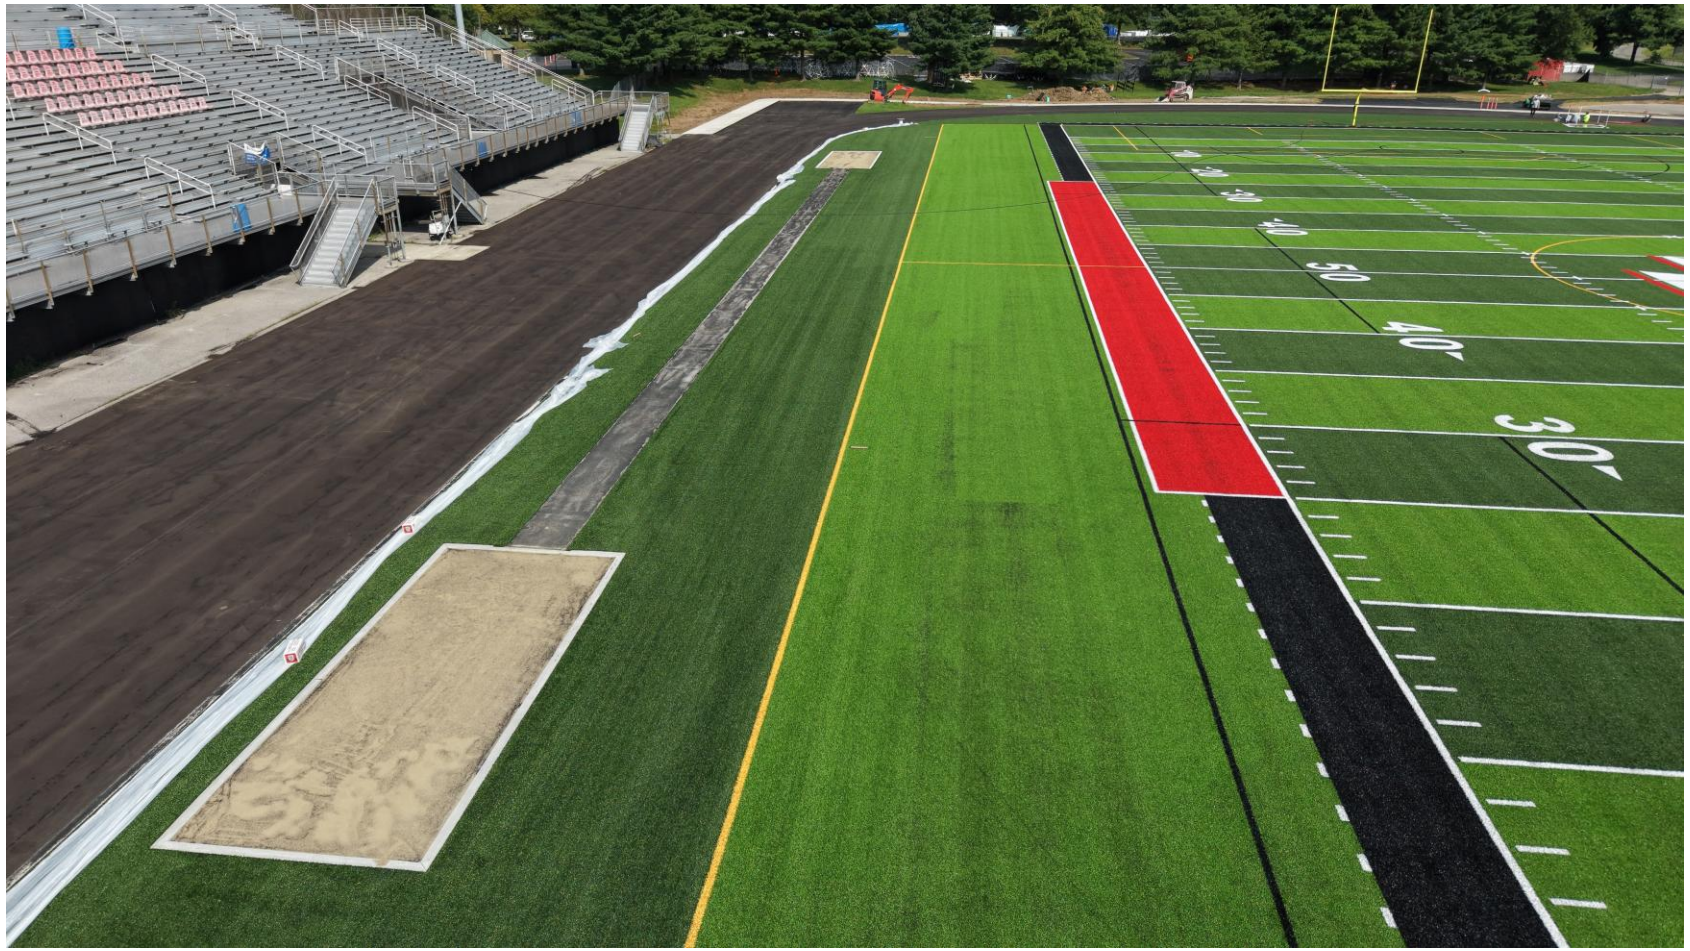

Paul Laurence Dunbar High School – Turf & Track Replacement

D- Zone

