Paul Laurence Dunbar High School – Roof Replacement

- **Completed/Work in Progress:**
  - Penthouse sloped roofing is 75% complete.
  - Thru wall flashing installation is complete for areas A and B.
  - Cafeteria is 100% based in.
  - Classroom areas are receiving cap sheet.
  - Penthouse metal wall panels are largely removed and weather barrier is installed.

- **Upcoming Look Ahead:**
  - Continue attachment of SBS system to CMU walls and thru wall flashing.
  - Cap sheet over remaining classroom and cafeteria areas.
  - Raising gas lines on MAU over cafeteria.
  - Edge metal and flashing tie ins.

Paul Laurence Dunbar High School – Roof Replacement


Weather barrier over Penthouse walls awaiting standing seam metal panels.




Paul Laurence Dunbar High School – Roof Replacement

SBS system flashing to screen wall installation.



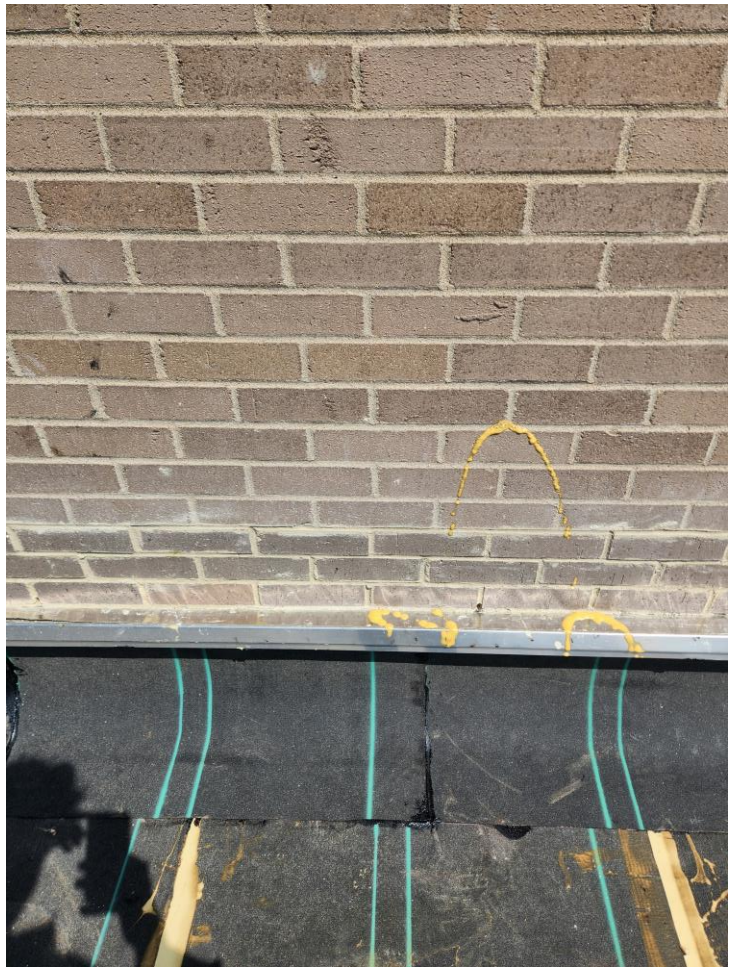

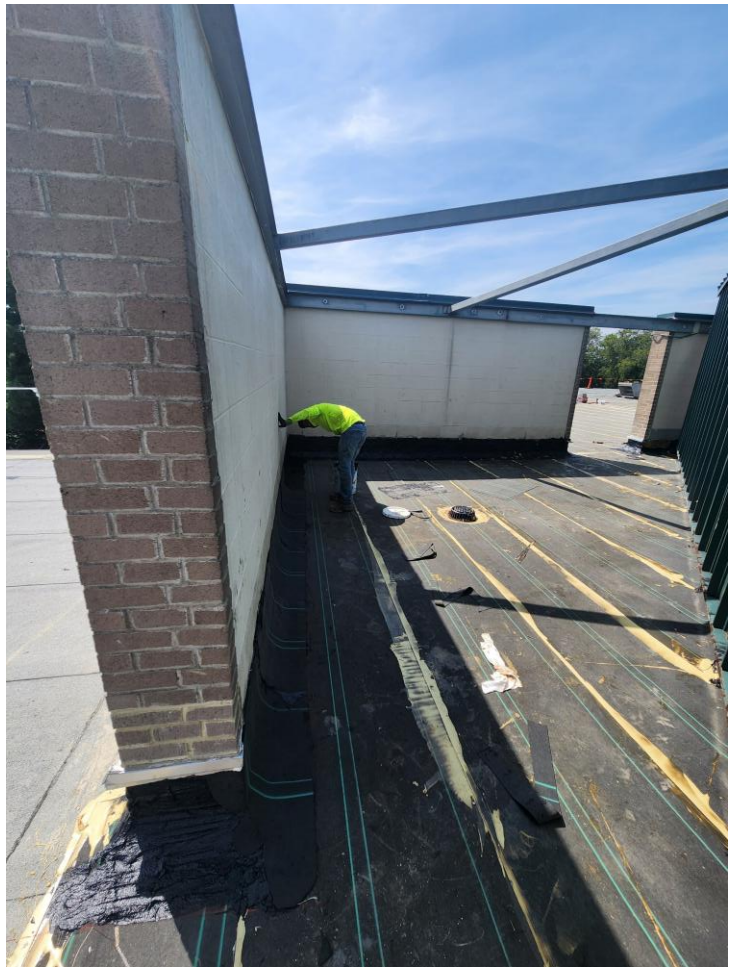

Paul Laurence Dunbar High School – Roof Replacement

Classroom areas are fully ‘based-in’ with SBS



Paul Laurence Dunbar High School – Roof Replacement

Cafeteria wing is fully ‘based-in’ and awaiting cap sheet.



Paul Laurence Dunbar High School – Roof Replacement

Cap sheet installation over classroom areas.



Paul Laurence Dunbar High School – Roof Replacement

Flashing installation on roof access hatch.



Paul Laurence Dunbar High School – Roof Replacement

Staggered joints in SBS system.



Paul Laurence Dunbar High School – Roof Replacement

Various materials stored at the site.

