Lake Mills High School
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

615 Catlin Dr., Lake Mills, Wi 53551 10/01/2026

What's New?

Things are really starting to come together at Lake Mills High School, and it's exciting to see the building take shape week after week! All phases of CMU are now complete, with the exception of the gym entrance, and the addition is really starting to show its character. The lobby structural steel is in place, Area A lobby precast planks are installed and grouted, and the gym storage roof joists are set. Inside, painting is completed in Room 106, while door and window blocking continues throughout the building. Every time we walk through the project, there's something new to see, and the spaces are becoming easier to picture as the finished high school.

There's no slowing down anytime soon! Up next, the team will be pouring the precast topping slab, setting the lobby roof joists, and getting decking installed throughout the lobby and gym storage areas. Gym roof joists will also be going in as the structure continues to rise. On the exterior, AVB detailing and spraying, brick insulation and brick installation, exterior CFMF, and roof blocking will all keep moving forward. With the structure, masonry, and exterior finishes progressing together, the addition is making some exciting strides! It won't be long before these spaces go from construction zones to places where students can learn, compete, and make memories. We're excited to keep watching this one come together!



Gym addition ready for bar joists!



Precast planks being installed for the new office area

DID YOU KNOW?

The new gym addition is 108 feet and 8 inches wide and the new gym joists are going to be 106 feet and 3 inches long and are coming to site in 1 piece at just over 106 feet long! These joists will support the entire gym roof structure.

Questions?

Sr Project Manager: Menno Huiser / mhuiser@findorff.com
Project Engineer: Ben Neumann / bneumann@findorff.com
Superintendent: Dave Ritter / dritter@findorff.com

Findorff
BUILDING & BEYOND

Lake Mills High School
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF



Gym storage bar joists

Work Coming Up


- Pour precast topping slab
- Set lobby roof joists
- Decking on lobby and gym storage
- Install gym roof joists
- Continue detailing and spraying AVB
- Install brick insulation and brick
- Exterior CFMF
- Roof Blocking
- RM117 painted wall logo

Completed Work!

- All phases of CMU (excluding gym entrance)
- Lobby structural steel
- Area A lobby precast planks
- Gym storage roof joists
- Grouting precast planks
- Painting RM106 (wrestling room)
- Door and window blocking



AVB at the new office entrance of the addition

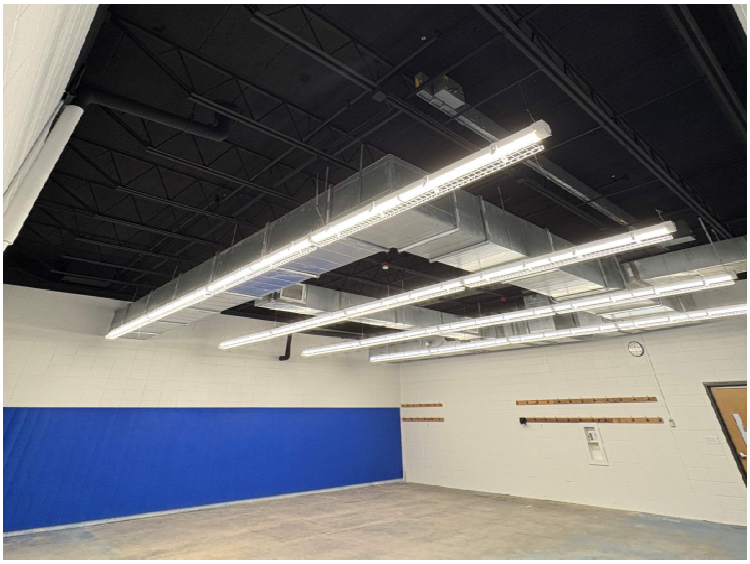

New paint in the wrestling rooms

Questions?

Sr Project Manager: Menno Huiser / mhuiser@findorff.com
Project Engineer: Ben Neumann / bneumann@findorff.com
Superintendent: Dave Ritter / dritter@findorff.com

Findorff
BUILDING & BEYOND

Lake Mills High School
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF



New exterior doors in Area E



Below grade brick and AVB installation



Precast planks installed for the office addition



West elevation with AVB detailing and spray started

Questions?

Sr Project Manager: Menno Huiser / mhuiser@findorff.com
Project Engineer: Ben Neumann / bneumann@findorff.com
Superintendent: Dave Ritter / dritter@findorff.com

Findorff
BUILDING & BEYOND

Drone Photos!!









Questions?

Sr Project Manager: Menno Huiser / mhuiser@findorff.com
Project Engineer: Ben Neumann / bneumann@findorff.com
Superintendent: Dave Ritter / dritter@findorff.com

Findorff
BUILDING & BEYOND
