PASADENA
Unified School District
FACILITIES DEPARTMENT

Interim Swing Space - Franklin ES

Rebuild Fire Damaged Buildings

Construction Progress Update

Report Date: August 28, 2026

Reporting Period - From: August 24, 2026 To: August 28, 2026

Prepared By: **Tammi Owens**

Project Scope of Work:

Site prep for New Admin, Multipurpose Room (MPR), and Kitchen Modular Buildings. New site wide Fire Alarm, Camera, and associated Low Voltage Systems, Site improvements to landscaping and hardscape.

Summary of Work Completed This Period: ONSITE

- Installed stainless steel beams for the lunch shelter, north and west canopy
- Continued rough-in work for the fire alarm and data systems.

Summary of Work Completed This Period: OFFSITE

- Continued progression of the MPR and Kitchen Building

Photo 1:

Description: Lunch shelter



Photo 2:

Description: North canopy



Photo 3:

Description: West canopy



Photo 4:

Description: Rough-in work for the fire alarm and data systems

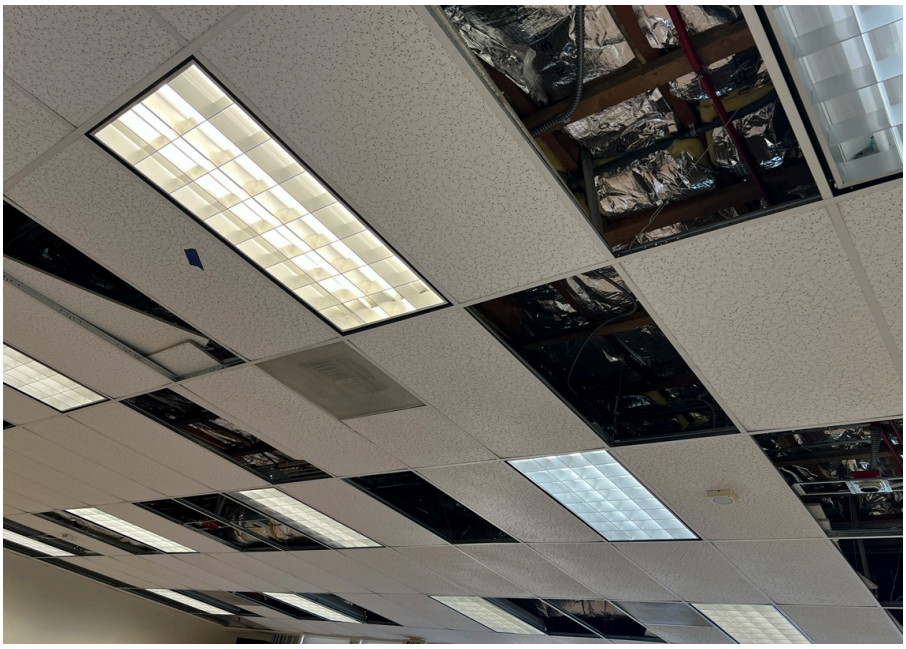


Photo 5:

Description: Continued MPR/Kitchen Building progress



Construction Alerts

- **Description:** No Alerts or Community Notices at this time**.**
- **Site Impact:** Installation of the Administration Building
- **Upcoming Work:** Receiving Administration Building modular segments, Drilling holes for the light pole foundations, Ongoing data and fire alarm rough in
- **Notes/Comments:**Thank you for your continued cooperation and patience as these improvements continue.

Reviewed By: Michael Dunning
