PASADENA Unified School District
FACILITIES DEPARTMENT

Longfellow Modernization Progress Update

Construction Progress Update

Report Date: 10/16/2026 **Prepared By:** Martin Martinez


Reporting Period From: 10/12/2026 **To:** 10/16/2026

1 Summary of Work Completed

- Work resumed this week on the pad for the new cafeteria building. The pad has been completed and certified. Electrical infrastructure was installed, and the casing was poured. Underground plumbing also concluded and the pad was backfilled.
- Metal framing has begun and is ongoing throughout both floors of A building. Mechanical layout started and is ongoing where possible. Drywall also started being installed where possible.
- At the north part of the campus excavation began for the footing for the new retaining wall. Depth was reached and rebar installation is ongoing.

2 Photos

Description: Underground plumbing infrastructure concluded and backfilled.

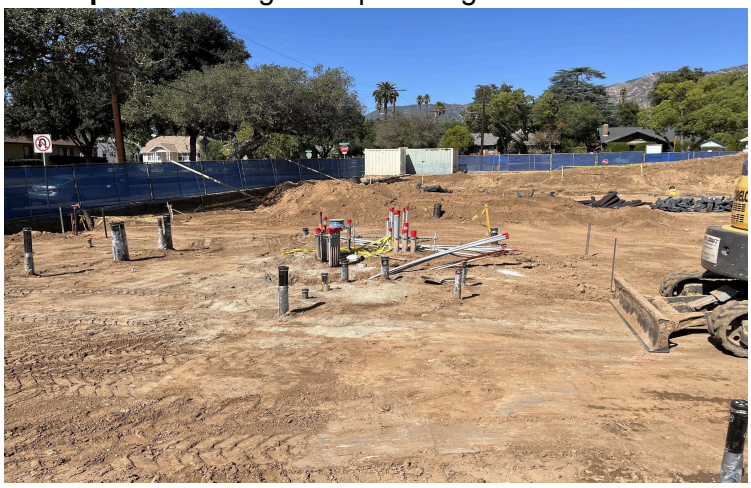

Description: Metal framing is ongoing followed by mechanical layout.



Description: Excavation for the new retaining wall. The footing excavation reached its depth and rebar is now



3 Construction Alerts

Description: Underground utility infrastructure for the new building has now concluded. The pad was backfilled. Metal walls are now being framed. HVAC ducts are now being placed where possible. The footing for the retaining wall now has rebar being installed.

Site Impact: The site is completely closed off. Approved personnel have to wear full PPE whenever onsite.

4 Upcoming Work

Metal framing will be ongoing in the available rooms. Mechanical layout will continue where possible. Foundation work for the new cafeteria building will begin. Installation of rebar will continue at the retaining wall footing.

5 Notes and Comments

Thank you for your continued cooperation and patience as these improvements continue.

Reviewed By: Michael Dunning
