Northwest
INDEPENDENT SCHOOL DISTRICT

FACILITIES, PLANNING & CONSTRUCTION UPDATE

October 26, 2026



The 2026-2027 Delivery Roadmap



DECEMBER 2026

CENTRAL TRANSPORTATION CENTER

EATON HS CAFETERIA

FEBRUARY 2027

BYRON NELSON HS: STADIUM

MAY 2027

EATON HS: ARENA


EATON HS: STADIUM

BYRON NELSON HS: ARENA


AUGUST 2027

DAVIS HS: CAMPUS
STADIUM
BROCK AG CENTER


District Portfolio Status Dashboard

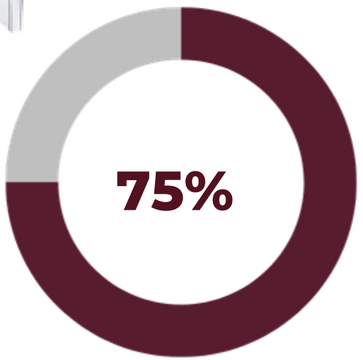


Central Transportation Relocation

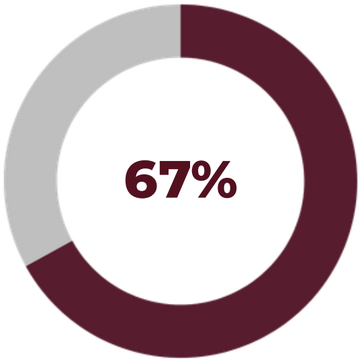


Davis High School

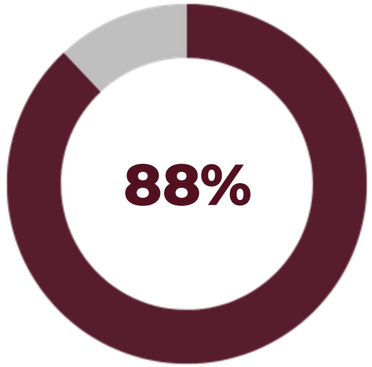


Byron Nelson HS Stadium

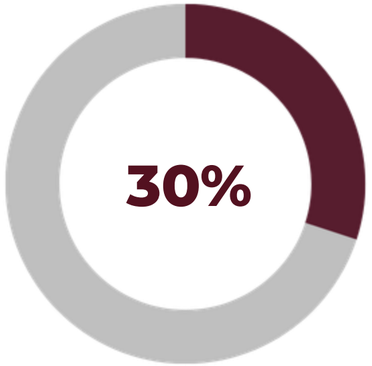


Byron Nelson HS Arena

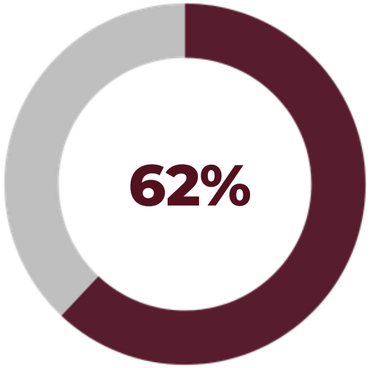

Eaton HS Stadium

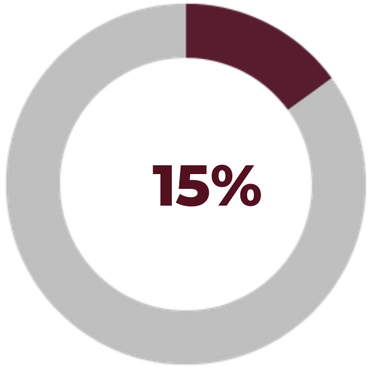

Eaton HS Arena

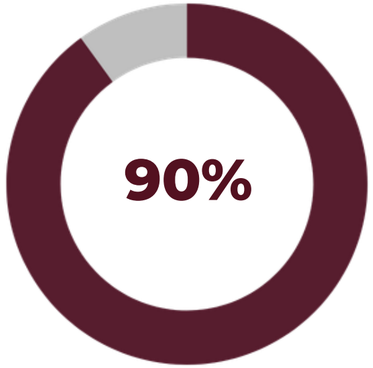

Eaton HS Cafeteria


Byron Nelson HS: Stadium


88% Complete | Target Delivery: February 2027



Byron Nelson HS: Arena

30% Complete | Target Delivery: May 2027

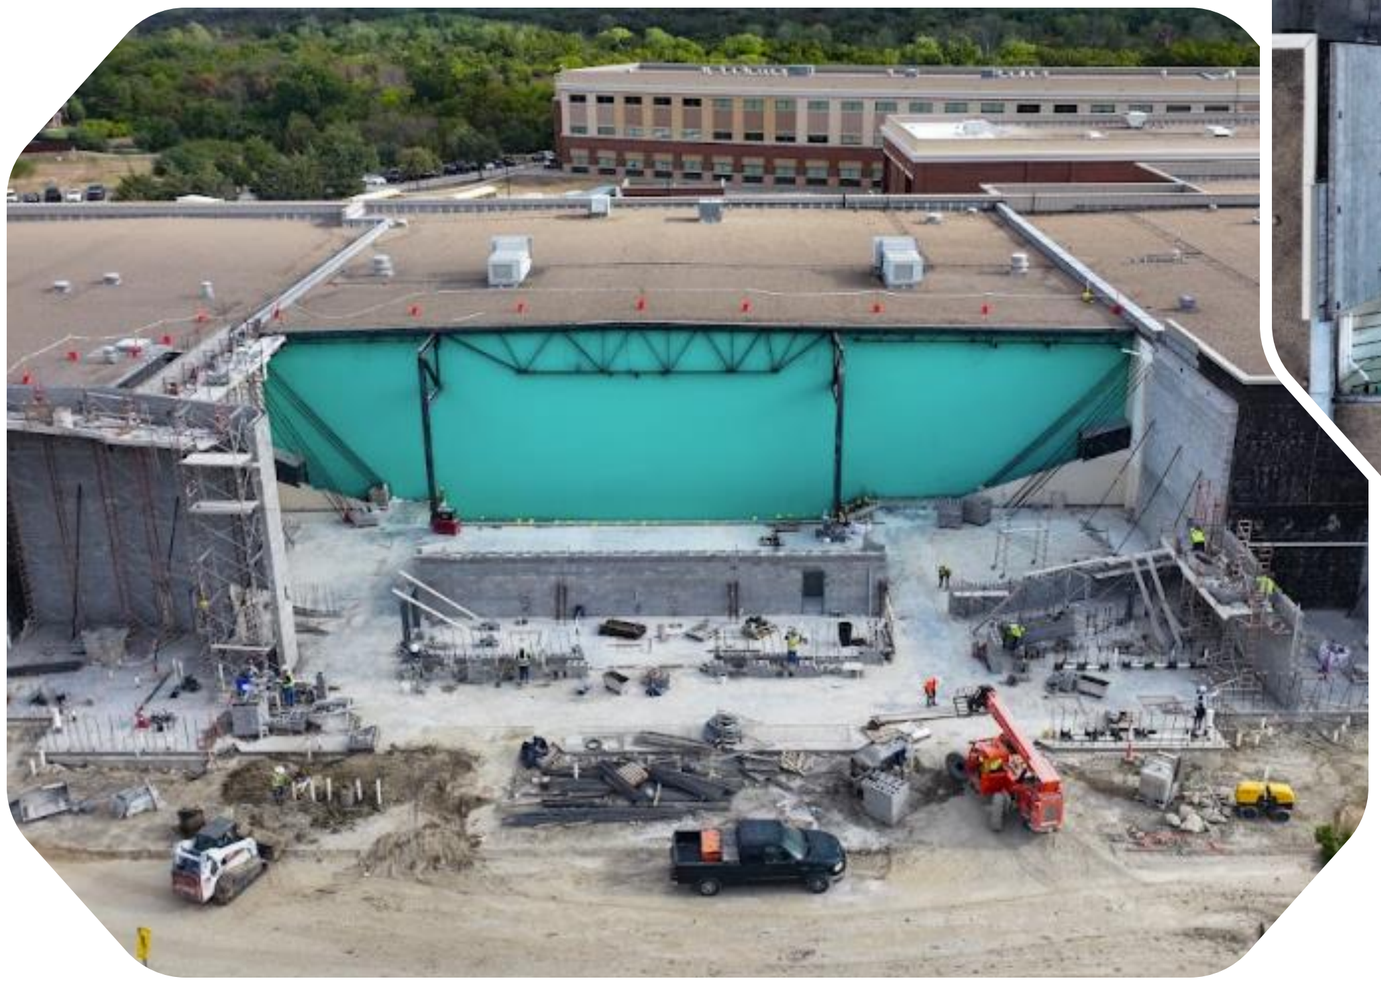

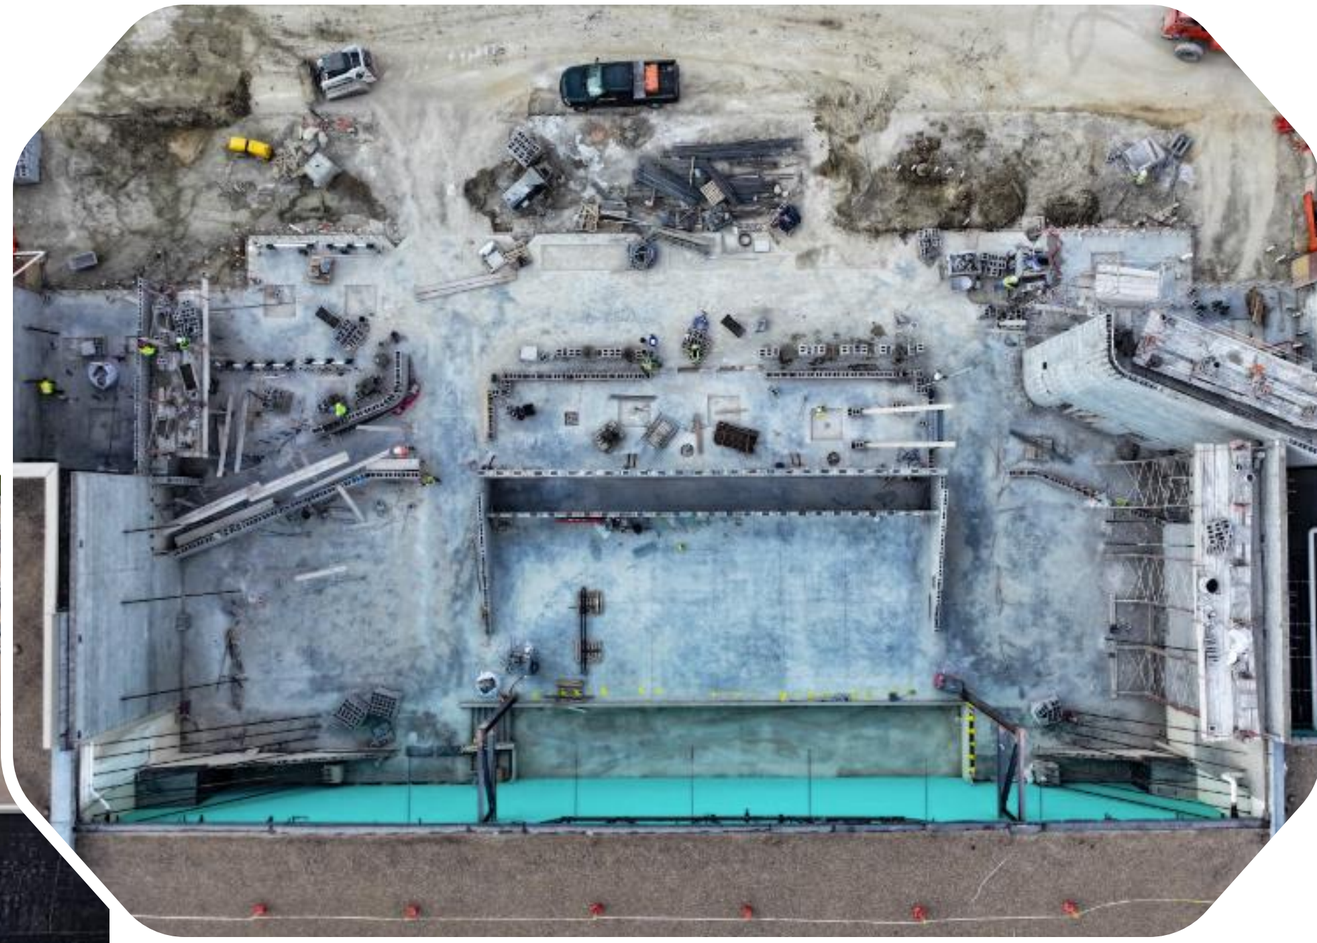

Eaton HS: Stadium

62% Complete | Target Delivery: May 2027



Eaton HS: Arena

15% Complete | Target Delivery: May 2027





Eaton High School: Cafeteria

85% Complete | Target Delivery: December 2026



Central Transportation

75% Complete | Opening: December 2026



Davis High School:

67% Complete | Target Delivery: August 2027



Davis High School:

67% Complete | Target Delivery: August 2027





TRACK OUR PROGRESS

www.nisdtxconstruction.org

Northwest Independent School District
Facilities, Planning and Construction

