DeKalb County School District | Operations

Project Update Report

Report Date	9/24/2026
Project Name/Number	Idlewood ES / 23336
Facility Name	Idlewood Elementary School
Area Superintendent	Dr. Terri Brown
Principal	Robin Elder
School Contact	Robin_elder@dekalbschools.org
Project Manager	Joseph King
Architect	Cooper Carry & Associates, INC
Contractor	Balfour Beatty Construction

Scope of Work:

Major building renovations, HVAC replacement, and fire sprinkler installation

---

Project Construction Budget: $33,054,126

Project Schedule Milestones:

- Design Completion: May 2025
- General Contractor Procurement: July 2024
- Construction Start: August 2025
- Phase 1 Completion: July 2026
- Construction End: July 2027

Current Project Status:

- Phase 2b Restroom flooring installation
- Punch list items completing in turned over area
- All classrooms have new HVAC systems installed
- Courtyard landscaping and regrading
- Generator replaced and electrical panel switched over

4-Week Look Ahead

- Above ceiling completion
- Painting in phase 2b
- Restroom fixtures and partitions


Project Photographs




Front canopy metal panel installation



Courtyard beginning landscaping

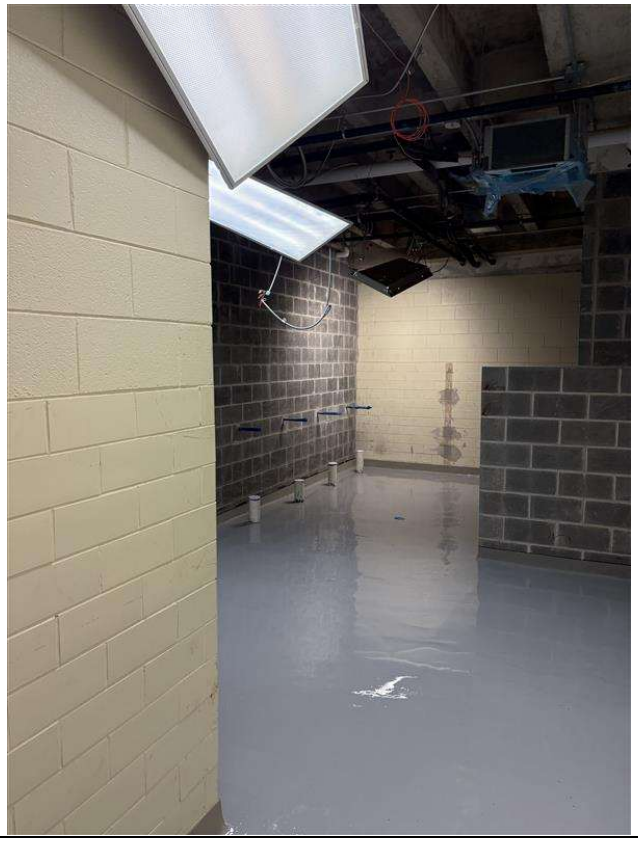

Gang restroom epoxy leveling

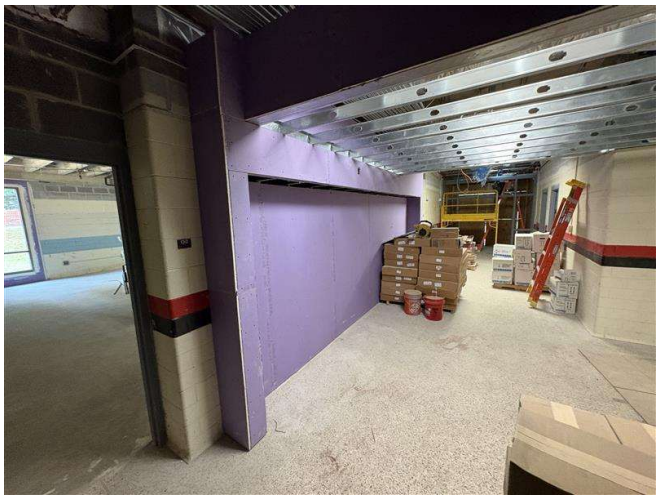

Hallway cubby and hard ceiling framing + drywall
