DeKalb County School District | Operations

Project Update Report

Report Date	10/10/26
Project Name/Number	Champion/35835
Principal	*Dr. Angel Rivers*
School Contact	*Dr. Angel Rivers*
Regional Superintendent	*Jacqueline Taylor*
Project Manager	Joseph King
Architect	SSOE, INC
Contractor	Balfour Beatty

Scope of Work

- Major building system replacement with emphasis on HVAC – Components
- Fire sprinkler installation
- Old Rock Gym design

Project Construction Budget $34,525,000

Project Schedule Milestones

- Design Completion – December 2022
- General Contractor Procurement – January 2024
- Construction Start – February 2024
- Construction End – July 2027

Current Project Status:


- 100% Complete with Phase 3 as of August 2026
- Phase 4 (Final Phase) to begin fall of 2026


4-Week Look Ahead

- Phased window replacement
- Install new furniture

End of Project Update Report

Photographs

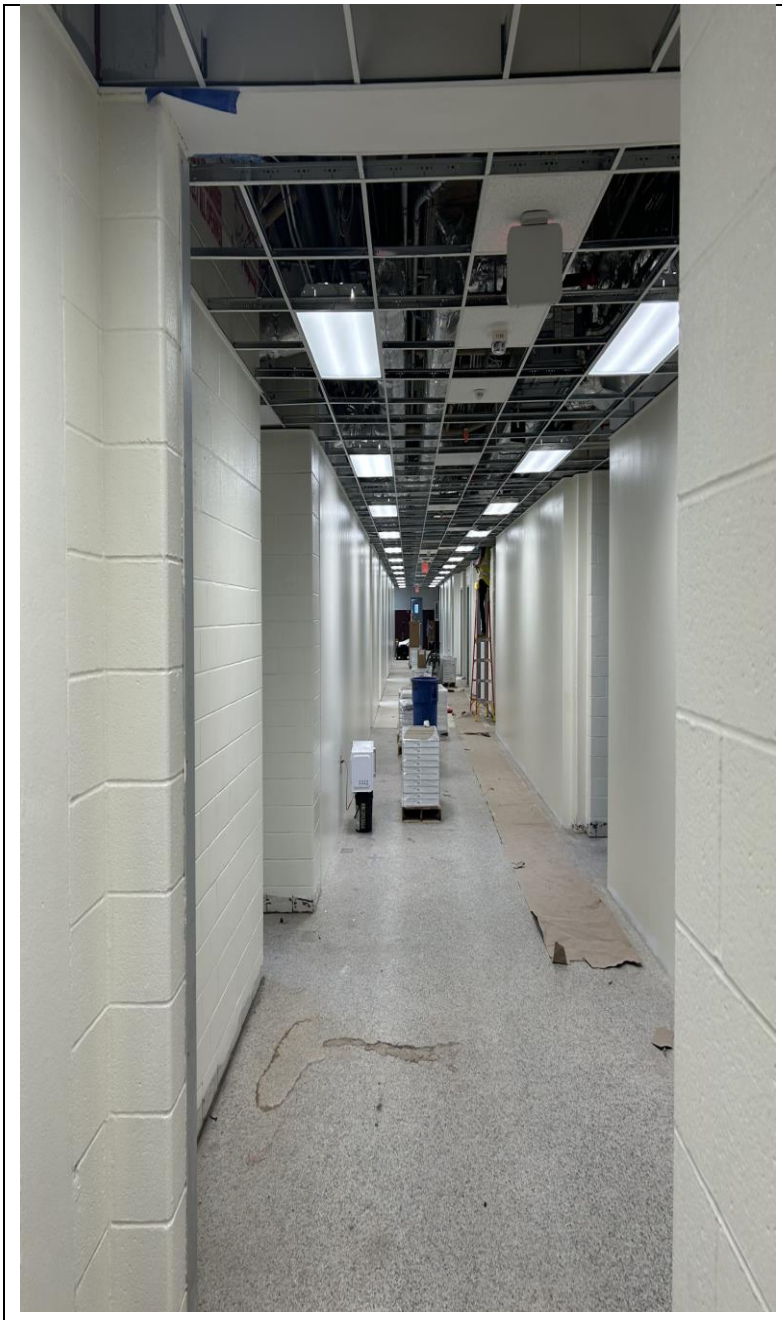

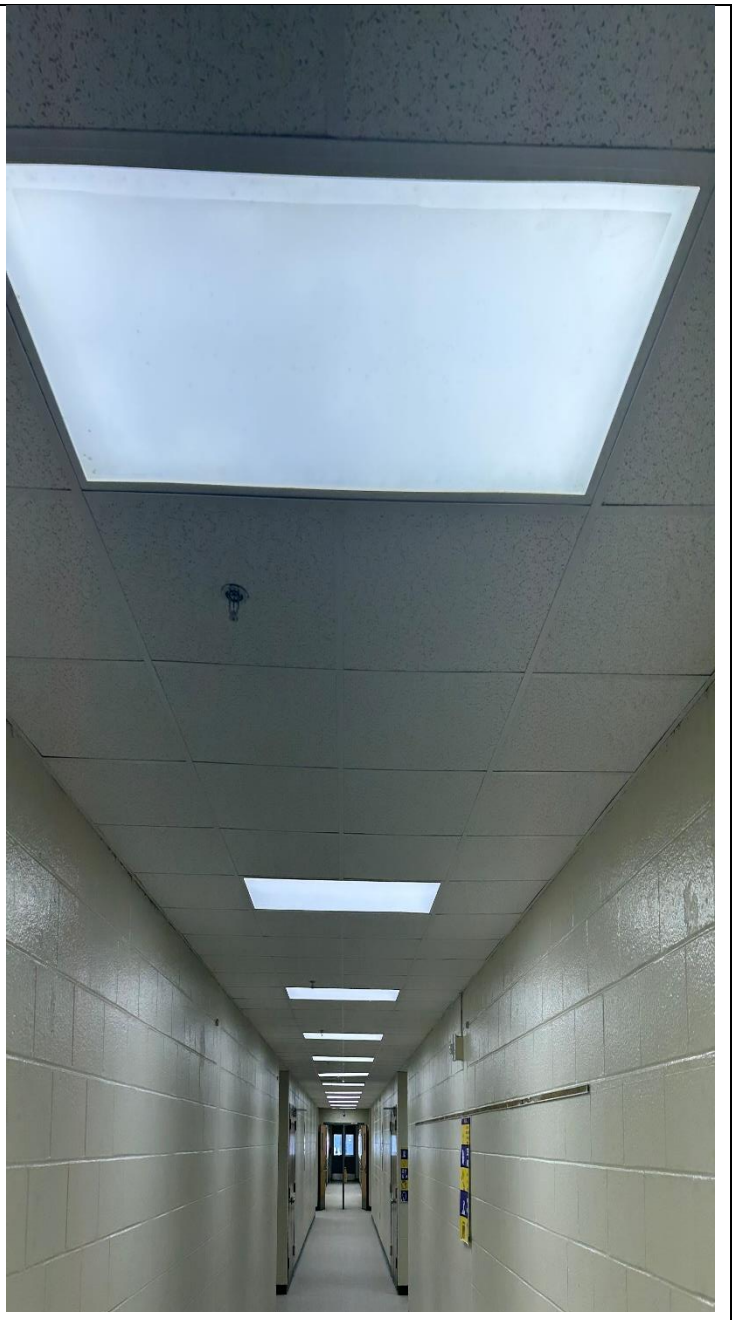

Caption	Caption
