DeKalb County School District | Operations

# Project Update Report

| | |
|---|---|
| Report Date | October 10, 2026 |
| Project Name/Number | Redan MS / 32235 |
| Facility Name | Redan MS |
| Area Superintendent | Bridgette Allen |
| Principal | Dr. Danielle Barnes |
| School Contact | Danielle_V_Barnes@dekalbschoolsga.org |
| Project Manager | Laura Flagg |
| Architect | GMC |
| Contractor | CWI |

**Scope of Work:**

- Final phase includes completing the renovation of the gym, cafeteria, administration offices, band and chorus rooms.

---

**Project Construction Budget:** $ 5,234,083

---

**Project Schedule Milestones**:

- Construction Start – June 2023
- Construction End – July 2026

---

**Current Project Status:**

- CWI installed the new ceiling grid and reinstalled ACT.
- Architect is reviewing turnover documentation.

---

**4-Week Look Ahead**

- CWI to complete turnover package.
- CWI to prepare for the final pay application.


# Project Photographs



Redan MS – Removing Kitchen Ceilings



Redan MS – Removing Kitchen Ceilings

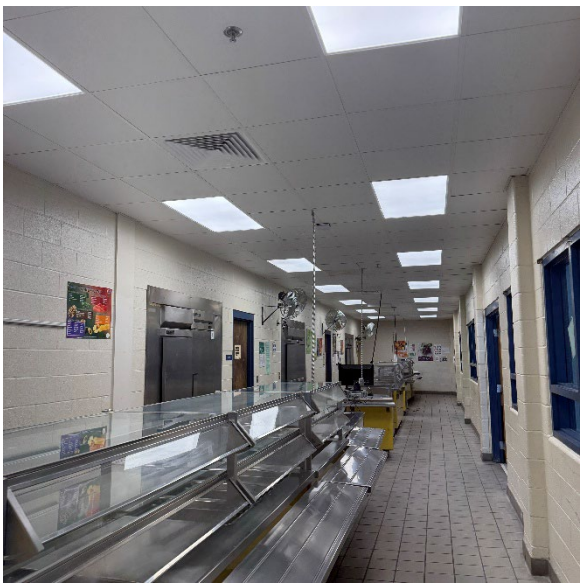

Redan MS – New Grid and ACT Installed



Redan MS – New Grid and ACT Installed
