DeKalb County School District | Operations

Project Update Report

Report Date	10/10/26
Project Name/Number	New Sequoyah MS & HS/ 10136
Principal	*Lauren Pells*
School Contact	*Lauren_Pells@dekalbschoolsga.org*
Regional Superintendent	*Jacqueline Taylor*
Project Manager	Joseph King
Architect	*GMC Architects*
Contractor	Gilbane

Scope of Work

- New construction of Sequoya MS and Sequoya HS

Project Construction Budget $235,000,000

Project Schedule Milestones

- Design Completion - January 2025
- General Contractor Procurement – February 2025
- Construction Start - February 2025
- Construction End – August 2029

Current Project Status:


- Middle school towers are complete
- Middle school steel is complete
- Middle school HVAC complete
- Water proofing complete

4-Week Look Ahead

- Interior painting of middle school
- Ceiling grid 70% complete
- Elevator 80% complete

End of Project Update Report

Photographs

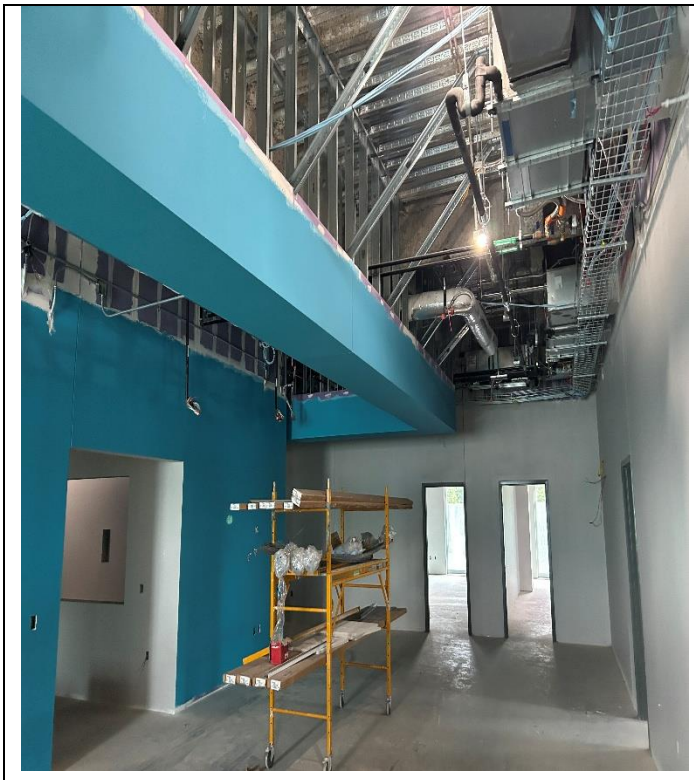

Caption



Caption
